



# Monitoring & Evaluation Cell

Planning & Development Department  
Government of Sindh



## ANNUAL REPORT 2014-15

Produced & Published by:

Monitoring & Evaluation Cell (MEC),  
Planning & Development Department,  
Government of Sindh

[www.mecsindh.gov.pk](http://www.mecsindh.gov.pk)





# MEC ANNUAL REPORT 2014-15

Prepared by: Naveed Mansoor, Director (MIS)

Reviewed by: Syed Imtiaz Ali Shah, DG-MEC

Approved by: Ajaz Ali Khan, ACS (Dev)



## Contents

<b>EXECUTIVE SUMMARY .....</b>	<b>4</b>
<b>VISION .....</b>	<b>8</b>
<b>MISSION .....</b>	<b>8</b>
<b>HISTORY OF MEC .....</b>	<b>9</b>
<b>FUNCTIONS OF MEC.....</b>	<b>11</b>
<b>THE MONITORING PROCESS - AUTOMATED.....</b>	<b>12</b>
<b>ADP 2014-15 ANALYSIS .....</b>	<b>13</b>
DISTRICT-WISE DISTRIBUTION OF FUNDS (RS. IN MILLION).....	13
DEPARTMENT-WISE DISTRIBUTION OF FUNDS .....	14
COMPARISON OF DISTRICT-WISE DISTRIBUTION OF FUNDS .....	15
2014 COMPARISON OF DISTRICT WISE POPULATION (PROJECTED) .....	16
<b>COST ANALYSIS OF ADP SCHEMES IN FY 2014-2015 .....</b>	<b>17</b>
<b>MONITORING CONDUCTED IN FY 2014-2015 .....</b>	<b>18</b>
<b>DEPARTMENT WISE MONITORING CHART .....</b>	<b>24</b>
<b>DISTRICT WISE MONITORING CHART .....</b>	<b>26</b>
<b>SUMMARY OF FIELD MONITORING OBSERVATION .....</b>	<b>27</b>
<b>MONTHLY MONITORING PERFORMANCE .....</b>	<b>28</b>
<b>MONTHLY MONITORING TREND.....</b>	<b>29</b>
<b>COMPLIANCES RECEIVED .....</b>	<b>30</b>
<b>COMPARISON OF MONITORING BY REGIONS .....</b>	<b>33</b>
<b>MONITORING OF ADP COMPLETED SCHEMES.....</b>	<b>35</b>
<b>THIRD PARTY MONITORING (TPM) .....</b>	<b>36</b>
<b>SECTOR ANALYSIS BY FIELD MONITORING .....</b>	<b>37</b>
ROADS: .....	37
IRRIGATION (WATER & DRAINAGE): .....	37
PUBLIC HEALTH AND ENGINEERING (PHED): .....	38
BUILDINGS: .....	39
EDUCATION: .....	40
HEALTH: .....	40
AGRICULTURE & FOREST/LIVESTOCK & FISHERIES/WOMEN DEVELOPMENT DEPARTMENT: .....	41
<b>ADP 2014-15 TECHNICAL ANALYTICS .....</b>	<b>42</b>
ADP 2014-15 HIGHLIGHTS .....	42
DEPARTMENTS REQUIRING BETTER PROJECT IMPLEMENTATION MONITORING HIGHLIGHT OF MAJOR SECTORS.....	42
DISTRICTS THAT NEED BETTER PROJECT IMPLEMENTATION HIGHEST UNSATISFACTORY SCHEMES .....	43
REPORTING PERFORMANCE BY REGIONAL OFFICES AT HYDERABAD AND SUKKUR .....	43
<b>FINANCIAL REVIEW: RELEASES AND UTILISATION .....</b>	<b>44</b>
<b>RECENT DECISIONS .....</b>	<b>46</b>
<b>MEDIA &amp; NEWSPAPER SNAPSHOTS .....</b>	<b>47</b>
<b>REVIEW MEETING OF SUKKUR .....</b>	<b>48</b>
<b>MONITORING SNAPSHOTS.....</b>	<b>49</b>
<b>PERFORMANCE OF THE MIS DIRECTORATE .....</b>	<b>52</b>
<b>THE WAY FORWARD .....</b>	<b>53</b>
<b>OBJECTIVE .....</b>	<b>53</b>
<b>MEC PLANS: .....</b>	<b>53</b>
<b>MIS PLANS: .....</b>	<b>53</b>
<b>FUTURE STRATEGY .....</b>	<b>54</b>
<b>MONITORING .....</b>	<b>54</b>
<b>ANNEXURE A – DETAIL OF COMPLETED SCHEMES .....</b>	<b>55</b>
<b>ANNEXURE B – MONITORED SCHEMES .....</b>	<b>83</b>
<b>ANNEXURE C - ACRONYMS .....</b>	<b>134</b>

## Executive Summary

This report presents a summary and analysis of results accomplished at Monitoring & Evaluation Cell, Planning & Development Department, Government of Sindh during fiscal year 2014-15. It emphasizes the findings and conclusions that have been compiled from various monitoring activities and data sources. Most of the data gathered from our online monitoring system FilMS (File Management System).



Monitoring and evaluation are important management tools to track progress and facilitate decision making. While some donor/funding agencies require some type of evaluative process, the greatest beneficiaries of an evaluation can be the community of people with whom your organization works. By closely examining your work, your organization can design programs and activities that are effective, efficient, and yield powerful results for the community.

Planning & Development Department, Government of Sindh, launched a project in 2010 for Strengthening of Monitoring & Evaluation Cell in Planning & Development Department, introducing Outsourcing for Third Party Monitoring, which aimed at strengthening of the Monitoring & Evaluation system of Sindh Government's Public Sector Projects and Schemes/Service Centres/Units. The project ended in 2015 with substantial capacity and capability enhancement.



**Syed Murad Ali Shah**

## MESSAGE FROM THE MINISTER

I am extremely pleased to present this Annual Report of Monitoring & Evaluation Cell, Planning & Development Department for the fiscal year ending 2014-15.

This report reveals some important highlights on the quality of work in public sector development projects, gathered through field monitoring conducted by MEC. It also sheds light on general bottlenecks and issues faced in execution of schemes while pointing out schemes that are satisfactory and unsatisfactory in their physical progress. However, much still needs to be done to improve the quality of works.

I hope that the availability of such information will help enhance future policies, planning and resource allocation by taking evidence based decisions. It will improve sustainable development in Sindh and will allow the Government to take corrective and preventive actions.

In the end, I would like to congratulate MEC for keeping up the practice of producing a concise journal of efforts and achievements.



**Ajaz Ali Khan**

## MESSAGE FROM THE ADDITIONAL CHIEF SECRETARY

In addition to being responsible for advising the government on development policy and planning which includes scrutiny, approval and sustainability of development schemes; an important aspect of its functions include life cycle of monitoring and evaluation of development programs and projects, through Monitoring and Evaluation Cell, to ensure timely progress and completion, of development works, to the satisfaction of target population, public at large and Provincial Government.

This Annual Report records the achievements of the Monitoring & Evaluation Cell during the last financial year 2014-15. The task of Scheme Monitoring is an enormous responsibility, and the team of this institution deserves appreciation. I am pleased to see MEC having done well to assist P&D in taking informed decisions based on their information from field monitoring.

It indeed gives me a great pleasure and a sense of pride that Monitoring and Evaluation Cell of Planning & Development has put together a comprehensive document on its endeavours during the year 2014-15.

This annual report of MEC presents data and achievement of various development projects, in addition to providing support to decision makers in evaluation of effectiveness of the project(s) vis-a-vis fulfilment of overall development objectives for the province.

As we move forward, we need to keep a balance among the different development priorities. The first priority must be to pay special attention to quality of works in public sector by continuous monitoring of development schemes.





**Syed Imtiaz Ali Shah**

.....

## MESSAGE FROM THE DIRECTOR GENERAL MEC

.....

I am honored to present the 2nd Annual Report for 2014-15 to record the activities and performance of the Monitoring & Evaluation Cell. MEC is proud to be assisting the P&D Department in pursuing its goals of precise service delivery in public works by keeping a strict watch on development schemes.

The Monitoring Reports of MEC as an external monitoring agency, generated through Field Monitoring contributes towards the transparency & accountability of the executing agencies / administrative departments in carrying out Public Works.

Quality in public works demand vigilant monitoring, quick reporting and prompt reaction. With highest level of efficiency in place through the use of innovative IT systems, MEC is able to keep the concerned authorities up to date with its online systems. MEC now acts with high efficiency through its paperless workflow environment. It uses the modern technology to collect all the monitoring data through an automated web-based workflow automation system, FilMS (File Management System), which connects our offices at Karachi, Hyderabad and Sukkur and helps the stakeholders in taking quick and informed decisions.

From the regular field monitoring visits to the development of web-based systems to facilitate easier, quicker and more accurate reporting of field monitoring information, MEC is helping to provide an improved basis for taking prompt decisions. MEC's evidence-based reports have brought immediate attention to resolve bottlenecks/issues and highlight schemes where the quality of work and physical progress is not satisfactory.

We are focused on the execution of our growth strategy while continuing to build the strength and capabilities of MEC. I am incredibly excited about our vision and initiatives. I truly believe that the best

output of MEC is yet to come and would become a model of excellence in service delivery.

## Vision

*Enable Precise Deliverables  
in Public Works through  
Proactive Facilitation*



## Mission

1. To ensure that the Standard of Quality is maintained in development projects
2. To keep a regular watch on the progress of schemes
3. To enable timely & informed decisions through efficient reporting
4. To promote and enhance institutional learning and knowledge through instant availability of chronological indicators
5. To coordinate with various authorities for smooth and unhindered implementation
6. Review and Evaluate the output & outcome of schemes



## History of MEC

- M&E Cell was established in 1985
- Total Development Outlay in 1985 was Rs. 1.533 billion
- Total Development Outlay in 2009-10: Rs. 90 billion
- Total strength of Cell in 1985: 29 including 8 officers
- Total strength of the Cell in 2009 was same as in 1985



### PRESENT

To strengthen the monitoring, Sindh Cabinet in its meeting held on 16-June-2008 decided that:

- "In order to improve the quality of construction, monitoring of projects by the Planning & Development Department and concerned Administrative Departments is an important requirement. However, in order to seek un-biased reports, Third Party Monitoring (TPM) of the projects has become very necessary. As such 1% funds out of the development schemes may be placed with the Planning & Development for Third Party Monitoring"
- Under ADB funded programme "The Sindh Growth & Rural Revitalization Programme (SGRRP)", one of the loan covenants is "to improve the monitoring and evaluation cell/system in P&D department of GOS by Strengthening the MEC"
- In order to ensure quality & transparency in public works and to fulfil the above conditions, a scheme namely "Strengthening of Monitoring &



Evaluation Cell P&D including out sourcing for third party monitoring" was approved by PDWP in December, 2008 with the following objectives:

- Program monitoring & evaluation would become an important input for Government's decision-making and prioritization, particularly in the budget process.
- Regular monitoring & evaluation would bring forward performance of ongoing activities at service centre, at the project, program, sector and unit level. These can thus act as a management tool leading to learning and improvement in future.
- Evaluation based on scientific monitoring would contribute to accountability mechanism, whereby executing agencies can be held accountable for performance of their activities.

## Functions of MEC


The M&E Cell deals with the following subjects:

1. Monitoring the progress and evaluation/examination of provincial development schemes
2. Verification of physical and financial progress of development schemes through field visits
3. Identifying bottlenecks in financial and physical progress of schemes included in the ADP
4. Preparing annual review document of ADP
5. Preparing working papers for the provincial cabinet on the review of ADP on monthly/quarterly basis
6. Scrutiny & compilation of Monthly Progress Reports of ADP received from A.D.s and District Governments
7. Coordination of federally funded projects
8. Compilation of monthly progress reports & review of federally funded projects executed by Government of Sindh
9. Coordination of President and Prime Minister directives
10. Review of President's directives pertaining to development
11. Coordination and review of Chief Minister's directive.




## The Monitoring Process - Automated

Following is the automated monitoring process used in MEC through online system called FILMS (File Management System)

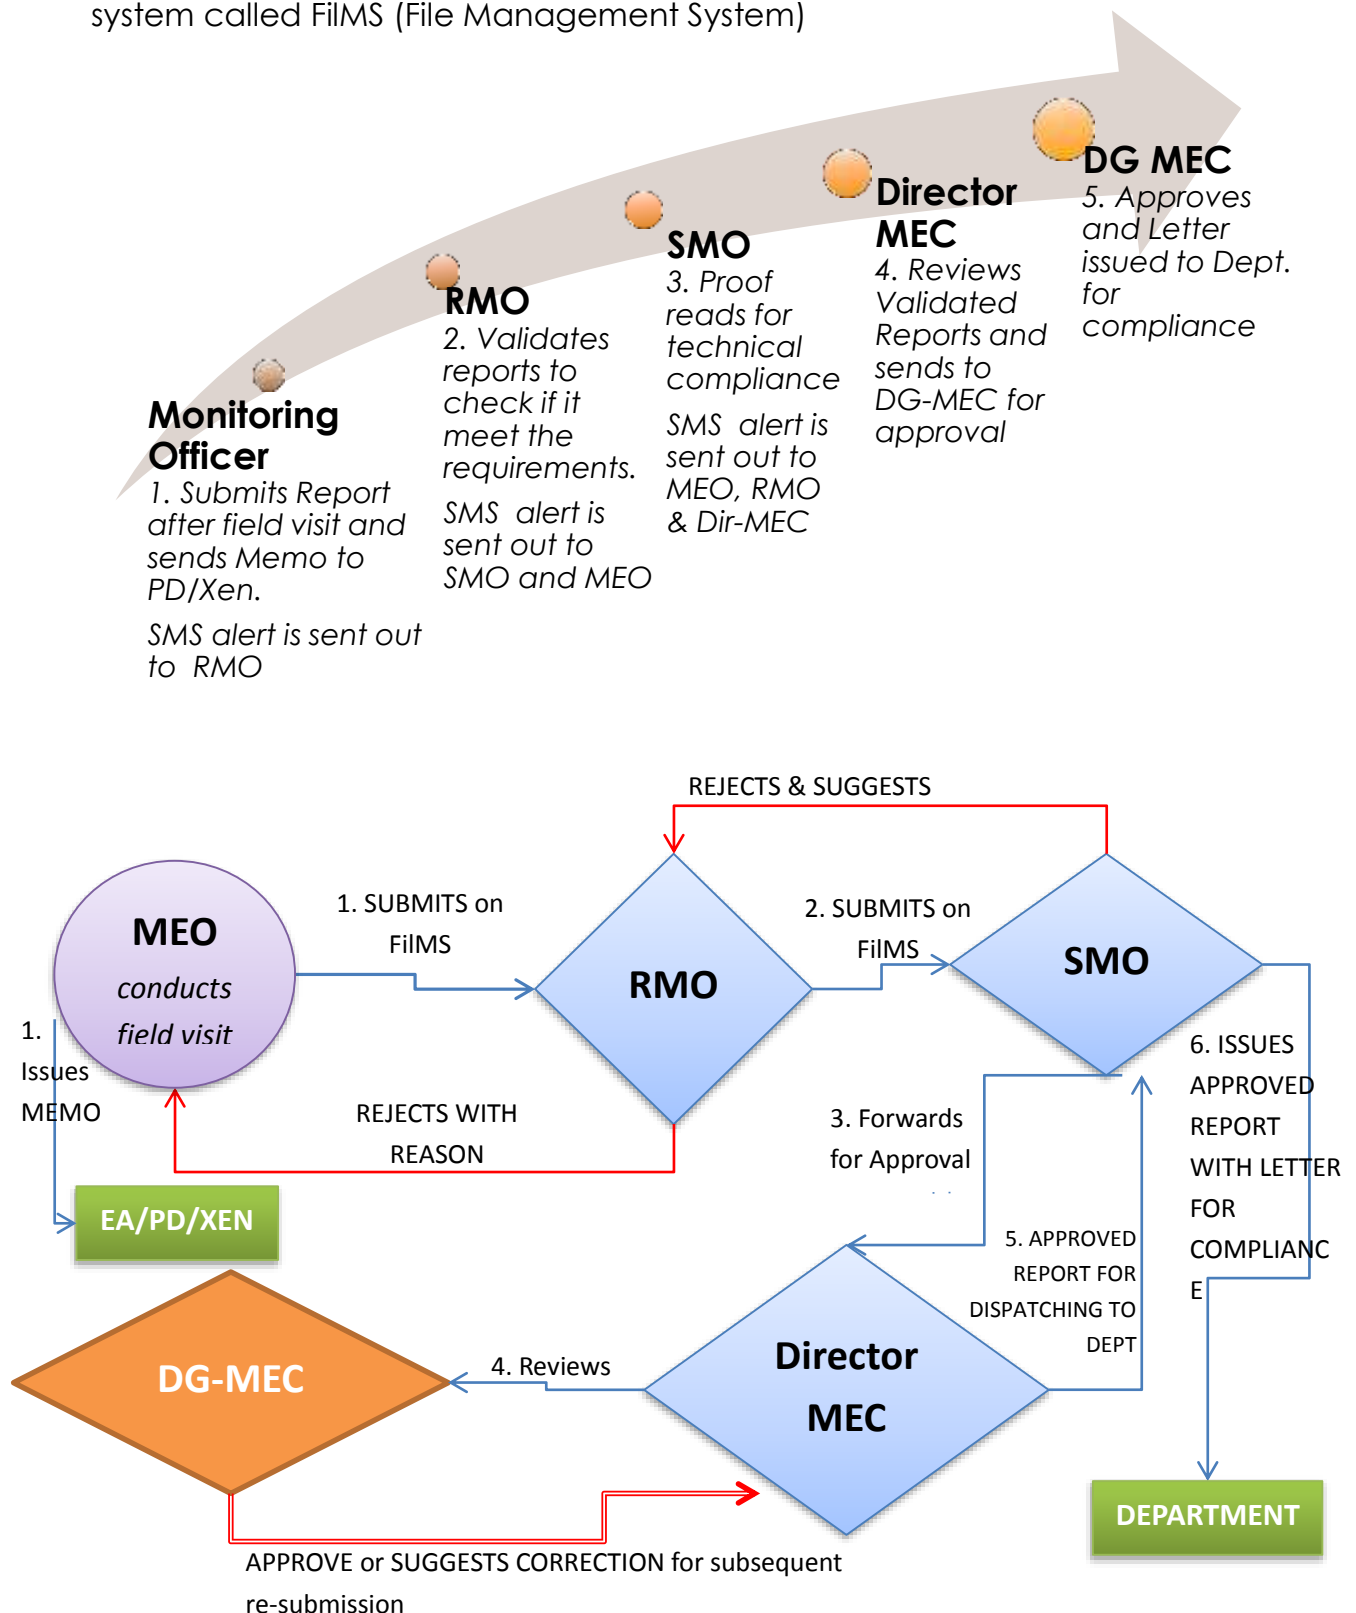


## ADP 2014-15 Analysis

### District-wise Distribution of Funds (Rs. in million)

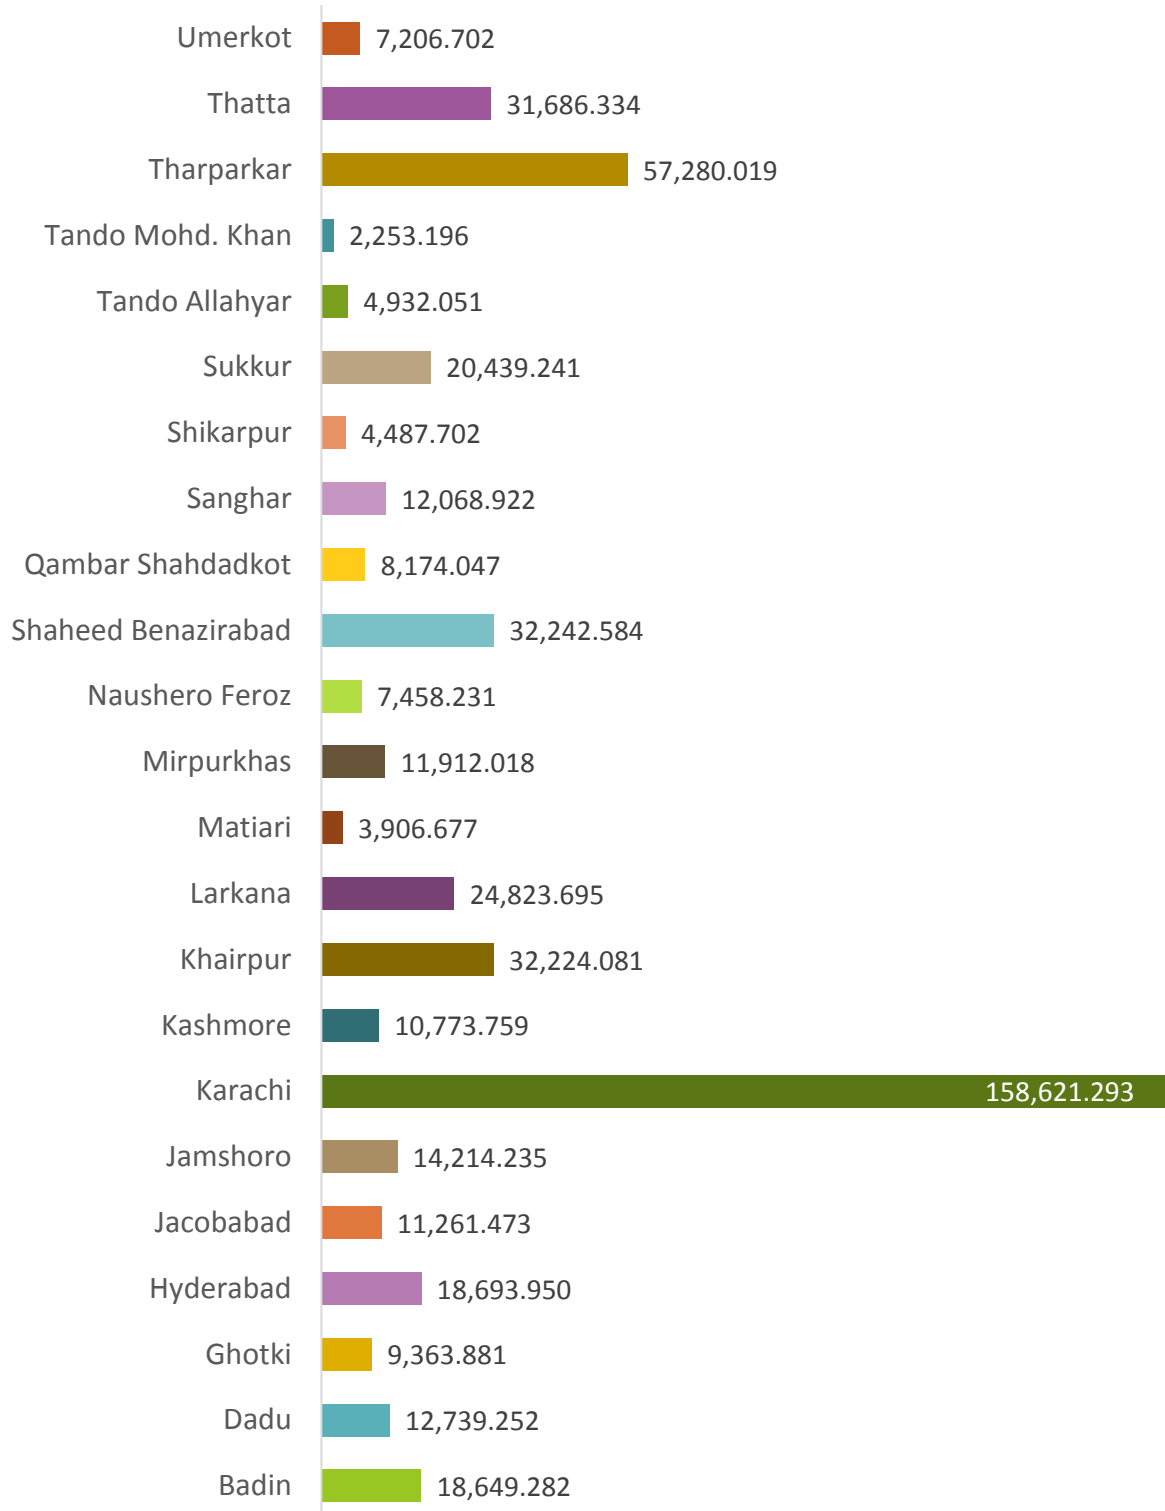


## Department-wise Distribution of Funds

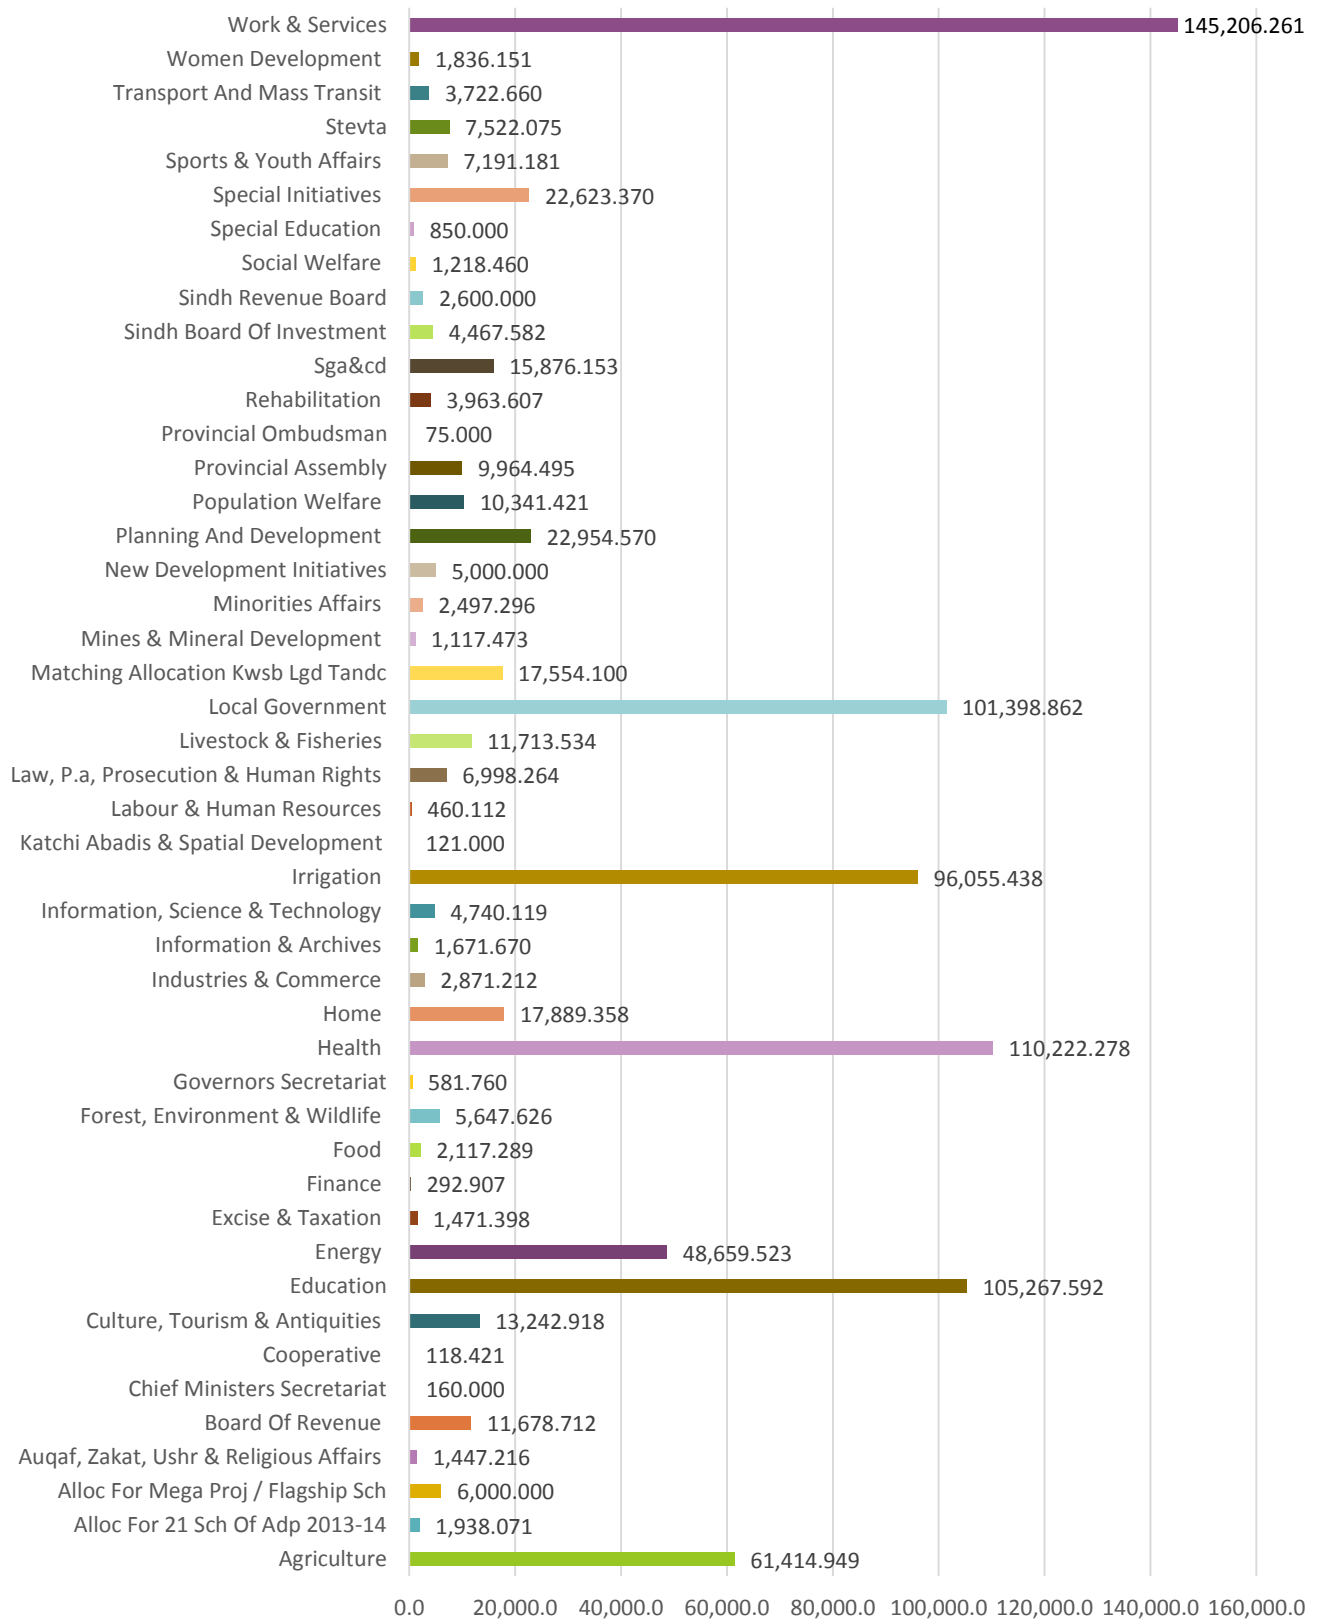




## Comparison of District-wise Distribution of Funds

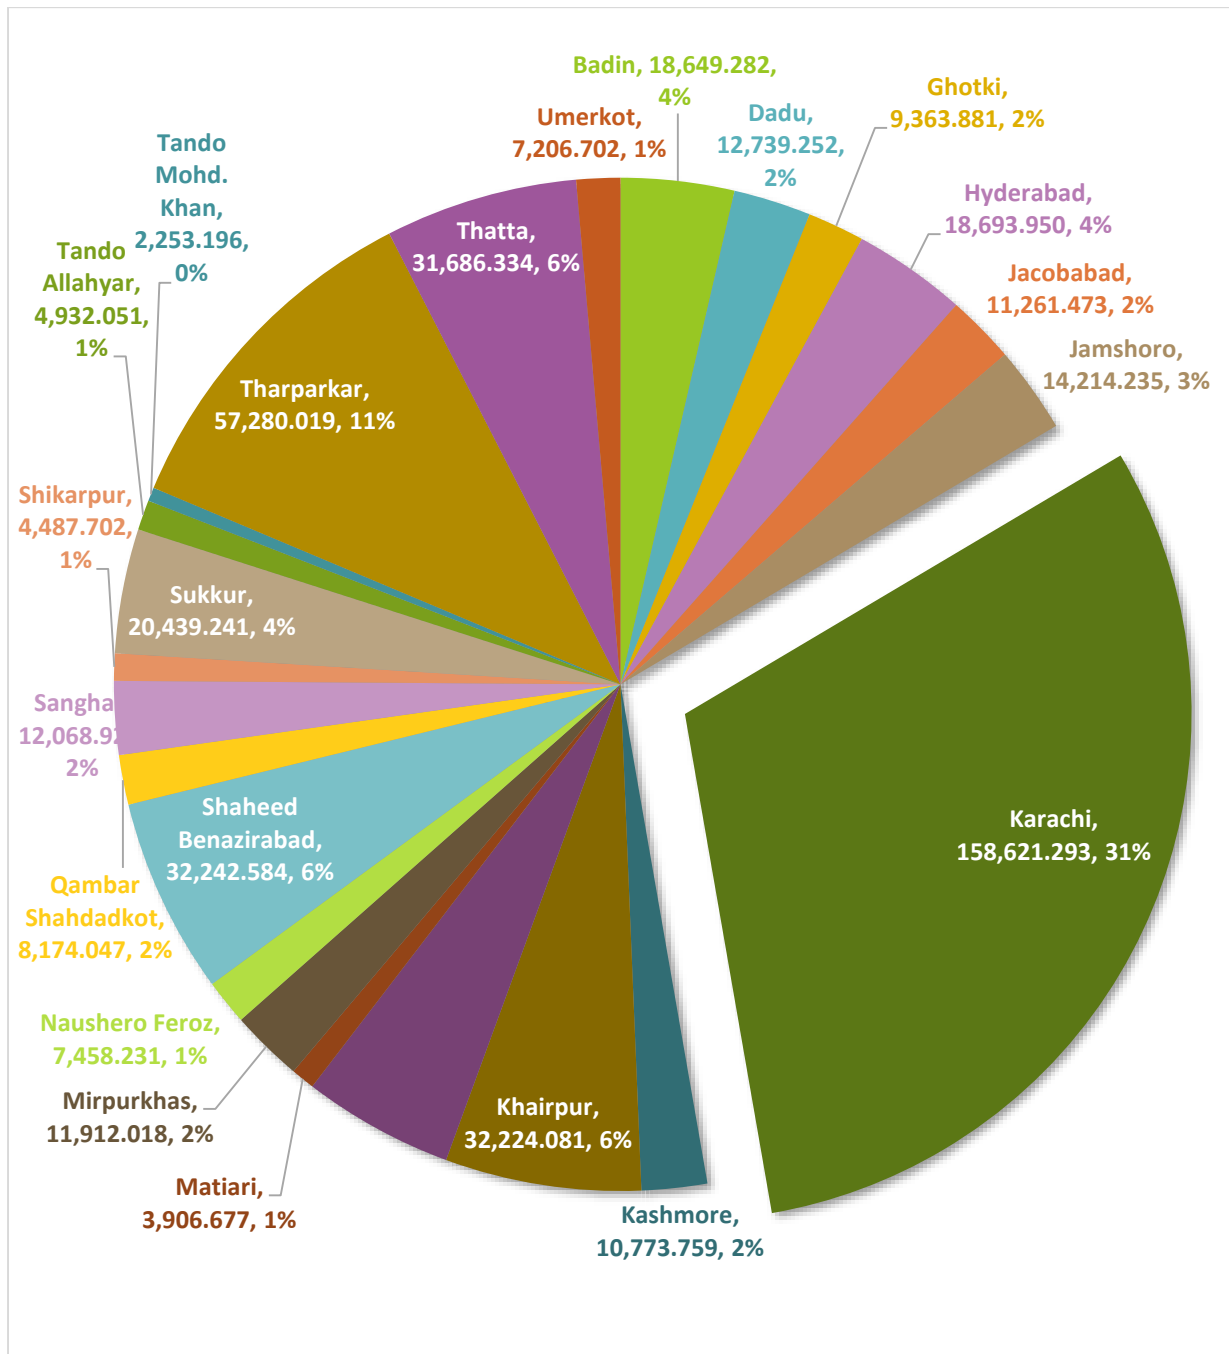

From the above chart it can be seen that the allocation of funds for Karachi were the highest with allocation of 30.6% followed by Tharparkar getting 11.1% of the total ADP outlay.


## 2014 Comparison of District Wise Population (Projected)

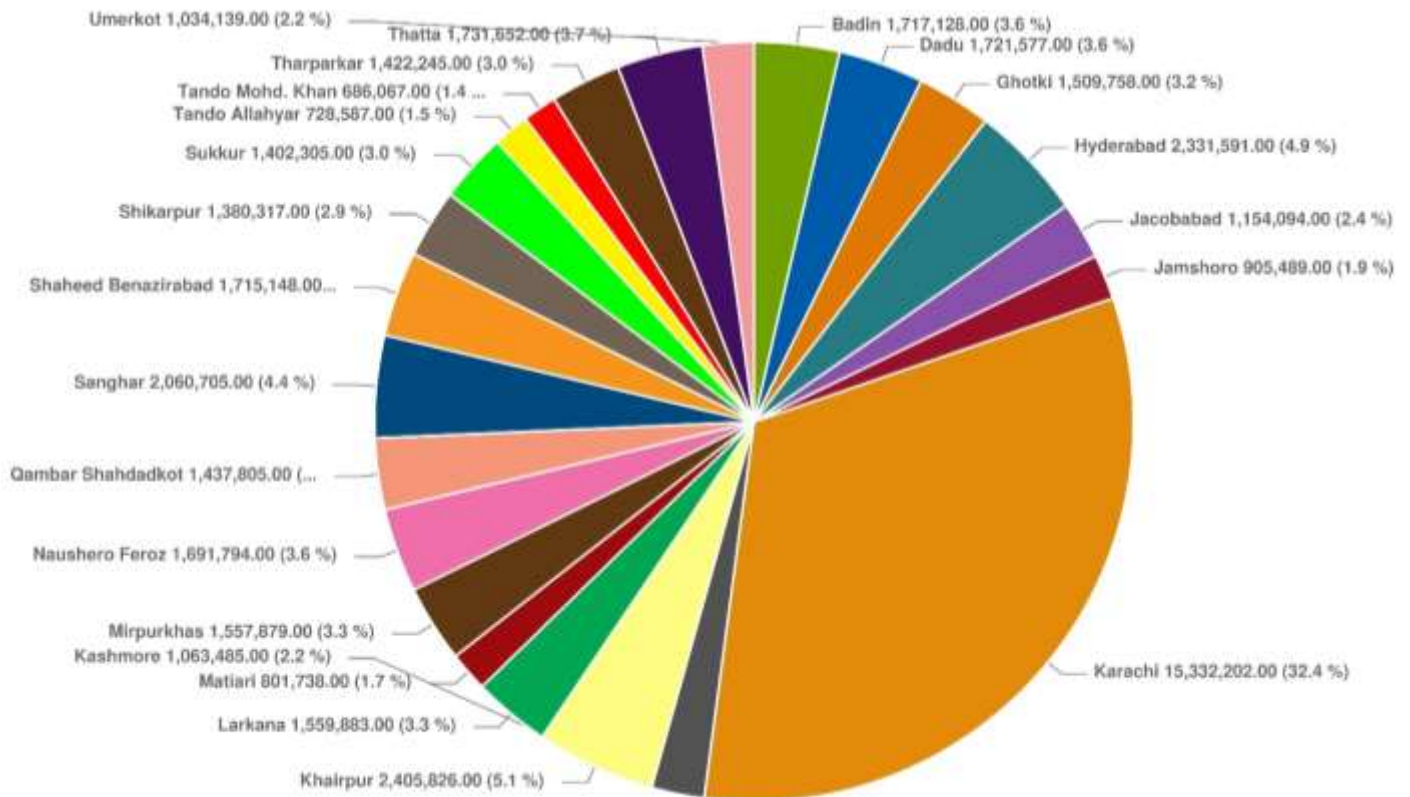

From the above chart it can be seen that the district which has the largest population is Karachi which holds 32.4% of the Total Population of Sindh

## Cost Analysis of ADP Schemes in FY 2014-2015

SCHEME COST (Rs. in million)	COUNT (# of Schemes)	TOTAL SCHEMES COST (Rs. in million)
5000 and above	19	155,192.65
Between 1000 and 5000	149	301,195.18
Between 500 and 1000	220	148,393.17
Below 500	2,550	295,981.09
<b>Total</b>	<b>2,938</b>	<b>900,762.09</b>

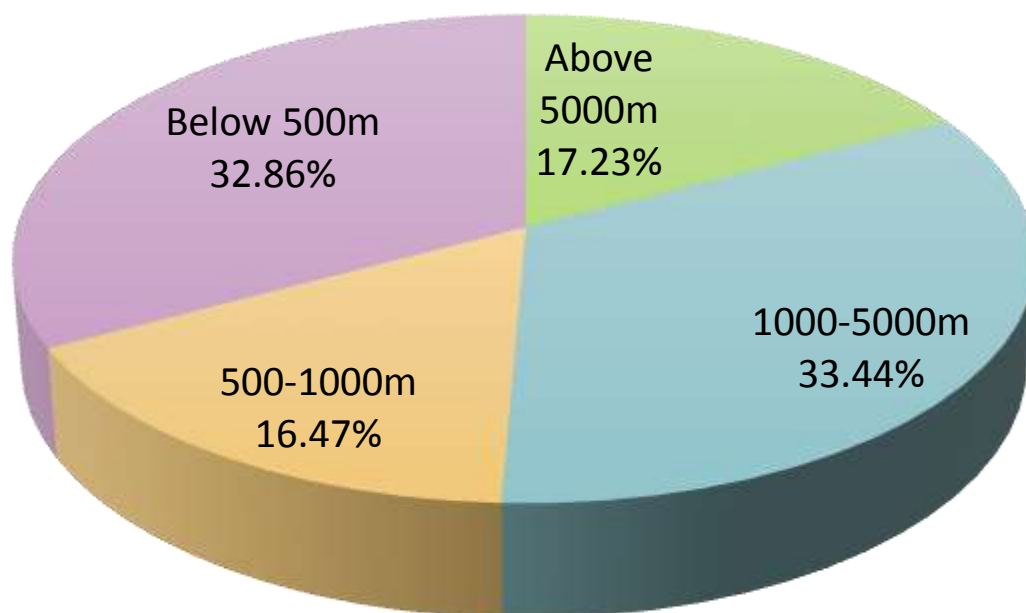

**Deduction:** From the above table and chart, it can be seen that about half of the ADP 2014-15 outlay comprised of schemes (168) which had a cost of Rs. 1 billion and above (33.44% + 17.23% = 50.67%)

## List of New Mega Schemes in FY 2014-15

S.#	ADP#	SCHEME NAME	LOCATION	SCHEME COST
<b>Agriculture</b>				
1.	26	Provision of Assistance to Farmers for Purchase of Wheel Type Tractors (Phase-IV)	Sindh	1,000.000
2.	31	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I ( World Bank Assisted)	Sindh	33,677.390
			<b>TOTAL:</b>	<b>34,677.390</b>
<b>Alloc. For Mega Proj / Flagship Sch</b>				
1.	2002	Allocation for Mega Projects / Flagship schemes	Sindh	6,000.000
			<b>TOTAL:</b>	<b>6,000.000</b>
<b>Culture, Tourism &amp; Antiquities Department</b>				
1.	103	Establishment of Mohatta Palace Museum Complex, Karachi (50% Sindh Government Share & 50% Federal Government Share)	Karachi	1,800.000
			<b>TOTAL:</b>	<b>1,800.000</b>
<b>Education</b>				
1.	386	Consolidation / improvement and provision of missing facilities in existing Public Schools in Sindh	Sindh	1,000.000
2.	402	Establishment of Public Schools for Girls @ Divisional Level in Sindh.	Sindh	1,000.000
3.	451	Establishment Boys/ Girls Degree College in Sindh. i. GBDC Sobho Dero ii. GBDC Bozdar Wada Distt Khairpur iii. GGDC Thull Distt Jacobabad iv. GBDC Chachro Distt Tharparkar v. GGDC Gulshan-e-Haded vi. GGDC New Karachi vii. Zamanabad Landhi viii. TaiserTown	Sindh	1,000.000
4.	509	Construction of Multipurpose Halls / Career Development Centres at Sukkur, Nawabshah & Larkana	Larkana, Shaheed Benazirabad, Sukkur	1,000.000
			<b>TOTAL:</b>	<b>4,000.000</b>
<b>Energy Department</b>				
1.	557	Improvement of Road from Sujawal to Badin, Rehabilitation of Damaged Road Portions. Scheme No.1(52 km)	Badin	1,880.484
2.	558	Improvement of Road Network from Badin to Wango Mor, Rehabilitation of Damaged Road Portions, Scheme No.II (length 32 km).	Badin	1,385.854
3.	576	Block Allocation for Energy Initiative	Sindh	5,000.000
			<b>TOTAL:</b>	<b>8,266.338</b>
<b>Food Department</b>				
1.	589	Construction of Open Platforms / Plinth for Grain Storage in Sindh	Sindh	1,127.371
			<b>TOTAL:</b>	<b>1,127.371</b>
<b>Health Department</b>				
1.	645	Establishment of OPD complex at civil hospital Karachi.	Karachi	1,500.000
2.	653	Pet Scanner at LMCH Hyderabad & CMCH Larkana.	Hyderabad, Larkana	1,200.000
3.	659	Establishment of 500 Bedded Teaching Hospital at LUMHS Jamshoro	Jamshoro	1,000.000
4.	660	Establishment of Institute of Pharmacy at LUMHS Jamshoro Sindh	Jamshoro	1,000.000

5.	738	Establishment of Health care Center for Non-Communicable Diseases at Karachi, Hyderabad and Sukkur including (1) Cardio Vascular Diseases (2) Urological Diseases (3) Cancer Diseases (4) Hypertension Diseases (5) Diabetic Diseases (6) Mental Diseases (7) blood	Hyderabad, Karachi, Sukkur	2,000.000
6.	742	Strengthening / Up gradation of Jinnah Sindh Medical University. Karachi.	Karachi	1,000.000
7.	743	Strengthening of health facilities at District Thatta. (i) Strengthening of RHC Var (20 bedded) at Taluka Ghorabari (ii) Up gradation of RHC baghan to the level of Taluka Hospital (30 bedded) Taluka Ketu Bunder. (iii) Up gradation of BHU Gharabari to the	Thatta	1,000.000
8.	751	Provision of Mobile Health Units with Memography Machine for Sindh.	Hyderabad, Karachi, Mirpurkhas, Sukkur	3,000.000
9.	776	Establishment of 100 bedded Hospital with Trauma Centre at Keamari Town, Karachi.	Karachi	1,000.000
10.	802	Establishment of Medical College and Upgradation of DHQ Hospital to the level of Teaching Hospital at Thatta	Thatta	1,500.000
11.	818	Rescue Ambulatory Services Program including Call Center in Sindh. (all Districts)	Sindh	1,500.000
12.	819	Establishment of integrated Health Management Information System in Sindh (all Districts)	Sindh	1,000.000
13.	820	Provision of Solar Energy System at All Cold Storage Facilities in Sindh. (all Districts)	Sindh	1,000.000
14.	825	Establishment of child Health care Institute Sukkur \$ 46 million (Korean)	Sukkur	1,000.000
			<b>TOTAL:</b>	<b>18,700.000</b>
<b>Home Department</b>				
1.	870	Construction of Residential Accommodation for Constable & Head Constable in Kyc: (616 NOs.)	Karachi	1,172.000
			<b>TOTAL:</b>	<b>1,172.000</b>
<b>Industries &amp; Commerce Department</b>				
1.	916	Development of Infrastructure at SITE Nooriabad, Karachi, Hyderabad & Sukkur.	Hyderabad, Jamshoro, Karachi, Sukkur	1,117.100
2.	917	Improvement of infrastructure Development at SITE Kotri & Nooriabad (Phase -II)	Jamshoro	1,003.370
			<b>TOTAL:</b>	<b>2,120.470</b>
<b>Information &amp; Archives Department</b>				
1.	922	Establishment of FM Radio Station	Karachi	1,067.430
			<b>TOTAL:</b>	<b>1,067.430</b>
<b>Information, Science &amp; Technology Department</b>				
1.	940	Sindh E-Government Cloud Applications	Karachi	1,297.464
			<b>TOTAL:</b>	<b>1,297.464</b>
<b>Irrigation Department</b>				
1.	1005	Restoration/Rehabilitation of LBOD and Kotri Drainage Network System including activation of Dhoras - Phase-II	Badin, Mirpurkhas, Tando Mohd. Khan, Thatta	3,000.000
2.	1009	Rehabilitation of SCARP Colonies, Drains, Left Over Pockets and Allied Structures work in Larkana-Shikarpur Drainage Project and Construction of Retaining wall along 6L Sub Drain parallel to Shaheedan Jo Mazar Ghari Khuda Bux Bhutto.	Larkana, Shikarpur, Sukkur	1,191.000

3.	1037	Rehabilitation / Restoration of Drainage Infrastructures and Construction of Retaining Wall around Larkana City on various Drains including 1R, 2R and 1R-C Sub Drain of Larkana South System, 1R Ghar Sub Drain and Reconstruction of Structures including VRB	Larkana	1,000.000
4.	1173	Rehabilitation / Lining of Irrigation Channels in Shaheed Benazirabad	Shaheed Benazirabad	1,500.000
			<b>TOTAL:</b>	<b>6,691.000</b>
<b>Local Government</b>				
1.	1348	Construction and Rehabilitation of Hyderabad Rural Road Taluka Tando Jam. (To be funded out of 10% Royalty share)	Hyderabad-Pack age	1,591.020
2.	1398	Karachi Package	Karachi-Package	1,000.000
3.	1405	Mirpurkhas City Development Package	Mirpurkhas-Package	1,000.000
4.	1462	Revamping of Gujjar Nallah including Service road KMC	Karachi	1,000.000
5.	1466	Up-gradation of Dhabeji Pumping Station	Karachi	1,230.590
6.	1475	65 MGD Additional Water Supply from Haliji to Pipri	Karachi	6,180.000
7.	1797	Upgradation of Pipe Line Water Supply Scheme Naukot-Mithi upto Chelhar	Tharparkar	1,105.990
8.	1978	Special Package of Development Schemes for Distt:Larkana	Larkana	1,000.000
			<b>TOTAL:</b>	<b>14,107.600</b>
<b>New Development Initiatives</b>				
1.	160	New Development Initiatives	Sindh	5,000.000
			<b>TOTAL:</b>	<b>5,000.000</b>
<b>Planning And Development Department</b>				
1.	2033	Expansion of UC Based Poverty Reduction Programme in Umerkot, Khairpur, Sanghar, Badin, Thatta & Mirpurkhas	Umerkot, Khairpur, Sanghar, Badin, Thatta, Mirpurkhas	4,000.000
2.	2035	Establishment of Regional Offices at Karachi, Larkana and Mirpurkhas & Strengthening of MIS Directorate in MEC, P&D Department	Karachi, Larkana, Mirpurkhas	1,091.470
3.	2038	Coastal Community Development Initiatives	Badin, Thatta, Sujawal	1,000.000
			<b>TOTAL:</b>	<b>6,091.470</b>
<b>Population Welfare Department</b>				
1.	2043	Integrated Procurement of Contraceptives and related items in Sindh.	Sindh	5,674.421
			<b>TOTAL:</b>	<b>5,674.421</b>
1.	2050	Establishment of Sindh Emergency services (Rescue1122)	Sindh	3,169.000
			<b>TOTAL:</b>	<b>3,169.000</b>
<b>Sindh Board Of Investment</b>				
1.	2104	Revival of Sick Industrial Units Phase-II (All Districts)	Sindh	2,000.000
			<b>TOTAL:</b>	<b>2,000.000</b>
<b>Sindh Revenue Board</b>				
1.	2105	Software for Data Center & Electronic Cash Register for Hotels & Restaurants	Sindh	1,000.000
2.	2106	Establishment of office and Training Academy for SRB	Karachi	1,600.000
			<b>TOTAL:</b>	<b>2,600.000</b>
<b>Special Initiatives Department</b>				
1.	2124	Establishment of Drinking Water Hubs (Phase-IV) for 500 Units	Sindh	3,000.000
2.	2125	Pilot Project for Mobile 12 Bedded Health Units	Sindh	1,650.000
3.	2126	Establishment of IBA Campus Thatta under Sukkur IBA	Thatta	1,000.000

4.	2127	Special Development Package for District Thatta and Sujawal	Thatta, Sujawal	1,500.000
			<b>TOTAL:</b>	<b>7,150.000</b>
<b>Transport And Mass Transit Department</b>				
1.	2214	Construction for Bus Rapid Transit (Green Line)	Karachi	3,000.000
			<b>TOTAL:</b>	<b>3,000.000</b>
<b>Work &amp; Services</b>				
1.	2417	Block provision for Improvement of roads in Sindh (N.Feroze, Khairpur, Suk, Gotki, Shikarpur, Larkano, Shahdadko, Jabad, Kashmore, Thatta, Hyderabad, TA Yar, T.M. Khan, Matiari, M.Khas, Sujawal, Thar, Sanghar, U.Kot, Badin, Jamshoro, S.B.A. Dadu & Karachi)	Sindh	2,000.000
2.	2437	W / R of road from Tando Fazal - Tando Mohammad Khan road mile 0/0-10/0 (16.1 Kms)	Hyderabad	1,000.000
3.	2487	W / R of road from Jam Sahib to Mundh Jamrao road mile 0/0-23/6 (38.21 Kms) (with Asphalt Surface)	Shaheed Benazirabad	3,840.000
4.	2816	Block provision for Construction of various road in Sind (Upper sindh ) 100 Kms (Larkana, Dadu, N. Feroz, Kambar, Ghotki, Sukkur, Kashmore & Shikarpur)	Larkana, Dadu, Naushero Feroz, Qambar Shahdadkot, Ghotki, Sukkur, Kashmore, Shikarpur	1,484.000
5.	2817	Block provision for Construction of various road in Sindh (Lower Sindh) 100 Kms (Matiari, T.A.Yar, TM Khan, Dadu, Jamshoro, Badin, Thatta, M.Khas, Tharparkar, U.Kot, Sanghar & S.B.A.)	Matiari, Tando Allahyar, Tando Mohd. Khan, Dadu, Jamshoro, Badin, Thatta, Mirpurkhas, Tharparkar, Umerkot, Sanghar, Shaheed Benazirabad	2,016.927
6.	2895	Construction of over Head Bridge on Railway Line Between Kotri city and the Industrial Area Kotri, District Jamshoro Sindh.	Jamshoro	1,255.975
7.	2925	Construction of City to City road with the assistance of Asian Development Bank (400 Kms)	Sindh	6,000.000
8.	2936	Realignment / Construction of bund from North side of Malir River, Karachi	Karachi	2,527.000
			<b>TOTAL:</b>	<b>20,123.902</b>
65		<b>TOTAL COST of MEGA SCHEMES:</b>		<b>155,835.86</b>

## Monitoring Conducted in FY 2014-2015

Following is the **department wise** observation in monitoring done in financial year 2014-15 by our two different region offices (Hyderabad and Sukkur):


S.#.	Departments / Sectors	# of Scheme	Satisfactory		Average		Un-Satisfactory		Reply Received
			#	%	#	%	#	%	#
1.	Agriculture,	40	20	50	8	20	12	30	10
2.	Antiquities,	15	1	7	7	47	7	47	0
3.	Auqaf,	3	0	0	1	33	2	67	0
4.	Board of Revenue,	11	1	9	6	55	4	36	0
5.	Coal and Energy,	3	0	0	1	33	2	67	0
6.	Cooperative,	1	0	0	1	100	0	0	0
7.	Culture,	17	0	0	13	76	4	24	4
8.	Education and Literacy,	57	5	9	29	51	23	40	25
9.	Energy,	7	2	29	5	71	0	0	0
10.	Environment,	1	0	0	0	0	1	100	0
11.	Excise & Taxation,	1	0	0	1	100	0	0	0
12.	Finance Dept,	1	0	0	1	100	0	0	0
13.	Forest, Wildlife & CDA,	21	13	62	4	19	4	19	0
14.	Governor Secretariat,	1	1	100	0	0	0	0	0
15.	Health,	130	14	11	46	35	70	54	11
16.	Home,	10	0	0	5	50	5	50	2
17.	Human Rights and Law,	10	0	0	6	60	4	40	1
18.	Industrial & Commerce,	5	0	0	2	40	3	60	1
19.	Information Technology,	2	0	0	1	50	1	50	0
20.	Irrigation (Water & Drainage),	100	32	32	42	42	26	26	6
21.	Labour Dept,	5	0	0	4	80	1	20	0
22.	Livestock and Fisheries,	34	3	9	20	59	11	32	16
23.	Local Government,	64	20	31	33	52	11	17	4
24.	Mines & Minerals,	2	0	0	2	100	0	0	0
25.	Minorities & Affairs,	4	2	50	0	0	2	50	0



26.	Physical Planning & Housing (Buildings),	2	0	0	1	50	1	50	0
27.	Planning & Development,	24	9	38	7	29	8	33	1
28.	Population Welfare,	4	0	0	3	75	1	25	0
29.	Provincial Ombudsman,	3	1	33	1	33	1	33	0
30.	Public Health Engineering,	75	9	12	48	64	18	24	1
31.	Rural Development,	4	1	25	2	50	1	25	1
32.	Sindh Board of Investment (SBI)	4	0	0	0	0	4	100	0
33.	Social Welfare,	4	0	0	2	50	2	50	1
34.	Special Initiatives Unit,	16	9	56	4	25	3	19	0
35.	Sports & Youth Affairs,	12	1	8	9	75	2	17	2
36.	STEVTa,	2	0	0	0	0	2	100	0
37.	Tourism,	3	0	0	2	67	1	33	0
38.	Transport & Comm. (Roads),	1	0	0	1	100	0	0	1
39.	Women Development,	6	1	17	2	33	3	50	1
40.	Work and Service,	116	12	10	71	61	33	28	46
		821	157		391		273		134

## Department Wise Monitoring Chart

Following is the **department wise** chart of schemes monitored

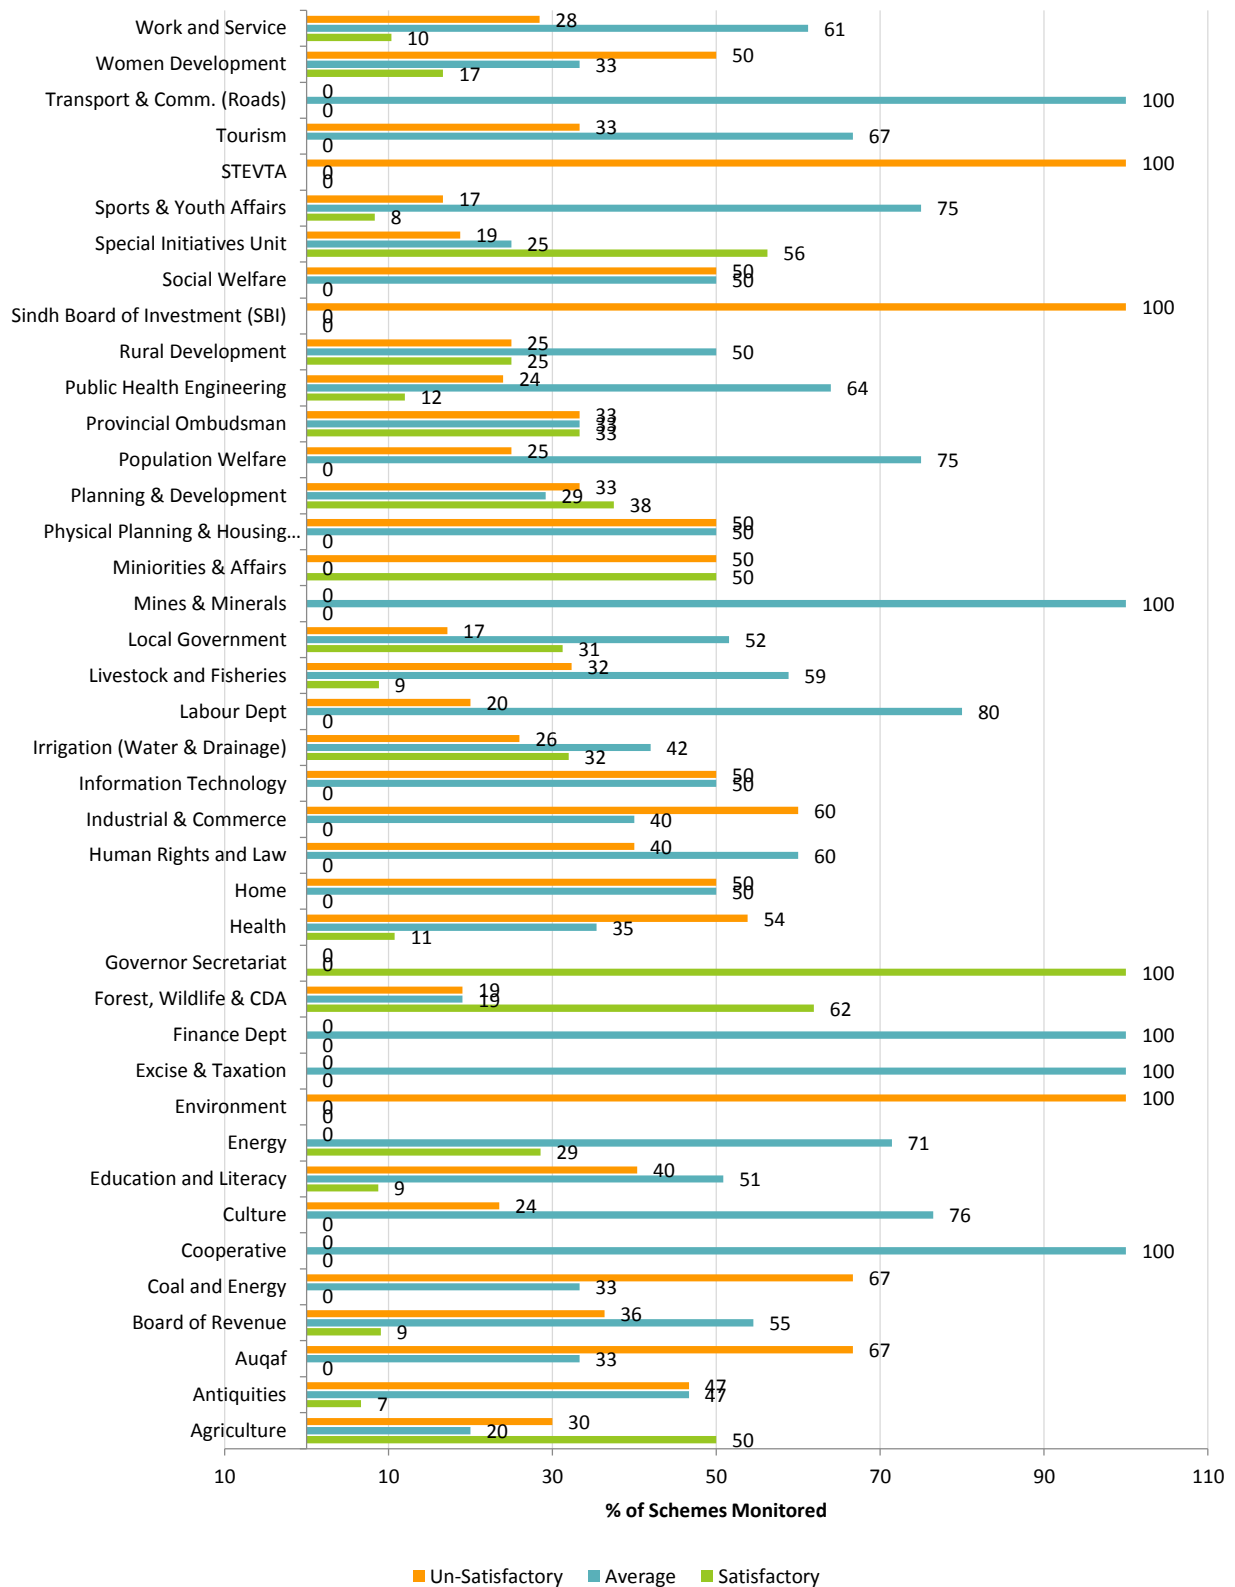


## District Wise Monitoring Statistics

Following is the analysis of **district-wise** monitoring done in financial year 2014-15 by our two different region offices (Hyderabad and Sukkur):




S.#.	Districts	# of Scheme Monitored	Satisfactory		Average		Un-Satisfactory	
			#	%	#	%	#	%
1.	Badin	41	2	4.88	24	58.54	15	36.59
2.	Dadu	40	7	17.50	24	60.00	9	22.50
3.	Ghotki	22	5	22.73	10	45.45	7	31.82
4.	Hyderabad	57	10	17.54	29	50.88	18	31.58
5.	Jacobabad	22	8	36.36	7	31.82	7	31.82
6.	Jamshoro	24	6	25.00	10	41.67	8	33.33
7.	Karachi	107	24	22.43	54	50.47	29	27.10
8.	Kashmore	9	3	33.33	0	0.00	6	66.67
9.	Khairpur	67	14	20.90	31	46.27	22	32.84
10.	Larkana	63	12	19.05	34	53.97	17	26.98
11.	Matiari	39	5	12.82	23	58.97	11	28.21
12.	Mirpurkhas	31	4	12.90	15	48.39	12	38.71
13.	Naushero Feroz	33	2	6.06	15	45.45	16	48.48
14.	Qambar Shahdadkot	16	2	12.50	9	56.25	5	31.25
15.	Sanghar	20	2	10.00	10	50.00	8	40.00
16.	Shaheed Benazirabad / Nawabshah	59	17	28.81	19	32.20	23	38.98
17.	Shikarpur	24	3	12.50	9	37.50	12	50.00
18.	Sujawal	5	2	40.00	2	40.00	1	20.00
19.	Sukkur	42	8	19.05	22	52.38	12	28.57
20.	Tando Allahyar	16	4	25.00	10	62.50	2	12.50
21.	Tando Mohd. Khan	8	0	0.00	3	37.50	5	62.50
22.	Tharparkar	25	4	16.00	17	68.00	4	16.00
23.	Thatta	43	13	30.23	9	20.93	21	48.84
24.	Umerkot	8	0	0.00	5	62.50	3	37.50
		<b>821</b>	<b>157</b>	<b>19.12</b>	<b>391</b>	<b>47.62</b>	<b>273</b>	<b>33.25</b>

## District Wise Monitoring Chart

Following is the **district-wise** analysis of the schemes monitored.

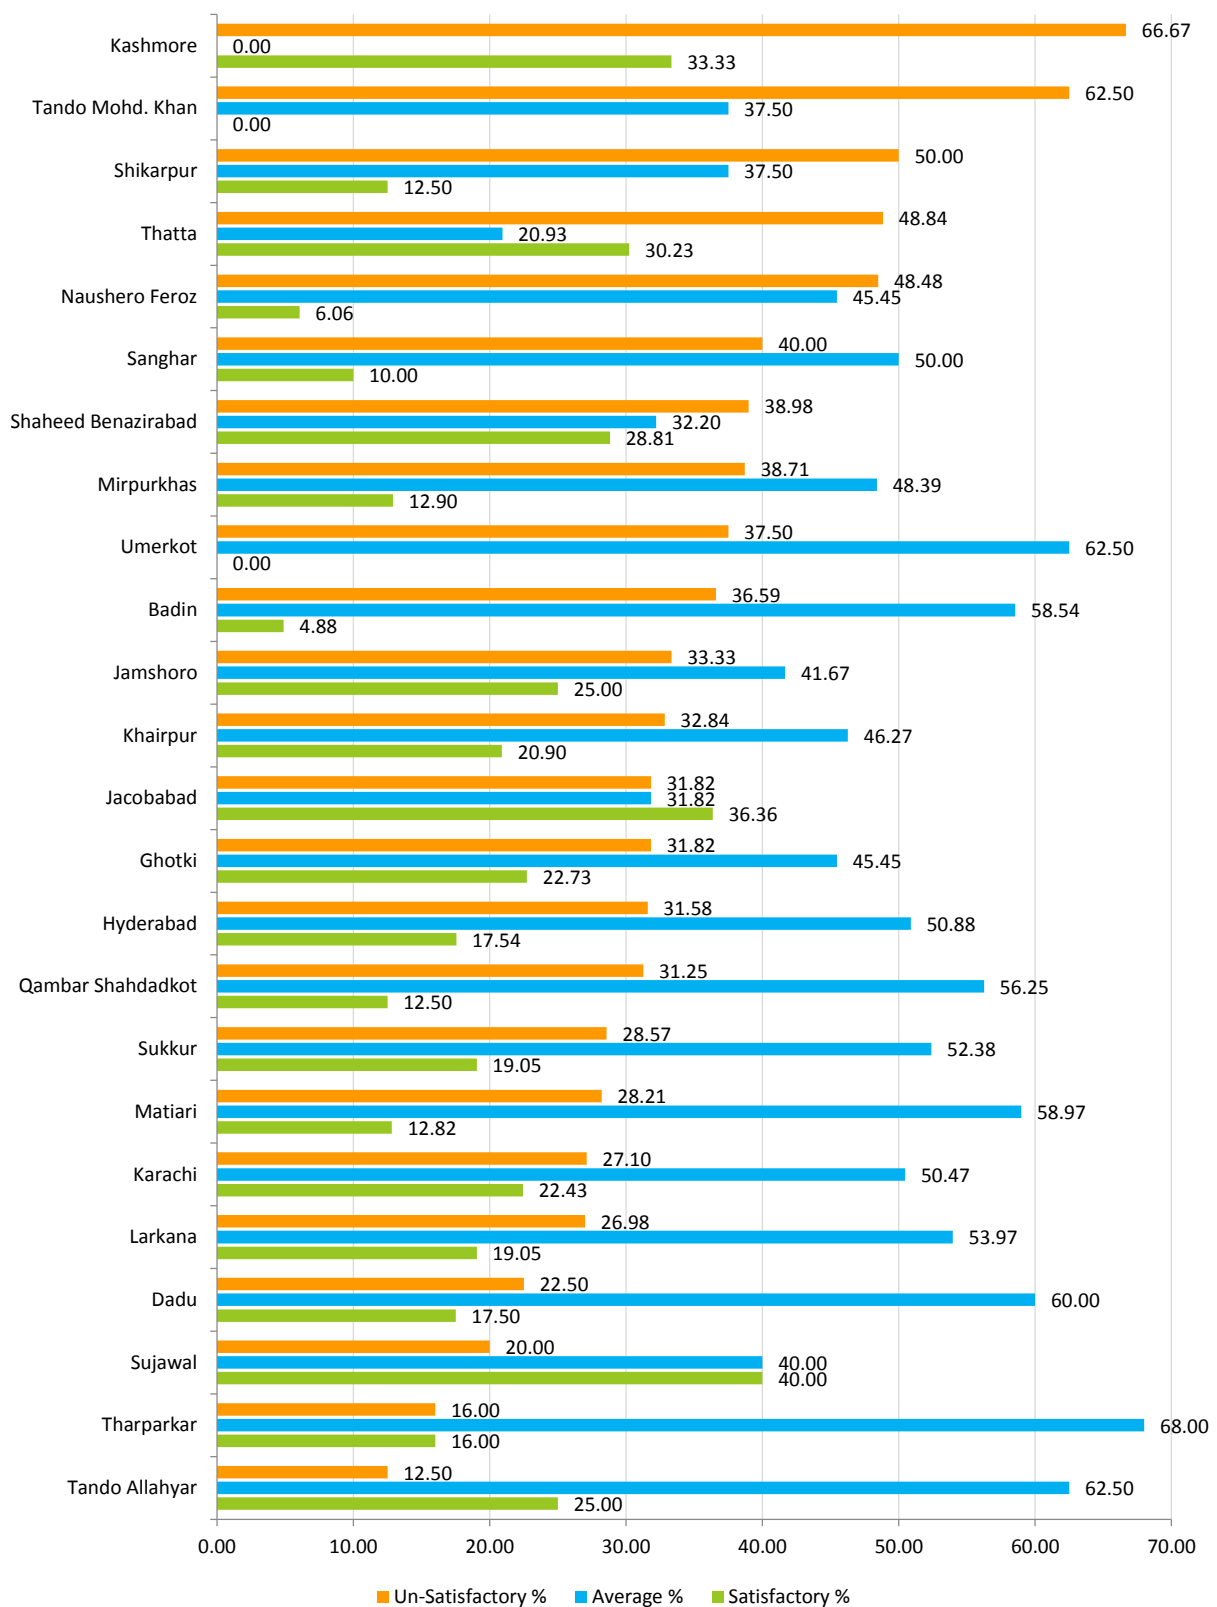

## Summary of Field Monitoring Observation

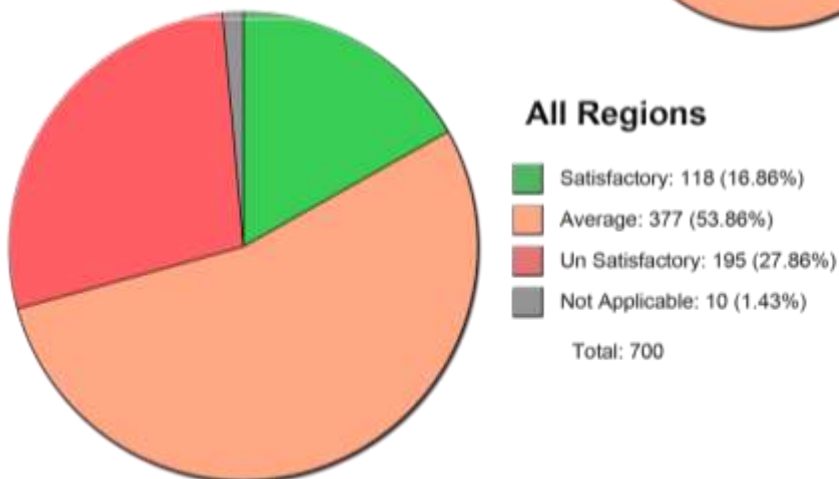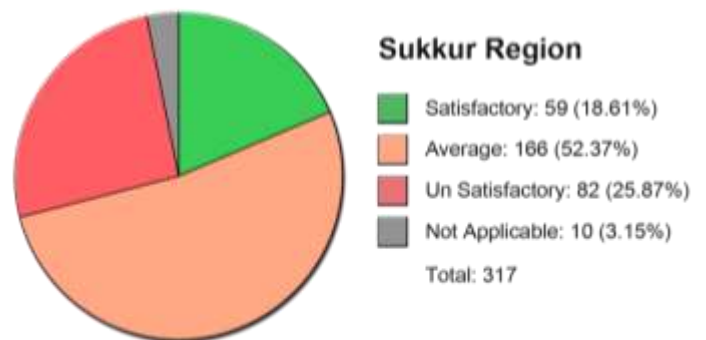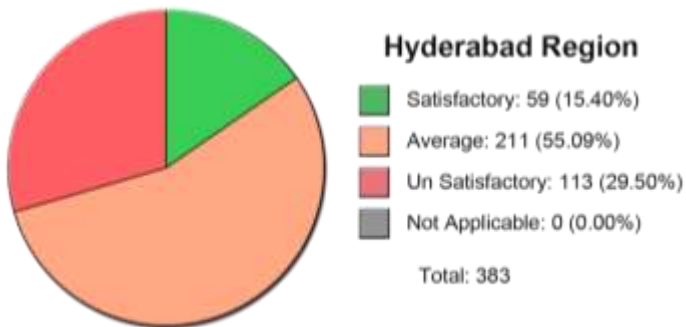


## Monthly Monitoring Performance

Following is the **month wise** monitoring summary conducted in financial year 2014-15 by our two regional offices (Hyderabad and Sukkur):

S.#.	Months	# of Schemes Monitored
1.	July	31
2.	August	37
3.	September	78
4.	October	71
5.	November	92
6.	December	93
7.	January	88
8.	February	13
9.	March	97
10.	April	78
11.	May	107
12.	June	36
<b>Total:</b>		<b>821</b>

## Monthly Monitoring Trend

Below is the graphical representation of month-wise monitoring in FY 2014-15:

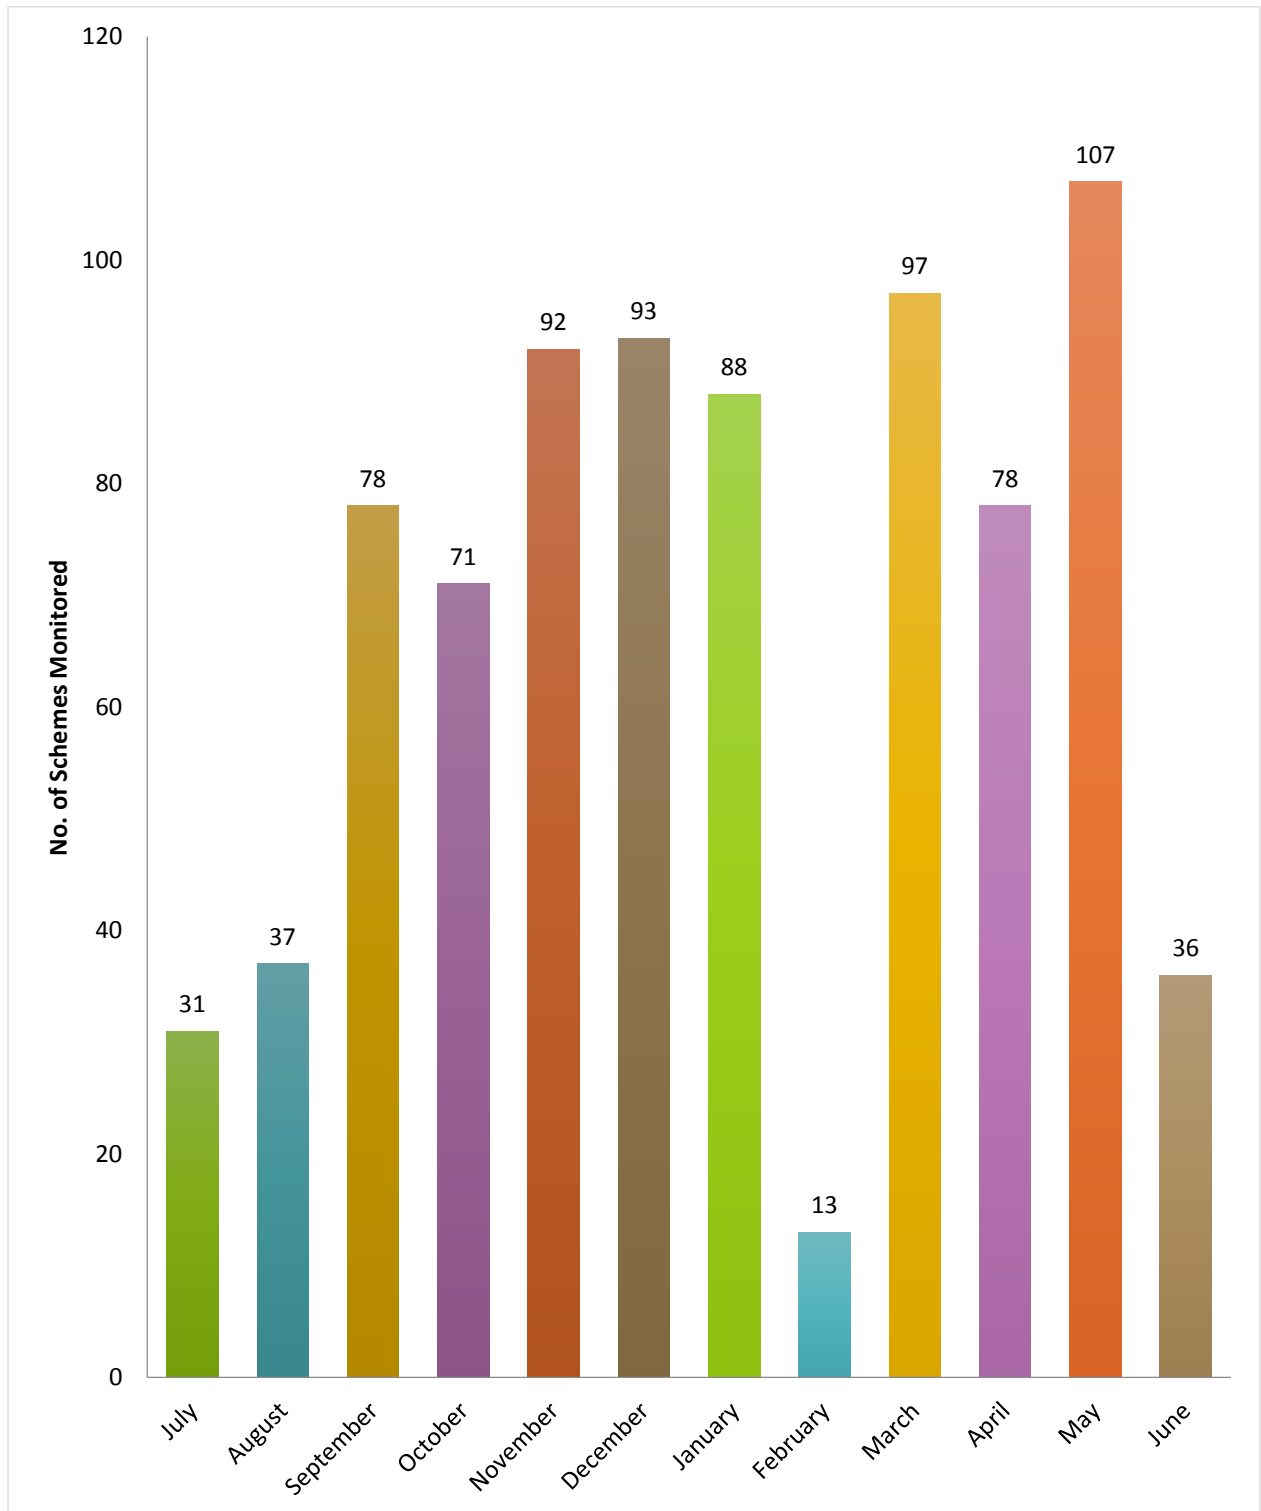


## Compliances Received

Financial year 2014-15, MEC monitored 821 development schemes out of 661 reports send to concern Administrative departments for compliance where as MEC only received 527 replies from various departments. Following is the tabular representation of available data.

S.#.	Department	# of Scheme
1.	Agriculture	10
2.	Culture	4
3.	Education and Literacy	25
4.	Health	11
5.	Home	2
6.	Human Rights & Law	1
7.	Industries & Commerce	1
8.	Irrigation	6
9.	Transport & Comm. (Roads)	1
10.	Women Development	1
11.	Livestock and Fisheries	16
12.	Local Government	4
12.	Planning & Development	1
13.	PHED	1
14.	Rural Development	1
15.	Sports & Youth	2
16.	Social Welfare	1
17.	Works & Service	46
<b>TOTAL COMPLIANCES RECEIVED:</b>		<b>134</b>
<b>TOTAL REPORTS SEND TO AD's:</b>		<b>661</b>
<b>TOTAL COMPLIANCE NOT RECEIVED:</b>		<b>527</b>




Below is graphical representation of the number of compliance received from various departments during the financial year 2014-2015

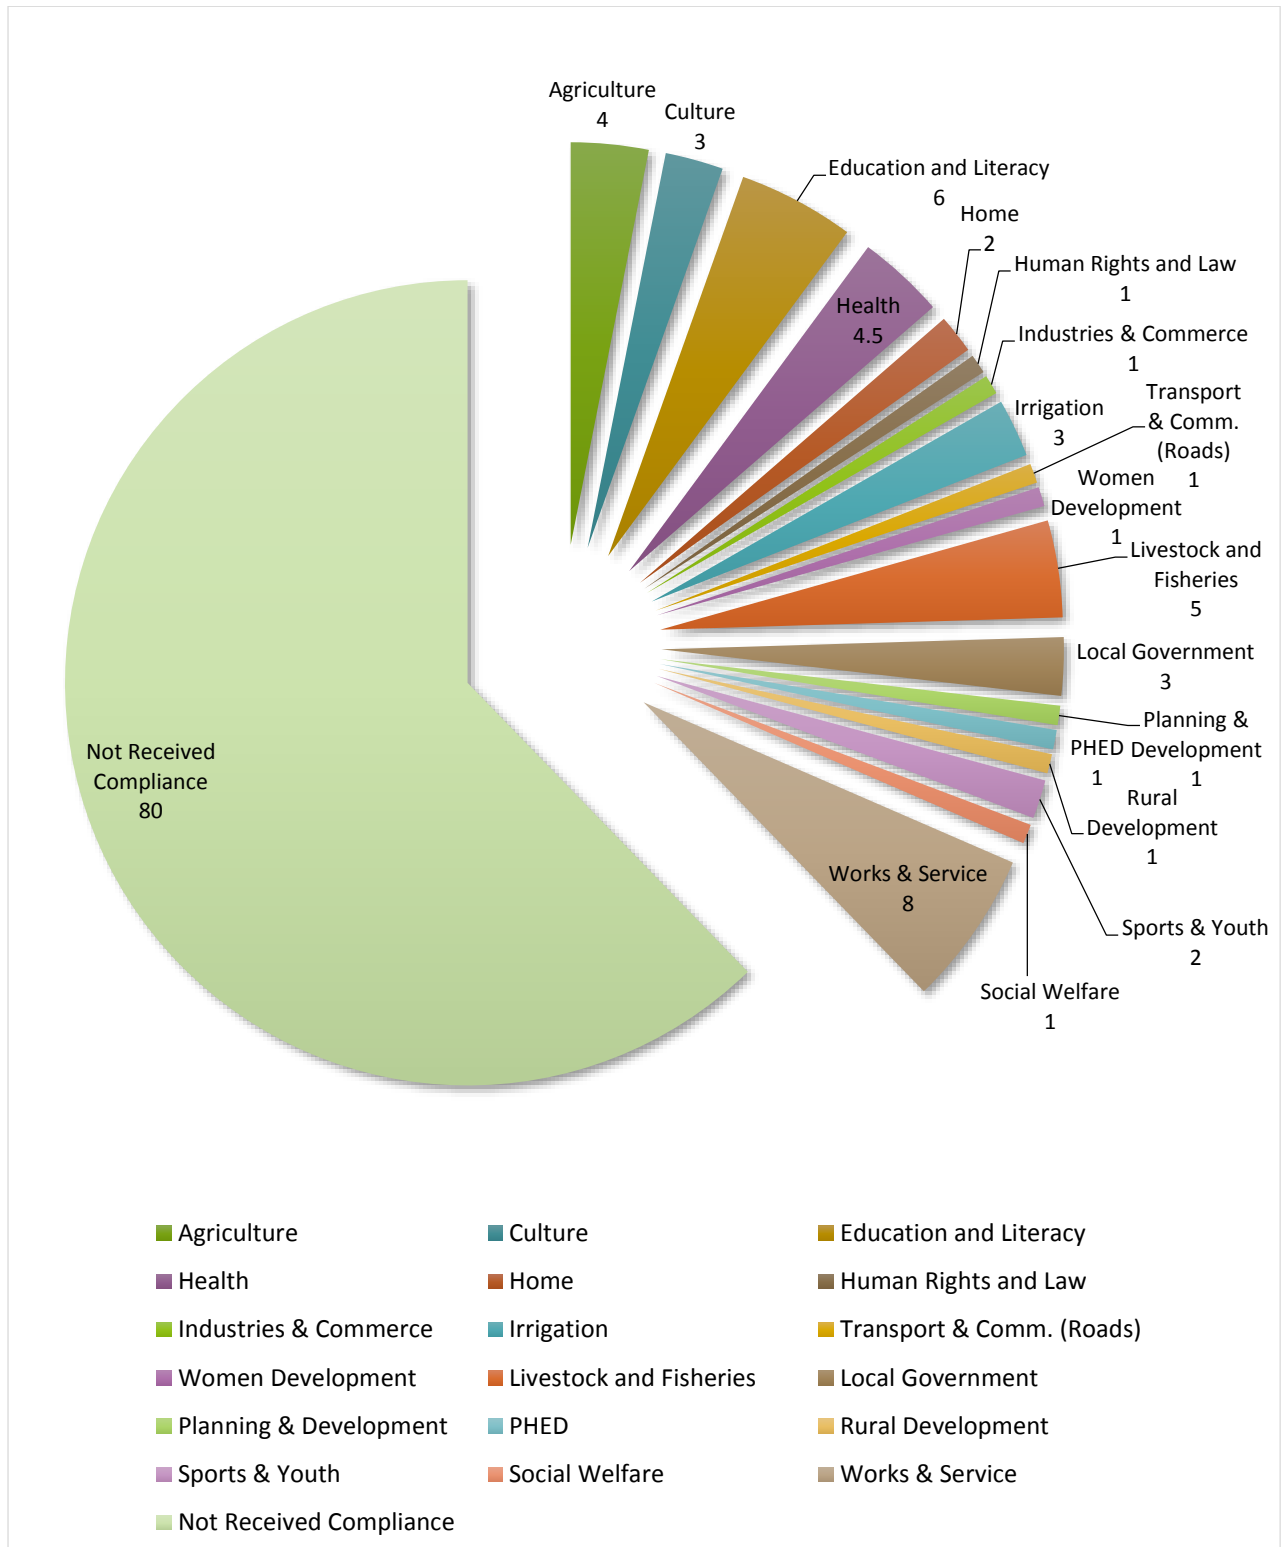

## Trend Analysis of Last 4 Years Monitoring

S.#	Financial Years	Total No. of ADP Schemes	Total No. of Schemes Monitored
1	2010-2011	1767	172 (9.73%)
2	2011-2012	1737	493 (28.38%)
3	2012-2013	2611	426 (16.32%)
4	2013-2014	2463	1141 (46.33%)
5	2014-2015	2352	821 (34.91%)

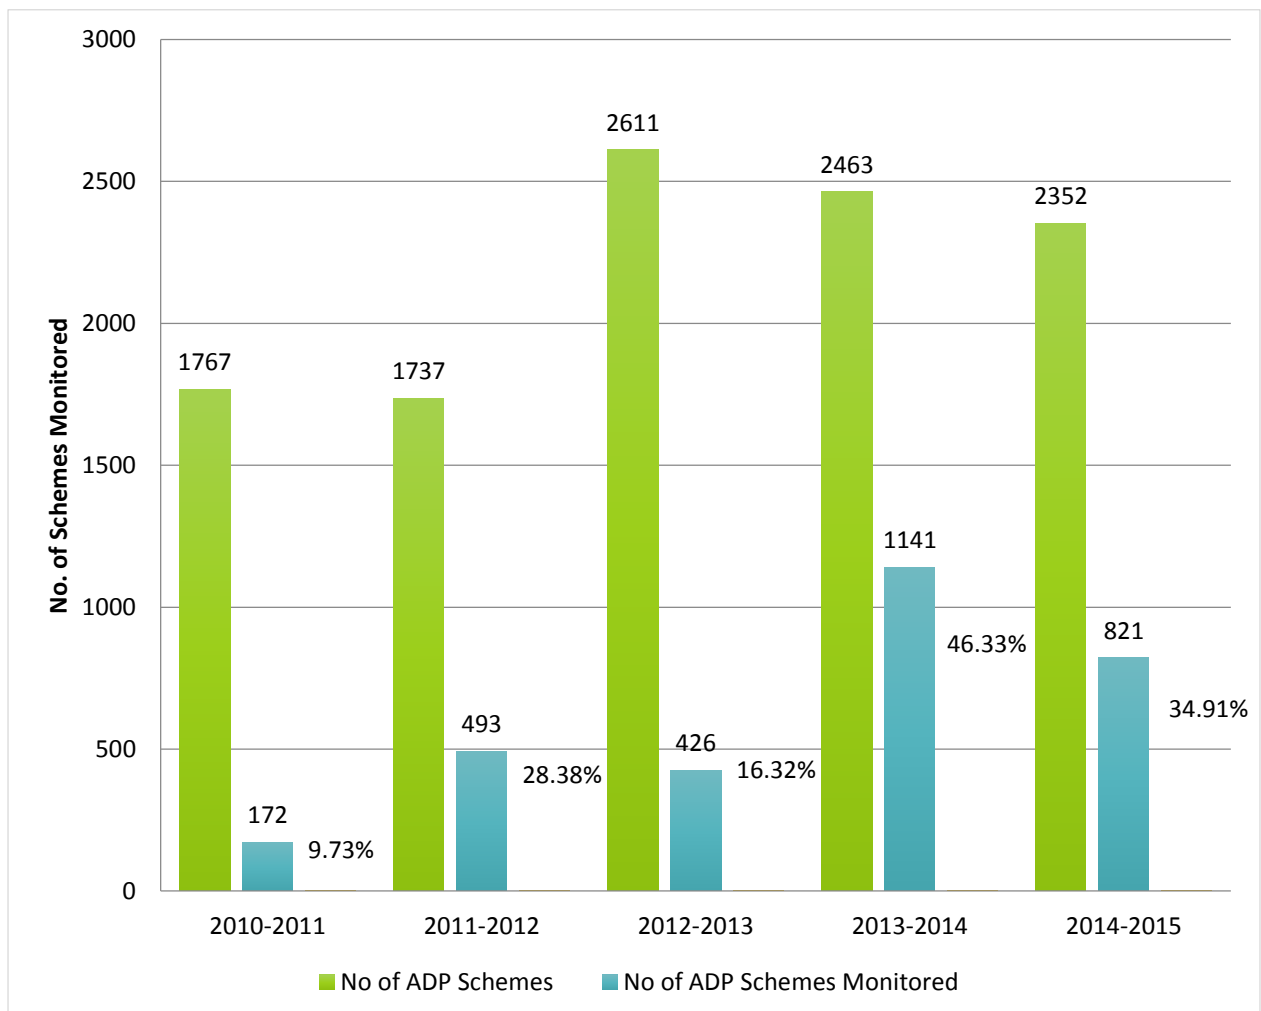


## Comparison of Monitoring by Regions

Department wise monitoring conducted by regional offices (Hyderabad & Sukkur):

S.#.	Departments / Sectors	Monitored by Hyderabad	Monitored by Sukkur
1.	Agriculture	13	27
2.	Antiquities	14	1
3.	Auqaf	1	2
4.	Board of Revenue	8	3
5.	Coal and Energy	3	0
6.	Cooperative	1	0
7.	Culture	13	4
8.	Education and Literacy	22	35
9.	Energy	6	1
10.	Environment	1	0
11.	Excise & Taxation	1	0
12.	Finance Dept	1	0
13.	Forest, Wildlife & Coastal Dev. Authority	4	17
14.	Governor Secretariat	1	0
15.	Health	81	49
16.	Home	9	1
17.	Human Rights and Law	8	2
18.	Industrial & Commerce	5	0
19.	Information Technology	2	0
20.	Irrigation (Water & Drainage)	79	21
21.	Labour Dept	5	0
22.	Livestock and Fisheries	31	3
23.	Local Government	31	33
24.	Mines & Minerals	2	0
25.	Minorities & Affairs	4	0
26.	Physical Planning & Housing (Buildings)	2	0
27.	Planning & Development	3	21
28.	Population Welfare	4	0
29.	Provincial Ombudsman	1	2
30.	Public Health Engineering	10	65
31.	Rural Development	2	2
32.	Sindh Board of Investment (SBI)	4	0
33.	Social Welfare	2	2
34.	Special Initiatives Unit	11	5
35.	Sports & Youth Affairs	6	6
36.	STEVEDA	0	2
37.	Tourism	2	1
38.	Transport & Comm.	1	0
39.	Women Development	3	3
40.	Work and Service	67	49
		<b>464</b>	<b>357</b>

## Graphical representation of Region Comparison

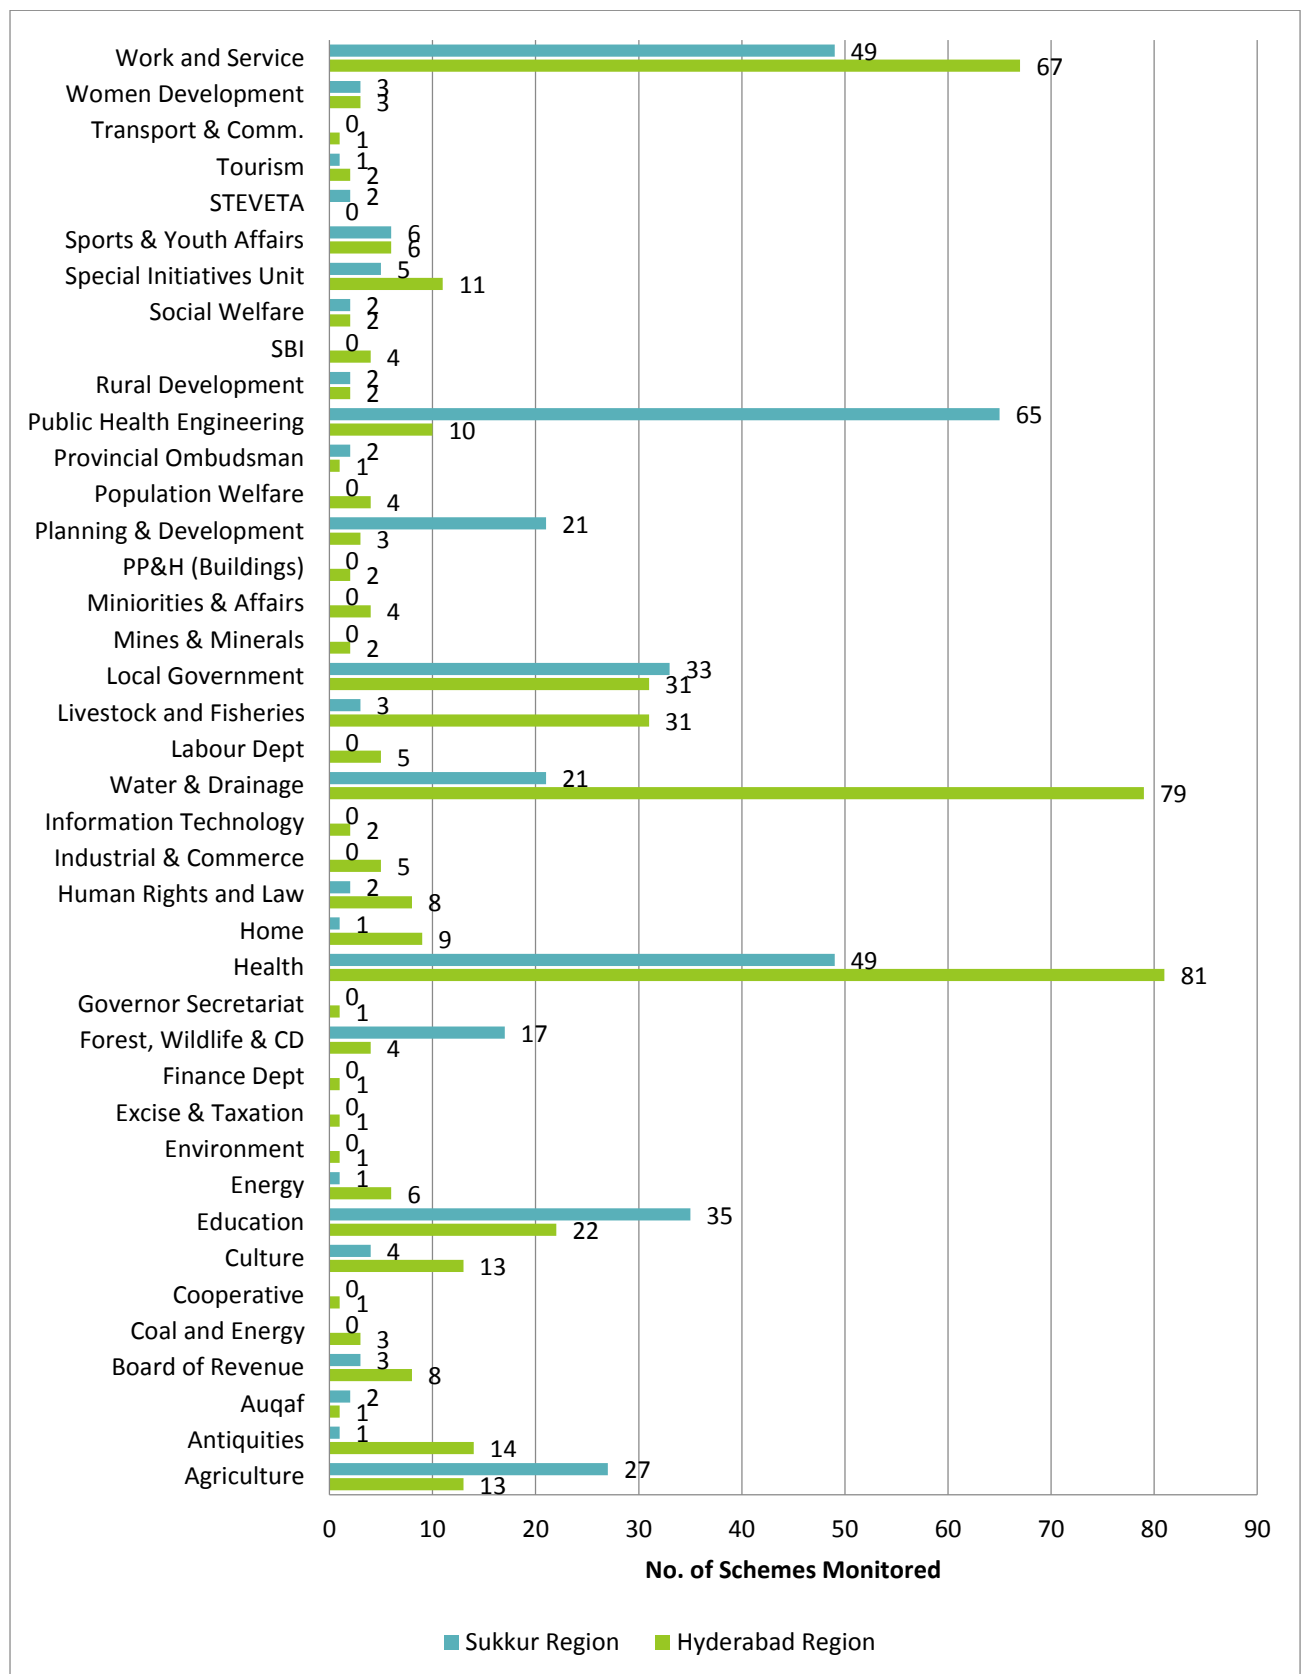

## Monitoring of ADP Completed Schemes

In compliance of Honorable Chief Minister Sindh Directives during the meeting held in the month of May-2015. Regional Monitoring Team of MEC visited 318 ADP schemes which were to be completed by June-2015, as committed by the respective Administrative Departments.

S.#.	Department	Number of Schemes			Total Schemes
		Completed	Not Completed	Not Visited	
1	Agriculture	3	1	0	4
2	Auqaf, Zakat, Ushr & Religious Aff.	2	1	0	3
3	Alloc For 21 Sch Of Adp 2013-14	1	0	0	1
4	Board Of Revenue Department	0	1	0	1
5	Culture, Tourism & Antiquities	18	1	0	19
6	Education	15	3	0	18
7	Energy Department	3	3	0	6
8	Governors Secretariat	2	0	0	2
9	Health Department	33	5	0	38
10	Industries & Commerce Department	1	0	0	1
11	Information & Archives Department	1	0	0	1
12	Information, Science & Technology	5	0	0	5
13	Irrigation Department	34	6	1	41
14	Katchi Abadis & Spatial Development Department	1	0	0	1
15	Law, P.A, Pros. & Human Rights	1	0	0	1
16	Local Government	82	25	0	107
17	Livestock & Fisheries Department	2	2	0	4
18	Minorities Affairs Department	1	0	0	1
19	Planning And Development	2	0	0	2
20	Population Welfare Department	1	0	0	1
21	Rehabilitation Department	1	0	0	1
22	SGA&CD	1	1	0	2
23	Sindh Board of Investment	0	0	1	1
24	Social Welfare Department	1	0	0	1
25	Special Initiatives Department	1	0	0	1
26	Sports & Youth Affairs Department	7	4	0	11
27	Women Development	3	0	0	3
28	Work & Services	36	5	0	41
<b>Total:</b>		<b>258</b>	<b>58</b>	<b>2</b>	<b>318</b>


Also see **Annexure - A** for Detail Report

## Third Party Monitoring (TPM)

- Sindh Cabinet taking initiate in its meeting held on 16-06-2008 to improve quality of construction, monitoring of projects by the Planning & Development Department is important requirement. In order to seek un-biased report, Third Part Monitoring (TPM) of the projects has become necessary.
- Year wise 1% Amount for Third Party Monitoring for every development scheme has been deposit into National Bank of Pakistan Account #: 1154-4 for the year 2008-09 to 2014-15.

Year wise 1% TPM Detail	
Year	Amount
2008-09	5.778 M
2009-10	22.184 M
2010-11	12.628 M
2011-12	29.787 M
2012-13	32.759 M
2013-14	33.416 M
2014-15	77.316 M
<b>Total</b>	<b>213.867 M</b>

Graphical Representation of 1% TPM Deposit into National Bank

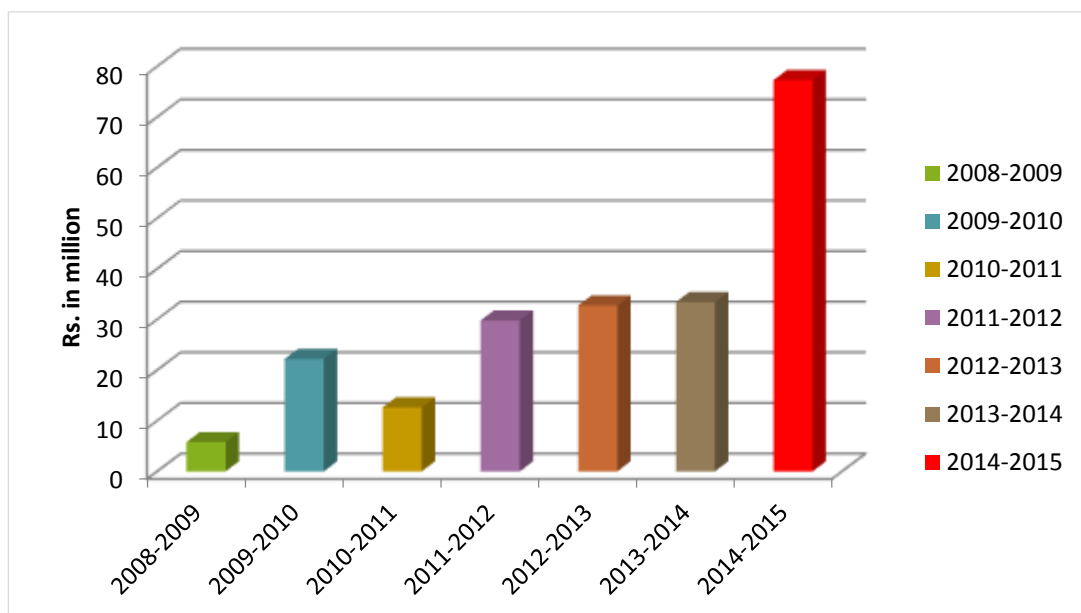

## Sector Analysis by Field Monitoring

### ROADS:

- Use of oversize & unsuitable stone in sub base & base
- Test regime is totally missing including Field Density tests and Soil classification tests etc.
- Compaction of earth work not being carried out as per specifications
- Meager allocation on some schemes which take years to complete
- Camber Control is missing; no use of camber plates at execution level
- Berms/shoulders are not properly dressed and compacted
- Uneven road top with undulations at certain places.(Road Grade not controlled properly)
- Improper control of super elevation at curves
- Use of poor quality bricks for road edging
- Concrete ratio less than specification in top slab of culverts
- Improper concrete cover to steel in concreting operations
- Lack of supervision was observed in execution work
- Engagement of more than one contractor on single project.

### IRRIGATION (WATER & DRAINAGE):

- Test Regime is totally missing in the works. No tests reports were available at site at all places.
- The backfilling is not being properly carried out along retaining walls.
- Suitability of material for embankment raising is not taken care of. No soil classification of the material is conducted from any reputable laboratory.

- It was found that sides of canals/minor/distributaries were not correctly dressed & sloped at both sides.
- Gaps / spaces in stone pitching works were not filled with specified cement mortar. Damaged stone pitching work was found at most of the places.
- In the stone work the size of stones was not as per specification & at most of the places the oversize stone was used. Quality of stones not up to mark.
- CC coping work was not found at most of stone pitching works.
- In most of the cases quality of plaster work was poor.
- Most culverts had no parapet walls.
- Quality of shuttering including props should be improved
- Spacing of Reinforcement Steel & user of Spacer Blocks to be ensured
- Deployment of engineering staff with contractors as per Pakistan Engineering Council By-laws
- Multiple contracts for small portion of work should be avoided

### **PUBLIC HEALTH AND ENGINEERING (PHED):**

- The main reason for non-functionality of PHED schemes is non-provision of electric connection./energization of the schemes
- The engineers lack the knowledge of the new methodology of working on M.S Pipe and P.E pipes
- The waste water is generally disposed in to the nearby river and canals without treatment at the oxidation ponds
- Sand blasting is not done for removal of rust from the pipes
- Wrapping & Coating of pipes is not properly done
- Welding /Jointing is done by the unskilled workers
- Sand Cushion to pipes was not provided at the bottom & side for the protection of thrust created by the water pressure



- Pressure testing not done of M.S. pipe & P.E pipe for checking the leakages in the joints and the pipe buried in the soil
- Oxidation ponds are not constructed at some places for natural treatment of water
- Invert levels and gradient is not being properly maintained with the result that water remains stagnant in most of the drains
- Low quality CC in streets is being done with improper cement concrete ratio & improper thickness.

## **BUILDINGS:**

- Test regime is totally missing in Building work also. Tests like slump test, gradation of fine & coarse aggregates, cube crushing test, steel tests (yield & tensile strength) & soil test(classification of soil) are not carried out in most of the cases
- Pakistan Engineering Council (PEC) bylaws require deployment of Project Engineers by the contractors. This requirement is being totally ignored
- Honey combing visible in many structures which shows improper mixing and placement of concrete (No concrete mix design is prepared even in heavy concreting work)
- Purchase of steel was generally being made locally having no recognized brand name. The use of under gauge steel was observed in some projects
- Appropriate attention is not being paid for quality of shuttering, use of spacer blocks for proper concrete cover and placement of reinforcement steel in structural members
- Quality of bricks and concrete blocks was not up to the mark.
- The compaction of the earth filling inside plinth is not taken care of.
- Lack of supervision was observed in execution work by the XEN concerned.

**EDUCATION:**

- Poor survey for need for establishment of a school in terms of enrollment
- Duplication of schools in some areas as source of funding varies i. e from federal, Provincial, district or other source
- Misuse of school buildings in villages especially used as autaq, store rooms, cattle farms, grain godowns, use in marriages , at one place in Shikarpur school was being used as a police station building
- Overall quality of work issues as in building sector generally, as mentioned in building sector
- The purchasing of Revenue component is centralized, hardly any data is given at district level as at local level they have very little knowledge regarding purchasing of revenue component

**HEALTH:**

- Overall quality of work issues as in building sector generally, as mentioned in building sector
- The purchasing of Revenue component is centralized, hardly any data is given at district level as at local level they have very little knowledge regarding purchasing of revenue component
- The health officials have very little knowledge to operate the latest & costly machines
- The machines are purchased & not installed at most of the places & kept in Packing for years
- The cold chain maintenance is very poor due to this vaccines & other drugs lose efficacy
- The duplication of Revenue component ites as no one knows from which source the purchasing has been made I,e Federal, Provincial,

Donor agency, NGO (no tagging of source is done for sake of identification)

- Hardly the procurement procedure for revenue component is shared with field teams.

## **AGRICULTURE & FOREST/LIVESTOCK & FISHERIES/WOMEN DEVELOPMENT DEPARTMENT:**

- The issues in the building work are the same as previously mentioned
- The utilization of Revenue component is the biggest issue of these departments
- A centralized purchasing system has been observed in most of the schemes. The regional offices are without financial powers to run their offices smoothly
- Lesser coordination by these departments with MEC team
- Delay in providing PC-I and Static Data related to scheme
- In Sindh Based Schemes District wise financial bifurcation is not provided
- Mostly Sindh based schemes are operated and controlled by the Head offices @ Hyderabad & local offices have little knowledge about the schemes

## ADP 2014-15 Technical Analytics

### ADP 2014-15 HIGHLIGHTS

- Highest portion of ADP portfolio (in terms of cost of schemes) was targeted towards Karachi with projects costing Rs. 158,621.293 followed by Tharparkar (Rs. 57,280.019), Khairpur (Rs. 57,280.019) and Thatta (Rs. 31,686.334).
- Highest amount was given to the Works & Services Department which had schemes costing Rs. 145, 206.261 followed by Health (Rs. 110,222.278), Education (Rs. 105,267.592) and Local Government (Rs. 101,398.862)
- Of the 2,938 schemes costing Rs. 900,762.084 in ADP 2014-15, there were 168 schemes which had a cost of over Rs. 1 billion. The total cost of these one billion and above schemes was about half (50.67%) of the total ADP cost.
- 1,279 New schemes were added costing Rs. 343,017.192 while 1659 schemes were retained from previous ADP costing Rs. 557,744.892. Cost of total ADP schemes was 2938 Rs. 900,762.084

### DEPARTMENTS REQUIRING BETTER PROJECT IMPLEMENTATION

#### Monitoring Highlight of Major Sectors

- Health: Of the 130 schemes Monitored, 54% (70 schemes) were found unsatisfactory
- Works & Services: Of the 116 schemes, 33% (28 schemes) were found unsatisfactory
- Irrigation: Of the 100 schemes, 26% (26 schemes) were found unsatisfactory
- Education: Of the 57 schemes, 40% (23 schemes) were found unsatisfactory
- Agriculture: Of the 40 schemes, 30% (12 schemes) were found unsatisfactory

## DISTRICTS THAT NEED BETTER PROJECT IMPLEMENTATION

### Highest Unsatisfactory Schemes

Of the 821 ADP 2014-15 schemes monitored, 273 were found to be unsatisfactory in physical progress. Below are the districts where there were highest percentage of schemes found to be unsatisfactory:

- Kashmore: 67% of the 9 schemes monitored were found unsatisfactory (6 schemes)
- Tando Mohammad Khan: 63% of the 8 schemes monitored were found unsatisfactory (5 schemes)
- Shikarpur: 50% of the 24 schemes monitored were found unsatisfactory (12 schemes)
- Thatta: 49% of the 43 schemes monitored were found unsatisfactory (21)
- Naushero Feroz: 48% of the 33 schemes monitored were found unsatisfactory (16 schemes)
- Sanghar: 40% of the 20 schemes monitored were found unsatisfactory (8)

On an average it has been observed that one-third of the schemes visited (273 of 821) were found to be unsatisfactory (one in every three schemes).

### Reporting Performance by Regional Offices at Hyderabad and Sukkur

Of the 700 schemes visited by Hyderabad and Sukkur offices, only 16.86% (118) were found to be satisfactory while 27.86% (195) unsatisfactory and rest were average.

*Note: Basis of these deductions can be found in this annual report in the form of charts and tables. All figures have been generated from the data obtained from the Finance Department.*

## Financial Review: Releases and Utilisation

S.#.	Department	# of Sch	Scheme Cost in Rs.	Exp Upto June 2014	Allocation	Releases	Exp July 2014 to June 2015	% Released against Allocation	% Utilized against Releases
1.	Alloc For Mega Proj / Flagship Sch	1	6,000.00	0.000	6,000.00	100.239	100.239	1.67%	100.00%
2.	Industries & Commerce	11	2,871.21	244.001	125.558	51.714	51.714	41.19%	100.00%
3.	Food	2	2,117.29	632.488	360.000	150.212	150.187	41.73%	99.98%
4.	Provincial Assembly	4	9,964.50	3,331.62	882.000	1,315.08	1,314.76	149.10%	99.98%
5.	Cooperative	1	118.421	91.710	26.711	10.947	10.932	40.98%	99.86%
6.	Irrigation	310	96,055.44	17,299.71	8,620.61	13,280.90	13,188.11	154.06%	99.30%
7.	Sindh Board Of Investment	8	4,467.58	1,198.15	2,376.00	2,332.32	2,313.84	98.16%	99.21%
8.	Excise & Taxation	7	1,471.40	120.100	176.400	85.091	84.383	48.24%	99.17%
9.	Energy	37	48,659.52	13,204.14	20,475.10	17,312.65	16,951.13	84.55%	97.91%
10.	Special Initiatives	11	22,623.37	6,623.88	10,200.00	8,011.07	7,780.20	78.54%	97.12%
11.	Matching Allocation Kwsb LGD T&C	3	17,554.10	1,595.03	2,000.00	1,117.50	1,050.39	55.88%	93.99%
12.	Board Of Revenue	7	11,678.71	5,695.32	3,149.96	1,519.77	1,427.78	48.25%	93.95%
13.	Labour & Human Resources	8	460.112	124.836	103.680	25.859	24.188	24.94%	93.54%
14.	Education	379	105,267.59	26,377.59	10,709.20	6,971.18	6,501.09	65.10%	93.26%
15.	Local Government	654	101,398.86	21,938.35	21,886.78	17,526.99	16,206.69	80.08%	92.47%
16.	New Development Initiatives	1	5,000.00	0.000	5,000.00	2,789.61	2,571.67	55.79%	92.19%
17.	Sports & Youth Affairs	68	7,191.18	2,678.28	1,152.00	636.626	573.772	55.26%	90.13%
18.	Information & Archives	11	1,671.67	58.274	241.443	106.584	95.348	44.14%	89.46%
19.	Agriculture	31	61,414.95	4,992.45	4,476.240	2,609.48	2,309.42	58.30%	88.50%
20.	Population Welfare	3	10,341.42	2,020.06	1,760.00	1,030.00	910.158	58.52%	88.36%
21.	Law, P.A, Prosecution & Human Rights	52	6,998.26	1,616.52	515.040	219.095	191.492	42.54%	87.40%
22.	Work & Services	706	145,206.26	35,621.52	9,744.48	11,132.63	9,507.48	114.25%	85.40%
23.	Home	83	17,889.36	3,210.36	1,583.02	1,219.82	1,037.87	77.06%	85.08%

24.	Culture, Tourism & Antiquities	99	13,242.92	3,468.31	1,602.72	950.053	803.882	59.28%	84.61%
25.	Planning & Development	17	22,954.57	5,304.67	4,214.13	1,249.20	1,019.20	29.64%	81.59%
26.	Social Welfare	8	1,218.46	226.965	153.360	83.077	66.843	54.17%	80.46%
27.	Health	210	110,222.28	24,338.65	13,224.92	9,663.23	7,248.04	73.07%	75.01%
28.	Stevta	15	7,522.08	1,834.38	720.000	408.255	305.197	56.70%	74.76%
29.	Information, Science & Technology	16	4,740.12	268.713	754.013	262.934	190.032	34.87%	72.27%
30.	Forest, Environment & Wildlife	23	5,647.63	591.093	966.240	504.288	363.360	52.19%	72.05%
31.	Minorities Affairs	13	2,497.30	395.523	567.810	236.394	164.550	41.63%	69.61%
32.	Alloc For 21 Sch Of Adp 2013-14	1	1,938.07	1,895.96	42.114	43.564	29.450	103.44%	67.60%
33.	Auqaf, Zakat, Ushr & Religious Affairs	19	1,447.22	376.994	266.400	170.748	110.089	64.09%	64.47%
34.	SGA & CD	44	15,876.15	3,717.10	1,800.39	682.489	434.805	37.91%	63.71%
35.	Katchi Abadis & Spatial Development	2	121.000	0.000	87.120	49.774	29.547	57.13%	59.36%
36.	Women Development	16	1,836.15	247.525	313.200	141.099	71.980	45.05%	51.01%
37.	Finance	4	292.907	96.907	30.793	14.640	7.291	47.54%	49.80%
38.	Governors Secretariat	4	581.760	67.995	113.995	93.154	44.994	81.72%	48.30%
39.	Livestock & Fisheries	26	11,713.53	4,488.24	2,070.67	799.455	357.610	38.61%	44.73%
40.	Provincial Ombudsman	1	75.000	57.423	16.526	6.896	2.532	41.73%	36.72%
41.	Mines & Mineral Development	8	1,117.47	468.442	279.420	91.041	21.234	32.58%	23.32%
42.	Transport & Mass Transit	4	3,722.66	188.864	3,216.00	472.138	43.007	14.68%	9.11%
44.	Rehabilitation	4	3,963.61	150.000	360.000	81.643	0.000	22.68%	0.00%
43.	Chief Ministers Secretariat	2	160.000	0.000	130.000	0.000	0.000	0.00%	N/A
45.	Sindh Revenue Board	2	2,600.00	0.000	480.960	0.000	0.000	0.00%	N/A
46.	Special Education	2	850.000	0.000	180.000	0.000	0.000	0.00%	N/A
	<b>TOTAL:</b>	<b>2938</b>	<b>900,762.08</b>	<b>196,858.13</b>	<b>143,155.00</b>	<b>105,559.42</b>	<b>95,666.50</b>	<b>73.74%</b>	<b>90.63%</b>

## Recent Decisions

Some of the important decisions recently taken include:

- Funds released by Finance Department to be based on the recommendation by MEC.
- Inspection Book to be maintained by the Executing Agencies.
- Publication of MEC Annual Report to be a regular activity.
- Schemes which are reported as Unsatisfactory by MEC and subsequently there is non-compliance, will be referred to anti-corruption agencies for necessary action.





## Media & Newspaper Snapshots

Photographs taken during the meetings with honourable Chief Minister in fiscal year 2014-15



Chief Minister Sindh Syed Qaim Ali Shah presiding over meeting regarding Progress Review Meeting at CM House Karachi



Chief Minister Sindh Syed Qaim Ali Shah presiding over meeting regarding Progress Review Meeting at CM House Karachi

## Review Meeting of Sukkur

Review meeting of Development Schemes progress of Sukkur chaired by Chief Secretary of Sindh





## Monitoring Snapshots

Few randomly picked snapshots of MEC field visit during fiscal year 2014-15.



Checking the steel design of pile bore



Main Entrance of to School Premises



DO MEC during visit with Monitoring team



Main Gate of Shiv ji Mandir



NICH front view of Main Building



Construction of Under-bypass at Hotel Mehran



Thickness of asphalt layer checked



Wheat Thresher at T. Jam workshop



Construction of gate



Director MEC, inspecting from E.A during visit



Plaster work almost completed of Main Building



Cattle race was made at village Tayab Sand for handling of animals





Width of carriage way is being checked in first mile



Briefing about Thar Coal Mithi project to ACS and DG-MEC



Work was not completed at RD 07



Work is in progress



Thickness of premix carpet verified



Inside View of Auditorium Hall

## Performance of the MIS Directorate

- Established **Data Centre** at Karachi, Networked Regional offices
- **Indigenously:**
  - Developed an improved Project Monitoring & Evaluation System (**PMESi**) for web-based electronic data management of ADP portfolio - extensive data mining, in-depth and comprehensive analytical features.
  - Developed Database driven MEC website Content Management System (**CMS**) with real-time statistics updates of field monitoring data.
  - Developed **Workflow Automation** system: File Management System (**FilMS**) – computerised the 5-staged process of report generation from the field by the Monitoring Officer to the issuance of report to the administrative department by the DG-MEC after due-diligences by the Regional Monitoring Officer, Sector Monitoring Officer and Director MEC.
  - **Trained** officers of MEC Hyderabad, Sukkur & Karachi on using and adopting technology.
  - FilMS now contains thousands of reports with report change **tracking** and **officer performance** analysis
  - Deployed Email Management Services
  - Policies & procedures at MIS Directorate are based on **ISO 9001:2008** QMS & **27001** ISMS
  - Over 500 PCIs Digitized for **Digital Library**
  - Developed CMS website of the parent P&D Department
  - Developed **Photo Galleria** for Visual Analytical Review of Monitored Schemes



## The Way Forward

### Objective

To make MEC a **Model of Excellence** and Establish its **Brand Equity** as the most efficient and capable entity



- **Awareness** – Create Familiarity with MEC and its services
- **Association** – Create a Good Perception of MEC
- **Attitude** – Enhance Service Value and Image
- **Attachment** – Service Delivery for Appreciation of Performance
- **Activity** - Participation & Involvement of all Stakeholders

### MEC Plans:

1. Strengthen MIS
2. Establish Regional Offices at Divisional Level across Sindh
3. Establish Scheme Evaluation Wing

### MIS Plans:

1. Web-based **Unique Project Identification Tool**
2. Develop **GIS** integrated with PMESi and FilMS
3. Extend **Workflow Automations in FilMS and PMESi** (fetch FD Updates)
4. Online **Complaint/Feedback Management System**
5. **Smart Phone Mobile Apps** for capturing real-time GPS coordinate of visuals and data
6. **Knowledge Management** – Document Sharing & Resource Pool
7. Implement Tier-4 **Business Continuity/Disaster Recovery** measures.

## Future Strategy

### Monitoring

- Expansion of Monitoring Capacity by establishing offices at Karachi, Mirpurkhas and Larkana – PC1 has been prepared and submitted for approval to set up regional office at Karachi and Larkana in the first phase.
- Enhancing Capability through Foreign Trainings and Allowances as incentives for the Human Resource
- Utilise ENABLING TECHNOLOGY for Non-Destructive Inspection of Infrastructure.



### MIS Directorate

- Develop and Implement Smartphone Application to monitoring schemes from the field – Monitoring Officers will be given spartphone to capture and send data online in real-time. PC1 has been prepared and submitted for approval.
- Increase Market-Based technically-skilled HR
- Upgrade Infrastructure, bandwidth and upgrade to Tier-3 ISMS compliant data-centre
- Increase process automation
- To mitigate the risk of trained and highly skilled HR turnover, which has been hired from the market, service regularisation is planned to ensure their retention.



## Annexure A – Detail of Completed Schemes

S.#	ADP No.	Department	Scheme Name	Estimated Cost	Visit Location	Visit Date	Reporting Status	To Be Completed in June 2015 or Not	Remarks
1	2	Agriculture	Introduction of Aerobic Rice Cultivation Technology (Thatta, Larkana, Jacobabad, Shikarpur, Kashmore, Kamber, Badin & Dadu)	13.661	MTOD	29/05/2015	Satisfactory	Yes	Completed
	2	Agriculture	Introduction of Aerobic Rice Cultivation Technology (Thatta, Larkana, Jacobabad, Shikarpur, Kashmore, Kamber, Badin & Dadu)	13.661	Shikarpur	05/04/2015	Not Applicable	No	Work not Started yet
	2	Agriculture	Introduction of Aerobic Rice Cultivation Technology (Thatta, Larkana, Jacobabad, Shikarpur, Kashmore, Kamber, Badin & Dadu)	13.661	Larkana	21/5/2015	Not Applicable	No	Work not Started yet
2	13	Agriculture	Construction of Compound Wall, Rehabilitation of Field Assistant House and Establishment of Agriculture Nursery at Agriculture Plot, Hyderabad	9.926	Hyderabad	29/05/2015	Average	No	Would not be completed Approx.50% of funds are yet to be released
3	27	Agriculture	Sindh On Farm Water Management Project (OFWMP) Comprehensive Project Cost. 3966.472 (2nd Revision)	3156.414	Sanghar	23-09-2014	Un-satisfactory	Yes	Completed
	27	Agriculture	Sindh On Farm Water Management Project (OFWMP) Comprehensive Project Cost. 3966.472 (2nd Revision)	3156.414	Badin	21-10-2014	Satisfactory	yes	Completed
4	29	Agriculture	Maintaining of Ground Water Table and Disposing Off Drainage water through Lined surface drain in Deh Chak-5, Village Mansoorabad, Salehpat	17.084	Khairpur	24/4/2015	Satisfactory	Yes	May be completed if remaining funds of 7.00 M released
5	34	Auqaf, Zakat, Ushr & Religious Affairs Department	Construction of Makhdoom Muhammad Hashim Thatvi Academy at Makli . (Revised)	28.833	Thatta	17/06/015	Average	Yes	Completed
6	35	Auqaf, Zakat, Ushr & Religious Affairs Department	Development, Repair & Renovation of Dargah Khairuddin Shah / Giay Shah	24.344	Sukkur	24/6/2015	Un-satisfactory	No	Due to lot of Deviations and mismanagement by consultant M/S Zaheeruddin & Co. and AD Auqaf Department the scheme will not be completed
7	36	Auqaf, Zakat, Ushr & Religious Affairs Department	Re-development of Dargah Lal Shahbaz Qalandar at Sehwan Sharif Phase-III (Revised)	260.797	Jamshoro	05/06/2015	Average	Yes	Completed

8	2937	Alloc For 21 Sch Of Adp 2013-14	Allocation for 21 schemes of ADP 2013-14 to be completed during 2014-15 (ADP No. 380 - Rs.2.739 M); (No. 381 - Rs. 3.339 M); (No. 382 - Rs. 4.020 M); (No. 383 - Rs. 1.560 M); (No. 419 - Rs. 0.578 M); (No. 513 - Rs. 2.016 M); (No: 516 - Rs. 0.824 M); (No. 663 - Rs. 3.080 M); (No. 670 - Rs. 4.724 M); (No. 672 - Rs. 4.954 M); (No. 726 - Rs. 1.046 M); (No. 784 - Rs. 0.445 M); (No. 802 - Rs. 3.336 M); (No. 814 - Rs. 0.804 M); (No. 640 - Rs. 1.000 M); (No: 1311 - Rs. 1.400 M); (No. 1260 - Rs. 0.590 M); (No. 1559 - Rs. 0.627 M); (No. 2009 - Rs. 1.615 M); (No. 2150 - Rs. 1.500 M); (No. 2165 namely road from Ghulam Nabi Chatoo to vill Hadi Bux Chatoo - Rs. 1.917 M);	1938.071	Sindh	05/04/2015	Average	Yes	
9	57	Board Of Revenue Department	Estt: of Sindh Civil Services Academy Reorganization and Rehabilitation of Tapedaers College at Hyderabad	56	Hyderabad	18/06/2015	Un-satisfactory	No	Would not be Completed Due to inept attitude and poor coordination b/w A.D. & the contractor
10	71	Culture, Tourism & Antiquities Department	Establishment of Makhdoom Khuhra Museum & Library at Dargah Makhdoom Khuhra Taluka Gambat, District Khairpur (TRUST)	47.297	Khairpur	24/4/2015	Average	Yes	The scheme was re-revised, 80-90% work completed, the work on Kashi work of mosque was in progress. An element of mistrust exist b/w Trustees & E/A which has caused delay of the scheme
11	72	Culture, Tourism & Antiquities Department	Documentation of Libraries of Culture Department in Sindh (Revised).	57.314	Karachi	13-05-2015	Average	Yes	Completed
12	73	Culture, Tourism & Antiquities Department	Printing of Gunj Sharif and recording of Shah jo Risalo.	13.866	Karachi	13-05-2015	Average	Yes	Completed
13	74	Culture, Tourism & Antiquities Department	Strengthening of Planning, Development, Monitoring, Implementation and Evaluation Cell in Culture & Tourism Department Karachi (Re-Revised).	49.359	Karachi	22-5-2015	Satisfactory	Yes	Completed
14	92	Culture, Tourism & Antiquities Department	Preparation and Publication of Braille in Sindhi Language	7.479	Hyderabad		Un-satisfactory	No	Would not be completed As stated by Mr.Ahsan Ahmed - Incharge (SLA) Hyderabad, no funds are released yet.

15	93	Culture, Tourism & Antiquities Department	Construction of Shades & Restoration of Marvi Well at Bhalwah, District Tharparkar (Revised)	23.831	Tharparkar	07/07/2015	Average	Yes	Completed
16	94	Culture, Tourism & Antiquities Department	Establishment of Public Library at Village Allah Ditto Bhanbhro, Taluka Bhiria, District N'Feroze	22.892	Naushero Feroz	20/5/2015	Average	Yes	
17	95	Culture, Tourism & Antiquities Department	Establishment of Open Air Theatre at Larkana District Larkana (Revised)	59.99	Larkana	18/5/2015	Average	Yes	
18	96	Culture, Tourism & Antiquities Department	Establishment of Shaheed Benazir Bhutto Museum at Sir Shah Nawaz Bhutto Library at Larkana	59.117	Larkana	18/5/2015	Average	Yes	The issue of face lifting is causing delay
19	97	Culture, Tourism & Antiquities Department	Establishment of Mithi Museum at Mithi (Revised)	59.991	Tharparkar	26-02-2015	Average	Yes	Already Completed
20	98	Culture, Tourism & Antiquities Department	Construction of Monuments at different Places in Sindh (PC-II) (Revised)	5.412	Sindh	25-05-2015	Average	Yes	
	98	Culture, Tourism & Antiquities Department	Construction of Monuments at different Places in Sindh (PC-II) (Revised)	5.412	Sindh	22/5/2015	Average	yes	
21	99	Culture, Tourism & Antiquities Department	Documentation of Sugharan Ji Kachehri and Printing of Books	10.322	Hyderabad, Karachi	05/04/2015	Average	Yes	Completed
22	100	Culture, Tourism & Antiquities Department	Printing of Unpublished Books on Culture	27.296	Karachi	13-05-2015	Average	Yes	Completed
23	101	Culture, Tourism & Antiquities Department	Rehabilitation / Renovation of Masoom Shah-Jo-Minaro and Library at Sukkur	27.464	Sukkur	05/11/2015	Average	Yes	
24	102	Culture, Tourism &	Up-gradation of Khalifo Muhammad Khan Jamali Library	2.83	Shaheed Benazirabad	05/06/2015	Average	Yes	completed if funds are provided

		Antiquities Department							
25	114	Culture, Tourism & Antiquities Department	Promotion of Tourism by Organizing events at various places in Sindh Province and participation at abroad	31.39	Karachi	20-05-2015	Un-satisfactory	Yes	Completed
26	119	Culture, Tourism & Antiquities Department	Provision of additional / missing facilities in PITHM at Karachi (Revised)	66.429	Karachi	20-05-2015	Average	Yes	Completed
27	120	Culture, Tourism & Antiquities Department	Gorakh Hills Development Project Phase-I Construction of Road from Wahi Pandhi to Gorakh Hill via Sain Luk Mile 0/0. 19/7	583.359	Dadu		Average	Yes	As stated by Mr. Gulzar Khusk (P.D.) Gorakh Project
28	127	Culture, Tourism & Antiquities Department	Extension / Repair & Renovation of Shah Jahan Restaurant at Thatta.	44.53	Thatta	18-05-2015	Average	Yes	Completed
29	407	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2004-05 Program) at Karachi 06, Ghotki 01, Benazirabad 01, Shikarpur 01, Jacobabad 01, Mirpurkhas 01, Dadu 01 (Revised)	532.278	Mirpur khas	11/11/2013	Un-satisfactory	Yes	
	407	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2004-05 Program) at Karachi 06, Ghotki 01, Benazirabad 01, Shikarpur 01, Jacobabad 01, Mirpurkhas 01, Dadu 01 (Revised)	532.278	Dadu	11/12/2013	Average	Yes	
	407	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2004-05 Program) at Karachi 06, Ghotki 01, Benazirabad 01, Shikarpur 01, Jacobabad 01, Mirpurkhas 01, Dadu 01 (Revised)	532.278	Karachi	13/12/2013	Average	Yes	
	407	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2004-05 Program) at Karachi 06, Ghotki 01, Benazirabad 01, Shikarpur 01, Jacobabad 01, Mirpurkhas 01, Dadu 01 (Revised)	532.278	Dadu, Ghotki, Jacobabad, Karachi, Mirpurkhas, Shaheed Benazir abad, Shikarpur		Not Applicable	Yes	
30	408	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2005-06 Program) at Karachi 05, Matiari 01, Tharparkar 01, Sanghar 01, Kamber 01, Larkana 01 N.Feroze 01 Sukkur 01 (Revised)	684.85	Qambar Shahdadkot	17/4/2015	Average	Yes	The physical status of scheme is completed but revenue component remains vague due to centralized procurement by Director General colleges karachi and no record was available at Regional Director colleges larkana.

	408	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2005-06 Program) at Karachi 05, Matiari 01, Tharparkar 01, Sanghar 01, Kamber 01, Larkana 01 N.Feroze 01 Sukkur 01 (Revised)	684.85	N. Feroze	22/4/2015	Average	yes	
	408	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2005-06 Program) at Karachi 05, Matiari 01, Tharparkar 01, Sanghar 01, Kamber 01, Larkana 01 N.Feroze 01 Sukkur 01 (Revised)	684.85	Matiari	19/11/2013	Average	Yes	
	408	Education	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2005-06 Program) at Karachi 05, Matiari 01, Tharparkar 01, Sanghar 01, Kamber 01, Larkana 01 N.Feroze 01 Sukkur 01 (Revised)	684.85	Karachi	24/12/2013	Average	Yes	
<b>31</b>	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	N. Feroze	18/6/2015	Un-satisfactory	Yes	
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Sukkur	04/06/2015	Un-satisfactory	yes	
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Khairpur	04/07/2015	Un-satisfactory	yes	
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	shikarpur	15/4/2015	Average	No	According to concerned XEN of Shikarpur the scheme would not be completed in all aspects upto June 2015 due to slow funding, revision of Sindh shedule rates & incomplete release of PC-I amount. It requires revision.
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Kamber	06/09/2015	Un-satisfactory	No	Funding Issue
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Thatta	17/02/2014	Un-satisfactory	Yes	
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Jamshoro	27/02/2014	Average	Yes	
	415	Education	Rehabilitation of existing Degree Colleges in Sindh (2008-09 Prog:) (86 Units)	854.903	Hyderabad	03/10/2014	Average	Yes	
<b>32</b>	418	Education	Establishment of Govt. Girls Degree College at Liaquatabad, Karachi (Revised)	184.156	Karachi	11-05-2012 13-02-2014	Satisfactory	Yes	
<b>33</b>	431	Education	Construction of Auditorium Hall at Cadet College Sanghar (Revised)	88.595	Sanghar	29/08/2015	Average	No	Would not be completed As per E/A; Rs.10 Million are yet to be released
<b>34</b>	432	Education	Construction of Building Pir Illahi Bux Law College at Dadu (Under Revision) (To be funded out of 10% Royalty share)	257.28	Dadu	13/7/2015	Average	Yes	Completed
<b>35</b>	437	Education	Miscellaneous Immediate Works of Cadet College Larkana	113.229	Larkana	13/5/2015	Satisfactory	Yes	

36	448	Education	Opening of Syed Noor Muhammad Shah GBDC Tharu Shah, District N.Feroze.	98.246	Naushero Feroz	18/6/2015	Average	Yes	Would be Completed
37	165	Education	Renovation of Six Schools of Govt. of Sindh Located at PAF Base Faisal. (06 Units)	122.707	Karachi	16-09-2014	Average	Yes	Completed
38	166	Education	Up-Gradation of Boys Primary School to Middle School at Village Rais Photo Khan Zardari U.C. Khairwah Taluka Moro District N.Feroze	10.844	Naushero Feroz	28/4/2015	Average	Yes	The scheme completed in all respects except electric work.
39	170	Education	Construction of Building in existing primary school at GBPS Dandhkaro U.C. Bolhari, Taluka Diplo	3.444	Tharparkar		Average	Yes	Completed
40	482	Education	Provision of Drinking Water & Purification for Sukkur Institute of Business (IBA Sukkur)	52	Sukkur	02/10/2015	Satisfactory	Yes	Would be completed
41	505	Education	Supplementing the Federal Program of Non Formal Education in Sindh through RSPs	401.814	Sindh	15/7/2015	Average	Yes	Already Completed
	505	Education	Supplementing the Federal Program of Non Formal Education in Sindh through RSPs	401.814	Sindh		Un-satisfactory	No	Would not be Completed As per E/A, the scheme is abandoned due to meagre releases against given financial allocation
42	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Shikarpur	06/12/2015	Un-satisfactory	No	Slow Progress, Honey combing, cracks, poor masonry, steel exposed & low compressive strength were the main reasons
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	N. Feroze	19//6/2015	Un-satisfactory	No	90% Work was Completed. It was noted some advance payment was made to contractor in one Unit.
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Ghotki	30/6/2015	Un-satisfactory	No	85% Work was Completed. It was noted some advance payment was made to contractor in Two Unit.
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Tando Mohammad Khan	11/04/2013	Average	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Sanghar	11/06/2013	Un-satisfactory	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Tando Allahyar	11/11/2013	Un-satisfactory	Yes	Rs. 17 milions are yet to be released

	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Dadu	18/11/2013	Un-satisfactory	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Thatta	18/11/2013	Un-satisfactory	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Hyderabad	25/11/2013	Average	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Jamshoro	27/11/2013	Un-satisfactory	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Tharparkar	19/12/2015	Un-satisfactory	Yes	Rs. 17 milions are yet to be released
	276	Education	Upgradation of Middle Schools to High Schools in Sindh (2005-06 Prog.)	955.858	Hyderabad	18/8/2014	Average	Yes	Rs. 17 milions are yet to be released
<b>43</b>	283	Education	Establishment of Single Section High School for Boys & Girls and Construction of Class Rooms in Existing Primary School at Shah Mardan Shah-II (Pir Pagara-VIII) Race Club, Gulshan-e-Iqbal, Karachi (Under Revision)	54.75	Karachi	16/09/2013	Satisfactory	Yes	Completed
<b>44</b>	293	Education	Up-gradation of Primary to Secondary School at Altaf Hussain Hali Gulberg Town Karachi	29.438	Karachi	22/05/2105	Average	Yes	Completed
<b>45</b>	398	Education	Remaining Work of GBSS Chanessar Goth & GSS PECHS Society Block 6 Karachi.	60	Karachi	21/05/2015	Average	Yes	Completed
<b>46</b>	261	Education	Construction of VIP Suites for Faculty of PITE Sindh, Nawabshah (Revised)	92.244	Shaheed Benazirabad	15/6/2015	Satisfactory	No	Physical Work was Completed while the amount of revenue component has not been released yet.
<b>47</b>	561	Energy Department	Village Electrification Programme in Sindh (Phase-V) (All Districts excludg. KESC licenced area)	905	Sukkur	06/03/2015	Not Started	No	Work was not executed Because changed in Scope
	561	Energy Department	Village Electrification Programme in Sindh (Phase-V) (All Districts excludg. KESC licenced area)	905	Shikarpur	26/6/2015	Not Applicable	No	Work was not executed
	561	Energy Department	Village Electrification Programme in Sindh (Phase-V) (All Districts excludg. KESC licenced area)	905	Ghotki	29/5/2015	Satisfactory	No	
	561	Energy Department	Village Electrification Programme in Sindh (Phase-V) (All Districts excludg. KESC licenced area)	905	Sindh	13-03-2015	Average	yes	50% Progress achieved
<b>48</b>	562	Energy Department	Electrification of Goths (Villages) in Karachi (Phase-IV), KESC licenced area).	95	Karachi	02/12/2015	Average	No	60% Progress achieved Completed As Stated by XEN
<b>49</b>	564	Energy Department	Electrification of Four Villages through Directorate of Village Electrification Programme Sindh (2 Villages within Licensed Area of HESCO & SEPCO each as pilot project)	6.12	Badin,Matiari,S hikarpur	19/05/2015	Average	No	Would not be Completed Due to shortage of material at store of HESCO (WAPDA) Hyderabad

	564	Energy Department	Electrification of Four Villages through Directorate of Village Electrification Programme Sindh (2 Villages within Licensed Area of HESCO & SEPCO each as pilot project)	6.12	Badin, Matiari, Shikarpur	13/7/2015	Not Applicable	No	Mr. Manzoor Ahmed Soomro Project Director SEPCO info through letter that this scheme is not executed in this Shikarpur.
50	541	Energy Department	Environmental and Social Studies, land use plan including resettlement framework and development of Geographic Information System (GIS) for Thar coalfield	230	Tharparkar	08/04/2015	Average	Yes	Completed
51	543	Energy Department	Installation of 31 R.O. Plants in Tharparkar and Umerkot Districts	1139.972	Tharparkar		Average	Yes	Completed
52	545	Energy Department	Marketing of Coal Resources of Sindh through Road Shows, Conferences, Seminars and Trainings to Attract Potential Investors and International Financing Institutes.	75	Sindh	08/04/2015	Average	Yes	Completed
53	613	Governors Secretariat	Const. of Office Block Sindh Governor's House Karachi.	28	Karachi		Average	Yes	Completed
54	616	Governors Secretariat	Supply and installation of security equipment in Governor's House Karachi.	89.99	Karachi	02/04/2015	Average	Yes	Completed
55	824	Health Department	Improvement of Children Hospital at North Karachi Rs. 1546.456 (JICA Grant) Rs. 129.496 (GOS) Total 1675.952	129.496	Karachi		Average	Yes	Completed
56	792	Health Department	Construction of International Hostel for 240 Students at Peoples Medical College Nawabshah. (Re-Revised) (C. 163.748+R.3.499).	167.248	Shaheed Benazirabad	06/12/2015	Average	Yes	Would be Completed
57	794	Health Department	Renovation & Rehabilitation of Auditorium Hall in the premises of Chandka Medical College Larkana. (C.5.390+R.22.841).	28.231	Larkana	06/10/2015	Average	Yes	Tenders are already invited for Revenue Components and Supply will be expected on 15 and 16 June 2015 according to account officer of SBBU, while Capital component is already completed in 2011 and 2012
58	796	Health Department	Construction of Girls Hostel for 200 under graduate / postgraduate students of Liaquat Medical College Jamshoro. (C.158.965+R.13.224).	172.189	Jamshoro	25-02-2015	Average	Yes	Completed
59	804	Health Department	Allotment of land Measuring 220 Acres for Establishment of Shaheed Mohtarma Benazir Bhutto Medical University, Larkana.	14.3	Larkana	27/7/2015	Satisfactory	Yes	Would be completed
60	663	Health Department	Renovation, Rehabilitation and Addition in TB Hospital (Institute of chest Diseases) at Ojha Campus, Dow University of Health Sciences, Karachi. (C. 345.206 + R. 38.911)	384.117	Karachi	09/09/2014	Average	No	Would not be completed As stated by E/A approx.Rs.35 Million are yet to be released



61	667	Health Department	Up gradation of Taluka Hospital Gambat to the level of Institute of Medical Sciences. (Revised). (C. 80.889+R.43.533).	124.422	Khairpur	06/02/2015	Average	No	Would not be Completed
62	668	Health Department	Establishment of Trauma Centre at Gambat Institute of Medical Sciences at Gambat. (Revised). (C. 122.676+R.119.045).	241.721	Khairpur	28/5/2015	Satisfactory	Yes	
63	673	Health Department	Establishment of Children Hospital at SIUT Karachi. (C. 344.000 SIUT+ R. 577.023 GOS. = 921.023)	577.023	Karachi	22/9/2014	Satisfactory	Yes	Completed
64	688	Health Department	Upgradation and Strengthening of Women and Children Hospital Shikarpur (Revised)	109.98	Shikarpur	04/10/2015	Average	No	Due to deviation from scope & payment issues a row b/w management i.e. Madam Zeenat Issani & contractor has erupted due to which the work has been halted & would not be completed.
65	689	Health Department	Upgradation of BHU at Punhal Khan Chandio to the level of A-Type RHC, District Shaheed Benazirabad. (Revised) (C. 83.990 + R. 22.805)	106.795	Shaheed Benazirabad	05/08/2015	Average	No	scope of work will not be completed
66	690	Health Department	Construction of Mother & Child Health Centre at UC Karimbux at village Bahadurpur Taluka Thul District Jacobabad. (C.36.455+R.12.153).	48.608	Jacobabad	17/6/2015	Average	No	Would not be Completed
67	692	Health Department	Strengthening of services of SIUT, Karachi (R. 194.320)	194.32	Karachi	03/12/2014	Satisfactory	Yes	Completed
68	695	Health Department	Repair / Renovation of DHQ Hospital (Civil (Hospital) Jacobabad, THQ Hospital Tull, Garhi Khairo and Construction of Female Nursing Hostel at Jacobabad. (C. 155.432 + R. 75.720)	231.152	Jacobabad	18/6/2015	Average	Yes	90% work is completed. Nursing Hostel, Mosque and Staff Quarters were in finishing phase.
69	705	Health Department	Construction of BHU at Village Deh Phulell UC Shahpur Jehania Taluka Kazi Ahmed. (C. 21.592+R.0.779).	22.371	Shaheed Benazirabad	13/4/2015	Average	Yes	Work is in progress
70	708	Health Department	Up gradation of BHU to RHC Haji Fateh Mohammad Rajar (C.48.521+R.15.902)	64.423	Umerkot	13-05-2015	Average	Yes	Completed
71	709	Health Department	Construction of BHU at Mureed Shaikh Taluka Ubaro. (C. 18.452 + R. 2.985) (To be funded out of 10% Royalty share)	21.437	Ghotki	22/6/2015	Satisfactory	Yes	Would be Completed
72	710	Health Department	Construction of Dispensary building (02 Nos) in Taluka Golarchi (i) village Allah Dino Karo Nohani (ii) village Haji Naymat Gujjar. (C.10.443+R.2.035).	12.478	Badin	26-5-2015	Average	Yes	Completed
73	711	Health Department	Construction of BHU Mohammad Ashraf Samoo Golari Taluka Talhar District Badin . (C. 20.629+R.2.260).	22.889	Badin	26-5-2015	Average	Yes	Completed
74	712	Health Department	Construction of BHU at village Haji Ramzan Chandio Taluka Badin. (C.20.303+R.2.260).	22.563	Badin	26-5-2015	Un-satisfactory	Yes	Completed

75	720	Health Department	Renovation & equipment for Maternity Home at Manghopir (C. 19.505 + R. 6.456)	25.961	Karachi	11/12/2014	Average	Yes	Completed
76	727	Health Department	Upgradation of Basic Health Unit to the level of Rural Health Centre, Ghulam Haider Shah, District Mirpurkhas. (C.43.485+R.11.058).	54.543	Mirpurkhas	07/06/2015	Average	Yes	Completed
77	728	Health Department	Upgradation of Basic Health Unit to the level of Rural Health Centre, Jhulri, District Mirpurkhas. (C.43.485+R.11.058).	54.543	Mirpurkhas	29-4-2015	Average	Yes	Completed
78	729	Health Department	Construction of two BHU at (i) Shah Faisal Colony (ii) korangi No.5 Karachi. (C.23.126+R.6.534).	29.66	Karachi	13-05-2015	Satisfactory	Yes	Completed
79	732	Health Department	Shaheed Benazir Bhutto Rehabilitation Centre for Burn and Rape Victims at Maternity Home of RHC old Thana Malir, Karachi (C.39.752+R.19.195)	57.947	Karachi	13-05-2015	Satisfactory	Yes	Completed
	732	Health Department	Shaheed Benazir Bhutto Rehabilitation Centre for Burn and Rape Victims at Maternity Home of RHC old Thana Malir, Karachi (C.39.752+R.19.195)	57.947	Karachi	28-11-2014	Average	yes	Completed
80	733	Health Department	SIUT Multi-Organ Transplant and biological Centre at Kathore Karachi. (Feasibility PC-2)	17.72	Karachi	07/10/2015	Average	Yes	Completed
81	782	Health Department	Construction of Shaheed Benazir Bhutto Hepatitis Centre at Dadu (To be funded out of 10% Royalty share)	35	Dadu	14/7/2015	Average	Yes	Completed
82	787	Health Department	Provision of dialysis facilities to poor patients through welfare society (all districts) except Karachi.	60	Hyderabad, Dadu, Jamshoro, Thatta, Badin, Mirpurkhas, Umerkot, Sanghar, Tharparkar, Sukkur, Shaheed Benazirabad, Naushero Feroze, Khairpur, Ghotki, Larkana, Qambar Shahdaskot, Shikarpur, Jacobabad, Kashmore, Sujawal, Matiari, Tando Allahyar, Tando Mohd. Khan	07/10/2015	Average	Yes	Completed

83	809	Health Department	Operational Support for EPI Sindh (all Districts)	199.611	Sindh	15/04/2014	Average	Yes	Completed
84	617	Health Department	Modernization of Electrification distribution network at Civil Hospital Karachi. (Re-revised) (C. 321.294)	321.294	Karachi	06/08/2015	Average	Yes	Completed
85	618	Health Department	Establishment of Accident Emergency /Trauma Centre at PMCH Nawabshah. (C. 85.018+R. 92.058)	177.076	Shaheed Benazirabad	05/08/2015	Average	Yes	
86	623	Health Department	Establishment of Shaheed Benazir Bhutto Skin Diseases Complex and Hepatology and Dental Deptt: at CMCH Larkana. (C. 89.227 + R. 45.689)	134.916	Larkana	06/10/2015	Average	Yes	Would be Completed
87	624	Health Department	Expansion & Improvement of Oncology Department & Upgradation of Neurology Department, Surgical ICU and establishment of colorectal unit in Surgical Unit V at Civil Hospital Karachi. (Revised) (C. 148.029 + R. 90.640)	238.669	Karachi	05/08/2015	Average	Yes	Completed
88	625	Health Department	Revamping / Revitalization of Shaikh Zaid Hospital for Women Larkana. (C. 109.480 + R. 51.872)	161.352	Larkana		Average	Yes	Already Completed
89	629	Health Department	Purchase & installation of Bed lift and purchase of Auto start 250KV Diesel / Gas Generator at Liaquat University Hospital Hyderabad / Jamshoro. (Revised). (C. 13.272+R. 24.757).	38.029	Hyderabad	18/5/2015	Average	Yes	Completed
90	630	Health Department	Strengthening of Eye Hospital, LUH, Hyderabad. (C. 86.089 + R. 58.705)	144.794	Hyderabad	20/03/2015	Average	Yes	Completed
91	632	Health Department	Revamping of Civil Hospital Karachi. (C. 198.650)	198.65	Karachi	05/08/2015	Average	Yes	Completed
92	638	Health Department	Purchase of equipment for Physiotherapy Department and Orthopaedic Operation Theatres at Civil Hospital Karachi. (R. 280.375).	280.375	Karachi	17-09-2014	Satisfactory	Yes	Completed
93	910	Industries & Commerce Department	Small Industrial Estate, Mithi (50 acres) (Revised)	56.082	Tharparkar	06/01/2015	Average	Yes	Completed
94	921	Information & Archives Department	Preservation of Karachi Registrar Office Record.	48.5	Karachi	13-05-2015	Satisfactory	Yes	Completed
95	932	Information, Science & Technology Department	Intranet setup for Govt. of Sindh (Phase-II)	59.861	Karachi	13-05-2015	Average	Yes	Completed
96	933	Information, Science & Technology Department	IT Training for capacity Building of Sindh Government Employees	59.4	Karachi	13-05-2015	Average	Yes	Completed
97	934	Information, Science & Technology Department	Mainstreaming of E-Government/ strengthening of Governance, Program Management, and Quality Assurance practices at IT Department	59.978	Karachi	13-05-2015	Average	Yes	Completed

98	936	Information, Science & Technology Department	Establishment of Video Conferencing System in Sindh (Phase-II)	246.586	Karachi	13-05-2015	Average	Yes	Completed
99	937	Information, Science & Technology Department	Data Centre for Govt of Sindh PC-II( Feasibility study for Centralized Data Centre)	56.733	Karachi	13-05-2015	Average	Yes	Completed
100	960	Irrigation Department	Construction of New Langho Surface Drainage Scheme Mahi Wah @ RD - 24	77.459	Ghotki	06/02/2015	Average	Yes	
101	961	Irrigation Department	Surface Drainage Scheme in Deh 23 Satpuri UC Dalel Dero Taluka Sakrand District Shaheed Benazirabad.	108.532	Shaheed Benazirabad	15/6/2015	Satisfactory	Yes	Would be Completed
102	963	Irrigation Department	Installation of Pumping Station at Deh Panwari & Deh Baran U/C Chanhen Near Sanwalabad Taluka Bhiria and Construction of Pumping Station (two nos. additional pumps) Behelain (L/S) at Rohri Canal (Revised).	35.74	Naushero Feroz	29/5/2015	Un-satisfactory	Yes	
103	968	Irrigation Department	Excavation & Earth work of Sim Nala from Ripri to Khura and construction of pumping station along right side Rohri Canal (between Setharja & Deparja)	57.79	Khairpur	24/7/2015	Un-satisfactory	No	Excavation work of sim nala is still remaining in some RD
104	970	Irrigation Department	Rehabilitation of 50 No Tube wells and Installation of 25 Nos. New Tube wells in Shikarpur Drainage Division.	189.861	Larkana, Shikarpur, Qambar Shahdadkot, Sukkur	13/7/2015 & 14/7/2015	Average	Yes	The scheme may go beyond 30th June 2015 due to non-provision of Electric connection by WAPDA at some Tube well locations
105	979	Irrigation Department	Construction of Two (02) Link Drains from Sanjar Chang to Sorahadi, Taluka Golarchi Badin.	749.967	Badin	17-9-2014	Satisfactory	Yes	Already Completed
106	988	Irrigation Department	Surface Drainage Scheme in Deh 18 & 19 Nusrat Taluka Daur Distt: SBA	135.768	Shaheed Benazirabad	23/7/2015	Average	Yes	Would be completed
107	993	Irrigation Department	Construction of Road Bridges Over Bathoro Branch Drain at RD-88.0 1-1L Kapoor Branch Drain at RD-32.0.	23.95	Thatta	12/01/2014	Satisfactory	Yes	Already Completed
108	994	Irrigation Department	Surface Drainage Scheme of 20.0 Cusecs at U.C. Oderolal Station Deh Jakhiri Taluka Matiari and Jhando Mari Drainage Scheme on Right Side of West Branch	59.831	Matiari	03/04/2015	Satisfactory	Yes	Completed
109	1004	Irrigation Department	Surface Drainage Scheme Deh Dalli Wadi Taluka & District Hyderabad.	154.957	Hyderabad	12/05/2014	Satisfactory	Yes	Completed
110	1041	Irrigation Department	Construction of Chief Engineer Sukkur Barrage Left Bank Region Office Complex (Revised).	123.499	Sukkur	13/5/2015	Satisfactory	Yes	Procurement in final stages
111	1042	Irrigation Department	Rehabilitation X-Regulators of Rohri Main Canal (Revised).	348.59	Khairpur, Naushero Feroz, Shaheed Benazirabad	16/6/2015	Average	No	Would Not be Completed

112	1043	Irrigation Department	Up-gradation & Construction of Compound Wall of Field Research Station at Kali Mori, Hyderabad.	19.99	Hyderabad	04/08/2015	Satisfactory	Yes	Completed
113	1047	Irrigation Department	Construction of Rest House 10 Nos. Staff Quarters for employees in Drainage Division LBOD Shaheed Benazirabad (Revised).	118.552	Shaheed Benazirabad	27/3/2015	Satisfactory	Yes	
114	1048	Irrigation Department	Shifting Head Regulator of Gilspi Minor Near 57 Regulator in Taluka Bakrani District Larkana	10.015	Larkana	06/10/2015	Not Started	No	No Work Started due to Land Dispute as reported by Mr. Nisar Laghari, XEN Northern Dadu division Larkana
115	1049	Irrigation Department	Construction of Annexy in District Shaheed Benazirabad in Nasrat Divn: (Revised).	73.671	Shaheed Benazirabad	27/3/2015	Satisfactory	Yes	
116	1056	Irrigation Department	Rehabilitation of Banks of Khirthar Branch from RD-0 to 116 & Extension of Open Type Modules along Khirthar Branch of Saifullah Magsi Branch Division, Shahdadkot (Revised).	535.135	Qambar Shahdadkot	27/7/2015	Not Visited	In Process	visit was cancelled due to flood Emergency declare in Sindh.
117	1058	Irrigation Department	Rehabilitation of Road Bridges at RD-9 & 25, Constructing New Road Bridge at RD-51, I/C Constructing Retaining Wall & Providing Stone Pitching along Dingro Wah.	20.213	Ghotki, Sukkur	06/01/2015	Average	No	The Scope not will be completed due to lesser allocation and releases
118	1064	Irrigation Department	Constructing of Pumping Station at RD-31 Kakole Branch and Construction of Bridge over Ganhwar Wah at RD - 10 near Village Ali Akbar Mugheri.	49.123	Dadu	02/09/2014	Average	Yes	Already Completed
119	1070	Irrigation Department	Rehabilitation / Renovation of Office / Residential Bungalows and Inspection Bungalows in Shahbaz Irrigation Division Sehwan	136.56	Jamshoro	27-04-2015	Average	Yes	Completed
120	1071	Irrigation Department	Rehabilitation / Construction of Selachi Minor & Road Bridges in Kandhkot Division Kashmore	75.928	Kashmore	29/4/2015	Average	Yes	
121	1073	Irrigation Department	Lining of Ghouspur Minor RD-0 to 35.0	178.125	Kashmore	16/7/2015	Un-satisfactory	Yes	Would be completed by July or August 2015
122	1076	Irrigation Department	Rehabilitation of Group Regulator at RD- 269 of BS Feeder	198.808	Kashmore	25/06/2015	Average	Yes	Already Completed
123	1079	Irrigation Department	Construction of 4 Nos. Bridges (i) Darro Branch RD-65 (ii) Baghan Bridge Deh Samme Jan U.C Karim (iii) Chorwah Village Ramzan Rind U.C Jhoke Sharif (iv) Fatya Wah Bridge Bathoro Canal Near Mehar Shah	59.114	Thatta	28-9-2014	Average	Yes	Already Completed
124	1080	Irrigation Department	Rehabilitation of Kalri Escape and Bhiryo Shedci Bridge / Regulator @ P.B. Bund Mile-3. Raj Wah Ex. P.F.L from Daro Branch & Remodelling of Khanti Link	133.655	Thatta	02/10/2014	Un-satisfactory	Yes	Completed
125	1090	Irrigation Department	Construction of Protection (Retaining Wall) along Warah Branch RD-211 to RD215 NIP Side I/C Akil Distry RD-23 to RD-25 NIP Side	112.721	Larkana	07/10/2015	Un-satisfactory	Yes	Completed with Reduced length of Retaining Wall
126	1095	Irrigation Department	Construction of Protection Bund Deh Bijarani near Village Ashraf Ali Khan Bijarani from Mile 0/0 - 0/6	19.917	Kashmore	26/06/2015	Average	Yes	Would be Completed
127	1100	Irrigation Department	Construction of stone pitching along Rohri Main Canal in vulnerable reaches of Rohri, Dad & Hala Division.	600	Matiari, Naushero	15/7/2015	Un-satisfactory	No	Funds are not released in Kandiaro Division,

					Feroz,Shaheed Benazirabad				Liabilities are remaining.
	1100	Irrigation Department	Construction of stone pitching along Rohri Main Canal in vulnerable reaches of Rohri, Dad & Hala Division.	600	Matuari,Nausher o Feroz,Shaheed Benazirabad	27/1/2015	Un-satisfactory	yes	Completed
128	1102	Irrigation Department	Rehabilitation of Hydraulic Regulators Gates in Khairpur Irrigation Circle Sukkur through Mechanical Circle in Sindh.	55	Khairpur	07/10/2015	Average	No	The scheme progress is slow due to funding issue.
129	1106	Irrigation Department	C.C. Lining of Khiyanri Minor from RD-0 to RD-18.5	59.856	Khairpur	06/04/2015	Average	Yes	
130	1109	Irrigation Department	C.C. Lining of New Shekhani Minor Ex-Rohri Main Canal at RD-829 IP Side, including Old Shekhani Minor, Chhar Minor & Tarah Tail.	400	Matuari	08/07/2014	Satisfactory	Yes	Completed
131	1110	Irrigation Department	Reh;/Re-Sectioning Jam Br: from RD 0 to 83 and Extension of Babra Minor EX: Jam Branch RD 15 to 19.3 (Baghar Circle)	198.761	Thatta	15/5/2014	Satisfactory	Yes	Completed
132	1118	Irrigation Department	De-silting along Mithrao Canal (in different reaches).	95.336	Mirpurkhas,Sanghar,Umerkot	13-01-2015	Un-satisfactory	Yes	Already Completed
133	1136	Irrigation Department	Pilot Project for Sealing of K.B Feeder Canal by Polymer	89.268	Thatta	28/1/2015	Average	Yes	Completed
134	1194	Irrigation Department	De-silting of Matli Branch Canal and off-taking channels of Phueleli System.	70	Badin	07/08/2015	Average	Yes	Completed
135	1195	Irrigation Department	Construction of Bridge over RD-132 Village Usman Mandhro, Arab Mandhro, Mirwah Talhar.	50	Badin	07/08/2015	Satisfactory	Yes	Completed
136	1245	Irrigation Department	Constructing Out-let i/c Channel Ex: Ranpur Dam, HEIS, Extension of Malji Bund and Stone Pitching and Three (03) Nos. Gabion Dams including Re-modelling of Lakhy-jo- Wandio Dam in Nagarparkar Area.	98.981	Tharparkar	14-05-2014	Satisfactory	Yes	Already Completed
137	1247	Irrigation Department	Construction of Kataro Weir Dam in Taluka District Thatta	272.57	Thatta	02/12/2015	Satisfactory	Yes	Already Completed
138	948	Irrigation Department	Feasibility study for the survey & designing of Surface Drainage and Works for the part command area of Mithrao, Khipro & Lower Nara Canal	35.7	Mirpurkhas,Shaheed Benazirabad,Sanghar	09/11/2014	Satisfactory	Yes	Completed
139	949	Irrigation Department	Feasibility Study Identifying the route to divert excessive flood water along River Indus.	49.27	Ghotki,Khairpur ,Sanghar,Tharparkar	23/9/2014	Satisfactory	Yes	Completed
140	950	Irrigation Department	Procurement of Consultancy Services for the Feasibility Study and Detailed Design for Repairing Master Drainage Plan for LBOD Drainage Division Shaheed Benazirabad.	16.047	Shaheed Benazirabad	27/03/2015	Average	Yes	Would be completed
141	1257	Katchi Abadis & Spatial Development Department	Allocation for Katchi Abadies & Spatial Dev. Dept.	30	Karachi,Tando Mohd. Khan	25-5-2015	Average	Yes	Completed

142	1291	Law, P.A, Prosecution & Human Rights Department	Construction of Record Room adjacent of Judicial Complex Badin	21.959	Badin	24-02-2015	Average	Yes	75% Progress Achieved
143	1426	Local Government	Development of Infrastructure of District Badin Water supply & Drainage (Khoski, Pangrio, Kadhan and Lawari Sharif)	192.237	Badin	07/06/2015	Average	Yes	Completed
144	1428	Local Government	Rehabilitation of water supply scheme K.N.Shah taluka K.N.Shah district Dadu. (To be funded out of 10% Royalty share)	120	Dadu	06/11/2015	Average	Yes	Completed
145	1431	Local Government	Provision of Sewage / drainage disposal i.e. main box drain 8400 ft and connecting secondary sewer at Yar Mohammad Goth and surrounding goths settlements UC-8 Gadap Town, Karachi.	90.88	Karachi	25-6-2015	Average	No	Would not be completed as stated by Mr.Zahid Sahab (XEN-GADAP) (PHED) Approx.50% of funds are yet to be released
146	1434	Local Government	Providing and Laying 54" dia main sewer for improvement of sewerage system from Lyari river to Godhra More of New Karachi, Town Karachi.	47.94	Karachi	25-5-2015	Average	Yes	Already Completed
147	1435	Local Government	Providing laying 24" 18' and 15" dia sewer for improvement in UC-3, 4, 5 and 11 of new Karachi town	29.56	Karachi	25-5-2015	Average	Yes	Already Completed
148	1436	Local Government	Umbrella PC-I for improvement of CC streets, internal road and water and sewerage system in different areas of Mehmoodabad and Gizri, district South	79.972	Karachi	25-5-2015	Satisfactory	Yes	Already Completed
149	1439	Local Government	Urban Water Supply Scheme Sehwan (Improvement and Extension) Taluka Sehwan (District Jamshoro) (Rs. 70.510 m. to be funded out of 10% Royalty Share)	125.48	Jamshoro	07/08/2015	Average	No	Would not be completed as stated by Mr.Idrees Memon Sahab of (PHED). Physical Progress is 50% Scheme is under revision
150	1441	Local Government	Improvement & ext. of Drainage Scheme Phulpota UC Behmena, Taluka Ratodero PS-37	20	Larkana	06/11/2015	Average	Yes	Power connection awaited
151	1442	Local Government	Construction of main drain and CC block from Burdi Mohalla to Gharibabad disposal via Hamid Shah colony UC Bukhair, taluka Khairpur	12	Khairpur	06/03/2015	Average	Yes	Would be Completed
152	1443	Local Government	Construction of drains and CC block at Katchi Abadis near Faizabad Saleemabad and Bhatti Mohalla UC Jeelani, taluka Khairpur	13	Khairpur	30/6/2015	Average	Yes	Already Completed
153	1448	Local Government	Village Malhi Colony Menghwar Paro and Village Lakho Unnar Menghwar Paro Deh 110 U.C Mirpur Old, Taluka Hussain Bux Mari District Mirpurkhas.	14.47	Mirpurkhas		Average	No	Would not be Completed As per E/A funds are yet to be released
154	1450	Local Government	Rehabilitation of infrastructure services Baba & Bhit island, TMA Keamari	49.963	Karachi	07/10/2015	Satisfactory	Yes	Completed

155	1452	Local Government	Providing & laying of 48" dia RCC storm water drain pipe line from prominent chowrangi to Marine Drive for the improvement of Block-2, Clifton, Saddar, Karachi.	15.363	Karachi	07/07/2015	Average	Yes	Completed as stated by Mr.Anwar Memon (XEN-SADDAR)
156	1455	Local Government	Rural Water Supply Scheme at Hashim Goth and its surrounding villages Gadap Town Karachi (Phase-I)	100	Karachi	07/07/2015	Average	Yes	Completed as stated by Mr.Nasrullah Memon Sahab
157	1458	Local Government	Umbrella PC-I for Improvement / Up-gradation of Parks / Playgrounds, Water & Sewerage System & CC Streets in the Areas of Clifton, DMC (South), Karachi	70	Karachi	30/6/2015	Satisfactory	Yes	Completed
158	1460	Local Government	Construction of new pumping station at Mian Wali Colony UC-09 SITE Town, Karachi	91.877	Karachi	07/06/2015	Average	Yes	Completed
159	1461	Local Government	Replacement/ Laying & P/L 24", 18", 12" & 8" dia sewerage line in UC No. 04, 08, 09, 10 & 11 Clifton/Saddar Town Karachi	20	Karachi	06/05/2015	Average	No	Would not be completed as stated by Mr.Anwar Memon (XEN-SADDAR) Scheme is under revision
160	1488	Local Government	Office accomodation for district govt. secretariat and renovation of existing office Ghotki at Mirpur Mathelo	59.753	Ghotki	29/6/2015	Average	No	Funding Issue
161	1496	Local Government	Construction of roads, footpaths, CC flooring and lighting arrangement in PS 117 (KMC)	99.98	Karachi	16-01-2014	Average	Yes	Already Completed
162	1504	Local Government	Rehabilitation of various roads of Taluka Sobhodero, Gambat, Kotdiji, Nara, Thari Mirwah, Kingri, Khairpur & Faiz Ganj.	354.188	Khairpur	06/09/2015	Average	No	Funding Issue
163	1508	Local Government	Improvement of Internal road of Kandhkot City. (To be funded out of 10% Royalty share)	182	Kashmore	25/6/2015 & 26/6/2015	Un-satisfactory	No	Funding Issue
164	1511	Local Government	Construction of 1.637 km dual road from Kiran Hospital road chowrangi to KBACH Society Karachi	97.802	Karachi	09/10/2014	Average	Yes	Already Completed
165	1513	Local Government	Rehabilitation of roads (25 Nos.) of Jacobabad District	164.931	Jacobabad	20 & 21/4/2015	Un-satisfactory	No	3.0 Million required for completion as informed by AEN.
166	1514	Local Government	Construction of Road from Humazo Nizamani to Village Allah Dad Bhurgari (1.6 Km)	12.103	Badin	16-10-2014	Average	Yes	Already Completed
167	1517	Local Government	Construction of road from Badin Sujawal road to village Fatehabad mile 0/0 - 1/2 (2 km)	10.435	Badin	16-10-2014	Un-satisfactory	Yes	Already Completed
168	1518	Local Government	Schemes for various roads (11 Kms.) in District Thatta.	59.298	Thatta	09/11/2014	Average	Yes	Already Completed
169	1520	Local Government	Construction of Link Road from Chotiaryoon City to Old Village Takya Pir Aijaz Ali Shah Road Mile 0/0-1/0(1.60 km) (To be funded out of 10% Royalty share)	14.643	Sanghar	23-09-2014	Un-satisfactory	Yes	Already Completed
170	1527	Local Government	Constt: of road from Nagori Kanta of Yousuf Goth to Rice Mills (1 Km)	13.968	Karachi	12/05/2014	Average	Yes	Already Completed
171	1529	Local Government	Constt: of road in District Mirpurkhas (8 Kms)	100	Mirpurkhas	09/05/2014	Average	Yes	Already Completed



172	1536	Local Government	Construction of Road from Waja Dad Muhammad Salar Goth via Goth Halo Salar Haji and Wali Dad Salar graveyard (5 Kms)	68.59	Karachi	22/07/2015	Average	Yes	Completed
173	1537	Local Government	Construction of Road from Super Highway Wad-E-Hussain to Nando village (5.40 Kms)	69.033	Karachi	22/07/2015	Average	Yes	Completed
174	1538	Local Government	Reconstruction of Gabol road Lyari, District South Karachi.	15	Karachi	20-5-2015	Average	Yes	Already Completed
175	1541	Local Government	Construction of CC Paver Road /Reconditioning of Road from various Streets of Khan Garh Mile 0/0-0/5 (1.00 km) (To be funded out of 10% Royalty share)	11.999	Ghotki	27/4/2015	Un-satisfactory	Yes	Work in progress
176	1542	Local Government	Construction of Road from Dargah Jam Lohar to Tomb Sharif City at Mile 0/0-1/3 Taluka T.B. Khan, District Jamshoro 0/0-1/3	20	Jamshoro	30-04-2015	Average	Yes	Already Completed
177	1544	Local Government	Improvement of internal Roads of Garden East Near Lasbella Karachi (3.5 Km)	40	Karachi		Average	Yes	Completed
178	1546	Local Government	Widening /Reconditioning of Road from National Highway Near Fast University to Faqeer Muhammad Goth and Jalbani Goth	32	Karachi		Average	Yes	Completed
179	1605	Local Government	Providing Solar Energy Lights for 09 (Rural) Union Councils of Taluka Khairpur	90	Khairpur	8 & 9/4/2015	Satisfactory	Yes	
180	1606	Local Government	Installation of Street Lights in various streets of Hindu Mohallah of Kashmore (Rs. 18.950 m. to be funded out of 10% Royalty Share)	20	Kashmore	30/4/2015	Satisfactory	Yes	If remaining Funds are released
181	1607	Local Government	Providing & Fixing Search / Street Lights and Generator for Shaheed Benazir Bhutto Cricket Ground Dadu. (To be funded out of 10% Royalty share)	20	Dadu	05/07/2015	Average	Yes	Completed
182	1611	Local Government	Construction/Addition of Class Rooms in Existing Primary Schools of Taluka Sakrand & Nawabshah (8 Units)	9.999	Shaheed Benazirabad	05/06/2015	Satisfactory	Yes	
183	1625	Local Government	Construction of Mother & Child Health Care Centre at Khairpur.	18.064	Khairpur		Average	Yes	would be completed
184	1650	Local Government	Rehabilitation of Civil Hospital, Khairpur	20	Khairpur	07/09/2015	Average	No	Revision of PC-I
185	1651	Local Government	Rehabilitation of Lady Willington Hospital, Khairpur	20	Khairpur		Average	No	Revision of PC-I
186	1654	Local Government	Reconstruction of Community Centre at Chaniser Goth, Karachi.	13.536	Karachi	07/10/2015	Satisfactory	Yes	Completed
187	1657	Local Government	Construction of Remaining Works of Eid Gah in Various Villages of Taluka Ratodero (12 Units)	30.5	Larkana	06/08/2015	Average	Yes	
188	1658	Local Government	Construction of Compound Wall to Graveyards in Various Villages of Taluka Ratodero (7 Nos)	16	Larkana	29/04/2015	Average	No	Would not be completed
189	1659	Local Government	Construction / Rehabilitation of Existing Mausoleums / Rehabilitation of Mosques and Remaining Works of Compound Wall of Imam Bargahs in Various Villages, Taluka Ratodero (9 Nos)	14.5	Larkana	18/5/2015	Satisfactory	Yes	
190	1662	Local Government	Construction of Eid Gah at Qazi Arif Town (To be funded out of 10% Royalty share)	15	Dadu	05/06/2015	Average	Yes	Completed

191	1664	Local Government	Renovation / Rehabilitation of Library, Press Club, Mosque, Police Headquarter, Massan, Gymkhana and ENT's gate damaged during rains 2012	11	Jacobabad	17/4/2015	Average	Yes	80% work was completed , remaining work was in progress .
192	1665	Local Government	Renovation / Rehabilitation of various Dargah damaged during rain 2012	9.5	Jacobabad	26/5/2015	Satisfactory	Yes	
193	1666	Local Government	Renovation / Rehabilitation of various Mosques and Madarasas damaged during rains 2012	5	Jacobabad	27/5/2015	Satisfactory	Yes	
194	1693	Local Government	Improvement & Extension of W/S Scheme Rajo Khanani (Revised).	54.109	Badin	06/01/2015	Average	Yes	Completed
195	1697	Local Government	Development schemes water connection from Mega Water Supply Project (40 Villages) District Mirpurkhas.	11.526	Mirpurkhas	07/06/2015	Average	Yes	Completed
196	1704	Local Government	Rural Water Supply Scheme for Village Nandhi Duburji Taluka Kot Ghulam Muhammad	10.784	Mirpurkhas	07/06/2015	Average	Yes	Completed
197	1708	Local Government	Rural W/S Scheme Saeed Pur Takkar. (To be funded out of 10% Royalty share)	18.556	Tando Mohd. Khan	07/06/2015	Average	No	Would not be Completed Approx.80% is work done. Certain civil components are yet to completed
198	1711	Local Government	Providing / Installation of R.O. Plants @ Village Manzoor Ali Khan Pitafi. (To be funded out of 10% Royalty share)	11.876	Tando Allahyar	09/04/2014	Average	Yes	Completed As stated by Mr. Abdul Nasir Soomro (AEN) Public Health. T.A.Yar
199	1714	Local Government	Water Supply Scheme Adam Hindu Goth, UC # 5 Songal	29.534	Karachi	07/07/2015	Satisfactory	Yes	Completed
200	1717	Local Government	Improvement & Extension of Water Supply Scheme Berani. (To be funded out of 10% Royalty share)	159.757	Sanghar	06/02/2015	Satisfactory	Yes	Completed
201	1729	Local Government	Water Supply Scheme for Village Kharoro Syed and Village Kharoro Charan	34.83	Umerkot	07/07/2015	Average	No	Would not be completed as stated by Mr.Waseem (Budget Officer) PHED Amount surrendered due to social conflict between local influentials
202	1735	Local Government	Constt. Of H.S.R at Sani Nenu Ram Ashram Islam Kot District Tharparkar.	15.714	Tharparkar	07/07/2015	Average	Yes	Completed As per list provided by the E/A
203	1741	Local Government	Improvement & Extension of Water Supply Scheme Kamber Ali Khan.	406.756	Qambar Shahdadkot	16/7/2015	Satisfactory	No	Still 5.0M are not released and awaited for power connection.
204	1743	Local Government	Water Supply Scheme for Miro Khan Town	49.53	Qambar Shahdadkot	06/10/2015	Average	No	Incomplete Civil Works, Laying of distribution lines and power connection.

205	1745	Local Government	Water Supply Scheme of Arab Khan Katohar & adjoining village.	16.81	Khairpur	06/08/2015	Average	Yes	Power connection awaited
206	1746	Local Government	Water Supply Scheme of Allah Bux Katohar.	18.79	Khairpur	06/08/2015	Average	Yes	Power connection awaited
207	1747	Local Government	Water Supply Scheme of Tando Masti.	12.6	Khairpur	01/07/2015	Average	Yes	Would be completed
208	1840	Local Government	Constt: of CC Block and CC Drains at various villages (3 Nos) District Hyderabad.	12	Hyderabad	19-5-2015	Satisfactory	Yes	Already Completed
209	1845	Local Government	Drainage Scheme for Village Kot Mirs Landhi UC Imam Bux, Taluka Kot Ghulam Muhammad.	10.557	Mirpurkhas	07/06/2015	Average	Yes	Completed
210	1846	Local Government	Rural Drg: Scheme Yousuf Goth Gadap Town at New Karachi Sarjani Chowrangi.	113.605	Karachi	07/07/2015	Average	No	Would not be Completed Due to heavy encroachment of land
211	1848	Local Government	Rural Drg: Scheme Khamiso Goth New Karachi Town.	121.415	Karachi		Average	Yes	Completed As per list provided by the E/A
212	1849	Local Government	Murad Memon Goth Drainage Scheme.	197.29	Karachi		Average	Yes	Completed As per list provided by the E/A
213	1857	Local Government	Rural Drainage Scheme Shahpur Rizvi	34.049	Tando Allahyar		Average	No	Would not be Completed As stated by Mr. Abdul Nasir Soomro (AEN) Public Health. T.A.Ya, Rs.10.00 Million are yet to be released
214	1865	Local Government	Improvement and extension of Urban Drainage Scheme Khadro. (Revised)	67.727	Sanghar	06/02/2015	Average	Yes	Completed
215	1868	Local Government	Drainage Scheme for Chhuch Jahan Khan.	20.76	Thatta		Average	Yes	Completed As per list provided by the E/A
216	1873	Local Government	C.C. Flooring & Drainage Scheme for Village Munger Khan Palijo and Muhammad Hassan Palijo District Thatta.	20.54	Thatta		Average	No	Would not be completed as stated by Mr. Waseem (Budget Officer) PHED Approx. Rs.10 Million are yet to be released
217	1880	Local Government	Drainage Scheme CC Block & Drains for Shahdad Kot City	13.834	Qambar Shahdadkot		Average	No	Some minor funds to be released
218	1887	Local Government	Drainage Scheme Syed Amir Ali Shah	11.581	Khairpur	23/12/2014	Satisfactory	Yes	Would be completed
219	1901	Local Government	Improvement & Extension of Drainage System in Sachal Colony Larkana City.	20.7	Larkana	29/04/2015	Average	Yes	Completed
220	1902	Local Government	Construction of C.C. Drains, C.C. Block and Paver Block in UC-8,9,10 and 11 of Larkana City.	24.92	Larkana	06/11/2015	Average	Yes	

221	1905	Local Government	Improvement & Extension of Urban Drg: Scheme Mehrabpur Taluka Mehrabpur	153.243	Naushero Feroz	13/02/2015	Average	No	Would not be completed
222	1914	Local Government	Drg: Sch: Village Shadi Khan Chandio Deh 23 Satpuri UC Dalel Dero Taluka Sakrand	7.296	Shaheed Benazirabad	05/08/2015	Satisfactory	Yes	
223	1923	Local Government	Rehabilitation of Drainage of Village Gharhi Hassan.	23.97	Jacobabad	17/6/2015	Satisfactory	Yes	
224	1925	Local Government	Improvement / Reconditioning of Road from Arif Builders Office to Malik Chowk Bachal Shah (Mile 0/0-1/2.0K.M) i/c Pumping Machinery and Rising Main.	21.282	Sukkur	13/3/2015	Average	Yes	
225	1926	Local Government	CC Blocks at Asif Colony Bachal Shah Miani.	17.43	Sukkur	18/02/2015	Average	Yes	Would be completed
226	1676	Local Government	Construction of Link road to villages of 500 population in Hyderabad Division (Matari, T.M. Khan, T. Allahyar, Badin, Dadu, Jamshoro & Thatta)	645.02	Hyderabad, Matari, Tando Mohd. Khan, Tando Allahyar, Badin, Dadu, Jamshoro, Thatta	06/03/2015	Average	No	Would not be completed Due to shortage of funds.
227	1680	Local Government	Construction of C.C. Road & Drainage System in Streets of (I) Samaro City & (II) Soofi Fageer District Umerkot	20	Umerkot	05/11/2015	Average	Yes	Already Completed
228	1687	Local Government	Mobile Drinking Water Testing & Safety Measuring Advisory Project (Jacobabad, Shikarpur, Larkana, Sukkur, Khairpur, SBA, Dadu, Jamshoro, Sanghar, Mirpurkhas, Thar, Thatta, N'Feroze, Ghotki, Kashmore, Kamber)	58.75	Jacobabad	16/6/2015	Average	Yes	Vehicles were purchased but no other data was provided by the P.D
	1687	Local Government	Mobile Drinking Water Testing & Safety Measuring Advisory Project (Jacobabad, Shikarpur, Larkana, Sukkur, Khairpur, SBA, Dadu, Jamshoro, Sanghar, Mirpurkhas, Thar, Thatta, N'Feroze, Ghotki, Kashmore, Kamber)	58.75	Sukkur	04/08/2015	Average	yes	Vehicles were purchased but no other data was provided by the P.D
	1687	Local Government	Mobile Drinking Water Testing & Safety Measuring Advisory Project (Jacobabad, Shikarpur, Larkana, Sukkur, Khairpur, SBA, Dadu, Jamshoro, Sanghar, Mirpurkhas, Thar, Thatta, N'Feroze, Ghotki, Kashmore, Kamber)	58.75	N. Feroze	22/4/2015	Average	yes	Vehicles were purchased but no other data was provided by the P.D
	1687	Local Government	Mobile Drinking Water Testing & Safety Measuring Advisory Project (Jacobabad, Shikarpur, Larkana, Sukkur, Khairpur, SBA, Dadu, Jamshoro, Sanghar, Mirpurkhas, Thar, Thatta, N'Feroze, Ghotki, Kashmore, Kamber)	58.75	Shikarpur	27/4/2015	Average	yes	Vehicles were purchased but no other data was provided by the P.D
	1687	Local Government	Mobile Drinking Water Testing & Safety Measuring Advisory Project (Jacobabad, Shikarpur, Larkana, Sukkur, Khairpur, SBA, Dadu, Jamshoro, Sanghar, Mirpurkhas, Thar, Thatta, N'Feroze, Ghotki, Kashmore, Kamber)	58.75	MTOD	01/06/2015	Satisfactory	yes	Already Completed
229	1690	Local Government	Constt: of C.C. drain i/c block & paver tiles in various units of UC-8, 9, 10, 16 & 19 Larkana City	40	Larkana	06/08/2015	Satisfactory	Yes	Would be Completed

230	1345	Local Government	Phase -I Drainage sytem componenets of 25 years Master Plan for Qasimabad Hyderabad (To be funded out of 10% Royalty share)	386.73	Hyderabad-Package	27-5-2013	Average	Yes	Already Completed
231	1347	Local Government	Construction of Storm water drain on both sides of Qasimabad main road from Alamdar Chowk to Sehrish Nagar, City School at Qasimabad Hyderabad. (To be funded out of 10% Royalty share)	81.01	Hyderabad-Package	27-5-2014	Un-satisfactory	Yes	Already Completed
232	1352	Local Government	Construction / Missing facilities of Education Building, Establishment of Shaheed Zulfiqar Ali Bhutto Memorial Library and Revenue Component of Sports complex Nawabshah.	265.477	Shaheed Benazirabad-Package	16/6/2015	Satisfactory	No	Funding Issue
233	1355	Local Government	Providing Water Supply & Drainage schemes at various places of District SBA.	80.687	Shaheed Benazirabad-Package	06/12/2015	Average	Yes	Power connection awaited
234	1358	Local Government	Construction/ Reconstruction & Rehabilitation of Integrated Elementry / Secondary Schools of District Shaheed Benazirabad	115.485	Shaheed Benazirabad-Package	05/07/2015	Satisfactory	Yes	
235	1362	Local Government	Renovation / Implementation and provision of additional facilities at existing Rural Health centre Garhi Khuda Bux Bhutto, Taluka Ratodero.	98.051	Larkana-Package	06/11/2015	Average	Yes	Already Completed
236	1365	Local Government	Integrated rehabilitation and provision of missing facilities to existing Secondary and Higher Secondary schools, District Larkana (15 units)	199.918	Larkana-Package	14/5/2015	Satisfactory	Yes	
237	1378	Local Government	Renovation & Improvement of Existing Playground i.e. Moulana Muhammad Ali Johar Park / Kakri Ground Lyari PC-I.	71.162	Karachi-Package	20-5-2015	Average	Yes	Already Completed
238	1379	Local Government	Repair, Renovatio & Rehabilitation of existing Primary / Secondary Schools of Lyari (Phase-II) (41 Units)	314.949	Karachi-Package	20-5-2015	Satisfactory	Yes	Completed
239	1382	Local Government	Rehabilitation / Improvement of internal streets by CC flooring in UC-1 to UC-5 Lyari Town	49.155	Karachi-Package	20-5-2015	Average	Yes	Already Completed
240	1386	Local Government	Improvement of street lights system on different roads/streets of DMC (South) Lyari Zone.	24.499	Karachi-Package	20-5-2015	Average	Yes	Already Completed
241	1387	Local Government	2-Lane, 2Way Flyover of water Pump Shahrah-e-Pakistan	493.95	Karachi-Package	01/01/2013	Satisfactory	Yes	Already Completed
242	1388	Local Government	2-Lane, 2Way Flyover at Aisha Manzil Shahrah-e-Pakistan	493.95	Karachi-Package	01/01/2013	Satisfactory	Yes	Already Completed
243	1391	Local Government	Construction of 3 Lane Flyover at Malir Halt at Shahrah -e-Faisal Karachi	386	Karachi-Package	09/10/2014	Satisfactory	No	Would not be completed
244	1399	Local Government	Construction,/ Renovation & Beautification of Mehran Markaz Building Sukkur	15	Sukkur-Package	23/6/2015	Average	Yes	Work was not executed as per PC-I, lot of Deviation from PC-I, Scope
245	1402	Local Government	Installation of Solar Lights @ various parts of Sukkur (Sukkur, Pano Akil, Salehpat, Rohri).	45	Sukkur-Package	23/6/2015	Average	No	Scope of Work as PC-I not completed, Revision was proposed but no any revision proposal submitted in P&D
246	1403	Local Government	Purchase of Buses/Coaches/Air Conditions For GMC Medical College Sukkur	20	Sukkur-Package	06/04/2015	Satisfactory	No	1 buses were purchased out of 3. 2 buses yet to

									be purchased while tenders are invited
247	1412	Local Government	Karachi South Package	400	Karachi-Package	22/07/2015	Average	Yes	Completed
248	1413	Local Government	Karachi West Package	400	Karachi-Package	29/07/2015	Average	Yes	Completed
249	1415	Local Government	Karachi Central Package	100	Karachi-Package	29/07/2015	Average	Yes	Completed
250	1320	Livestock & Fisheries Department	Strengthening of Research & Training Institute for Livestock Dev. @ Tando Muhammad Khan	59.189	Tando Mohd. Khan	28-5-2015	Un-satisfactory	Yes	Completed
251	1322	Livestock & Fisheries Department	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic Diseases in Sindh. (Hyd, T. Allahyar, Tharparkar, Dadu, Sukkur, Larkana, N.Feroze & Karachi)	59.926	Larkana	06/08/2015	Satisfactory	Yes	Would be Completed
	1322	Livestock & Fisheries Department	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic Diseases in Sindh. (Hyd, T. Allahyar, Tharparkar, Dadu, Sukkur, Larkana, N.Feroze & Karachi)	59.926	N. Feroze	19/06/2015	Average	yes	Would be Completed
	1322	Livestock & Fisheries Department	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic Diseases in Sindh. (Hyd, T. Allahyar, Tharparkar, Dadu, Sukkur, Larkana, N.Feroze & Karachi)	59.926	Sukkur	16/4/2015	Satisfactory	yes	Completed
	1322	Livestock & Fisheries Department	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic Diseases in Sindh. (Hyd, T. Allahyar, Tharparkar, Dadu, Sukkur, Larkana, N.Feroze & Karachi)	59.926	MTOD	29-5-2015	Satisfactory	yes	Completed
252	1333	Livestock & Fisheries Department	Constt: of veterinary centre @ village Muqem Khuda Bux Dahri, Taluka Qazi Ahmed, District Shaheed Benazir Abad.	6	Shaheed Benazirabad	13/4/2015	Un-satisfactory	No	No tenders issued by the E/A despite releases in September, 2014 hence no work started at site. The completion period of the scheme was June, 2015.
253	1339	Livestock & Fisheries Department	Introduction of Culture of High value Brackish Water fish in Sindh	48.096	Badin	11-09-2014 24-09-2014 5/5/2015	Un-satisfactory	No	Would not be completed Due to non hiring of Consultant
	1339	Livestock & Fisheries Department	Introduction of Culture of High value Brackish Water fish in Sindh	48.096	Thatta	11-09-2014 24-09-2014 5/5/2015	Un-satisfactory	No	Would not be completed Due to non hiring of Consultant
254	2016	Minorities Affairs Department	Construction of Bhamdara Hall and rooms of SHANKAR Anand Temple and Renovation / Remaining Works of SAMADA ASHRAM Temple, Shikarpur	29.777	Shikarpur	15/5/2015	Satisfactory	Yes	

255	2027	Planning And Development Department	Expansion of Union Council Based Poverty Reduction Programme	2009.52	Jacobabad, Tharparkar	09/06/2013	Satisfactory	Yes	Already Completed
256	2036	Planning And Development Department	Survey, Documentation and Scientific Studies of plant remedies used for the treatment of infectious skin diseases in Sindh.	23.604	Sindh		Average	Yes	Completed
257	2041	Population Welfare Department	Population Welfare Program Sindh (2010-15)	4548	Sindh		Un-satisfactory	Yes	Completed
258	2049	Rehabilitation Department	Provision of external works for the Turkish Housing for flood affected people of Thatta District	228.607	Thatta	18-05-2015	Average	Yes	Completed
259	2062	Sga&Cd	Renovation & Rehabilitation of Block No.A, AA & AB Jacoblines Flats of staff of Commissioner Karachi	70.94	Karachi		Average	No	As per ADP 2015-16; this is ongoing scheme and expected to be completed in June 2016. As stated by concerned Mr. Asadullah Shaikh (XEN) Provincial Buildings.
260	2096	Sga&Cd	Implementation of Capacity Building	60	Karachi		Average	Yes	Completed
261	2104	Sindh Board Of Investment	Revival of Sick Industrial Units Phase-II (All Districts)	2000	Benazirabad	15/6/2015	Worst	In Process	Administrative Department did not respond. A reminder was also issued to the Chairman SBI. It is requested to take the matter at higher level
	2104	Sindh Board Of Investment	Revival of Sick Industrial Units Phase-II (All Districts)	2000	Sukkur	06/04/2015	Not Applicable	In Process	Administrative Department did not respond. A reminder was also issued to the Chairman SBI. It is requested to take the matter at higher level
	2104	Sindh Board Of Investment	Revival of Sick Industrial Units Phase-II (All Districts)	2000	Sindh	05/12/2015	Un-satisfactory	yes	Completed
262	2107	Social Welfare Department	Economic Empowerment Support to Urban / Rural Orphan Girls, Women & Handicapped Through Out Sindh	83.648	N. Feroze	18/06/2015	Average	Yes	
	2107	Social Welfare Department	Economic Empowerment Support to Urban / Rural Orphan Girls, Women & Handicapped Through Out Sindh	83.648	Benazirabad	06/12/2015	Average	yes	

	2107	Social Welfare Department	Economic Empowerment Support to Urban / Rural Orphan Girls, Women & Handicapped Through Out Sindh	83.648	Khairpur	17/6/2015	Un-satisfactory	yes	completed as reported but the machines were not physically verified due to non cooperation of officers of social welfare dept. Khairpur
	2107	Social Welfare Department	Economic Empowerment Support to Urban / Rural Orphan Girls, Women & Handicapped Through Out Sindh	83.648	Sindh	27-5-2015	Average	yes	Completed
263	2117	Special Initiatives Department	Establishment of Drinking Water Hubs (Phase-I) for 500 Units (2nd Revision on 03.01.13)	3017.056	Sindh		Average	Yes	Completed
264	2132	Sports & Youth Affairs Department	Construction of Pavilion and Seating facilities for Football Stadium at Baldia and Boxing Facilities at Lyari	159.337	Karachi	18-03-2015	Average	Yes	Completed
265	2135	Sports & Youth Affairs Department	Construction of Sports Pavilion at Dokri, Ratedero and Municipal Stadium Larkana.	126.9	Larkana	06/11/2015	Average	No	Ratodero 90% Completed, Larkana 80% Completed, Dokri 50% to 60% Completed. Revision of Scheme Proposed but revision not submitted in P&D
266	2136	Sports & Youth Affairs Department	Construction of Sindh Sports Complex Nazimabad.	49.998	Karachi		Average	Yes	Already Completed
267	2137	Sports & Youth Affairs Department	Development of Ground at (i) Union Football grassy ground, (ii) Mohammadan Football Ground Sector-11, Orangi Town, (iii) Foot ball Stadium F.B area, Rashid Minhas Road, (iv)Korangi No.6, Near Govt: Girls College with Seating Capacity.	47.504	Karachi	29-5-2014	Average	Yes	Already Completed
268	2138	Sports & Youth Affairs Department	Construction of Sports Stadium at Shahdadpur	59.221	Sanghar	20-5-2015	Average	Yes	Completed
269	2139	Sports & Youth Affairs Department	Construction of Ground at (i) Women Football and Hockey Grounds at Block-I, North Nazimabad, (ii) Raees Mamoon Khan Malkani Cricket Ground Taluka Jati (iii) Cricket Ground grassy and pavilion dressing room Liaquat Medical University Jamshoro (iv) Foot ball ground at Shah Wali Ullah Colony, Sector11 1/2, Orangi Town, Karachi (v) Foot ball ground Bilal Nagar, UC Dhabeji, Thatta.	54.505	Jamshoro,Karachi,Thatta	21-5-2015	Average	No	Would not be completed Would not be completed
270	2141	Sports & Youth Affairs Department	Contruction of Benazir Shaheed Bhutto Sports Stadium at Cadet College Sanghar & Larkana.	89.388	Larkana,Sanghar	20-5-2015	Average	No	Would not be completed Due to delay in release of funds



	2141	Sports & Youth Affairs Department	Construction of Benazir Shaheed Bhutto Sports Stadium at Cadet College Sanghar & Larkana.	89.388	Larkana, Sanghar	18/5/2015	Satisfactory	yes	Completed
271	2142	Sports & Youth Affairs Department	Construction of Table Tennis Complex at Block F North Nazimabad.	27.965	Karachi	29-5-2014	Average	Yes	Completed
272	2148	Sports & Youth Affairs Department	Construction of Gama Sports Stadium at Mirpurkhas (Revised)	59.973	Mirpurkhas	20-10-2014	Average	Yes	80% Progress Achieved Completed
273	2162	Sports & Youth Affairs Department	Construction of Shaheed Zulfiqar Ali Bhutto Sports Complex at Mirpurkhas	36.138	Mirpurkhas	07/01/2015	Average	Yes	Completed
274	2182	Sports & Youth Affairs Department	Establishment of Youth Hostel for Girls Karachi.	23.322	Karachi	21-5-2015	Average	No	Would not be completed Due to slow funding
275	2215	Women Development Department	Establishment of Sales & Display Resource Centre at Karachi.	35.541	Karachi	13-11-2014	Un-satisfactory	Yes	Completed
276	2216	Women Development Department	Establishment of Day Care Centre at Karachi.	37.754	Karachi	09/10/2014	Average	Yes	Already Completed
277	2217	Women Development Department	Establishment of Women Complaint Cells in Sindh for Aid to Women in Distress.	69.529	Hyderabad, Karachi, Larkana, Shaheed Benazirabad, Sukkur		Un-satisfactory	Yes	Completed
278	2923	Work & Services	Reconstruction / Rehabilitation of 2010 Flood affected roads in Lower Sindh & Upper Sindh areas (Jacobabad, Kashmore, Shikarpur, Kamber, Dadu, Jamshoro & Thatta)	1256.9	Jacobabad	11/5/2015 to 14/5/2015	Average	Yes	physically & financially completed, some quality issues observed
	2923	Work & Services	Reconstruction / Rehabilitation of 2010 Flood affected roads in Lower Sindh & Upper Sindh areas (Jacobabad, Kashmore, Shikarpur, Kamber, Dadu, Jamshoro & Thatta)	1256.9	Kashmore	11/5/2015 to 14/5/2015	Average	yes	physically & financially completed, some quality issues observed
	2923	Work & Services	Reconstruction / Rehabilitation of 2010 Flood affected roads in Lower Sindh & Upper Sindh areas (Jacobabad, Kashmore, Shikarpur, Kamber, Dadu, Jamshoro & Thatta)	1256.9	shikarpur	11/5/2015 to 14/5/2015	Average	yes	physically & financially completed, some quality issues observed
	2923	Work & Services	Reconstruction / Rehabilitation of 2010 Flood affected roads in Lower Sindh & Upper Sindh areas (Jacobabad, Kashmore, Shikarpur, Kamber, Dadu, Jamshoro & Thatta)	1256.9	Kamber	11/5/2015 to 14/5/2015	Average	yes	physically & financially completed, some quality issues observed
279	2233	Work & Services	Block Scheme for Construction of Rural Access Road in Lower Sindh 260 Kms. (Matiari, T.A.Yar, TM Khan, Dadu, Jamshoro, Badin, Thatta, M.Khas, Tharparkar, U.Kot, Sanghar & S.B.A.)	1462.22	Matiari, Tando Allahyar, Tando Mohd. Khan, Dadu, Jamshoro,		Average	Yes	Completed

					Badin, Thatta, Mirpurkhas, Tharparkar, Umerkot, Sanghar, Shaheed Benazirabad				
280	2242	Work & Services	Scheme proposed by the MPA's of District Sanghar.	85.483	Sanghar	16-04-2015	Average	Yes	Already Completed
281	2248	Work & Services	W/R of Road from Bhiria Padidan Road to Mahram Khan Nagore via Samolabad Road mile 0/0-4/0.	58.041	Naushero Feroz	19/6/2015	Average	Yes	Would be Completed
282	2264	Work & Services	Widening & Construction of road from Chota Gate to Abdul Karim Gabol and village Faiz Muhammad Gabol via Haji Ali Bux Gabol village mile 0/0-3/6 (6.00 Kms)	46.907	Karachi	18-08-2014	Average	Yes	Already Completed
283	2278	Work & Services	W/R of road from Lakhi Shikarpur road to Shikarpur Larkana road (Shikarpur Bye Pass) mile 0/0-6/0 (Asphalt concrete) (9.66 Kms)	93.755	Shikarpur	13/4/2015 & 14/4/2015	Average	Yes	Completed
284	2290	Work & Services	Improvement Tando Adam Berani Kundiari with asphalt surface Mile 0/0-26/4 = 26-4 = 42.66 Kms..	421.403	Sanghar	28-5-2015	Average	Yes	Already Completed
285	2297	Work & Services	W/R of Road from Shikarpur to Jaggan mile 0/0-14/4 (23.33 Kms)	123.734	Shikarpur		Un-satisfactory	Yes	Would be Completed
286	2311	Work & Services	W/R of road from Nawabshah Airport Road to Khadhar via Mian Shore road mile 0/0-8/1 (13.0 Kms)	222.22	Shaheed Benazirabad	16/6/2015	Average	Yes	Would be Completed
287	2318	Work & Services	Improvement of road from Mirpurkhas - Sindhri road to Khan road via Lal Chand Bungalow mile 0/0-8/0 (12.88 Kms)	80.295	Mirpurkhas	09/12/2014	Average	Yes	Already Completed
288	2325	Work & Services	Improvement / Construction of Ghotki Khanpur Road to village Abdul Sattar via village changlani & Ahmed Raj Wah mile 0/0-2/4 (4.0 kms)	31.803	Ghotki	29/6/2015	Average	Yes	
289	2326	Work & Services	Improvement of road from Sindh Jamat Cooperative Housing Society Qaidabad and Charan Para over head Tank Meena Mosque, Ibrahim Hydery (5Kms) mile 0/0-3/1.	48.689	Karachi	06/05/2015	Satisfactory	Yes	Completed
290	2339	Work & Services	Improvement of road from Talhar Bye Pass (Hyderabad road to Tando Bago road) road mile 0/0-3/6 (6.03 Kms).	42.727	Badin	11/11/2014	Un-satisfactory	Yes	Already Completed
291	2350	Work & Services	Reconditioning of road from Old National Highway @ 216 to Sangrah Mori via Raja CNG road mile 0/0-3/1 (5.0 Kms)	83.967	Shaheed Benazirabad	23/7/2015	Average	Yes	Would be completed
292	2352	Work & Services	Re-construction of Shahdadpur Gupchani Road mile 0/0-1/1 (1.80 Kms) (Shahdadpur town Portion)	26.533	Sanghar	26-5-2015	Average	Yes	Already Completed
293	2391	Work & Services	Improvement / Construction of Road from New Bus Terminal to village Bilawal Khoso mile 0/0-1/0 (1.609 Km) (i/c C.C Block).	15.705	Sukkur	04/06/2015	Average	Yes	
294	2396	Work & Services	Reconditioning of road from Jhalo road to Dargah Malkani Sharif road mile 0/0-1/4 (2.4 Km) UC Siyal. (To be funded out of 10% Royalty share)	16.277	Dadu	15-05-2015	Average	Yes	Already Completed
295	2399	Work & Services	Widening and Improvement of road from Kambar City to village Ber Sharif (6 Kms)	76	Qambar Shahdadkot	20/05/2015	Un-satisfactory	No	

296	2405	Work & Services	Reconditioning of road from Sakrand Mehrabpur to Mari Jalbani Dad Wahi Road Mile 0/0-2/4(4 km)	22.889	Shaheed Benazirabad	24/7/2015	Average	Yes	Would be completed
297	2410	Work & Services	Improvement of Larkana Circular of Road mile 0/0-10/0 (16.09 Kms)	307.65	Larkana	15/05/2015	Satisfactory	Yes	Completed
298	2411	Work & Services	Widening / Reconditioning of Road from Larkana Koreja via Saidudero Pitafi Road mile 0/0-4/2 (6.83 Kms).	146.256	Larkana	15/07/2015	Un-satisfactory	Yes	May be completed by 20th July
299	2545	Work & Services	Construction of road from Muhammad Hassan Keerio village Deh Lakha road mile 0/0-5/5.	51.71	Sanghar	13/01/215	Average	Yes	Completed
300	2560	Work & Services	Constructio of road from Sarwar Pir road to Ghoram Nohani Goth Taluka Golarchi mile 0/0-1/7 (3.00 Kms)	19.391	Badin	13-02-2014	Average	Yes	Already Completed
301	2564	Work & Services	Constructrion of road from Jeewan Khan Pitafi road to Maikhana Khirohi mile 0/0-3/1 (5.00 Kms) (To be funded out of 10% Royalty share)	39.485	Ghotki	29/6/2015	Average	Yes	Already Completed
302	2565	Work & Services	Construction of road from G.T road to Reharki Sahib, Poojwadyoon Deweryoon, Sahib and S.S.D Dham Raheerki Sahib (5.00 Kms).	40.931	Ghotki	30/6/2015	Un-satisfactory	Yes	Already Completed
303	2582	Work & Services	Construction / Widening / Reconditioning & Resurfacing of Umerkot Bye Pass road mile 0/0-16/6 = 16-6 (M) = 26.96 Kms..	134.432	Umerkot	24-03-2015	Average	Yes	Already Completed
304	2597	Work & Services	Construction of road from Jhangara Naing road to Dargah Shaikh Dhaman mile 0/0-1/7 (3.0 Kms).	47.29	Jamshoro	28-10-2014	Average	Yes	Already Completed
305	2611	Work & Services	Land Acquisition for construction of Dualization Tando Allahyar Bye-Pass road (Northern Side) road mile 0/0-3/7(6.20 km).	120.825	Tando Allahyar	19-5-2014	Average	No	Would not be completed Due to dispute of Land Acquisition
306	2614	Work & Services	Construction / Improvement of road from Mirpurkhas Umerkot road to Mirpurkhas Sanghar road (Bye pass road with asphalt concrete mile 0/0-1/7 (3 Kms).	86.8	Mirpurkhas	26-12-2014	Average	Yes	Already Completed
307	2635	Work & Services	Construction of road from Super Highway to Farsi Garden mile 0/0-1/7 (3.00 Kms)	40.05	Karachi	12/04/2014	Un-satisfactory	Yes	Completed
308	2658	Work & Services	Construction of matted road, from Diggu Farm to Aarab Rind Village (2 Kms).	21.084	Umerkot	06/01/2015	Average	Yes	Already Completed
309	2671	Work & Services	Construction of Road from Garhi Khuda Bux Bhutto Bypass	50.902	Larkana	20/05/2015	Average	Yes	
310	2704	Work & Services	Construction of Road from Thikratho Salehpat to Road to Moharam Ali Village Mile 0/0-0/7 (1.40 Km)	12.51	Sukkur	06/04/2015	Average	Yes	Already Completed
311	2811	Work & Services	Construction of Road from Goni to village Chutto Faqir (1.61 Kms)	15.144	Sukkur	04/07/2015	Un-satisfactory	Yes	
312	2812	Work & Services	Construction of Road from Primary School Kanderi to Ruhai Faqir mile 0/0-1/0 (1.60 Km)	14.854	Sukkur		Average	Yes	Scheme Physically Completed at Last visit on 5/12/2014 as reported by concerned MEO
313	2813	Work & Services	Construction of road in village Photo Khan Zardari	37.416	Naushero Feroz	28/7/2015	Not Visited	No	No Single activity executed as scheme

									<p>duplicated with ADP # 2604(2014-15) therefore no allocation were given.</p>
314	2839	Work & Services	Construction of road from Punjodero to Garhi Khuda Bux Bhutto	55	Larkana	07/10/2015	Average	Yes	Would be completed
315	2874	Work & Services	Construction of Bridge Tando Jan Muhammad Dehi Road oer Naseer Canal at Mile 5/4	6.02	Mirpurkhas		Not Started	No	Would not be completed Amount surrendered due to non closure period of water at Naseer Canal.
316	2877	Work & Services	Construction/Improvement of 4.5 Km Road of Awan Road Sukkur City Mile 0/0-2/7 (4.26 Km)	85.26	Sukkur	07/09/2015	Un-satisfactory	Yes	Completed
317	2890	Work & Services	Construction of Bridges in various District of Province (Badin, Thatta, Malir, Tharparkar, Sanghar, Khairpur & Sukkur)	331.95	Badin, Thatta, Karachi, Tharparkar, Sanghar, Khairpur, Sukkur	14/7/2015	Average	No	Total three number of bridges to be constructed under the Umbrella of block scheme out of which two bridges (One bridge RD 99 Saleh Put and other at Thari Mir Wah Over Mir Wah Canal) found completed where as bridge over nara canal at RD-522 near Gulab Chang village remain under progress. where pile work executed.
	2890	Work & Services	Construction of Bridges in various District of Province (Badin, Thatta, Malir, Tharparkar, Sanghar, Khairpur & Sukkur)	331.95	Sindh	20/10/2014	Average	yes	Completed
318	2920	Work & Services	Construction of road from Chachro to Khinsar mile 0/0-25/0 (40 Kms)	547.781	Tharparkar	06/02/2015	Satisfactory	Yes	Already Completed

## Annexure B – Monitored Schemes

Department wise schemes monitored from 01-July-2014 to 30-June-2015 are as follows:

S.#	Department	ADP#	Name of Project	Visit Date	Status
1.	Agriculture, GOS	1	Development and promotion of quality seed through public private partnership in Sindh (Larkana)	24-10-2014	Average
2.	Agriculture, GOS	1	Development and Promotion of Quality Seed through Public Private partnership in Sindh (Q.Skot)	30-10-2014	Average
3.	Agriculture, GOS	1	Development and Promotion of quality seed through public private partnership in Sindh.	19-08-2014	Un-Satisfactory
4.	Agriculture, GOS	1	Development and promotion of quality seed through public private partnership in Sindh(Shikarpur)	13-10-2014	Average
5.	Agriculture, GOS	2	Introduction of Aerobic Rice Cultivation technology in Sindh.	28-05-2015	Satisfactory
6.	Agriculture, GOS	4	Rehabilitation of Rice and Cotton Research Station, Thatta	24-03-2015	Un-Satisfactory
7.	Agriculture, GOS	6	Standardization of sugar testing & variety development laboratory for sugar crops.	11-08-2014	Satisfactory
8.	Agriculture, GOS	10	Horticulture Training project for increasing earning capability of subsistence farmers(Revised) Khairpur	16-09-2014	Satisfactory
9.	Agriculture, GOS	12	Adoption of Farmers Field School Approach in Agriculture Extension for Dissemination Agriculture Technology Among the Farming Communities(Khairpur)	10-03-2015	Satisfactory
10.	Agriculture, GOS	12	Adoption of farmers field school approach in agriculture extension for dissemination of agriculture technology among the farming community.	29-04-2015	Average
11.	Agriculture, GOS	14	Establishment of Agro -Export Processing Zone for Fruits, Vegetables, Flowers, Allied Processing Products from Local Farms/ Processing Units to Overseas Markets ( Nausheroferoze),	08-07-2014	Un-Satisfactory
12.	Agriculture, GOS	14	Establishment of Agro -Export Processing Zone for Fruits, Vegetables, Flowers, Allied Processing Products from Local Farms/ Processing Units to Overseas Markets ( SBA,)	19-08-2014	Un-Satisfactory
13.	Agriculture, GOS	16	Construction of Training Resource Center and Repair of Existing Facilities at ATI, Sakrand(REVENUE COMPONENT)	18-08-2014	Un-Satisfactory
14.	Agriculture, GOS	22	Subsidy Assistance on Agriculture Implements for Farm Mechanization (Project Cost Rs. 794.42 million with GOS share Rs.400.0 million, Farmer's shares Rs. 394.420 million).Khairpur	12-08-2014	Satisfactory
15.	Agriculture, GOS	22	Subsidy Assistance on Agriculture Implements for Farm Mechanization (Project Cost Rs. 794.42 million with GOS share Rs.400.0 million, Farmer's shares Rs. 394.420 million).Sukkur	12-09-2014	Satisfactory
16.	Agriculture, GOS	22	Subsidy Assistance on Agriculture Implements for Farm Mechanization (Project Cost Rs. 794.42 million with GOS share Rs.400.0 million, Farmer's shares Rs. 394.420 million).Jacobabad	22-09-2014	Satisfactory
17.	Agriculture, GOS	22	Subsidy Assistance On Agriculture Implements For Farm Mechanisation(SBA)	20-10-2014	Satisfactory
18.	Agriculture, GOS	22	Subsidy assistance on Agriculture implements for farm mechanization (Larkana)	23-10-2014	Satisfactory
19.	Agriculture, GOS	22	Subsidy assistance on Agriculture implements for farm mechanization (Ghotki)	27-10-2014	Satisfactory
20.	Agriculture, GOS	22	Subsidy assistance on Agriculture implements for farm mechanization (N.Feroze)	29-10-2014	Un-Satisfactory

21.	Agriculture, GOS	22	Subsidy assistance on Agriculture implements for farm mechanization (Shikarpur)	11-10-2014	Satisfactory
22.	Agriculture, GOS	22	Subsidy Assistance on Agriculture Implements for farm mechanisation (QSKOT)	17-11-2014	Satisfactory
23.	Agriculture, GOS	22	Subsidy Assistance on Agriculture Implements for Farm Mechanization (Project Cost Rs. 794.42 million with GOS share Rs.400.0 million, Farmer's shares Rs. 394.420 million).	26-04-2015	Satisfactory
24.	Agriculture, GOS	23	Provision of Assistance to farmers on purchases of 11000 Nos. wheel type tractors. (Phase-III)	24-06-2015	Satisfactory
25.	Agriculture, GOS	23	Construction of Khajoor Mandi @ Khairpur	16-01-2014	Un-Satisfactory
26.	Agriculture, GOS	25	Modernization of training and research facility in Agri. Engineering through establishment of Agri. engineering training institute at Nareja	14-10-2014	Un-Satisfactory
27.	Agriculture, GOS	26	Replacement of earth moving machinery in Sindh (Phase-II).	17-12-2013	Satisfactory
28.	Agriculture, GOS	27	Subsidy Assistance on Agriculture Implements for Farmer Mechanization.	11-06-2014	Satisfactory
29.	Agriculture, GOS	27	Sindh On Farm Water Management Project (OFWMP) Comprhensive Project Cost. 3966.472 (2nd Revision) Ghotki	22-08-2014	Satisfactory
30.	Agriculture, GOS	27	Sindh on farm management Project (OFWMP) comprehensive 3966.472(2nd Revision) Shikarpur District	09-09-2014	Un-Satisfactory
31.	Agriculture, GOS	27	Sindh on farm management Project (OFWMP) comprehensive 3966.472(2nd Revision) Jacobabad District	17-09-2014	Average
32.	Agriculture, GOS	28	Provision of Assistance Farmers on Purchase of 11000 Nos:Wheel Type Tractors.(Phase -III) (Larkana District)	25-02-2014	Satisfactory
33.	Agriculture, GOS	28	Provision of Assistance Farmers on Purchase of 11000 Nos:Wheel Type Tractors.(Phase -III) (Khairpur District)	19-02-2014	Satisfactory
34.	Agriculture, GOS	34	Sindh On-Farm Water Management Project- Comprehensive (Malir Karachi)	08-05-2014	Un-Satisfactory
35.	Agriculture, GOS	34	Sindh On-Farm Water Management Project- Comprehensive (District Dadu)	16-05-2014	Un-Satisfactory
36.	Agriculture, GOS	34	Sindh on farm management project (comprehensive) District khairpur	18-06-2014	Average
37.	Agriculture, GOS	34	Sindh On farm Water Management Project (Comrehensive) Nauoshero Feroze	19-06-2014	Average
38.	Agriculture, GOS	34	Sindh On-Farm Water Management Project- Comprehensive (District Jamshoro)	03-07-2014	Satisfactory
39.	Agriculture, GOS	34	Sindh On-Farm Water Management Project- Comprehensive (District Hyderabad)	09-07-2014	Un-Satisfactory
40.	Agriculture, GOS	34	Sindh On Farm Water Management Project (OFWMP) Comprhensive Project Cost. 3966.472 (2nd Revision) Larkana	16-07-2014	Average
41.	Antiquities, GOS	38	Establishment of Institutions for Preservation of Tangible Heritage.	08-05-2014	Un-Satisfactory
42.	Antiquities, GOS	40	Establishment of Archaeological Museum at Sukkur	29-05-2014	Un-Satisfactory
43.	Antiquities, GOS	41	Conservation and Improvement of Old Free Masons Lodge Establishment of Wild Life Museum at Karachi. (Under Revision)	17-06-2014	Average
44.	Antiquities, GOS	42	Establishment of Museum of Epigraphy at Karachi Phase-I,(Under Revision)	17-06-2014	Average
45.	Antiquities, GOS	44	Conservation & Rehabilitation of Shahjhan Mosque Thatta (Under Revision).	08-05-2014	Satisfactory
46.	Antiquities, GOS	50	Construction of site Museum & up gradation & promotion of visitor facilities at Makli).	08-05-2014	Un-Satisfactory
47.	Antiquities, GOS	130	Restoration, Conservation and Rescue of Mukhi House and Establishment of Mukhi House Museum.	01-01-2015	Average
48.	Antiquities, GOS	134	Construction of the Office of Department of Antiquities and Sub Offices under Revision	12-08-2014	Un-Satisfactory
49.	Antiquities, GOS	134	Construction of the Office of Department of Antiquities and Sub Offices under Revision	18-08-2014	Un-Satisfactory
50.	Antiquities, GOS	138	Rehabilitation of Board of Revenue Offices Barack-79	21-05-2015	Average
51.	Antiquities, GOS	140	Establishment of Cell for Scientific Investigation and Rehabilitation of Traditional Mural and Other Paintings (Under Revision)	22-09-2014	Average

52.	Antiquities, GOS	142	Upliftment of Site Museum at Amri	28-04-2015	Un-Satisfactory
53.	Antiquities, GOS	143	Establishment of Site Museum at Miani	02-01-2015	Un-Satisfactory
54.	Antiquities, GOS	145	Construction of N.A Baloch Institute under Revision	05-09-2014	Average
55.	Antiquities, GOS	148	Restoration & Conservation of KhudaAbad Mosque & Tombs Taluka Hala	23-01-2015	Average
56.	Auqaf, GOS	35	Development Repair Renovation of Dargah Khairudin Shah /Jeay Shah District Sukkur. ADP # 35 of 2014-15	23-06-2015	Worst
57.	Auqaf, GOS	65	Renovation of Dargah Hazrat Makhdoom Nooh Sarwar Hala Phase-II	16-04-2014	Average
58.	Auqaf, GOS	70	Development Repair Renovation of Dargah Khairudin Shah /Jeay Shah District Sukkur	21-01-2014	Un-Satisfactory
59.	Board of Revenue, GOS	52	Construction of Deputy Registrar office Sukkur	05-05-2015	Average
60.	Board of Revenue, GOS	52	Construction of office of District Registrar at Karachi and sub Registrar offices	12-05-2015	Worst
61.	Board of Revenue, GOS	52	Construction of Deputy Registrar office Khairpur	22-05-2015	Average
62.	Board of Revenue, GOS	52	Construction of Office of District Registrar at Karachi and Sub-Registrar Offices 22 Nos at Head Quarters all Districts in Sindh.	29-12-2014	Un-Satisfactory
63.	Board of Revenue, GOS	81	Development of townships in major urban centers (50,000 Nos 120 square yard plots with all civic services.	20-01-2015	Average
64.	Board of Revenue, GOS	82	Construction of Office of District Registrar at Karachi and Sub-Registrar Offices 22 Nos at Head Quarters all Districts in Sindh	18-03-2013	Average
65.	Board of Revenue, GOS	82	Construction of Office of District Registrar, at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sindh	25-04-2014	Satisfactory
66.	Board of Revenue, GOS	82	Construction of Office of District Registrar, at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sindh	28-04-2014	Un-Satisfactory
67.	Board of Revenue, GOS	82	Construction of Office of District Registrar, at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sindh	02-04-2014	Average
68.	Board of Revenue, GOS	84	Preservation of Record in the Directorate of Settlement, Survey and Land Record by Scanning, Filming, Cataloging and Digitalization of Maps R and S System	23-06-2014	Average
69.	Board of Revenue, GOS	88	Estt of Sindh Civil Services Academy Reorganization and Rehabilitation of Tapedar College at Hyderabad	12-06-2014	Un-Satisfactory
70.	Coal and Energy, GOS	98	Improvement of Road Network from Thatta to Wango Mor Via Sujawal, Badin with construction of five by passes, rehabilitation of damaged road portions and rehabilitation / reconstruction of structures phase I	22-05-2014	Un-Satisfactory
71.	Coal and Energy, GOS	540	Planning, Designing and Construction of Thar Airport at Islamkot (U/R)	08-04-2015	Un-Satisfactory
72.	Coal and Energy, GOS	547	Improvement & Widening Road Network from Seaport Karachi to Thar Coalfield Area via Thatta, Badin, Wango, Mithi, Islamkot (Phase-I Upto Wango More 124.5 Mile= 200 KM) (Revised)	11-03-2015	Average

73.	Cooperative, GOS	60	Construction of Sindh Government Cooperative College Hyderabad	08-04-2015	Average
74.	Culture, GOS	68	Establishment of Cultural Complex in Sindh (Phase-II)	19-11-2014	Average
75.	Culture, GOS	72	Documentation of libereries of Culture Department in Sindh	13-05-2015	Average
76.	Culture, GOS	77	Establishment of Cultural Centres at various places in Sindh (Jamshoro, Tharparkar, Thatta, S.B.A, Badin, Shikarpur, Jacobabad	17-12-2014	Un-Satisfactory
77.	Culture, GOS	78	Improvement & Extension of public libraries in Sindh	08-07-2014	Average
78.	Culture, GOS	78	Improvement & Extension of Public Libraries in Sindh (Karachi, Hyderabad, Jamshoro, Khairpur Mirs, Dadu, Larkana Shikarpur	08-08-2014	Un-Satisfactory
79.	Culture, GOS	79	Sindh Indigenous Traditional Crafts Company (SITCO) (Capacity Building & Assistance to Producers / Civil Society Organziations)	18-03-2015	Average
80.	Culture, GOS	80	Establishment of Cultural Complex & Model Library at New Karachi. (Under Re-Revision)	11-09-2014	Average
81.	Culture, GOS	100	Printing of Unpublished Books on Culture	13-05-2015	Average
82.	Culture, GOS	110	Establishment of Open Air Theatre at Larkana.	16-01-2014	Average
83.	Culture, GOS	116	Estt of Cultural Complex in Sindh Phase-2.	18-03-2014	Un-Satisfactory
84.	Culture, GOS	117	Construction of Larkana Art Complex at Larkana.	26-06-2014	Average
85.	Culture, GOS	117	Allocation of Early Works at Keenjhar Lake Thatta	14-04-2015	Un-Satisfactory
86.	Culture, GOS	118	Establishment of Shaheed Benazir Bhutto Museum at Sir Shahnawaz Bhutto Library Larkana.	24-02-2014	Average
87.	Culture, GOS	132	Establishment of Cultural Centre at Various places in Sindh at 1.Thano Bula Khan 2.Nangarparkar 3.Jhampir 4.Sakrand 5.Badin 6.Shikarpur 7.Jacobabad.	13-05-2014	Average
88.	Culture, GOS	133	Improvement & Extension of public libraries in Sindh	16-04-2014	Average
89.	Culture, GOS	133	Improvement & Extension of public libraries in Sindh	26-06-2014	Average
90.	Culture, GOS	136	Establishment of Shikarpur City Museum (Under Revision)	14-10-2014	Average
91.	Education and Literacy, GOS	0	Construction / Reconstruction / Raising Of Compound Wall & Construction Of Guard Room @ Public School Hyderabad	29-05-2015	Average
92.	Education and Literacy, GOS	154	UP-GRADATION OF PRIMARY SCHOOL TO MIDDLE SCHOOLS IN SINDH	24-10-2013	Un-Satisfactory
93.	Education and Literacy, GOS	154	Upgradation of Primary School to Middle School in Sindh (475 units) (2005-06 Programe) (Compliance Visit)	18-08-2014	Average
94.	Education and Literacy, GOS	155	Addition of class Room, in Existing Primary Schools/ Construction of Building in Existing Primary Schools in Sindh (2005-06 Prog.). Education works Div.III Karachi (Unit visited = 02 nos).	28-11-2013	Average
95.	Education and Literacy, GOS	155	Addition of Class Rooms in Existing Primary Schools / Construction of Two Roomed Building in Existing Primary Schools in Sindh (2005-06 Programme) (Compliance Visit )	12-08-2014	Average
96.	Education and Literacy, GOS	155	Addition of Class Rooms in existing Primary Schools (600 Class Rooms) / Construction of Two Roomed building in existing Primary Schools (600 Class Rooms) in Sindh 2005-06 Programme. (COMPLIANCE)	12-06-2014	Average



97.	Education and Literacy, GOS	161	Up-Gradation of Primary School to Middle School at GBPS Rais Photo Khan Zardari U/C Khair Wah Taluka Moro District Naushahro Feroze ADP#161 (2013-14).	29-01-2014	Un-Satisfactory
98.	Education and Literacy, GOS	162	A.D.P.NO:162 President's Education Sector Reforms (ESR) Programme- Provision of Missing Facilities (2009-10 Programme)	08-05-2014	Un-Satisfactory
99.	Education and Literacy, GOS	164	Introduction of Computer Education in Middle Schools in Sindh (230 Units) (2007-08 Prog)	14-10-2014	Un-Satisfactory
100.	Education and Literacy, GOS	164	Introduction of Computer Education in Middle Schools in Sindh (230 Units) (2007-08 Prog)	21-10-2014	Average
101.	Education and Literacy, GOS	164	Introduction of Computer Education in Middle Schools in Sindh (230 Units) (2007-08 Programme)	17-11-2014	Un-Satisfactory
102.	Education and Literacy, GOS	164	ADP: 164 (2014-15) Introduction of Computer Education in Existing Middle Schools In Sindh 2007-08	20-11-2014	Un-Satisfactory
103.	Education and Literacy, GOS	165	Renovation of Six Schools of Govt. of Sindh Located at PAF Base Faisal. (06 Units)	16-09-2014	Average
104.	Education and Literacy, GOS	166	ADP # 166 (2014-15) Up-Gradation of Primary School to Middle School at GBPS Rais Photo Khan Zardari U/C Khair Wah Taluka Moro District Naushahro Feroze	28-04-2015	Un-Satisfactory
105.	Education and Literacy, GOS	181	Up-Gradation of Middle School to High School in Sindh of 2005-06 Prog: District Shikarpur	24-10-2013	Un-Satisfactory
106.	Education and Literacy, GOS	181	Up-gradation of Middle Schools to High Schools in Sindh (2005-06 Programme	04-11-2013	Un-Satisfactory
107.	Education and Literacy, GOS	181	Upgradation of Middle School to High Schools in Sindh (2005-06 Prog.) (Compliance Visit)	18-08-2014	Average
108.	Education and Literacy, GOS	181	Up-gradation of Middle Schools to High Schools in Sindh 2005-06 Programme. (175 Units) District Naushahro Feroze = 10 Units (ADP No: 181)	19-06-2014	Un-Satisfactory
109.	Education and Literacy, GOS	182	Up-Gradation of Secondary School to Higher Secondary Schools in Sindh (2005-06) unit-I	12-11-2013	Average
110.	Education and Literacy, GOS	183	Addition of Class Rooms and Construction / Re-construction of Buildings in Existing Secondary / Higher Secondary Schools in Sindh (2005-06 Prog.)	24-11-2014	Average
111.	Education and Literacy, GOS	187	Establishment of Single Section High Schools in Sindh. (2008-09 Program). (District Dadu)	06-02-2014	Un-Satisfactory
112.	Education and Literacy, GOS	187	ESTABLISHMENT OF SINGLE SECTION HIGH SCHOOLS IN SINDH (53 UNITS) IN SINDH OF (2008-09 PROGRAMME) (District Shikarpur 4 Units)	11-03-2014	Un-Satisfactory
113.	Education and Literacy, GOS	187	ADP No:187 (2013-14) Establishment of Single Section High Schools in Sindh (53 Units) (2008-09 Programme) District Naushahro Feroze = 02 Units.	17-03-2014	Un-Satisfactory
114.	Education and Literacy, GOS	189	Establishment of Public School at Kamber @ Shahdadkot ADP #189 (2013-14)	28-04-2014	Un-Satisfactory

115.	Education and Literacy, GOS	195	Reconstruction of Government Boys Secondary School Jacob Line No.1&2, Karachi	17-06-2014	Un-Satisfactory
116.	Education and Literacy, GOS	217	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2004-05 Program) at Karachi 06, Ghotki 01, Benazirabad 01, Shikarpur 01, Jacobabad 01, Mirpurkhas 01, Dadu 01 (Revised)	12-12-2013	Average
117.	Education and Literacy, GOS	228	Establishment of Cadet College Kakar, Dadu (under revision)	22-04-2014	Average
118.	Education and Literacy, GOS	239	ADP NO. 239 (2013-14) Establishment of Govt. Boys/Girls Degree Colleges in Sindh (2010-11 Prog:)(23 Units) District Naushahro Feroze	29-05-2014	Un-Satisfactory
119.	Education and Literacy, GOS	241	Establishment of Cadet College Khairpur ADP No. 241 of 2013-2014	12-05-2014	Not Applicable
120.	Education and Literacy, GOS	244	Reconstruction of Women Degree College Korangi No.6, Karachi	13-02-2014	Un-Satisfactory
121.	Education and Literacy, GOS	255	Miscellaneous Immediate Works of Cadet College Larkana ADP No.255 of 2013-14	14-05-2014	Satisfactory
122.	Education and Literacy, GOS	261	Construction of VIP Suits for Faculty of Provincial Institute of Teacher Education (PITE) Sindh Nawabshah ADP#261	19-08-2014	Satisfactory
123.	Education and Literacy, GOS	268	Immediate Needs for Establishment of Benazir Bhutto Shaheed University Lyari, Karachi at Government Boys Degree College - Lyari (Opening of Tenders on 11th August 2014)	21-08-2014	Average
124.	Education and Literacy, GOS	269	ADP No, 269 .	12-02-2014	Average
125.	Education and Literacy, GOS	271	ADP No:271 / 2013-14	11-02-2014	Average
126.	Education and Literacy, GOS	275	Establishment of Public School in Sindh 2007-08 Programme Ghotki @ Ubauro District Ghotki. ADP No: 275 (2014-15)	21-08-2014	Average
127.	Education and Literacy, GOS	276	Immediate Needs of QUEST, Nawabshah	10-02-2014	Average
128.	Education and Literacy, GOS	298	ADP #298 (2014-2015) Establishment of Single Section High School @ Mir Ali Bazar Khairpur 2012-13 Programme	17-07-2014	Average
129.	Education and Literacy, GOS	302	Repair / Renovation of Educational Institute of Gulshan-e-Iqbal Town	17-09-2014	Average
130.	Education and Literacy, GOS	408	Introduction of Post-Graduate Courses in 12 Existing Degree Colleges (2005-06 Program) ADP#408 (2014-15)	17-04-2015	Average
131.	Education and Literacy, GOS	409	Establishment of Govt. Boys/Girls Colleges in Sindh (23-Units) 2010-11 Programme at Daur. ADP #409	18-08-2014	Average
132.	Education and Literacy, GOS	409	A.D.P.NO: 409 (2014-15) ESTABLISHMENT OF (BOYS/GIRLS) DEGREE COLLEGES IN SINDH 23 UNITS	12-08-2014	Average

133.	Education and Literacy, GOS	411	Establishment of Cadet College at Mithi District Tharparkar	31-03-2015	Average
134.	Education and Literacy, GOS	415	Rehabilitation of Existing Degree Colleges in Sindh @ GDC Karoondi 2008-09 Programme (ADP No: 415)	07-04-2015	Un-Satisfactory
135.	Education and Literacy, GOS	415	A.D.P.NO:415 (2014-15) REHABILITATION OF EXISTING DEGREE COLLEGES IN SINDH (2008-09 PROGRAMME) DISTRICT SHIKARPUR	15-04-2015	Average
136.	Education and Literacy, GOS	425	Construction of Building for Existing Degree Colleges in Sindh at Qazi Ahmed, 2011-12 Programme.	21-10-2014	Average
137.	Education and Literacy, GOS	425	Construction of Building for Existing Degree Colleges in Sindh at Qazi Ahmed, 2011-12 Programme. ADP# 425 (2014-15)	21-12-2014	Satisfactory
138.	Education and Literacy, GOS	426	ADP No: 426 of 2014-15	13-08-2014	Un-Satisfactory
139.	Education and Literacy, GOS	429	Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh	01-12-2014	Un-Satisfactory
140.	Education and Literacy, GOS	429	Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh	21-10-2014	Un-Satisfactory
141.	Education and Literacy, GOS	429	Compliance Visit of Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh	16-05-2015	Satisfactory
142.	Education and Literacy, GOS	433	Establishment of Government Degree College Tando Bago, District Badin (Revised)	16-04-2015	Average
143.	Education and Literacy, GOS	440	Establishment of Sindh College o Art & Design Sukkur ADP # 440.	11-07-2013	Average
144.	Education and Literacy, GOS	448	ADP No:448 (2014-15) Opening of Syed Noor Muhammad Shah Government Boys Degree College Tharushah District Naushahro Feroze	20-08-2014	Average
145.	Education and Literacy, GOS	472	Establishment of Sachal College of Agriculture Engineering & Technology at Khairpur Mirs Constituent College of Sindh Agriculture University Tandojam ADP# 472	11-08-2014	Average
146.	Education and Literacy, GOS	507	Extension and Rehabilitation of Pir Illahi Bux Literacy tower Sukkur 2010-11 programe ADP # 507 of 2014-15	07-08-2014	Satisfactory
147.	Education and Literacy, GOS	1196	Restoration of Historical Educational Institutions in Sindh (07 Units) District Naushehro Feroze. ADP# 1196 (2011-12) Compliance Report	20-06-2014	Un-Satisfactory
148.	Energy, GOS	544	Installation of Reverse Osmosis (Deasalisation) Plant at 25 villages of Tharparkar	26-08-2014	Average
149.	Energy, GOS	549	Water Carrier From Nabisar to Islamkot Thar Coalfield (Revised).	26-08-2014	Average
150.	Energy, GOS	551	Up gradation of Two R.O. Plants at Mithi and Islamkot	15-06-2015	Average
151.	Energy, GOS	561	Village Electrification Programme in Sindh (Phase-V) (All Districts exclude. KESC licence area).	13-03-2015	Average
152.	Energy, GOS	561	Village Electrification Programme in Sindh (Phase-V) (All Districts exclgd. KESC licenced area) Ghotki	29-05-2015	Satisfactory
153.	Energy, GOS	562	Electrification of Goths (Villages) in Karachi (Phase-IV), KESC licensed area).	02-12-2014	Satisfactory

154.	Energy, GOS	564	Electrification of four Villages through Directorate of village electrification Programme Sindh	15-05-2015	Average
155.	Environment, GOS	602	Study for E- Waste Management in Sindh province.	09-03-2015	Worst
156.	Excise & Taxation, GOS	333	Construction of Offices of Excise & Taxation in new Districts (5 units).	03-01-2014	Average
157.	Finance Dept, GOS	338	Construction of 7 new Treasury Offices in Sindh	17-04-2014	Average
158.	Forest, Wildlife & CDA, GOS	343	Plantation on Vacated Encroached Forests Lands in Sindh (Sanghar @ Khipro)	25-02-2014	Un-Satisfactory
159.	Forest, Wildlife & CDA, GOS	343	Planting on vacated encroached forests lands in Sindh(SBA )	10-04-2014	Satisfactory
160.	Forest, Wildlife & CDA, GOS	348	Production of 30-Million tree saplings for meeting the annual targets of tree plantation campaign in Sindh( Afforestation Division SBA)	10-03-2014	Satisfactory
161.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division SBA)	10-03-2014	Satisfactory
162.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division N.Feroze)	21-04-2014	Un-Satisfactory
163.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division Khairpur)	25-04-2014	Un-Satisfactory
164.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division SUKKUR)	13-05-2014	Satisfactory
165.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh(Aff; Division SUKKUR)	09-05-2014	Satisfactory
166.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Guddu Barrage Afforestation Division Mirpur Mathelo(Ghotki)	20-05-2014	Satisfactory
167.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division GHOTKI)	20-05-2014	Satisfactory
168.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division Q.SHADADKOT)	22-05-2014	Un-Satisfactory
169.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division Larkana)	28-04-2014	Satisfactory
170.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division, Shikarpur)	16-04-2014	Satisfactory
171.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division, Jacobabad)	23-04-2014	Satisfactory

172.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh (Kashmore Kandhkot )	18-04-2014	Satisfactory
173.	Forest, Wildlife & CDA, GOS	348	Production of 30 Million Tree Saplings for meeting the Annual targets of Tree Plantation Campaign in Sindh( Social Forestry Division Sukkur)	09-05-2014	Satisfactory
174.	Forest, Wildlife & CDA, GOS	350	Tree Planting in Badin District.	12-06-2014	Average
175.	Forest, Wildlife & CDA, GOS	352	Rehabilitation Restoration and Management of Flora and Fauna in Pai Forest District shaheed Benazirabad	24-06-2014	Average
176.	Forest, Wildlife & CDA, GOS	591	Possible role of Mangroves in curbing Sea intrusion in indus Delta	29-01-2015	Satisfactory
177.	Forest, Wildlife & CDA, GOS	597	Geo-referred demarcation and construction of Earthen bunds for protection of forest land and upgradation of GIS Laboratory at Hyderabad (Larkana, Kandhkot, Shikarpur, Dadu, Sukkur, Ghotki, Khairpur, SBA, Sanghar, Thatta, T.M. Khan, Karachi, N. Feroze	16-03-2015	Average
178.	Forest, Wildlife & CDA, GOS	609	Conservation and Propagation of Bio-Diversity in District Tharparkar	12-05-2015	Average
179.	Governor Secretariat, GOS	616	Supply and installation of security equipments in Governor's House Karachi.	04-02-2015	Satisfactory
180.	Health, GOS	283	Provision of MRI / CT Scan & Generator for Civil Hospital Karachi, Chandka Medical College Hospital Larkana, Peoples Medical College Hospital Nawabshah at District Benazir Abad and Liaquat Universtiy Hospital Hyderabad / Jamshoro	26-02-2014	Un-Satisfactory
181.	Health, GOS	351	ADP No# 351 Establishment of burns center in Sindh	15-01-2014	Un-Satisfactory
182.	Health, GOS	366	Construction of Neuro Science Complex at CMCH Larkana, containing: 1. Neurosurgery Department. 2. Neuro Medicine (Neurology Department) 3. Psychiatry Department	30-04-2014	Average
183.	Health, GOS	366	Construction of Neuro Science Complex at CMCH Larkana, containing: 1. Neurosurgery Department 2. Neuro Medicine (Neurology Department) 3. Psychiatry Department	30-04-2014	Un-Satisfactory
184.	Health, GOS	370	Revamping & Revitalization of Shaikh Zaid Hospital for women Larkana	06-03-2014	Un-Satisfactory
185.	Health, GOS	372	Establishment of 50 bedded Medical & Surgical ICU and expansion of Casualty & OPD Department with strengthening of other units at GMMMCH, Sukkur	16-12-2013	Average
186.	Health, GOS	372	Establishment of Medical & Surgical ICU and Expansion of Casualty & OPD Department @ G.M.C Hospital Sukkur	08-08-2014	Un-Satisfactory
187.	Health, GOS	377	Provision of Free medicines for Blood Cancer patients in Sindh province	30-04-2014	Un-Satisfactory
188.	Health, GOS	380	Establishment of Thelesemia Centre in Sindh. (Through relevant Civil Society Organization)	11-03-2014	Un-Satisfactory
189.	Health, GOS	381	Establishment of Burns Centre in Sindh. (Through relevant Civil Society Organization) (1) Liaquat University Hospital Hyderabad (2) Chandka Medical College Hospital Larkana (3) GMMM College Hospital Sukkur (4) Civil Hospital Mirpurkhas (5) Sindh Govt	07-02-2014	Un-Satisfactory

190.	Health, GOS	382	Establishment of Cardiac Centre in Sindh. (Through relevant Civil Society Organization) (1) Civil Hospital Karachi (2) Liaquat University Hospital Hyderabad (3) Chandka Medical College Hospital Larkana (4) GMMM College Hospital Sukkur (5) Peoples Med	22-01-2014	Un-Satisfactory
191.	Health, GOS	382	Establishment of Cardiac Centre in Sindh. (Through relevant Civil Society Organization) (1) Civil Hospital Karachi (2) Liaquat University Hospital Hyderabad (3) Chandka Medical College Hospital Larkana (4) GMMM College Hospital Sukkur (5) Peoples Med	10-02-2014	Un-Satisfactory
192.	Health, GOS	382	Establishment of Cardiac Centre in Sindh. (Through relevant Civil Society Organization) (1) Civil Hospital Karachi (2) Liaquat University Hospital Hyderabad (3) Chandka Medical College Hospital Larkana (4) GMMM College Hospital Sukkur (5) Peoples Med	17-02-2014	Un-Satisfactory
193.	Health, GOS	383	Establishment of Urological Services in Sindh (Through relevant Civil Society Organization)	22-01-2014	Un-Satisfactory
194.	Health, GOS	383	Establishment & Strengthening of Urological Services in Sindh. (Through relevant Civil Society Organization). (1) Liaquat University Hospital Hyderabad. (2) Chandka Medical College Hospital Larkana (3) Peoples Medical College Hospital Shaheed Benazir	10-02-2014	Un-Satisfactory
195.	Health, GOS	384	Provision of MRI/CT Scan & Generator for Civil hospital Karachi, chandka medical college hospital larkana, peoples medical college hospital nowabshah at district Benazirabad, and Liaquat university hospital Hyderabad/jamshoro.	31-01-2014	Un-Satisfactory
196.	Health, GOS	384	Provision of MRI / CT Scan & Generator for Civil Hospital Karachi. Peoples Medical College	22-02-2014	Un-Satisfactory
197.	Health, GOS	415	Expansion & Improvement of DHQ Hospitals in Sindh (04 Nos.)	16-04-2014	Satisfactory
198.	Health, GOS	419	Construction of Basic Health Unit at village Nather Detho Taulka & District Nausharo Feroz	05-03-2014	Un-Satisfactory
199.	Health, GOS	421	Expansion & Improvement of DHQ Hospital in Sindh (06 Nos) (1) Thatta (2) Dadu (3) Naushero Feroze (4) Mirpurkhas (5) Sanghar (6) Mirpur Mathelo	07-02-2014	Un-Satisfactory
200.	Health, GOS	421	Expansion & Improvement of DHQ Hospital in Sindh (06 Nos) (1) Thatta (2) Dadu (3) Naushero Feroze (4) Mirpurkhas (5) Sanghar (6) Mirpur Mathelo	03-04-2014	Average
201.	Health, GOS	421	Expansion & Improvement of DHQ Hospital in Sindh (06 Nos) (1) Thatta (2) Dadu (3) Naushero Feroze (4) Mirpurkhas (5) Sanghar (6) Mirpur Mathelo	26-06-2014	Un-Satisfactory
202.	Health, GOS	421	ADP# 421/2013-14 Expansion & Improvement of DHQ Hospitals in Sindh (06 Nos.)	24-04-2014	Average
203.	Health, GOS	421	Expansion & Improvement of DHQ Hospitals in Sindh (06 Nos.)	21-04-2014	Average
204.	Health, GOS	433	Establishment of Gynae Ward at 36 Bedded hospital, Nazimabad, Karachi	12-03-2014	Un-Satisfactory
205.	Health, GOS	435	Const. of Maternity Home at UC Mehar Taluka Ghorabari District Thatta	23-04-2014	Un-Satisfactory
206.	Health, GOS	435	Const. of Maternity Home at UC Mehar Taluka Ghorabari District Thatta	23-04-2014	Un-Satisfactory
207.	Health, GOS	436	Provision of PCR, Cell Separator, Platelet Agitator at Hospitals at Defunct Divisional Headquarters in Sindh	07-03-2014	Un-Satisfactory
208.	Health, GOS	443	Strengthening of services of SIUT, Karachi	11-03-2014	Satisfactory
209.	Health, GOS	445	Construction of Government Dispensary at Village Chanda Singh Taluka Kazi Ahmed District Shaheed Benazirabad ADP#445	12-02-2014	Un-Satisfactory
210.	Health, GOS	446	Construction of Government Dispensary at village Abdul Ghafoor Keerio, Taluka Kazi Ahmed District Shaheed Benazirabad ADP#446	11-02-2014	Un-Satisfactory

211.	Health, GOS	448	Repair & renovation of DHQ Hospital Civil hospital, THQ Thul, THQ Garhi- Khairo and construction of Female Nursing Hostel at Jacobabad.	22-05-2014	Un-Satisfactory
212.	Health, GOS	450	Construction of Government Dispensary at Village Sohno Khan Khoso Taluka Miro Khan District Kamber Shahdadkot	26-02-2014	Average
213.	Health, GOS	451	Construction of Dispensary Kora Khan Lakhan, District Ghotki	31-03-2014	Average
214.	Health, GOS	452	Up gradation of THQ Hospitals at Shahdakot Qubo Saeed Khan, Nasirabad Sujawal and Miro Khan	27-06-2014	Un-Satisfactory
215.	Health, GOS	454	Up gradation & revamping of THQ Hospital in side (39 Nos.) & Construction of emergency cum Trauma Centers in THQ Hospitals (41 Nos.)	31-03-2014	Un-Satisfactory
216.	Health, GOS	455	Shaheed Mohtarma Benazir Bhutto Floor at Kidney Centre Post Graduate Training Institute (TKCI) Karachi	11-03-2014	Satisfactory
217.	Health, GOS	463	Construction of Government Dispensary at Village Hotjowahan UC Hebrri Talka Kazi Ahmed District Nawabshah	17-06-2014	Satisfactory
218.	Health, GOS	464	Construction of Government Dispensary at Village S. Miskeen Shah UC Khair Shah Talka Nawabshah	17-06-2014	Satisfactory
219.	Health, GOS	465	Construction of Government Dispensary at Village Dahani Bux Zardari UC Khair Shah Talka Nawabshah.	17-06-2014	Satisfactory
220.	Health, GOS	511	Construction of International Hostel for 240 Students at Peoples Medical College Nawabshah ADP#511	12-02-2014	Un-Satisfactory
221.	Health, GOS	512	Purchase of land for women (200) acres for construction of women medical University @ Shaheed Benazirabad.	21-07-2014	Un-Satisfactory
222.	Health, GOS	513	Construction of Dental Faculty Chandka Medical College Larkana	05-03-2014	Un-Satisfactory
223.	Health, GOS	517	Construction of Girls Hostel for 200 under graduate / post graduate students of Liaquat Medical College Jamshoro.	10-03-2014	Average
224.	Health, GOS	519	Establishment of Medical College at Karachi.	27-03-2014	Satisfactory
225.	Health, GOS	522	Establishment of Medical College at Mirpurkhas.	03-04-2014	Un-Satisfactory
226.	Health, GOS	523	Strengthening of Safe Blood transmission Reforms in Sindh.	30-04-2014	Un-Satisfactory
227.	Health, GOS	527	Operational Support for EPI Sindh.	15-04-2014	Un-Satisfactory
228.	Health, GOS	528	Provincial Tuberculosis Control Programme in Sindh.	10-04-2014	Un-Satisfactory
229.	Health, GOS	528	Provincial Tuberculosis Control Programme in Sindh.	27-05-2014	Un-Satisfactory
230.	Health, GOS	529	Extension of Malaria Control Programme for role back Malaria initiative in Sindh.	27-05-2014	Un-Satisfactory
231.	Health, GOS	529	Extension of Malaria Control Programme for role back Malaria initiative in Sindh.	26-06-2014	Un-Satisfactory
232.	Health, GOS	531	Prevention & Control of Hepatitis in Sindh. Chief Minister Initiatives.	25-04-2014	Un-Satisfactory
233.	Health, GOS	531	Prevention & Control of Hepatitis in Sindh. Chief Minister Initiatives.	21-05-2014	Un-Satisfactory
234.	Health, GOS	617	Modernization of Electrification distribution network at Civil Hospital Karachi. (Re-revised) (C. 321.294)	08-06-2015	Average
235.	Health, GOS	624	Expansion & Improvement of Oncology Department & Upgradation of Neurology Department, Surgical ICU and establishment of colorectal unit in Surgical Unit V at Civil Hospital Karachi. (Revised) (C. 148.029 + R. 90.640)	08-05-2015	Average
236.	Health, GOS	629	Purchase & installation of Bed lift and purchase of Auto start 250KV Diesel / Gas Generator at Liaquat University Hospital Hyderabad / Jamshoro. (Revised). (C. 13.272+R. 24.757).	18-05-2015	Average
237.	Health, GOS	630	Strengthening of Eye Hospital, LUH, Hyderabad.	20-03-2015	Average
238.	Health, GOS	631	Shaheed Benazir Bhutto Accident Emergency & Ancillary Services Complex at Civil Hospital Karachi. (Re-Revised). (C. 3645.649+R.2619.586)	05-03-2015	Average
239.	Health, GOS	632	Revamping of Civil Hospital Karachi. (C. 198.650)	08-05-2015	Average



240.	Health, GOS	635	Establishment of 50 bedded Medical & Surgical ICU and expansion of Casualty & OPD Department at LUH, Hyderabad.	02-07-2014	Average
241.	Health, GOS	635	Establishment of 50 bedded Medical & Surgical ICU and expansion of Casualty & OPD Department at LUH, Hyderabad.(C. 134.530+ R. 149.004).	02-02-2015	Average
242.	Health, GOS	643	Strengthening and Improvement of National Institute of Child Health (N.I.C.H.), Karachi.	10-12-2014	Un-Satisfactory
243.	Health, GOS	661	Construction of 400 Bedded Hospital at NIPA Chowrangi Gulshan-e-Iqbal Karachi. (Revised). (C. 1076.250 + R. 660.109)	16-02-2015	Average
244.	Health, GOS	663	Renovation, Rehabilitation and Addition in TB Hospital (Institute of chest Diseases ) at Ojha Campus, Dow University of Health Sciences, Karachi. (C. 345.206 + R. 38.911)	09-09-2014	Un-Satisfactory
245.	Health, GOS	664	Expansion & Rehabilitation of CJ Institute of Psychiatry Hyderabad including construction of new female ward, Rehabilitation Centre & OPD block. (Revised)	16-09-2014	Un-Satisfactory
246.	Health, GOS	669	Up gradation of THQ Hospitals to the level of DHQ Hospital in Sindh (newly created District) : i) Tando Mohammad Khan ii) TandoAllahyar iii) Jamshoro	03-04-2015	Average
247.	Health, GOS	670	Expansion & Improvement of DHQ Hospital in Sindh (1) Badin (2) Khairpur (3) Shikarpur (4) Mithi (Revised). (C.3162.206+R.1394.212).	10-02-2015	Average
248.	Health, GOS	670	Expansion & Improvement of DHQ Hospital in Sindh (1) Badin (2) Khairpur (3) Shikarpur (4) Mithi (Revised). (C.3162.206+R.1394.212).	06-01-2015	Un-Satisfactory
249.	Health, GOS	671	Establishment of Cardiac Emergency Center at Baldia Town Karachi.	28-10-2014	Un-Satisfactory
250.	Health, GOS	671	Establishment of Cardiac Emergency Center at Baldia Town Karachi. (C.149.857+R.149.077).	08-05-2015	Satisfactory
251.	Health, GOS	673	Establishment of Children Hospital at SIUT Karachi. (C. 344.000 SIUT+ R. 577.023 GOS. = 921.023)	22-09-2014	Satisfactory
252.	Health, GOS	678	Expansion & Improvement of Urban Health Centre in Karachi District. (1) Orangi No-15 (2) Malir City (3) Kaemari and (4)construction of additional Indoor Block at Sindh Government Hospital, Korangi No. 5, Karachi.	04-12-2014	Average
253.	Health, GOS	678	Expansion & Improvement of Urban Health Centre in Karachi District. (1) Orangi No-15 (2) Malir City (3) Kaemari and (4)construction of additional Indoor Block at Sindh Government Hospital, Korangi No. 5, Karachi.	15-12-2014	Average
254.	Health, GOS	678	Expansion & Improvement of Urban Health Centre in Karachi District. (1) Orangi No-15 (2) Malir City (3) Kaemari and (4)construction of additional Indoor Block at Sindh Government Hospital, Korangi No. 5, Karachi.	15-12-2014	Un-Satisfactory
255.	Health, GOS	678	Expansion & Improvement of Urban Health Centre in Karachi District. (1) Orangi No-15 (2) Malir City (3) Kaemari and (4)construction of additional Indoor Block at Sindh Government Hospital, Korangi No. 5, Karachi.	16-12-2014	Average
256.	Health, GOS	680	Establishment of 50 Bedded Hospital / Maternity Home in Gulistan-e-Jouhar Karachi. (Revised) (C.264.852+R.61.302)	26-01-2015	Un-Satisfactory
257.	Health, GOS	683	Establishment of Department of Serobiological and providing power generation by gas along with heat recovery system at Ojha Campus of DUHS, Karachi. (C. 310.811+ R.99.454)	26-01-2015	Average
258.	Health, GOS	687	Up gradation of THQ Hospitals to the level of DHQ Hospital in Sindh (newly created District 04 Nos) i) Kamber ii) Umerkot iii) Kashmore iv)Matari. (C.1538.205+R.833.995).	22-06-2015	Average
259.	Health, GOS	690	Construction of Mother & Child Health Center at UC Karimbux at village Bhadurpur Taluka Thul District Jacobabad	23-07-2014	Un-Satisfactory
260.	Health, GOS	691	Establishment of Ancillary and other services at 400 bedded Hospital at NIPA, Karachi.(C. 311.882 + R. 5.919)	17-02-2015	Average



261.	Health, GOS	695	Repair / Renovation of DHQ Hospital (Civil (Hospital) Jacobabad, THQ Hospital Tull, Garhi Khairo and Construction of Female Nursing Hostel at Jacobabad	18-06-2015	Average
262.	Health, GOS	698	Up gradation of Taluka Hospital Sehwan to the level of Institute of Medical Sciences.	27-10-2014	Average
263.	Health, GOS	699	Up gradation & revamping of THQ Hospital in sindh (39 Nos.) & Construction of emergency cum Trauma Centers in THQ Hospitals (41 Nos.)	26-03-2015	Average
264.	Health, GOS	699	Up gradation & revamping of THQ Hospital in side (39 Nos.) & Construction of emergency cum Trauma Centers in THQ Hospitals (41 Nos.)	04-07-2014	Un-Satisfactory
265.	Health, GOS	699	Up gradation & revamping of THQ Hospital in side (39 Nos.) & Construction of emergency cum Trauma Centers in THQ Hospitals (41 Nos.)	10-07-2014	Un-Satisfactory
266.	Health, GOS	699	Up gradation & revamping of THQ Hospital in sindh (39 Nos.) & Construction of emergency cum Trauma Centers in THQ Hospitals (41 Nos.) (all Districts) (C.1415.876+R.1918.285)	27-08-2014	Un-Satisfactory
267.	Health, GOS	701	Contt of 50 Bedded Hospital at Block-13 FB Area, District Central Karachi. (C.255.646 + R.52.196)	24-10-2014	Average
268.	Health, GOS	702	Establishment of Shaheed Benazir Bhutto Medical Complex at National High way, near Razaqabad, Bin Qasim Town Karachi. (C. 1120.582 + R. 308.857)	13-10-2014	Un-Satisfactory
269.	Health, GOS	708	Up gradation of BHU to RHC Haji Fateh Mohammad Rajar (C.48.521+R.15.902)	12-05-2015	Average
270.	Health, GOS	711	Construction of BHU Mohammad Ashraf Samoo Golari Taluka Talhar District Badin . (C. 20.629+R.2.260).	17-09-2014	Un-Satisfactory
271.	Health, GOS	712	Construction of BHU at village Haji Ramzan Chandio Taluka Badin. (C.20.303+R.2.260).	17-09-2014	Un-Satisfactory
272.	Health, GOS	714	Establishment of Pediatric Center in Mirpurkhas. (C.78.383+R.34.563).	21-08-2014	Un-Satisfactory
273.	Health, GOS	720	Renovation & equipments for Maternity Home at Manghopir	12-11-2014	Average
274.	Health, GOS	724	Up gradation of 3 Maternity Home in Karachi. PIB Colony Soldier Bazar Jahangir Road, Karachi.	17-11-2014	Average
275.	Health, GOS	724	Up gradation of 3 Maternity Home in Karachi. PIB Colony Soldier Bazar Jahangir Road, Karachi.	17-11-2014	Average
276.	Health, GOS	724	Up gradation of 3 Maternity Home in Karachi. PIB Colony Soldier Bazar Jahangir Road, Karachi.	17-11-2014	Average
277.	Health, GOS	726	Upgradation of Rural Health Centre to the level of THQ, Mirwah, District Mirpurkhas. (C.80.639+R.39.336).	21-08-2014	Un-Satisfactory
278.	Health, GOS	728	Upgradation of Basic Health Unit to the level of Rural Health Centre, Jhulri, District Mirpurkhas. (C.43.485 + R.11.058).	11-09-2014	Un-Satisfactory
279.	Health, GOS	729	Construction of two BHU at(i) Shah Faisal Colony (ii) Korangi No.5 Karachi. (C.23.126+R.6.534).	13-05-2015	Average
280.	Health, GOS	731	Providing additional Facilities in Rural Health Center at Naudero Taluka Rutodero District Larkana	27-08-2014	Un-Satisfactory
281.	Health, GOS	732	Shaheed Benazir Bhutto Rehabilitation Centre for Burn and Rape Victims at Maternity Home of RHC old Thana Malir, Karachi (C.39.752+R.19.195)	28-11-2014	Average
282.	Health, GOS	732	Shaheed Benazir Bhutto Rehabilitation Centre for Burn and Rape Victims at Maternity Home of RHC old Thana Malir, Karachi (C.39.752+R.19.195)	13-05-2015	Average
283.	Health, GOS	796	Construction of Girls Hostel for 200 under graduate / postgraduate students of Liaquat Medical College Jamshoro. (C.158.965+R.13.224).	25-02-2015	Un-Satisfactory
284.	Health, GOS	797	Establishment of Medical College at Hyderabad.(C.984.973+R.409.494).	16-01-2015	Average
285.	Health, GOS	801	Establishment of Medical College at Mirpurkhas. (C.1526.708+R.523.122).	23-01-2015	Un-Satisfactory
286.	Health, GOS	805	Strengthening of safe blood transmission reforms in Sindh (Sukkur)	16-02-2015	Average

287.	Health, GOS	809	Operational Support for EPI Sindh (all Districts) Kamber	10-12-2014	Average
288.	Health, GOS	809	Operational Support for EPI Sindh (all Districts) Khairpur	16-12-2014	Un-Satisfactory
289.	Health, GOS	809	Operational Support for EPI Sindh (all Districts) Kashmore Kandhkot	29-12-2014	Satisfactory
290.	Health, GOS	809	Operational Support for EPI Sindh (all Districts) Jacobabad	23-12-2014	Un-Satisfactory
291.	Health, GOS	809	Operational Support for EPI Sindh (all Districts) SBA	12-01-2014	Un-Satisfactory
292.	Health, GOS	810	Prevention of Tuberculosis Control Program in Sindh (Jacobabad)	24-12-2014	Average
293.	Health, GOS	810	Prevention of Tuberculosis Control Program in Sindh (SBA)	12-01-2015	Un-Satisfactory
294.	Health, GOS	810	Prevention of Tuberculosis Control Program in Sindh (Qamber Shahdadkot)	26-01-2015	Un-Satisfactory
295.	Health, GOS	810	Prevention of Tuberculosis Control Program in Sindh (Ghotki)	29-01-2015	Un-Satisfactory
296.	Health, GOS	811	Extension of Malaria Control Programme for Roll Back Malaria initiative in Sindh. (all Districts)	15-09-2014	Average
297.	Health, GOS	811	Extension of Malaria control programme for roll back Malaria initiative in Sindh(all District) Khairpur	23-01-2015	Average
298.	Health, GOS	811	Extension of Malaria Control Programme for role back Malaria initiative in Sindh (all districts).	28-04-2015	Satisfactory
299.	Health, GOS	812	Prevention & control of Blindness Program in Sindh (all Districts)	29-10-2014	Un-Satisfactory
300.	Health, GOS	812	Prevention & Control of Blindness Program in Sindh. (all Districts) Larkana	09-12-2014	Average
301.	Health, GOS	813	Prevention & Control of Hepatitis in Sindh. Chief Minister Initiatives. (all Districts)	07-01-2015	Un-Satisfactory
302.	Health, GOS	813	Prevention & Control of Hepatitis in Sindh. Chief Minister Initiatives. (all Districts)	14-01-2015	Un-Satisfactory
303.	Health, GOS	813	Hepatitis Prevention & Control Programme Sindh- Chief Minister Sindh Initiatives (all districts).	07-05-2015	Satisfactory
304.	Health, GOS	814	Establishment of Health Sector Reforms Unit in Sindh. (all Districts)	13-05-2015	Average
305.	Health, GOS	815	Enhance HIV/ AIDS control programme in Sindh. Exp 6.434 million (all Districts)	24-10-2014	Un-Satisfactory
306.	Health, GOS	815	Enhance HIV/AIDS Control Programme in Sindh. Exp 6.434 million. (all Districts) Larkana	18-12-2014	Average
307.	Health, GOS	815	Enhance HIV/AIDS Control Programme in Sindh. Exp 6.434 million. (all Districts)	08-05-2015	Satisfactory
308.	Health, GOS	817	Child Survival Program in Sindh	18-05-2015	Un-Satisfactory
309.	Health, GOS	1354	Rehabilitation of Peoples Medical College Hospital Nawabshah, District Shaheed Benazirabad	06-05-2015	Satisfactory
310.	Home, GOS	544	Construction of Buildings for Sindh Police at various location under Police Package (2 unit visited)	21-04-2014	Average
311.	Home, GOS	570	Construction of District Jail at Thatta for 250 Prisoners	23-04-2014	Un-Satisfactory
312.	Home, GOS	827	Construction of Buildings for Sindh Police at various locations under Police Package	16-07-2014	Average
313.	Home, GOS	831	Constt. Of Police Station B-Section, Tando Adam District Sanghar	15-01-2015	Average
314.	Home, GOS	832	Construction of Police Station Khahi District Sanghar	13-04-2015	Un-Satisfactory
315.	Home, GOS	838	Construction of Police Station (Category-C) & Bachelor Barracks (Ground+1) at Nindo District Badin	09-06-2015	Average
316.	Home, GOS	879	Construction of New District Jail NawabShah for 250 Prisoners.	15-10-2014	Un-Satisfactory
317.	Home, GOS	882	Rehabilitation Renovation of Jails in Sindh (Karachi Hyderabad Dadu Sanghar Badin Mirpurkhas S.B.A Sukkur Shikarpur Khairpur Larkana Jacobabad).	16-10-2014	Un-Satisfactory

318.	Home, GOS	882	Rehabilitation Renovation of Jails in Sindh (Karachi Hyderabad Dadu Sanghar Badin Mirpurkhas S.B.A Sukkur Shikarpur Khairpur Larkana Jacobabad)	02-02-2015	Un-Satisfactory
319.	Home, GOS	887	Improvement /Strengthening of Security of Central Prison in Sindh @ Karachi, Hyderabad Sukkur & Larkana.	23-10-2014	Average
320.	Human Rights and Law, GOS	864	Provision of Bar Room & Library in Judl Distt across the Sindh	07-05-2014	Average
321.	Human Rights and Law, GOS	883	Construction of officer's official's residential accommodation for the prosecutors in Sindh.	29-04-2014	Un-Satisfactory
322.	Human Rights and Law, GOS	884	ADP # 884, Automation of Law, Prosecution & HR Department, Government of Sindh.	27-05-2014	Un-Satisfactory
323.	Human Rights and Law, GOS	1269	Construction of 4 Nos. Bungalows @ Tando Muhammad Khan	25-05-2015	Average
324.	Human Rights and Law, GOS	1270	Construction of 2 Nos. Bungalows @ Matiari.	02-12-2014	Un-Satisfactory
325.	Human Rights and Law, GOS	1278	Construction of New Annexe Buildings No. I & II Courts in the premises of Sindh High Court Karachi	12-11-2014	Average
326.	Human Rights and Law, GOS	1283	Construction of Bar room library,Litigant shade with canteen and Vehicle shade at High Court Circuit Bench at Larkana.	18-05-2015	Average
327.	Human Rights and Law, GOS	1291	Construction of Record Room adjacent of Judicial Complex Badin	24-02-2015	Un-Satisfactory
328.	Human Rights and Law, GOS	1314	Construction of offices for the prosecutor in Sindh. (22 Nos)	17-07-2014	Average
329.	Human Rights and Law, GOS	1314	Construction of offices for the prosecutor in Sindh. (22 Nos)	02-07-2014	Average
330.	Industrial & Commerce, GOS	911	Up-gradation of 9 SIEs (Thatta, Sanghar, Dadu, Hala, Badin, Nawabshah, Rohri and I.P. Sehwan, Mirpurkhas). (Under revision)	26-05-2015	Un-Satisfactory
331.	Industrial & Commerce, GOS	911	Up-gradation of 9 SIEs (Thatta, Sanghar, Dadu, Hala, Badin, Nawabshah, Rohri and I.P. Sehwan, Mirpurkhas). (Under revision)	12-03-2015	Un-Satisfactory
332.	Industrial & Commerce, GOS	911	Up-gradation of 9 SIEs (Thatta, Sanghar, Dadu, Hala, Badin, Nawabshah, Rohri and I.P. Sehwan, Mirpurkhas). (Under revision)	16-03-2015	Average
333.	Industrial & Commerce, GOS	911	Up-gradation of 9 SIEs (Thatta, Sanghar, Dadu, Hala, Badin, Nawabshah, Rohri and I.P. Sehwan, Mirpurkhas).	24-03-2015	Average
334.	Industrial & Commerce, GOS	911	Up-gradation of 9 SIEs (Thatta, Sanghar, Dadu, Hala, Badin, Nawabshah, Rohri and I.P. Sehwan, Mirpurkhas). (Under revision)	24-03-2015	Un-Satisfactory
335.	Information Technology, GOS	613	Intranet setup for Govt. of Sindh	10-04-2014	Average

336.	Information Technology, GOS	614	IT Training for capacity Building of Sindh Government Employees	10-04-2014	Un-Satisfactory
337.	Irrigation (Water & Drainage), GOS	621	Establishment of Planning, Monitoring & Evaluation Cell in Irrigation & Power Department.	24-03-2014	Un-Satisfactory
338.	Irrigation (Water & Drainage), GOS	636	Extension of 1R Western Mir Link Drain (25 RDs).	16-05-2014	Un-Satisfactory
339.	Irrigation (Water & Drainage), GOS	650	Construction of Pumping Stations at Village Muhammad Din Dogar, Sui Kandhar Minor and Village Matto Dahri.(Compliance report)	23-06-2014	Satisfactory
340.	Irrigation (Water & Drainage), GOS	653	Construction of Link Drains Haji Abdullah Shah, Haji Ahmed Zour, Budho Qambrani, Bhaneri Link Drain of TalukaTandoBago& Badin.	16-05-2014	Un-Satisfactory
341.	Irrigation (Water & Drainage), GOS	654	Installation of Pumping Station at Deh Panwari & Deh Baran U/C Chahen Near Sanwalabad Taulka Bhiria and Construction of Pumping Station (two nos. additional pumps) Behelain (L/S) at Rohri Canal	19-05-2014	Un-Satisfactory
342.	Irrigation (Water & Drainage), GOS	681	CC lining of Nurrar Branch Drain, Mari Branch Drain, & Brick lining of D/Channel of tubewell No. F-188	10-04-2014	Average
343.	Irrigation (Water & Drainage), GOS	683	Construction / Extension of Sub-Drain S-2R from RD-24+674 to 72+194 in Taluka & District Sanghar (Provincial Ombudsman Decision)	19-03-2014	Average
344.	Irrigation (Water & Drainage), GOS	686	Construction of Surface Drainage Scheme in Deh Dethki in Union Council Shahmir Rahu Taluka New Saeedabad District Matiari.	19-06-2014	Average
345.	Irrigation (Water & Drainage), GOS	696	Sanction Link Drain for Drain Out Rainy/Surplus Water of Four Dehs Kas, Dhandh Dhabho, Ali Pur and Soomra, U.C. Mula Katiyar and Extension of Bukhari Link Drain at RD-8 to 16 & Dhandi Link Drain RD-10 to 16 Deh Seerani and Sathia, Taluka Bulri Shah K	26-05-2014	Un-Satisfactory
346.	Irrigation (Water & Drainage), GOS	698	Construction of Road Bridges Over Bathoro Branch Drain at RD-88.0 1-1L Kapoor Branch Drain at RD-32.0.	26-05-2014	Un-Satisfactory
347.	Irrigation (Water & Drainage), GOS	702	Surface Drainage Scheme in Deh Dhargel, Deh Dubbar and Deh Jumaan Taluka Khipro Distrcit Sanghar.	16-04-2014	Satisfactory

348.	Irrigation (Water & Drainage), GOS	707	Construction of Chief Engineer Sukkur Barrage Left Bank Region Office Complex	08-04-2014	Average
349.	Irrigation (Water & Drainage), GOS	722	Providing Back Berm & Stone pitching along K B F Lower RD 0 to 22 & Pinyari Feeder Lower RD - 90 to 100.(Compliance Report).	27-08-2014	Un-Satisfactory
350.	Irrigation (Water & Drainage), GOS	722	Providing Back Berm & Stone pitching along K B F Lower RD 0 to 22 & Pinyari Feeder Lower RD - 90 to 100.(Compliance report).	19-08-2014	Average
351.	Irrigation (Water & Drainage), GOS	726	Rehabilitation / Replacement X-Regulators & Head Regulators in SIDA.	27-01-2014	Satisfactory
352.	Irrigation (Water & Drainage), GOS	726	Rehabilitation / Replacement X-Regulators & Head Regulators in SIDA	16-01-2014	Average
353.	Irrigation (Water & Drainage), GOS	729	Enhancing Capacity Building of Discharge Observation in the Command of Three Barrages and up-Gradation of Soil Mechanics & Hydraulic Laboratory Karachi and Workshop of Gauging Sub-Division.(Compliance report)	08-04-2014	Satisfactory
354.	Irrigation (Water & Drainage), GOS	748	Construction of Pumping Station at RD-31 Kakole Branch and Construction of Bridge Over Ganwar Wah at RD-10 near Village Ali Akbar Mugheri in Rice Canal Division	05-03-2014	Average
355.	Irrigation (Water & Drainage), GOS	749	Construction of Bridge Over Sangi Distry at RD-4-5 Near Village Haji Ali Sher Chang	12-03-2014	Un-Satisfactory
356.	Irrigation (Water & Drainage), GOS	760	Revitalization of Mechanical Wing of Irrigation Department.	31-01-2014	Un-Satisfactory
357.	Irrigation (Water & Drainage), GOS	761	Rehabilitation of Gates in Rohri Canal Circle through Mechanical Circle.	18-06-2014	Average
358.	Irrigation (Water & Drainage), GOS	761	Rehabilitation of Gates in Rohri Canal Circle through Mechanical Circle.	19-06-2014	Satisfactory
359.	Irrigation (Water & Drainage), GOS	761	Rehabilitation of Gates in Rohri Canal Circle through Mechanical Circle. ADP # 761 (2013-14)	23-06-2014	Average

360.	Irrigation (Water & Drainage), GOS	762	New Manufacturing / Replacement of Gates of Head Regulator and X-ing Regulators of Kotri Barrage Region.(Compliance visit).	18-11-2014	Satisfactory
361.	Irrigation (Water & Drainage), GOS	764	Rehabilitation / Renovation of Office / Residential Bungalows and Inspection Bungalows in Shahbaz Irrigation Division Sehwan.	20-03-2014	Satisfactory
362.	Irrigation (Water & Drainage), GOS	768	Lining of Ghouspur Minor RD-0 to 35	12-03-2014	Un-Satisfactory
363.	Irrigation (Water & Drainage), GOS	782	Construction of 2 Nos. Bridges at Village Muhammad Omar Jhakro and Muhammad Mirbahr, Taluka Sujawal.(Compliance report).	27-08-2014	Satisfactory
364.	Irrigation (Water & Drainage), GOS	790	Restoration of Flood Damages to Gaj Diversion Bund at RD-2+700, 5+000, 12+000 & 13+000 in Southern Dadu Division.	25-02-2014	Average
365.	Irrigation (Water & Drainage), GOS	797	Construction Retaining wall along Abul Wah from RD-55+00 to 58+00 and 92+00 to 94+00 Both sides Gambat and Ranipur City area and Construction Retaining wall along Mehrab Wah from RD-0+00 to 5+00 and 14+00 to 19+00 Both Sides Sobhoderi City area	09-04-2014	Average
366.	Irrigation (Water & Drainage), GOS	802	Rehabilitation & Re-sectioning of Nasir Branch from RD-110 to 142 Tando Allahyar-II Distry: from RD-0 to 43 & Gharib Distry: from RD-0 to 32.Compliance visit report.	03-10-2014	Satisfactory
367.	Irrigation (Water & Drainage), GOS	804	Repair / Replacement of Damaged Deck Slab of Road Bridge over Rohri Main Canal at RD-806 (Hala-Shahdadpur Road) and Construction of Bridge on Sarhal Minor-2 to connect Village Gul Muhammad Solangi U.C Khahi Qasim, Taluka Bhiria	19-06-2014	Average
368.	Irrigation (Water & Drainage), GOS	804	Repair / Replacement of Damaged Deck Slab of Road Bridge over Rohri Main Canal at RD-806 (Hala-Shahdadpur Road) and Construction of Bridge on Sarhal Minor-2 to connect Village Gul Muhammad Solangi U.C KhahiQasim, TalukaBhiria.	19-06-2014	Satisfactory
369.	Irrigation (Water & Drainage), GOS	805	Earth work along Kurkaim Minor from RD-0 to 46+400 Both sides	19-05-2014	Average
370.	Irrigation (Water & Drainage), GOS	812	Providing Stone Pitching on Both Sides Mirwah Canal from RD-78+600 to 93+600 D/S Bhurgri Regulator to Shah Abdul Latif University	19-03-2014	Un-Satisfactory
371.	Irrigation (Water & Drainage), GOS	814	Rehabilitation of Dhandho Minor Ex-Rohri Main Canal at RD-845.	19-06-2014	Average

372.	Irrigation (Water & Drainage), GOS	814	Rehabilitation of Dhandho Minor Ex-Rohri Main Canal at RD-845.	19-06-2014	Average
373.	Irrigation (Water & Drainage), GOS	815	C.C. Lining of New Shekhani Minor Ex-Rohri Main Canal at RD-829 IP Side, including Old Shekhani Minor, Chhar Minor & Tarah Tail.	23-05-2014	Un-Satisfactory
374.	Irrigation (Water & Drainage), GOS	818	Reh./Re-Sectioning Jam Br: from RD 0 to 83 and Extension of Babra Minor EX: Jam Branch RD 15 to 19.3 (Baghar Circle)	15-05-2014	Satisfactory
375.	Irrigation (Water & Drainage), GOS	832	Construction of Malir Memon Goth Weir Across Malir Nadi, Karachi. (Compliance visit report).	10-06-2014	Satisfactory
376.	Irrigation (Water & Drainage), GOS	833	Constructing Out-let i/c Channel Ex: Ranpur Dam, HEIS, Extension of Malji Bund and Stone Pitching and Three (03) Nos. Gabion Dams including Re-modelling of Lakhy-jo- Wandio Dam in Nagarparkar Area.	14-05-2014	Satisfactory
377.	Irrigation (Water & Drainage), GOS	835	Construction of Recharge Dam Malirirri in Union Council JahngaraTaluka Sehwan District Jamshoro in Central Kohistan	24-07-2014	Average
378.	Irrigation (Water & Drainage), GOS	836	Construction of Kataro Weir Dam in Taluka District Thatta.	10-06-2014	Satisfactory
379.	Irrigation (Water & Drainage), GOS	837	Construction of Mohan & Haleli Recharge Dam in Central Kohistan District Dadu.	27-06-2014	Average
380.	Irrigation (Water & Drainage), GOS	839	Construction of Ashoro Kach Diversion Bund Dam in Central Kohistan.	27-06-2014	Satisfactory
381.	Irrigation (Water & Drainage), GOS	948	Feasibility study for the survey & designing of Surface Drainage and Works for the part command area of Mithrao, Khipro & Lower Nara Canal.	11-09-2014	Satisfactory
382.	Irrigation (Water & Drainage), GOS	949	Feasibility Study Identifying the route to divert excessive flood water along River Indus.	23-09-2014	Satisfactory
383.	Irrigation (Water & Drainage), GOS	956	Construction of 1RE Sub Drain RD-0 To 35 (Village Abdul Wahab Khoso), Sub Drain Qubo Saeed Khan RD-0 To 65, 3LA Sub Drain RD-0 To 37 & Extension Of 3R Sub Drain RD-18 To 32 of Shahdadkot System.	28-08-2014	Average

384.	Irrigation (Water & Drainage), GOS	957	Extension of 1R Western Mir Link Drain (25 RDs).	26-05-2015	Average
385.	Irrigation (Water & Drainage), GOS	967	Construction of 20 cusecs Pumping Station at U.C Bhale Dino Kaka in Deh Kaka.	20-11-2014	Un-Satisfactory
386.	Irrigation (Water & Drainage), GOS	967	Construction of 20 cusecs Pumping Station at U.C Bhale Dino Kaka in Deh Kaka.(Compliance report).	03-03-2015	Average
387.	Irrigation (Water & Drainage), GOS	971	Construction of Pumping Stations of 80 Cusecs to Control Water Logging Salinity and Drain out monsoon Water at Chamber, District Tando Allahyar.	14-01-2015	Average
388.	Irrigation (Water & Drainage), GOS	973	Construction of Surface Drainage Scheme of Deh Dobi and Akanwari in Taluka& District Sanghar.	02-10-2014	Average
389.	Irrigation (Water & Drainage), GOS	979	Construction of Two (02) Link Drains from Sanjar Chang to Sorahadi, Taluka Golarchi Badin.(Compliance report)	17-09-2014	Satisfactory
390.	Irrigation (Water & Drainage), GOS	984	Construction of Surface Drainage Scheme in Deh Dethki in Union Council Shahmir Rahu Taluka New Saeedabad District Matiari.(compliance report)	05-11-2014	Average
391.	Irrigation (Water & Drainage), GOS	991	Sanction Link Drain for Drain Out Rainy/Surplus Water of Four Dehs Kas, Dhandh Dhabho, Ali Pur and Soomra, U.C. Mula Katiyar and Extension of Bukhari Link Drain at RD-8 to 16 & Dhandi Link Drain RD-10 to 16 Deh Seerani and Sathia, Taluka Bulri Shah K	19-11-2014	Average
392.	Irrigation (Water & Drainage), GOS	993	Construction of Road Bridges Over Bathoro Branch Drain at RD-88.0 1-1L Kapoor Branch Drain at RD-32.0. (compliance report)	01-12-2014	Satisfactory
393.	Irrigation (Water & Drainage), GOS	994	Surface Drainage Scheme of 20.0 Cusecs at U.C. Oderolal Station Deh Jakhiri Taluka Matiari and Jhando Mari Drainage Scheme on Right Side of West Branch.	05-09-2014	Average
394.	Irrigation (Water & Drainage), GOS	994	Surface Drainage Scheme of 20.0 Cusecs at U.C. Oderolal Station Deh Jakhiri Taluka Matiari and Jhando Mari Drainage Scheme on Right Side of West Jamrao Branch Tando Allahyar (Compliance Visit)	04-03-2015	Satisfactory
395.	Irrigation (Water & Drainage), GOS	995	Construction of Link of German Dhoro Outfall Drain from RD 0.0 to 15.0 Link of Jherruck Sub Drain from RD 0.0 to 15.0 Samki Link Drain of Ghorabari O/F Drain RD 0 to 15, water course X-ing/Road Bridge along Jam Sakro Outfall Drain RD 140.0 and Constr	11-11-2014	Un-Satisfactory



396.	Irrigation (Water & Drainage), GOS	997	Rehabilitation of Drainage Network and Allied Works in District Thatta (PS-88)	24-09-2014	Un-Satisfactory
397.	Irrigation (Water & Drainage), GOS	999	Construction of Link Drain at RD 0.0 to 25 out-falling in Seerani Branch Drain at RD 40 IP side for Village Pir Buksho and ARO Pusio, U.C Seerani; (ii) Construction of Link Drain RD 0.0 to 14 out-falling in 6-R Tando Bago Sub-Drain at RD 22 IP side f	15-10-2014	Un-Satisfactory
398.	Irrigation (Water & Drainage), GOS	1002	Construction of Ladiun Branch Drain System (Remaining Works).	17-11-2014	Average
399.	Irrigation (Water & Drainage), GOS	1004	Surface Drainage Scheme Deh Dalli Wadi Taluka & District Hyderabad.	05-12-2014	Satisfactory
400.	Irrigation (Water & Drainage), GOS	1015	REMOVING DEFICIENCIES & CONSTRUCTION OF REMAINING WORKS OF PHULL DAULATPUR DRAINAGE SCHEME, DISTRICT NAUSHAROFEROZE.	09-12-2014	Not Applicable
401.	Irrigation (Water & Drainage), GOS	1017	SURFACE DRAINAGE SCHEME IN DEH 28 & 38 DAD ,U.C CHANESAR-I , TALUKA NAWABSHAH, DISTRICT SHAHEED BENAZIRABAD.	12-12-2014	Not Applicable
402.	Irrigation (Water & Drainage), GOS	1018	REHABILITATION OF EXISTING SEEPAGE WELLS ALONG ROHRI MAIN CANAL OF DRAINAGE DIVISION LBOD, SHAHEED BENAZIRABAD	08-12-2014	Not Applicable
403.	Irrigation (Water & Drainage), GOS	1019	SURFACE DRAINAGE SCHEME FOR ACTIVATION OF DITCH CHANNEL PARALLEL TO JAMRAO CANAL IN DRAINAGE DIVISION LBOD, SHAHEED BENAZIRABAD.	11-12-2014	Not Applicable
404.	Irrigation (Water & Drainage), GOS	1020	REHABILITATION OF EXISTING SEEPAGE WELLS (JRS) ALONG JAMRAO CANAL OF DRAINAGE DIVISION LBOD, SHAHEED BENAZIRABAD	10-12-2014	Not Applicable
405.	Irrigation (Water & Drainage), GOS	1021	SURFACE DRAINAGE SCHEME IN DEH DINO SHAH, DEH 73 NASRAT & FARMABAD TALUKA DAUR & SAKRAND, DISTRICT SHAHEED BENAZIRABAD.	11-12-2014	Not Applicable
406.	Irrigation (Water & Drainage), GOS	1022	Rehabilitation of Existing Seepage Wells along RMC and Seepage Wells (JRS) along Jamrao, Construction of Village Road Bridge W/C aqueducts and Inlets at various point and Extension of existing Drains at different locations including Allied Structures	05-01-2015	Not Applicable
407.	Irrigation (Water & Drainage), GOS	1036	Installation of 100 new tube wells	25-02-2015	Average

408.	Irrigation (Water & Drainage), GOS	1039	Assuring Water Supply for Karachi upgrading Kinjhar Lake System (under Urban Water Supply).	14-04-2015	Satisfactory
409.	Irrigation (Water & Drainage), GOS	1040	Training Institute of Irrigation & Power Department Hyderabad.	08-07-2014	Average
410.	Irrigation (Water & Drainage), GOS	1043	Up-gradation & Construction of Compound Wall of Field Research Station at Kali Mori, Hyderabad.	08-04-2015	Satisfactory
411.	Irrigation (Water & Drainage), GOS	1049	Construction of Annexy District Shaheed Benazir Abad @ Nawabshah (A.D.P No. 1049)	09-05-2015	Satisfactory
412.	Irrigation (Water & Drainage), GOS	1051	Rehabilitation & Renovation of Office Buildings (i) Akram Wah Division Badin (ii) office of Rohri Canal Circle including inspection Bungalow Shahdadpur.	06-11-2014	Average
413.	Irrigation (Water & Drainage), GOS	1054	Sindh Water Sector Improvement Project Phase-I (WSIP-I) (Revised Cost Rs. 30,353 Million - World Bank Loan) (Ghotki / Khairpur / Sanghar / Mirpurkhas / T.M. Khan / Umerkot / Hyderabad / Badin / Kashmore / Sukkur).	18-09-2014	Average
414.	Irrigation (Water & Drainage), GOS	1061	ADP# 1061, 2014-15 Rehabilitation of Masu Wah (Brick Lining) RD. 100 to 107	01-04-2015	Average
415.	Irrigation (Water & Drainage), GOS	1064	Constructing of Pumping Station at RD-31 Kakole Branch and Construction of Bridge over Ganhwar Wah at RD - 10 near Village Ali Akbar Mugheri.	09-02-2015	Average
416.	Irrigation (Water & Drainage), GOS	1078	Renovation of VIP Rest House office Block and Boat Club at Keenjhar Lake of Hillaya Sub-Division.	21-08-2014	Satisfactory
417.	Irrigation (Water & Drainage), GOS	1079	Construction of 4 Nos. Bridges (i) Daru Branch RD-65 (ii) Baghan Bridge Deh Samme Jan U.C Karim (iii) Chorwah Village Ramzan Rind U.C Jhoke Sharif (iv) Fatya Wah Bridge Bathoro Canal Near Mehar Shah.hgf	25-09-2014	Average
418.	Irrigation (Water & Drainage), GOS	1084	Rehabilitation of Khesano Minor-II, Hadeki Disty from RD-0 to 53, Mell Minor Rd-0 to 25 & Lining of Noori Disty from RD-0 to 38.(Compliance report)	27-03-2015	Average
419.	Irrigation (Water & Drainage), GOS	1100	Construction of stone pitching along Rohri Main Canal in vulnerable reaches of Rohri, Dad & Hala Division.	27-01-2015	Un-Satisfactory

420.	Irrigation (Water & Drainage), GOS	1104	Adding Spans to Aral Regulator and Remodelling of Leading Channels.	16-10-2014	Average
421.	Irrigation (Water & Drainage), GOS	1109	C.C. Lining of New Shekhani Minor Ex-Rohri Main Canal at RD-829 IP Side, including Old Shekhani Minor, Chhar Minor & Tarah Tail.	07-08-2014	Satisfactory
422.	Irrigation (Water & Drainage), GOS	1117	Rehabilitation of Irrigation Channels & Infrastructure at Taluka Ghorabari District Thatta.	08-12-2014	Average
423.	Irrigation (Water & Drainage), GOS	1118	De-silting along Mithrao Canal (in different reaches).	13-01-2015	Un-Satisfactory
424.	Irrigation (Water & Drainage), GOS	1119	De-silting along Rohri Main Canal system from RD-891 to 1038 and its off-taking channels, Nasir Branch System from RD-0 to 80 and RD-247 to 354 and its off-taking channels including Repair/Reconstruction of Modules in Nasir Division Hyderabad	17-12-2014	Average
425.	Irrigation (Water & Drainage), GOS	1120	Construction of 06 Nos. Desalination / R.O. Plants around Manchhar Lake.	12-03-2015	Average
426.	Irrigation (Water & Drainage), GOS	1124	Lining of Darelo Minor RD-0 to 21.4 and Grhore Minor RD-0 to 26.20 (Tail Reaches) (Nara Canal A.W.B.)	26-02-2015	Average
427.	Irrigation (Water & Drainage), GOS	1126	Providing Stone Pitching along Daro Branch RD 0 to 50 and Pinyari Branch RD 130 to 145 both side (Pinyari Circle).	28-08-2014	Un-Satisfactory
428.	Irrigation (Water & Drainage), GOS	1127	Reconstruction of Head Regulator Daro Branch and Tail Regulator Daro Branch RD 168 and Protection Wall Town area along Pinyari Branch 0 to 6 both side (Pinyari Circle)	28-08-2014	Satisfactory
429.	Irrigation (Water & Drainage), GOS	1130	Retaining wall along Dadu Canal RD 598 to 608 NIP, 598 to 605 IP (Opposite Dadu Town-Regulator 85 mile D/S Retaining wall 04 RDs Both sides., Retaining Wall Mehar Branch RD 7 to 13 near Village Malook Kalhoro, X-Regulator 95th mile D/S retaining Wall	17-10-2014	Average
430.	Irrigation (Water & Drainage), GOS	1131	Construction of Pumping Scheme along MNV Drain for Feeding Tail of Pakka Disty and Khudabad Minor.	10-02-2015	Average
431.	Irrigation (Water & Drainage), GOS	1134	Earth Work and Stone Pitching along Faridabad Ring Bund RD-0 to 7.5	10-02-2015	Satisfactory

432.	Irrigation (Water & Drainage), GOS	1135	Re modelling / Re-sectioning of Branches, Minors	09-12-2014	Average
433.	Irrigation (Water & Drainage), GOS	1136	Pilot Project for Sealing of K.B Feeder Canal by Polymer	28-01-2015	Satisfactory
434.	Irrigation (Water & Drainage), GOS	1246	Construction of Recharge Dam Malirirri in Union Council Jhngara Taluka Sehwan District Jamshoro in Central Kohistan.(Compliance visit).	08-01-2015	Satisfactory
435.	Irrigation (Water & Drainage), GOS	1247	Construction of Kataro Weir Dam in Taluka District Thatta.	12-02-2015	Satisfactory
436.	Irrigation (Water & Drainage), GOS	1248	Construction of Mohan & Haleli Recharge Dam in Central Kohistan.(Compliance visit).	08-01-2015	Satisfactory
437.	Labour Dept, GOS	844	Construction & Reconstruction offices of Assistant Directors Labor Department in Sindh Province (5 units)	07-05-2014	Un-Satisfactory
438.	Labour Dept, GOS	844	Construction & Reconstruction offices of Assistant Directors Labor Department in Sindh Province (5 units)	15-05-2014	Average
439.	Labour Dept, GOS	845	Construction Repair of Office Building of Directorate of Labor Hyderabad Sukkur	09-06-2014	Average
440.	Labour Dept, GOS	1259	Construction of Buildings for Employment Exchange in Sindh (Phase-I)	26-02-2015	Average
441.	Labour Dept, GOS	1259	Construction of Buildings for Employment Exchange in Sindh (Phase-I)	08-01-2015	Average
442.	Livestock and Fisheries, GOS	889	Improvement of Existing Livestock Farms in Sindh.	21-08-2014	Un-Satisfactory
443.	Livestock and Fisheries, GOS	895	Strengthening of Viral and Protozoan Disease Diagnostic Facilities at Central Veterinary Diagnostic Laboratory (CVDL) Tando Jam	09-05-2014	Satisfactory
444.	Livestock and Fisheries, GOS	898	Establishment of Disease Control Zone of livestock in sindh	07-05-2014	Average
445.	Livestock and Fisheries, GOS	898	Establishment of disease control zone of livestock in sindh	14-04-2014	Satisfactory
446.	Livestock and Fisheries, GOS	910	Model Village for Fishermen at Hawksbay Karachi, Zero Point Badin, Manchar Lake & Keenjhar Lake Thatta	01-04-2014	Un-Satisfactory

447.	Livestock and Fisheries, GOS	914	Strengthening & Improvement of Fish & Shrimp Hatcheries in Sindh	05-03-2014	Un-Satisfactory
448.	Livestock and Fisheries, GOS	914	Strengthening & Improvement of Fish & Shrimp Hatcheries in Sindh.	01-04-2014	Average
449.	Livestock and Fisheries, GOS	1319	Establishment of Cattle Colonies with District and Private participation Phase-I	07-04-2015	Un-Satisfactory
450.	Livestock and Fisheries, GOS	1319	Establishment of Cattle Colonies with District and Private participation Phase-I	07-04-2015	Average
451.	Livestock and Fisheries, GOS	1320	Strengthening of Research & Training Institute for Livestock Dev.@ Tando Muhammad Khan	18-09-2014	Un-Satisfactory
452.	Livestock and Fisheries, GOS	1322	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic diseases in Sindh (Eight Districts).	29-05-2015	Satisfactory
453.	Livestock and Fisheries, GOS	1322	Pilot project on surveillance of Bovine Tuberculosis, Brucellosis and Zoonotic Diseases in Sindh (Eight District)	16-04-2015	Average
454.	Livestock and Fisheries, GOS	1322	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic diseases in Sindh (Eight Districts).	11-07-2014	Average
455.	Livestock and Fisheries, GOS	1322	Pilot Project on Surveillance of Bovine Tuberculosis, Brucellosis and other Zoonotic Diseases in Sindh.	31-10-2014	Average
456.	Livestock and Fisheries, GOS	1322	Pilot project on Surveillance of Bovine Tuberculosis, Brucellosis & other Zoonotic Diseases in Sindh	15-12-2014	Average
457.	Livestock and Fisheries, GOS	1322	Pilot project on Surveillance of Bovine Tuberculosis, Brucellosis & other Zoonotic Diseases in Sindh	18-12-2014	Average
458.	Livestock and Fisheries, GOS	1324	Strengthening of Sindh Poultry Vaccine Centre Korangi, Karachi	12-11-2014	Average
459.	Livestock and Fisheries, GOS	1325	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Sheds.	11-05-2015	Average
460.	Livestock and Fisheries, GOS	1325	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Sheds.	12-05-2015	Average
461.	Livestock and Fisheries, GOS	1325	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Sheds.	13-05-2015	Average
462.	Livestock and Fisheries, GOS	1325	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Controlled Atmosphere Shed.	22-06-2015	Un-Satisfactory
463.	Livestock and Fisheries, GOS	1325	Expansion of Poultry Hatcheries & Backyard Farming in Sindh, Including controlled atmosphere sheds	18-08-2014	Average
464.	Livestock and Fisheries, GOS	1325	Expansion of poultry hatcheries & backyard farming in Sindh including poultry controlled atmosphere sheds.	29-09-2014	Average

465.	Livestock and Fisheries, GOS	1326	Establishment of disease control zone of livestock in Sindh	30-10-2014	Average
466.	Livestock and Fisheries, GOS	1327	Establishment of Stationery and Mobile Veterinary Diagnostic lab. Units for disease confirmation and control in Milk and Meat zone of Sindh Province.	11-11-2014	Average
467.	Livestock and Fisheries, GOS	1328	Surveillance and characterization of circulating pathogens of poultry in Sindh including avian influenza containment program	19-08-2014	Average
468.	Livestock and Fisheries, GOS	1329	Establishment of Bio-safety level laboratories and Quality Enhancement Cell for highly pathogenic virus vaccine development	19-08-2014	Average
469.	Livestock and Fisheries, GOS	1331	The project on sustainable Livestock Development for Rural Sindh (Rs. 702.00 Million – ½ JICA Grant in Aid, Provincial contribution).	11-08-2014	Average
470.	Livestock and Fisheries, GOS	1331	The Project on sustainable livestock development for rural Sindh	23-12-2014	Average
471.	Livestock and Fisheries, GOS	1331	The project on sustainable Livestock Development for Rural Sindh (Rs. 702.00 Million – JICA Grant in Aid, Provincial contribution). – Compliance visit	27-05-2015	Un-Satisfactory
472.	Livestock and Fisheries, GOS	1338	Model Village for fishermen at hawksbay Karachi, Zero point Badin, Manchar Lake & Keenjhar Lake Thatta	24-03-2015	Un-Satisfactory
473.	Livestock and Fisheries, GOS	1339	Introduction of Culture of High Value Brackish Water Fishes in Sindh	11-09-2014	Un-Satisfactory
474.	Livestock and Fisheries, GOS	1339	Introduction of Culture of High Value Brackish Water Fishes in Sindh	24-09-2014	Un-Satisfactory
475.	Livestock and Fisheries, GOS	1339	Introduction of Culture of High Value Brackish Water Fish in Sindh	05-05-2015	Un-Satisfactory
476.	Local Government, GOS	55	Construction of paving block and surface drain at various street village Gosarji UC 20 Tamachani Sukkur. ADP.NO:55	10-06-2014	Un-Satisfactory
477.	Local Government, GOS	963	Widening Main Korangi Road Including Causeway from KPT Flyover to Korangi Crossing	16-06-2014	Satisfactory
478.	Local Government, GOS	979	Rehabilitation of Makrani Masjid Bunder Road Sukkur.	02-10-2014	Average
479.	Local Government, GOS	1001	Installation of Solar lights @ various parts of Sukkur(Sukkur, Pano Akil ,Salehpat & Rohri)	06-08-2014	Average

480.	Local Government, GOS	1007	Construction of Paving block in various streets of village Gulab Burir, Taluka Rohri.	27-06-2014	Average
481.	Local Government, GOS	1009	Construction of paving block and Surface Drain at Soomra Mohallah Loco Shed Rohri.	10-06-2014	Average
482.	Local Government, GOS	1036	Strengthening Plan of Infrastructure Nawabshah	21-10-2013	Satisfactory
483.	Local Government, GOS	1056	Constt of Surface Drains and CC Block at Balocah Colony	13-06-2014	Un-Satisfactory
484.	Local Government, GOS	1057	Constt of Main Drains and CC Block	13-06-2014	Average
485.	Local Government, GOS	1119	Constraction of Mehran Highway extenation from labour sequire to Qasim port road (Ph-II) (KMC).	06-12-2013	Satisfactory
486.	Local Government, GOS	1127	Rehabilitation of Road Secstor 35 and 36 Korangi Karachi (KMC).	11-12-2013	Satisfactory
487.	Local Government, GOS	1137	Construction of 0.5 Km dual road from Kiran Hospital road Chowrangi to KBACH Society Karachi. (KMC).	06-12-2013	Satisfactory
488.	Local Government, GOS	1206	Rehabilitation of RHC's at various Talukas at Sobhodero, Kingri, Faizganj & Thari Mirwah (04 Nos)	07-07-2014	Un-Satisfactory
489.	Local Government, GOS	1391	Construction of 3 Lane Flyover at Malir Halt at Shahrah -e-Faisal Karachi	10-09-2014	Satisfactory
490.	Local Government, GOS	1393	Construction of Road from Navy Wall to Chashma Goth in Bin Qasim Town (3 km)	16-12-2014	Satisfactory
491.	Local Government, GOS	1399	Construction /Renovation & Beautification of Mehran Markaz Building Sukkur	07-07-2014	Un-Satisfactory

492.	Local Government, GOS	1401	Construction of surface drains, mateling of road & supply of electricity & transformers @ various streets of iron market Golimar Sukkur.	16-07-2014	Average
493.	Local Government, GOS	1422	Rehab. of sewerage system in Clifton, Block-4, Karachi.	25-05-2015	Average
494.	Local Government, GOS	1434	Providing and Laying 54" dia main sewer for improvement of sewerage system from Lyari river to Godhra More of New Karachi, Town Karachi.	25-05-2015	Satisfactory
495.	Local Government, GOS	1440	Cnnstruction of C.C BLOCK & C.C Drains in various Villages of Taluka Ratodero PS	14-07-2014	Average
496.	Local Government, GOS	1442	Constt of Main Drains and CC Block from Burdi Mohalla to Ghareeb Abad disposal via Hamid Shah Colony U/C Bukhari Taluka Khairpur	03-06-2015	Average
497.	Local Government, GOS	1442	Construction of main drain and CC block from Burdi Mohalla to Gharibabad disposal via Hamid Shah colony UC Bukhair, taluka Khairpur.	09-09-2014	Un-Satisfactory
498.	Local Government, GOS	1443	Construction of drains and CC block at Katchi Abadis nearFaizabad Saleemabad and Bhatti Mohalla UC Jeelani, taluka Khairpur	30-06-2015	Average
499.	Local Government, GOS	1443	Construction of drains and CC block at Katchi Abadis nearFaizabad Saleemabad and Bhatti Mohalla UC Jeelani, taluka Khairpur	10-09-2014	Average
500.	Local Government, GOS	1505	Construction of Zulfiiqar Oil Tanker Parking Terminal Zulfiiqarabad Karachi (KMC).	09-09-2014	Satisfactory
501.	Local Government, GOS	1506	Rehabilitation of City roads of Badin i/c Side drains.	24-02-2015	Average
502.	Local Government, GOS	1511	Construction of 1.637 km dual road from Kiran Hospital road chowrangi to KBACH Society Karachi	10-09-2014	Average
503.	Local Government, GOS	1514	Construction of Road from Humazo Nizamani to Village Allah Dad Bhurgari (1.6 Km)	16-10-2014	Average



504.	Local Government, GOS	1517	Construction of road from Badin Sujawal road to village Fatehabad mile 0/0 - 1/2 (2 km)	16-10-2014	Un-Satisfactory
505.	Local Government, GOS	1518	Schemes for various roads (11 Kms.) in District Thatta.	11-09-2014	Un-Satisfactory
506.	Local Government, GOS	1520	Construction of Link Road from Chotiaryoon City to Old Village Takya Pir Aijaz Ali Shah Road Mile 0/0-1/0(1.60 km)	23-09-2014	Un-Satisfactory
507.	Local Government, GOS	1527	Constt: of road from Nagori Kanta of Yousuf Goth to Rice Mills (1 Km)	05-12-2014	Average
508.	Local Government, GOS	1529	Construction of Road in District Mirpurkhas (8KM)	05-09-2014	Average
509.	Local Government, GOS	1602	Construction of Retention Weir / Dam at Gajjan Khan Village, GADAP Town, Karachi.	09-09-2014	Un-Satisfactory
510.	Local Government, GOS	1605	Providing Solar Energy Lights for 09 (Rural) Union Councils of Taluka Khairpur	08-04-2015	Satisfactory
511.	Local Government, GOS	1605	Providing Solar Energy Lights for 09 (Rural) Union Councils of Taluka Khairpur	28-07-2014	Satisfactory
512.	Local Government, GOS	1606	Installation of Street Lights in various streets of Hindu Mohallah of Kashmore (Rs. 18.950 m. to be funded out of 10% Royalty Share)	30-04-2015	Satisfactory
513.	Local Government, GOS	1607	Providing & Fixing of Search / Street Light & Generator for SBB Cricket ground Dadu.	07-05-2015	Average
514.	Local Government, GOS	1611	ADP-1611 of 2014-15.Construction/Addition of Class Room in Existing Primary Schools of Taluka Sakrand & Nawabshah District Shaheed Benazirabad (08 Units)	06-05-2015	Satisfactory
515.	Local Government, GOS	1623	Rehabilitation and Construction / Re-construction of veterinary Hospital / Dispensaries and Centers in District Khairpur (39 Units) ADP.NO:1623	31-03-2015	Average

516.	Local Government, GOS	1657	Construction of New Eid Gah(12 Nos.)in various villages of Taluka Ratodero P S-37	21-08-2014	Average
517.	Local Government, GOS	1657	Construction of New Eid Gah(12 Nos.)in various villages of Taluka Ratodero P S-37	08-06-2015	Average
518.	Local Government, GOS	1659	Construction / Rehabilitation of Existing Mausoleums / Rehabilitation of Mosques and Remaining Works of Compound Wall of Imam Bargahs in Various Villages, Taluka Ratodero (9 Nos)	19-05-2015	Satisfactory
519.	Local Government, GOS	1660	Construction of Shaheed Mohammad Anwar Bhutto Memorial Library at village Bangul Dero, Taluka Ratodero	20-05-2015	Satisfactory
520.	Local Government, GOS	1661	Construction of Public Park at various places in Latifabad	24-10-2014	Average
521.	Local Government, GOS	1662	Construction of Eid Gah at Qazi Arif Town District Dadu	06-05-2015	Average
522.	Local Government, GOS	1662	Construction of Eid Gah including Mosque at Qazi Arif Town District Dadu	26-09-2014	Average
523.	Local Government, GOS	1665	Renovation / Rehabilitation of various Dargah damaged during rain 2012-	26-05-2015	Average
524.	Local Government, GOS	1666	Renovation / Rehabilitation of various Mosques and Madarsas damaged during rains 2012	27-05-2015	Satisfactory
525.	Local Government, GOS	1667	Rehabilitation/Renovation of jaral Shah Dargah at Larkana	22-08-2014	Satisfactory
526.	Local Government, GOS	1667	Rehabilitation/Renovation of jaral Shah Dargah at Larkana	10-06-2015	Satisfactory
527.	Local Government, GOS	1694	Water Supply Scheme Sardar Ahmed Shah	12-08-2014	Average

528.	Local Government, GOS	1695	Water Supply Scheme Khasai	13-08-2014	Average
529.	Local Government, GOS	1706	Improvement & Extension of water supply Scheme Bothro District Dadu	15-01-2015	Average
530.	Local Government, GOS	1730	Water Supply Scheme Nabi Sir Thar	07-04-2015	Average
531.	Local Government, GOS	1845	Drainage Scheme for village Kot Mirs Landhy U/C Imam Bux Taluka Kot Ghulam Muhammad District Mirpur Khas	27-01-2015	Un-Satisfactory
532.	Local Government, GOS	1849	Murad Memon Goth Drainage Scheme.	29-10-2014	Average
533.	Local Government, GOS	1879	Construction of RCC Covered Main Nala at various places (6 Nos) District Shahdadkot	05-05-2015	Average
534.	Local Government, GOS	1893	Development Scheme of NA 204 Larkana Construction of C.C drains i/c C.C blocks for various U.Cs.	18-11-2014	Average
535.	Local Government, GOS	1902	Construction of C.C drains i/c Brick CC Block in UC- 8,9,10&11 Larkana City	10-06-2015	Average
536.	Local Government, GOS	1922	Contruction of rural drainage scheme of new Balochabad housing society village Baloch Khan Jalbani Taluka Mirpur Mathelo	21-11-2014	Un-Satisfactory
537.	Local Government, GOS	1999	Greater Karachi Sewerage Plan (S-III) [Cost Rs. 7982.00 million with Federal Share of Rs. 3991.00 million]	09-04-2015	Average
538.	Local Government, GOS		Installation of R.O (Reverse Osmosis) Plants for the improvement of water supply in Keamari Town (12 Units visited).	08-04-2014	Satisfactory
539.	Local Government, GOS		Installation of R.O (Reverse Osmosis) Plants for the improvement of water supply in Lyari Town (Six Unit visited).	07-04-2014	Satisfactory

540.	Mines & Minerals, GOS	1248	E-Govt. Agency Specific General Application - Website on Geo-Data Phase-II setup of Geo-Data Centre	15-04-2014	Average
541.	Mines & Minerals, GOS	1253	Water Supply scheme for the Camp Office of D.G. M&MD at Nagarparkar including Rest House & Residence of staff of M&MD.	25-06-2014	Average
542.	Minorities & Affairs, GOS	2011	Construction Repair and Renovation Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs)	10-09-2014	Un-Satisfactory
543.	Minorities & Affairs, GOS	2011	Construction Repair and Renovation Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs).	03-10-2014	Satisfactory
544.	Minorities & Affairs, GOS	2011	Construction Repair and Renovation Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs).	31-10-2014	Un-Satisfactory
545.	Minorities & Affairs, GOS	2011	Construction Repair and Renovation Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs).	10-11-2014	Satisfactory
546.	Physical Planning & Housing (Buildings), GOS	338	Construction of 7 new Treasury Offices in Sindh	25-04-2014	Un-Satisfactory
547.	Physical Planning & Housing (Buildings), GOS	863	Construction of District Court Building at Matiari.	19-02-2014	Average
548.	Planning & Development, GoS	0	Procurement Of Solid Waste Collection Equipments (Trucks & Skips)-Lot-1 & Lot-2.	07-07-2014	Average
549.	Planning & Development, GoS	1267	Modernization / Rehabilitation and establishment of industrial units in rural areas through Public Private Partnership (Agro cluster program) Small & Medium Enterprises, (phase-i).	20-03-2014	Average
550.	Planning & Development, GoS	1268	Provision of Basic Health Facilities & primary health care For Poor populations	05-03-2014	Average
551.	Planning & Development, GoS	1268	To reduce maternal and infant morbidity and mortality To raise contraceptive prevalence by providing a range of quality of reproduction health services	11-03-2014	Average
552.	Planning & Development, GoS	1268	Filtration Plant for the Flood Affectees at Khairpur & Sukkur Regions (District Jacobabad) CDP	29-03-2014	Un-Satisfactory
553.	Planning & Development, GoS	1268	Filtration Plant for the Flood Affectees at Khairpur & Sukkur Regions (District Kashmore Kandhkot) CDP	20-03-2014	Un-Satisfactory

554.	Planning & Development, GoS	1268	Filtration Plant for the Flood Affectees at Khairpur & Sukkur Regions (district shikarpur) CDP	31-03-2014	Un-Satisfactory
555.	Planning & Development, GoS	1268	Filtration Plant for the Flood Affectees at Khairpur & Sukkur Regions(District Khairpur) CDP	17-04-2014	Un-Satisfactory
556.	Planning & Development, GoS	1268	Elementary School Through cluster Schools in District Shikarpur and Kashmore Kandhkot(District Kashmore)CDP	21-03-2014	Un-Satisfactory
557.	Planning & Development, GoS	1268	Elementary School Through cluster Schools in District Shikarpur and Kashmore Kandhkot(District Shikarpur) CDP	24-03-2014	Un-Satisfactory
558.	Planning & Development, GoS	1268	1.provid safe drinking water facility through installation of 160 hand pumps along with water testing	12-03-2014	Satisfactory
559.	Planning & Development, GoS	1268	Water and Sanitation Project Jacobabad (CDP)	28-03-2014	Satisfactory
560.	Planning & Development, GoS	1268	Economic empowerment of rural women through establishment of rally training centre and out let in city Jacobabad, district Jacobabad(CDP)	27-03-2014	Satisfactory
561.	Planning & Development, GoS	1268	Union Council Based Poverty Reduction Program Jacobabad (CDP Scheme)	08-04-2014	Satisfactory
562.	Planning & Development, GoS	1268	Provide Safe Drinking Water Facility Through installation of 250 hand pumps & Construction of 250 Pit Latrines.(CDP Scheme).	14-03-2014	Satisfactory
563.	Planning & Development, GoS	1268	CDP ADP # 1268 Improving the designs of quilts &Creating market Linkages of 200 Women	28-03-2014	Average
564.	Planning & Development, GoS	1268	Improved Personal Hygiene (Construction of Pit Latrines),(CDP Scheme)	11-03-2014	Satisfactory
565.	Planning & Development, GoS	1268	The establishment of Larkana Model School(LMS) @ UC-6 Larkana District Larkana	05-03-2014	Un-Satisfactory

566.	Planning & Development, GoS	1268	The establishment of Model School @ UC-7 Larkana District Larkana	06-03-2014	Average
567.	Planning & Development, GoS	1268	Provide Safe drinking water facility through installation of 350 Hand Pumps along with water testing & Construction of 350 Latrines in 10 villages. ADP # 1268	21-04-2014	Satisfactory
568.	Planning & Development, GoS	1268	Economic Empowerment of Rural Women Through Establishment of Ralli Training Center and Outlet. (CDP Scheme)	11-03-2014	Satisfactory
569.	Planning & Development, GoS	1282	Development Project for Bhit Shah Town. (Phase - II)	18-06-2014	Un-Satisfactory
570.	Planning & Development, GoS	2026	Community Development Program through Civil Society Organizations and others, including Corporate Sector (District Development Association Tharparkar (DDAT), establish of Multi skill development centre at Islamkot	08-04-2015	Average
571.	Planning & Development, GoS	2027	Expansion of Union Council Based Poverty Reduction Programme (Jacobabad)	23-06-2015	Satisfactory
572.	Population Welfare, GOS	1286	Population Welfare Program (2010-15) in Sindh	16-06-2014	Average
573.	Population Welfare, GOS	2041	Population Welfare Program Sindh (2010-15)	09-02-2015	Un-Satisfactory
574.	Population Welfare, GOS	2041	Population Welfare Program in Sindh (2010-2015)	18-02-2015	Average
575.	Population Welfare, GOS	2041	Population welfare Program in sindh (2010-2015)	25-02-2015	Average
576.	Provincial Ombudsman, GOS	1288	Construction of Provincial ombudsman Regional office um-Residences at Nawabshah.	10-02-2014	Un-Satisfactory
577.	Provincial Ombudsman, GOS	1288	Construction of Provincial Ombudsman Regional office cum-Residence in Sindh (3 Nos) At Larkana.	25-02-2014	Satisfactory
578.	Provincial Ombudsman, GOS	2048	Construction Provincial Ombudsman Regional Offices-cum-Residences (3 Nos.)at Mirpurkhas, Larkana and Nawabshah and purchase of plots (Headquarter and Nine 09 Regional Office Phase-I)	23-04-2015	Average

579.	Public Health Engineering, GOS	0	Drainage Scheme & CC Block for Village Ganwar Mashori,	10-07-2014	Satisfactory
580.	Public Health Engineering, GOS	487	Drainage Scheme for Village Saindad Banbhan P.O Halani, Taluka Mehrabpur. ADP # 487( 2011-12)	30-05-2014	Un-Satisfactory
581.	Public Health Engineering, GOS	1202	Basic facilities available or to be needed to make the Model Village Fatuhal Zardari U.C Gohram Mari, Taluka Sakrand, (Drainage Scheme)	25-10-2013	Un-Satisfactory
582.	Public Health Engineering, GOS	1202	Basic facilities available or to be needed to make the Model Village Fatuhal Zardari U.C Gohram Mari, Taluka Sakrand, (Water Supply Scheme)	25-10-2013	Un-Satisfactory
583.	Public Health Engineering, GOS	1293	Water supply scheme of various villages of Dumlotte & Kathore District Karachi.	16-06-2014	Average
584.	Public Health Engineering, GOS	1294	Bulk water supply scheme of various villages of Gadap Town, Karachi.	17-06-2014	Un-Satisfactory
585.	Public Health Engineering, GOS	1302	Urban W/S Scheme Thull Town. ADP # 1302.	25-06-2014	Average
586.	Public Health Engineering, GOS	1309	Improvement & Extension of Urban Water Supply Scheme Lakhi (Filtration).	25-03-2014	Average
587.	Public Health Engineering, GOS	1322	Imp: & Extension Water Supply Scheme Kamber Ali Khan. (Compliance Visit)	17-12-2013	Average
588.	Public Health Engineering, GOS	1327	Extension of Water Supply Scheme of Village Mori Manger, Shaikh Hafiz and Alam Abro Taluka & District Hyderabad (Modified)	27-06-2014	Satisfactory
589.	Public Health Engineering, GOS	1333	W/S Scheme of Allah Bux Katohar,	13-02-2014	Un-Satisfactory
590.	Public Health Engineering, GOS	1334	Water Supply Scheme of Tando Masti .	15-04-2014	Satisfactory

591.	Public Health Engineering, GOS	1335	Water Supply Scheme Syed Amir Ali Shah.	16-04-2014	Satisfactory
592.	Public Health Engineering, GOS	1336	Water Supply Scheme for Village Dhup Waro.	14-02-2014	Un-Satisfactory
593.	Public Health Engineering, GOS	1337	TRAIL BORING & PUMPING MACHINERY FOR DRIB MEHAR SHAH TALUKA KINGRI, DISTRICT KHAIRPUR.	11-04-2014	Average
594.	Public Health Engineering, GOS	1338	W/S Scheme of Arab Khan Katohar & adjoining village.	15-04-2014	Average
595.	Public Health Engineering, GOS	1339	Providing the Facility of Drinking Ground Water to Khairpur City (Remaining Areas 09 Villages)	07-04-2014	Satisfactory
596.	Public Health Engineering, GOS	1359	Providing Water Supply & Drainage Schemes @ various places of District Shaheed Benazir Abad.	10-11-2014	Average
597.	Public Health Engineering, GOS	1381	Water Supply Scheme for Village Haji Behram Khan Berhamani Deh 99 Nasrat U.C 60th Mile.	27-05-2014	Average
598.	Public Health Engineering, GOS	1382	Water Supply Scheme Deh-89 Nawabshah. ADP # 1382.	26-05-2014	Un-Satisfactory
599.	Public Health Engineering, GOS	1400	Urban Drainage Scheme Tando Allahyar.	10-04-2014	Un-Satisfactory
600.	Public Health Engineering, GOS	1402	Imp: & Ext: Drainage Scheme Kamber (Compliance Visit).	16-12-2013	Average
601.	Public Health Engineering, GOS	1409	Rehabilitation of Drainage Scheme Shah Ladhani.	21-05-2014	Average
602.	Public Health Engineering, GOS	1412	Improvement & Extension Drainage Scheme Karoondi.	20-03-2014	Un-Satisfactory



603.	Public Health Engineering, GOS	1414	Improvement & Extension of Drainage Scheme Banguldero.	24-02-2014	Un-Satisfactory
604.	Public Health Engineering, GOS	1415	Improvement & Extension of Drainage Scheme Naudero	25-02-2014	Satisfactory
605.	Public Health Engineering, GOS	1416	DRAINAGE SCHEME RATODERO	26-02-2014	Average
606.	Public Health Engineering, GOS	1417	Improvement & Extension of Drainage Scheme Dodai.	26-06-2014	Average
607.	Public Health Engineering, GOS	1418	Improvement & Extension of Drainage Scheme Hala Town	18-06-2014	Average
608.	Public Health Engineering, GOS	1419	Imp: & Ext: of Rural Drg: Scheme Dabhro Taluka Kandiaro.	21-04-2014	Un-Satisfactory
609.	Public Health Engineering, GOS	1419	Imp: & Ext: of Rural Drg: Scheme Dabhro Taluka Kandiaro.	19-06-2014	Un-Satisfactory
610.	Public Health Engineering, GOS	1420	Imp: & Ext: of Urban Drg: Scheme Mehrabpur Taluka Mehrabpur.	10-03-2014	Average
611.	Public Health Engineering, GOS	1421	Imp: & Ext: Drainage Scheme Naushero Feroze.	13-05-2014	Average
612.	Public Health Engineering, GOS	1423	Rehabilitation of Urban Drainage Scheme Tharo Shah.	20-06-2014	Un-Satisfactory
613.	Public Health Engineering, GOS	1426	Development of Infrastructure of District Badin Water supply & Drainage (Khoski, Pangrio, Kadhan and Lawari Sharif)	09-06-2015	Average
614.	Public Health Engineering, GOS	1430	Improvement and Extension of urban drainage scheme Jam Nawaz Ali Distt. Sanghar.	23-06-2014	Average

615.	Public Health Engineering, GOS	1431	Improvement & Extension of Drainage Scheme Garhi Yasin	19-02-2014	Average
616.	Public Health Engineering, GOS	1440	Rural Drainage Scheme Kamu Shaheed .	27-02-2014	Average
617.	Public Health Engineering, GOS	1441	Rural Drainage Scheme Likpur.	28-02-2014	Average
618.	Public Health Engineering, GOS	1441	Improvement & ext. of Drainage Scheme Phulpota UC Behmena, Taluka Ratodero PS-37	24-10-2014	Average
619.	Public Health Engineering, GOS	1442	Modified Disposal of Sewerage i/c Treatment Plant of Behar colony, Khanzada colony, Ghosia colony, Gareebabad colony etc. into river indus downstream of kotri city taluka kotri Distt. Jamshoro	24-06-2014	Un-Satisfactory
620.	Public Health Engineering, GOS	1444	Thull Drainage Scheme.	20-02-2014	Un-Satisfactory
621.	Public Health Engineering, GOS	1445	Water Supply Scheme of Arab Khan Katohar & adjoining village.	26-01-2015	Average
622.	Public Health Engineering, GOS	1458	Construction of Drains Schemes Doongries UC Mori.	22-05-2014	Average
623.	Public Health Engineering, GOS	1459	Construction of Surface Drains for Village Matla and Jumo Gadhi UC Mori.	29-04-2014	Satisfactory
624.	Public Health Engineering, GOS	1463	Drainage scheme village Sabab Abro District Naushero Feroze.	29-05-2014	Average
625.	Public Health Engineering, GOS	1479	Constt of CC Block and CC Drains at various villages (3 Nos) District Hyderabad	20-06-2014	Un-Satisfactory
626.	Public Health Engineering, GOS	1491	CC Blocks at Asif Colony Bachal Shah Miani. ADP # 1491.	09-07-2014	Average

627.	Public Health Engineering, GOS	1711	Providing / Installation of R.O Plant at Village Manzoor Ali Khan Pitafi District Tando Allah Yar	04-09-2014	Average
628.	Public Health Engineering, GOS	1737	Improvement & Extension of Water Supply Scheme Bhirya City (Under Revision)	11-09-2014	Average
629.	Public Health Engineering, GOS	1739	Improvement & Extension of Rural Water Supply Scheme Bahu Khoso, Taluka Thull.	27-08-2014	Average
630.	Public Health Engineering, GOS	1742	Constt. of Water Supply Scheme of various villages (15 Nos villages at District Kamber @ Shahdadkot)	09-01-2015	Average
631.	Public Health Engineering, GOS	1746	Water Supply Scheme of Allah Bux Katohar.	14-01-2015	Average
632.	Public Health Engineering, GOS	1747	Water Supply Scheme of Tando Masti.	07-01-2015	Average
633.	Public Health Engineering, GOS	1748	Water Supply Scheme for Village Dhupwaro.	25-02-2015	Average
634.	Public Health Engineering, GOS	1754	W/S Scheme for Village Haji Behram Khan Birhmani, Deh 99 Nasart UC 60th Mile, Taluka Daur.	25-03-2015	Average
635.	Public Health Engineering, GOS	1879	Construction of RCC Covered Main Nala at various places (6 Nos) District Shahdadkot	30-10-2014	Average
636.	Public Health Engineering, GOS	1880	Drainage Scheme CC Block & Drains for Shahdad Kot City	30-10-2014	Un-Satisfactory
637.	Public Health Engineering, GOS	1882	Extension & Rehabilitation of Drainage Scheme for Kot Diji Kot Banglow.	22-12-2014	Un-Satisfactory
638.	Public Health Engineering, GOS	1885	Construction of Drainage System at Dargah Astan-e-Alia Miskeenpur (Mehran Sari)	26-02-2015	Average

639.	Public Health Engineering, GOS	1886	Construction of Drains Schemes Doongries UC Mori.	20-03-2015	Satisfactory
640.	Public Health Engineering, GOS	1887	Drainage Scheme Syed Amir Ali Shah	23-12-2014	Average
641.	Public Health Engineering, GOS	1890	Imp: & Ext: of Drainage Scheme New Gud UC Purano Abad Taluka Bakrani.	18-11-2014	Average
642.	Public Health Engineering, GOS	1891	Construction of C.C drains i/c Brick pavement & CC Block for various villages of Taluka Dokri	23-09-2014	Average
643.	Public Health Engineering, GOS	1892	C.C Drains I/CC Blocks in various Muhalla of UC-7Larkano City	23-10-2014	Average
644.	Public Health Engineering, GOS	1894	Construction of C.C Block and CC Drains in various Villages of Taluka Rato Dero (10 villages).	08-12-2014	Average
645.	Public Health Engineering, GOS	1895	Construction of C.C Block and CC Drains in various Villages of Taluka Rato Dero (9 villages).	17-11-2014	Average
646.	Public Health Engineering, GOS	1896	Construction of C.C Block and C.C Drains (Open Drains) in UC-I and UC-II Taluka Rato Dero	18-11-2014	Average
647.	Public Health Engineering, GOS	1897	Construction of C.C Drains and CC Block in various Colonies/Muhallas of Rato Dero Town, Garhi Khuda Bux Bhutto & Bungul Dero	09-12-2014	Average
648.	Public Health Engineering, GOS	1898	Construction of C.C. Drains and C.C. Block of various U.C's of PS-38 Taluka District Larkana.	17-11-2014	Average
649.	Public Health Engineering, GOS	1902	Construction of C.C drains i/c Brick CC Block in UC- 8,9,10&11 Larkana City	22-09-2014	Average
650.	Public Health Engineering, GOS	1905	Improvement & Extension of Urban Drg: Scheme Mehrabpur Taluka Mehrabpur	13-02-2015	Average

651.	Public Health Engineering, GOS	1911	Drainage Scheme Village Moledino Rajper	16-01-2015	Average
652.	Public Health Engineering, GOS	1923	Rehabilitation of Drainage of Village Gharhi Hassan.	16-10-2014	Satisfactory
653.	Public Health Engineering, GOS	1926	CC Blocks at Asif Colony Bachal Shah Miani.	18-02-2015	Average
654.	Rural Development, GOS	1529	Construction of road at village Ak Macchi to Dhani Bux Sattar Dino Bachal Khaskheli District Matiari Phase I	20-06-2014	Un-Satisfactory
655.	Rural Development, GOS	1678	Constt: of C.C Topping in Village Ghulam Nabi Brohi and Ismail Brohi UC Jam Sahib Taluka Daur.(ii) C.C Topping in Village Pheroze Shah Pharsi UC Ismail Khan Brohi & Ali Murad Brohi UC Jam Sahib Taluka Daur. (iii).C.C Topping in Ward No: 3,7,8, UC Dau	11-11-2014	Average
656.	Rural Development, GOS	1687	Mobile Water Testing and safety measuring advisory project	06-01-2015	Satisfactory
657.	Rural Development, GOS	1691	Construction of C.C Topping, Brick Pavement & Open Surface Drain (Drainage System) Water Tank In (i) Ghareeb Abad U/C Daur, (ii) Village Aitabar Khan Rind U/C Jamal Shah, (iii) Village Wali Mohammad U/C Abul Hassan, (iv) Village Foji Mohammad Siddiqu	13-11-2014	Average
658.	Sindh Board of Investment (SBI)	1566	Investment Promotion in Sindh.	12-05-2014	Un-Satisfactory
659.	Sindh Board of Investment (SBI)	1567	Marketing of Sindh for attracting Investment (Under Revision).	12-05-2014	Un-Satisfactory
660.	Sindh Board of Investment (SBI)	1573	Revival of Sick Industrial units.	12-05-2014	Un-Satisfactory
661.	Sindh Board of Investment (SBI)	2104	Revival of sick industrial units Rs 2000 Million Phase -II	12-05-2015	Un-Satisfactory
662.	Social Welfare, GOS	1578	Establishment of Darul Aman @ district Mohtarma Shaheed Benazirabad.	11-02-2014	Average
663.	Social Welfare, GOS	2107	Economic empowermenal girlurt support to urban & ruralgirls,women & handicapped through out sindh	18-06-2015	Un-Satisfactory
664.	Social Welfare, GOS	2108	Capacity building of the officers & officials of social welfare department, Government of Sindh.	10-09-2014	Un-Satisfactory

665.	Social Welfare, GOS	2111	Establishment of Community Development Center for She Male Person 03 Units in Sindh.	17-02-2015	Average
666.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 1 IV ) Title of Project for WWF-P: Integrated approach to skill development & provision of sustainable livelihood.	26-03-2014	Average
667.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 2 II ) Title of Project for Larr Development Association (LDA): Reduce the intensity of water born & epidemic diseases by providing	08-04-2014	Satisfactory
668.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 2 1/2 II ) Title of Project for GSSA: 1/2 Safe Drinking Water & Sanitation Project in rural areas of District Dadu	22-04-2014	Satisfactory
669.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 2 1/2 II ) Title of Project for WWF-P: 1/2 Water filtration plants for providing clean drinking water to the flood affected 1/2 . Location:	18-04-2014	Un-Satisfactory
670.	Special Initiatives Unit, GOS	1268	ADP#: 1268 Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 2 II ) Title of Project for SAFWCO: 2 Water filtration plants for providing clean drinking water to the flood affected	23-04-2014	Un-Satisfactory
671.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 1 IV ) Title of Project for Fatimid Foundation: 1 Blood screening & provide 500 safe blood to the population of Tando Allah Y	25-04-2014	Satisfactory
672.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 1 1/2 1/2 IV ) Project Title for BASIC Development Foundation: 1/2 Economic Empowerment of Rural Craftswomen through	05-05-2014	Satisfactory
673.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 1 1/2 1/2 III ) Project Title for Basic Urban Services for Katchi Abadies (BUSTI): 1/2 Participatory WASH Developmen	17-05-2014	Satisfactory
674.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Phase 1 II, III & IV ) Title of Project for LRBT: 1 Eye Surgeries & Sight restoring cataract surgeries of poor people of Sindh 1	27-05-2014	Satisfactory
675.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector. Project Title for Indus Rural Development Organization (IRDO): 1/2 Gender Information Technology Centre under Skill Development / Women Empo	09-06-2014	Satisfactory
676.	Special Initiatives Unit, GOS	1268	Community Development Program (CDP) through Civil Society Organizations and others, including Corporate Sector (Green Sahara Foundation)	19-06-2014	Average
677.	Special Initiatives Unit, GOS	2118	Establishment of Drinking Water Hubs (Phase-II) for 750 Units (Khairpur)	12-08-2014	Un-Satisfactory

678.	Special Initiatives Unit, GOS	2118	Establishment of Drinking Water Hubs (Phase-II) for 750 Units (Nausheroferoze)	20-08-2014	Average
679.	Special Initiatives Unit, GOS	2118	Establishment of Drinking Water Hubs (Phase-II) for 750 Units( Shikarpur)	05-08-2014	Average
680.	Special Initiatives Unit, GOS	2118	Establishment of Drinking Water Hubs (Phase-II) for 750 Units( Qamber Shahdadkot)	28-08-2014	Satisfactory
681.	Special Initiatives Unit, GOS	2118	Establishment of Drinking Water Hubs (Phase-II) for 750 Units.(Larkana)	29-08-2014	Satisfactory
682.	Sports & Youth Affairs, GOS	1597	Construction of Sports Stadium in Sindh (8 Nos)(Districts) Hala, Kotri, Tandojam, Mithi Sanghar, Shikarpur, Jacobabad & Tando Allahyar (Part-I).(under revision)	19-05-2014	Average
683.	Sports & Youth Affairs, GOS	1597	Construction of Sports Stadium in Sindh (8 Nos.) @ Shikarpur	18-04-2014	Un-Satisfactory
684.	Sports & Youth Affairs, GOS	1600	Construction of Sports Stadium covering remaining District in Sindh (08 units) Nausheroferoz, Khairpur, Ghotki, Kamber, Kashmore, Dadu, T.M. Khan and Matiari	17-04-2014	Un-Satisfactory
685.	Sports & Youth Affairs, GOS	1600	Construction of Sports Stadium covering remaining District in Sindh (08 units) Nausheroferoz, Khairpur, Ghotki, Kamber, Kashmore, Dadu, T.M. Khan and Matiari	22-04-2014	Average
686.	Sports & Youth Affairs, GOS	1618	Construction/ Rehabilitation of Bakhtawar Sports Pavilion /Mini Stadium Naudero District Larkana.	26-02-2014	Average
687.	Sports & Youth Affairs, GOS	1618	Construction/ Rehabilitation of Bakhtawar Sports Pavilion /Mini Stadium Naudero District Larkana.	26-02-2014	Average
688.	Sports & Youth Affairs, GOS	1621	Laying of Synthetic Hockey Turf at Railway Ground Sukkur. ADP # 1621	19-03-2014	Satisfactory
689.	Sports & Youth Affairs, GOS	1628	Construction of Sports Complex Thatta.	13-05-2014	Average
690.	Sports & Youth Affairs, GOS	2128	Construction of Sports Stadium in Sindh (8 Nos) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar) (Under Revision	01-10-2014	Average
691.	Sports & Youth Affairs, GOS	2132	Construction of Pavilion and Seating facilities for Football Stadium at Baldia and Boxing Facilities at Lyari-Baldia	27-02-2015	Average
692.	Sports & Youth Affairs, GOS	2132	Construction of Pavilion and Seating facilities for Football Stadium at Baldia and Boxing Facilities at Lyari.	18-03-2015	Average
693.	Sports & Youth Affairs, GOS	2148	Construction of Gama Sports Stadium at Mirpurkhas (Revised)	20-10-2014	Average
694.	STEVT, GOS	1649	Establishment of Monotechnic Institute at Garhi Khuda Bux ADP # 1649	26-06-2014	Un-Satisfactory
695.	STEVT, GOS	1650	Establishment of Vocational Training Centre at Kashmore ADP # 1650	13-06-2014	Un-Satisfactory
696.	Tourism, GOS	1655	Establishment of Motel at Nagarparkar District Tharparkar (Revised)	25-06-2014	Average
697.	Tourism, GOS	1661	Construction of motel / Hotel at Garhi Khuda Bux Bhutto (Larkana)	07-02-2014	Un-Satisfactory

698.	Tourism, GOS	1664	Development of the Summer Resorts at Gorakh Hills District Dadu, Sindh	16-05-2014	Average
699.	Transport & Comm. (Roads), GOS	2212	Construction of Bus Terminals in Thatta & Badin, and Kamber Shahdadkot at Miro Khan.	16-04-2015	Average
700.	Women Development, GOS	1670	Establishment of Women Complaint Cells in Sindh for Aid to Women in Distress.	24-02-2014	Un-Satisfactory
701.	Women Development, GOS	1670	Establishment of Women Complaint Cells in Sindh for Aid to Women in Distress.	28-02-2014	Un-Satisfactory
702.	Women Development, GOS	2215	Establishment of Sales & Display Resource Centre at Karachi.	13-11-2014	Un-Satisfactory
703.	Women Development, GOS	2216	Establishment of Day Care Centre at Karachi	10-09-2014	Satisfactory
704.	Women Development, GOS	2217	Establishment of women Complaint Cells in Sindh for aid to women in distress	01-10-2014	Average
705.	Women Development, GOS	2376	W/R of Road from Adilpur to Mathelo mile 0/0-7/0 (11.20 Kms)	08-08-2014	Average
706.	Work and Service, GOS	52	Construction of link road from Makhdoom Ghulam Muhuddin Colony/Essani street (Manoo Machi) to Khanth road via irrigation katcha bund Road mile 0/0-2/4.	23-10-2014	Worst
707.	Work and Service, GOS	95	Construction of O/H bridge at Pano Akil Cantt phatak no. 01 (Mahar Bazar) Railway crossing Pano Akil	12-03-2015	Satisfactory
708.	Work and Service, GOS	121	Establishment of Makhdoom Khuhra Museum & Library at Dargah Makhdoom Khuhra Sharif District Khairpur	28-05-2015	Worst
709.	Work and Service, GOS	711	Construction of Basic Health Unit at Village Ashraf Samoon, Taluka Talhar, District Badin	26-05-2015	Average
710.	Work and Service, GOS	712	Construction of Basic Health Unit at Village Haji Ramzan Chandio, Taluka Matli, District Badin	26-05-2015	Un-Satisfactory
711.	Work and Service, GOS	1114	ADP # 1114 of 2013-14 Construction of Roads/ Side Drains/ CC Blocks and pavers of Khairpur City	11-11-2013	Average
712.	Work and Service, GOS	1510	Construction of Overhead Bridge over main Railway line at Tehri Phatak along National Highway Khairpur city	13-08-2014	Satisfactory



713.	Work and Service, GOS	1540	Widening and Reconditioning of Link Road from National Highway (East) to Shah Waliullah Oriental College Mansoorah Road Mile 0/0-2/4	23-10-2014	Un-Satisfactory
714.	Work and Service, GOS	1597	ADP No 1597 (2013-14) Construction of Sports stadium in Sindh (8Nos) Jacobabad Component	23-04-2014	Un-Satisfactory
715.	Work and Service, GOS	1690	Improvement/Realignment of curves of existing roads Unit No. (8) Improvement/Realignment of curves approaches along Sanghar Khipro off-taking road mile 15/0-15/1+330ft. (0.30 KMs)	29-05-2014	Worst
716.	Work and Service, GOS	1692	Construction of Various roads in Sindh 90.0 Kms.	10-12-2013	Average
717.	Work and Service, GOS	1692	Construction of Various roads in Sindh (90km), District Matiari (3 unit visited)	05-12-2013	Average
718.	Work and Service, GOS	1736	W/R of road from Bossan to ratodero Jacobabad road mile 0\0-10\0 (16.10 Kms.)	31-03-2014	Un-Satisfactory
719.	Work and Service, GOS	1747	W/R of road from 60th Mile to Packi Chowdagi via Bachehri road mile 0/0-10/3=(16.69 km)	26-05-2014	Average
720.	Work and Service, GOS	1754	W/R of road from Umerkot to Kunri mile 0/0-21/2 (34.19 Kms)	27-06-2014	Average
721.	Work and Service, GOS	1755	Widening/ Reconditioning From Kandiaro Tharushah via Darbelo Road Mile 0/0-12/0. (19.30 Km)	19-06-2014	Average
722.	Work and Service, GOS	1759	Improvement of Road, Manhero road to vill Ghulam Panjabi road mile 0/0-8/1 (13.07km)	27-05-2014	Average
723.	Work and Service, GOS	1767	Reconditioning/Construction of road from Old N.H way Phulpota Pahore via Lashari Road Mile 0/0-2/2.	16-05-2014	Average
724.	Work and Service, GOS	1780	W/R of road from Salehpat to Sikandarabad mile 0/0 " 25/2 (40.54 Kms)	13-05-2014	Un-Satisfactory
725.	Work and Service, GOS	1791	W/R of road from Thari Mirwah Bozdar Wada Road Mile 0/0-8/0.	18-06-2014	Average
726.	Work and Service, GOS	1797	Improvement of road from Sukkur bye pass to Sukkur Airport via airport bye pass i/c link to airport Bagerji road mile 0/0 " 1/5 with 2" Asphalt.	16-05-2014	Satisfactory
727.	Work and Service, GOS	1798	W/R of road from Lakhi Shikarpur road to Shikarpur Larkana road (Shikarpur Bye Pass) mile 0/0-6/0 (9.66 Kms.)	23-06-2014	Average
728.	Work and Service, GOS	1821	W & R of road from Karachi "Thatta-Hyderabad road to Jhampir mile 0/0-16/0	20-05-2014	Satisfactory
729.	Work and Service, GOS	1824	Reconditioning of road from Mian Shoro via Kally Bux Rind Sakrand City road mile 0/0-3/5	28-05-2014	Average
730.	Work and Service, GOS	1825	Reconditioning of road from Daleel Dero to Allah Dito Rind road mile 0/0-2/2	20-06-2014	Average

731.	Work and Service, GOS	1849	W/R OF ROAD FROM ADILPUR QAZI BADAL ROAD TO DARI CHACHAR MILE 0/0-2/0 (3.20 KMS).	04-06-2014	Average
732.	Work and Service, GOS	1852	W/R OF ROAD FROM UBAURO TO RETTI MILE 0/0-6/4 (10.45 KMS)	05-06-2014	Un-Satisfactory
733.	Work and Service, GOS	1853	W/R OF ROAD FROM RETTI TO KAMOON SHAHEED MILE 0/0-8/5 (13.88 KMS)	05-06-2014	Un-Satisfactory
734.	Work and Service, GOS	1856	Rehabilitation of road (Dual Carriage Way) roads Begam Nusrat Bhutto Secreteriat Road Mile 0/0-0/1+330 . (0.30 Km).	22-07-2014	Average
735.	Work and Service, GOS	1860	widening/Reconditioning of Bakrani Bridge to Dokri Via Mehrabpur and Z.A Bhutto Agriculture College mile 0/0-6/2 (10.06 KMS).	06-03-2014	Average
736.	Work and Service, GOS	1866	Improvement of road from Bhan Talti road mile 0/0-6/0 (9.6 Kms)	20-10-2014	Satisfactory
737.	Work and Service, GOS	1905	Improvement / Reconditioning of Larkana Circular road mile 0/0-10/0 (16.00 KMS).	15-05-2014	Satisfactory
738.	Work and Service, GOS	1906	Widening / Reconditioning of road from Larkana Naudero to Koreja Via Saidudero Pitaffi road mile 0/0/-4/2. ( 6.83 Km½s)	14-05-2014	Average
739.	Work and Service, GOS	1963	Construction of Badin Khoski Road at point Scape to Lawari Nando Road Via Noor Muhammad Farooqi Mile 0/0-6/0	28-11-2014	Average
740.	Work and Service, GOS	1965	Construction of road from Khalifo Qasim Æ€ Jhudo road to Olya Khan Shah road via Talib Odejo and Noor Kiryo mile 0/0-6/4 (10.45 Kms)	14-02-2014	Average
741.	Work and Service, GOS	1979	Construction of road from Bhango Pholri road (Ameer Poto) to village Ghulam Rasool Janwari via Kamalo Bhango Haji Murad Burdi Pir Bux Rajper & Kalhora village Mile 0/0-7/4.	07-05-2014	Un-Satisfactory
742.	Work and Service, GOS	1981	Construction of road from Gul Mohammad village to Ghulam Nabi Jodh via Khadim Kharal Road Mile 0/0-5/0. (8.04 Km).	08-05-2014	Average
743.	Work and Service, GOS	1983	Construction of road from Ripri Baharo to Ramzan Ja Pirr. 0/0 - 6/0 mile	16-05-2014	Un-Satisfactory
744.	Work and Service, GOS	1984	Construction of road from Badeh to Radhan Village Via Seehar Railway Station along Sehwani Sarak mile 0/0-12/0 (19.31 Kms).	06-03-2014	Un-Satisfactory
745.	Work and Service, GOS	1990	CONSTRUCTION OF ROAD FROM VASS TO MATTO MANGRIO MILE 0/0 Åžã, -ã€œ 12/4.	14-03-2014	Average
746.	Work and Service, GOS	1993	CONSTRUCTION OF ROAD FROM VILLAGE WATER MALANO TO VILLGE BHAMBHO MALANO TO VILLAGE DHANI BUX MALIK.TO VILLAGE ADAM GOPANG VIA THATH MINOR MILE 0/0 -4/0 (6.44 KMS)	26-11-2013	Average
747.	Work and Service, GOS	2021	Construction of Sindh Coastal Highway Sakro / Gaghar Phatak - Ketri Bandar - Shah Ghorabari/ Bunder - Ali Bunder (Ghaghar Phatak - Ketri Bunder Phase-1) of 90.0 Kms	15-05-2014	Satisfactory
748.	Work and Service, GOS	2055	Construction of road from Badin Sujawal Road at Mile 28/4 to Rasheed abad Mile 0/0-3/1 =5.0 Kms	21-07-2014	Average

749.	Work and Service, GOS	2101	Construction of Mirpurkhas By pass road connect Hyderabad road Tando Adam road Khan road and Sindhri road with over head bridge near Ratanabad Road Mile 0/0-11/0 (M) = 17.71 Kms .	24-06-2014	Un-Satisfactory
750.	Work and Service, GOS	2186	Construction of road from Jafar Boohar to Dargah Shah Qadir Mile 0/0-0/5 (1.00 Kms)	06-05-2014	Average
751.	Work and Service, GOS	2187	Construction of road shah kapoor road to Haji Juman Khoso road mile 0/0-0/5 =(1.0 Km)	06-05-2014	Un-Satisfactory
752.	Work and Service, GOS	2242	Scheme proposed by the MPA's of District Sanghar.	13-04-2015	Average
753.	Work and Service, GOS	2249	Widening / Reconditioning Hala " Shahdadpur " Sanghar with asphalt surface Mile 0/0-43/1 = (69.58 Km)	14-01-2015	Un-Satisfactory
754.	Work and Service, GOS	2250	Construction / Improvement of road from Ruk Garhiyaseen amrot new Sharo Abro Mile 0/0-12/2 (19.6 Km)	12-08-2014	Un-Satisfactory
755.	Work and Service, GOS	2264	Widening & Construction of road from Chota Gate to Abdul Karim Gabol and village Faiz Muhammad Gabol via Haji Ali Bux Gabol village mile 0/0-3/6 (6.00 Kms)	18-08-2014	Average
756.	Work and Service, GOS	2265	W.R of road from 68th mile Mori to 3 Chak via wasni Bitt road mile 0/0-12/0 (19.30 Kms).	18-08-2014	Average
757.	Work and Service, GOS	2271	W/R of road from Ghulam Bund to Dhandhi Sangrar via Fakirabad mile 0/0 - 10/0 (16.09 Kms)	08-07-2014	Average
758.	Work and Service, GOS	2273	W/R of National Highway Chandan Escape to Oderolal station Via Deh dari road Mile 6/1-14/1.	02-10-2014	Average
759.	Work and Service, GOS	2275	W/R of road from Main Mirpurkhas - Mirwah road to meet Mirwah - Kot Ghulam Muhammad road via Mir Khalid Landhi mile 0/0-17/0	24-12-2014	Average
760.	Work and Service, GOS	2280	Reconditioning of road from Kashmore to Badani via Gehlapur mile 0/0-20/0 (32.18 Kms.)	26-09-2014	Un-Satisfactory
761.	Work and Service, GOS	2287	Improvement of Hyderabad Tando Fazal Seri Road Mile 2/0-24/0	08-07-2014	Average
762.	Work and Service, GOS	2302	W/R of Johi Bhan road 0/0-11/4 (18.40 Kms)	07-01-2015	Average
763.	Work and Service, GOS	2303	Improvement of road from Indus Highway old alignment mile 5/6-17/4 (18.92 KM Asphalt)	20-10-2014	Average
764.	Work and Service, GOS	2318	Improvement of road from Mirpurkhas - Sindhri road to Khan road via Lal Chand Bungalow mile 0/0-8/0 (12.88 Kms)	12-09-2014	Average
765.	Work and Service, GOS	2319	Reconditioning of road from Matiar- Nasarpur road to village Kot Zainul Abidin Shah road mile 0/0-3/1	15-07-2014	Average
766.	Work and Service, GOS	2325	IMPROVEMENT / CONSTRUCTION OF ROAD FROM KHANPUR ROAD TO VILLAGE ABDUL SATTAR VIA VILLAGE ABDUL SATTAR VIA VILAGE CHANGLANI & AHMED RAJWAH MILE 0/0-2/4 (4.00 KMS).	15-09-2014	Average

767.	Work and Service, GOS	2326	Improvement of road from Sindh Jamat Cooperative Housing Society Qaidabad and Charan Para over head Tank Meena Mosque, Ibrahim Hydery (5Kms) mile 0/0-3/1.	13-11-2014	Average
768.	Work and Service, GOS	2326	Improvement of road from Sindh Jamat Cooperative Housing Society Qaidabad and Charan Para overhead Tank Meena Mosque, 5 Kms	05-06-2015	Satisfactory
769.	Work and Service, GOS	2329	Widening/ Reconditioning of road from Indus Highway to Aminani Sharif via Cattle Farm road mile 0/0-5/0(8 Km) (To be funded out of 10% Royalty share)	19-11-2014	Average
770.	Work and Service, GOS	2330	Reconditioning of road from Punj Mori to village Jhalo mile 0/0-6/4 (10.4Km) UC Siyal (To be funded out of 10% Royalty share)	20-11-2014	Average
771.	Work and Service, GOS	2334	Reconditioning of road from Chatto Mori to Jhumiro Mori via village Haji Mohammad Ramzan Chandio road mile 0/0-5/2 (8.45 Kms)	16-04-2015	Average
772.	Work and Service, GOS	2335	W/R of road from Khorwah to Khorwah Chowk mile 0/0-8/0 (12.88)	07-11-2014	Un-Satisfactory
773.	Work and Service, GOS	2338	Improvement of road from Talhar By Pass (Badin road to Tando Bago road) mile 0/0-1/0 (1.61 Kms).	06-11-2014	Average
774.	Work and Service, GOS	2339	Improvement of road from Talhar Bye Pass (Hyderabad road to Tando Bago road) road mile 0/0-3/6 (6.03 Kms).	11-11-2014	Un-Satisfactory
775.	Work and Service, GOS	2347	W/R of road Thana Bula Khan Bypass mile 0/0-2/4 (4.00 Kms).	23-04-2015	Average
776.	Work and Service, GOS	2354	Reconditioning of road from village Morio Meerbahar to Molidino Mirbahar road mile 0/0-3/0 (4.83 Kms)	02-02-2015	Average
777.	Work and Service, GOS	2357	W/R of road from Chamber to Hyderabad Gulab Laghari Shaikh Bhirkio road via Miran Khorri Jalal Mori including links to village Abdul Rehman Memon and Riaz Memon 0/0-12/4 (20.12 Kms)	03-10-2014	Average
778.	Work and Service, GOS	2391	Improvement / Construction of Road from New Bus Terminal to village Bilawal Khoso mile 0/0-1/0 (1.609 Km) (i/c C.C Block).	06-04-2015	Average
779.	Work and Service, GOS	2391	Construction of road from New Bus Terminal to Village Bilawal Khosso mile 0/0 - 1/0 (1.609 Kms)	21-07-2014	Average
780.	Work and Service, GOS	2400	W/R of Road from Saeedabad to Shaheed Banzariabad Road including Bridge over Rohri Canal Mile 6/0-25/0 (30.57 Km)	19-08-2014	Average
781.	Work and Service, GOS	2403	Improvement/Repair of Road from Baghan Jangesser Road to M. Hussian Otho via Dargah Khair Shah Mile 0/0-3/6 (6.0 Km)	31-12-2014	Average
782.	Work and Service, GOS	2412	W/R of road from Gambat Agra upto Razi Dero Road Mile 0/0-11/0 (17.69 Km).	25-09-2014	Average
783.	Work and Service, GOS	2543	Construction of road from N.H way via Mehar Shah Main Drain upto Wada Mahesar Road Mile 0/0-7/0.	19-09-2014	Un-Satisfactory
784.	Work and Service, GOS	2545	Construction of road from Muhammad Hassan Keerio village Deh Lakha road mile 0/0-5/5.	13-01-2015	Average

785.	Work and Service, GOS	2549	Construction of road from Chachro Vakrio to ADY JO TAR Mile 0/0-44/0	30-12-2014	Average
786.	Work and Service, GOS	2550	Construction of road from Kaloi to Diplo via Luss Farm mile 0/0-39/2 = 39-2 (M) = 63.19 Kms. (Under Revision)	29-09-2014	Average
787.	Work and Service, GOS	2564	CONSTRUCTION OF ROAD FROM JEWAN KHAN PITAFI TO MAIKHANA KHIROHI MILE 0/0-3/1 (5.00 KMS).	16-09-2014	Un-Satisfactory
788.	Work and Service, GOS	2565	Construction of road from G.T road to Reharki Sahib, Poojwadyoon Deweryoon, Sahib and S.S.D Dham Raherki Sahib (5.00 Kms).	07-08-2014	Un-Satisfactory
789.	Work and Service, GOS	2566	Construction of road from Kamber Railway Track, new Nazar Mohalla alongwith Rice Canal IP Side to Circular By-Pass 5.00 Kms	25-08-2014	Un-Satisfactory
790.	Work and Service, GOS	2569	Construction of Road from Sanhri Sarak to Noor Wah mile 0/0-18/6 (30.0 Kms)	26-08-2014	Un-Satisfactory
791.	Work and Service, GOS	2570	Construction / Repair of road from Tando Bago Jhudo road at mile 17/0 to connect Tando Bago Digri road at point Alamabad mile 0/0-8/6 (14.08 Kms)	10-03-2015	Average
792.	Work and Service, GOS	2572	Construction of of road from Phurdo Jamali to Khadaro Mile 0/0-7/0	27-11-2014	Average
793.	Work and Service, GOS	2577	Construction of road from Mâ€™Khas to Nâ€™Shah along old alignment Road Mile 0/0-43/0 = 43-0 (M) = 69.23 Kms.	19-03-2015	Average
794.	Work and Service, GOS	2582	Construction / Widening / Reconditioning & Resurfacing of Umerkot Bye Pass road mile 0/0-16/6 = 16-6 (M) = 26.96 Kms..	24-03-2015	Average
795.	Work and Service, GOS	2584	Construction of link road from Cheeta Chowk to Haji Arab via Mokaryar Haji Adam Nohri mile 0/0-9/3 (15 Kms)	25-03-2015	Un-Satisfactory
796.	Work and Service, GOS	2596	Construction of road from Shah Bukhari road to Lundi Shakh mile 0/0-4/1	28-10-2014	Average
797.	Work and Service, GOS	2597	Construction of road from Jhangara Naing road to Dargah Shaikh Dhaman mile 0/0-1/7 (3.0 Kms).	28-10-2014	Average
798.	Work and Service, GOS	2614	Construction / Improvement of road from Mirpurkhas Umerkot road to Mirpurkhas Sanghar road (Bye pass road with asphalt concrete mile 0/0-1/7 (3 Kms).	26-12-2014	Average
799.	Work and Service, GOS	2615	Construction of road from Hyderabad Road to meet Mirwah Road near Abdin Pump (Mirpurkhas Southern bye pass) Mile 0/0-7/4 (12.7 KMS)	08-08-2014	Satisfactory
800.	Work and Service, GOS	2617	Construction of road from Sukhio Miri to Amir Peer Mori via Budhar Babanyoon including links to Qadir Bux Chahwan, Roshan Chahwani Wadero Qasim Panhwar Wali Muhammad Bughio Haji Ali Akber Chahwan Ghulam Nabi Bughio and Nasurllah Bughio mile 0/0-5/0	18-12-2014	Average
801.	Work and Service, GOS	2635	Construction of road from Super Highway to Farsi Garden mile 0/0-1/7 (3.00 Kms)	04-12-2014	Un-Satisfactory

802.	Work and Service, GOS	2671	Construction of Garhi Khuda Bux Khan Bhutto Bye Pass road offtaking from Ratodero Naudero road at mile 6/0 to meet Banguldero Garhi Khuda Bux Khan Bhutto road at mile 4/3 along inspection path of 6-L Zakria Sim Drain mile 0/0-1/1 (1.80 Kms)	20-05-2015	Un-Satisfactory
803.	Work and Service, GOS	2698	Construction of road from Fazal Sahito to village Gul Mohammad Shah Taluka Kandiaro Road Mile 0/0-0/5. (1.00 Km).	30-09-2014	Average
804.	Work and Service, GOS	2704	Construction of road from Thikratho Salehpat road to Moharam Ali Mahar Village Mile 0/0 - 0/7	02-10-2014	Average
805.	Work and Service, GOS	2785	Construction of road from Village Khasso to Village Saleh Arain mile 0/0 - 0/7 (1.4 Km) UC Sultanpur District Sukkur ADP No: 2785	10-07-2014	Un-Satisfactory
806.	Work and Service, GOS	2804	Const. of road from Chamber Mirwah road Near 32 Mail Mori to Kandiaro Farm Cane Cate Tando Allahyar Sugar Mills Mile: 0/0-0/5 (1.0 Km).	18-02-2015	Average
807.	Work and Service, GOS	2811	Construction of Road from Goni to village Chutto Faqir	04-12-2014	Un-Satisfactory
808.	Work and Service, GOS	2904	Construction of road from Usman Behan to Chotiaryoon mile 0/0-57/4.	15-01-2014	Un-Satisfactory
809.	Work and Service, GOS	2906	Construction of road from chachro Waori Hirar Vaghiji - Veri Bahroo to Dano Dhandhal mile 0/0-78/0 = 78-0 (M) = 125.58 Kms.	26-08-2014	Average
810.	Work and Service, GOS	2910	Construction of road from Mithi Loonhair Kharo Amro Gogasar Katho to Nohto noon Road Mile 0/0-28/0 (45.08 Kms.)	29-09-2014	Satisfactory
811.	Work and Service, GOS	2913	Construction of road from Thario-jo-Tar to Dano via Pilo mile 0/0-31/6.	30-09-2014	Satisfactory
812.	Work and Service, GOS	2920	Construction of road from Chachro to Khinsar mile 0/0-4/4	02-06-2015	Satisfactory
813.	Work and Service, GOS		Infrastructure development work at Deh luqman khairpur	14-11-2014	Average
814.	Work and Service, GOS		Improvement of Road from Ex- National Highway to internal streets of Gulistan-e-Sajjad UC No. 3 Taluka Qasimabad	22-07-2014	Average
815.	Work and Service, GOS		Reconditioning of road from National Highway Bye pass to Session Court District Matiari	20-08-2014	Average
816.	Work and Service, GOS		Construction of link road on Hyderabad Branch to Village Qasim Ji Wasi Road Mile 0/0-1/0 District Matiari	20-08-2014	Average
817.	Work and Service, GOS		Construction of road from Talhar- Tando Bago road to village saifal Chandio	22-12-2014	Un-Satisfactory
818.	Work and Service, GOS		Construction of Road puran point sher mohamamd kaloi to kalomal village	22-12-2014	Average

819.	Work and Service, GOS	Construction of link road from Haji Umer Narejo road to village Qadir Narejo Deh 122	04-02-2015	Average
820.	Work and Service, GOS	Reconditioning of Road from Digri Tando Ghulam Ali @ Naga bus stop to Haji Noor Hassan Chandio village Mile 0/0-2/1	04-02-2015	Average
821.	Work and Service, GOS	Construction of Road from Aklyoon to Lehria Bheel	16-03-2015	Un-Satisfactory

## Annexure C - Acronyms

Acronym	Detail
ACS	Additional Chief Secretary
AD	Administrative Department
ADB	Asian Development Bank
ADP	Annual Development Plan
CD/CDA	Coastal Development Authority
CDWP	Central Development Working Party
CM	Chief Minister
CMS	Content Management System
DC	Deputy Commissioner
DDWP	District Development Working Party
DEV	Development
DG	Director General
DS	Deputy Secretary
EA	Executing Agency
FD	Finance Department
FiIMS	File Management Service
FY	Fiscal Year
GIS	Geographic Information System
GOS	Government Of Sindh
GPS	Global Positioning System
HR	Human Resource
IMP	Implementation
KMC	Karachi Metropolitan Corporation
M&E	Monitoring and Evaluation
MEC/M.E.C	Monitoring and Evaluation Cell
MEO/MO	Monitoring and Evaluation Officer
MIS	Management Information System
P&D	Planning and Development
PD	Project Director
PDWP	Provincial Development Working Party
PHED	Public Health Engineering Department
PM	Prime Minister
PMESI	Project Monitoring and Evaluation System Improved
PS	Personal Secretary
RMEO/RMO	Regional Monitoring and Evaluation Officer
SBI	Sindh Board of Investment
SGACD	Services General Administration and Coordination
SGRRP	Sindh Growth and Rural Rehabilitation Program
SMEO/SMO	Sector Monitoring and Evaluation Officer
SMS	Short Messaging Service
TPM	Third Party monitoring
XEN	Executive Engineer
