

ACTIVE
ALERT
AWARE



M & E Cell ANNUAL REPORT 2016-17

Prepared & Published by
Monitoring & Evaluation Cell
Planning & Development Department
Government of Sindh



MEC ANNUAL REPORT 2016-17

Prepared by: Naveed Mansoor, Director (MIS) P&D

Verified by: Riaz Ali Abbasi, Ex-Director (MEC), P&D

Reviewed by: Syed Imtiaz Ali Shah, Ex-D.G. (MEC), P&D
Faisal Ahmed Uqaili, Director General MEC, P&D

Approved by: Muhammad Waseem, Chairman, P&D Board

INTENTIONALLY LEFT BLANK

#430, 3rd Floor, Tughlaq House, Sindh Secretariat, Karachi. +92-21-99211927

CONTENTS

CONTENTS	3
EXECUTIVE SUMMARY	5
MESSAGE FROM THE CHAIRMAN, P&D BOARD, GOVT. OF SINDH.....	6
MESSAGE FROM THE EX-DIRECTOR GENERAL MEC	7
MESSAGE FROM THE DIRECTOR GENERAL MEC	8
HISTORY OF MEC	11
THE MONITORING PROCESS – FULLY AUTOMATED & PAPERLESS.....	13
ADP PROGRESS MONITORING DASHBOARD	14
FINANCIAL TREND ANALYSIS OF PROVINCIAL ADP	17
COST ANALYSIS OF ADP SCHEMES IN FY 2016-2017.....	20
DEPARTMENT-WISE ADP BUDGET ALLOCATION IN FY 2016-17	22
DEPARTMENT-WISE MONITORING CONDUCTED IN FY 2016-17.....	23
RESPONSE RECEIVED FROM LINE DEPARTMENTS.....	26
DEPARTMENT-WISE UNSATISFACTORY SCHEMES	27
DEPARTMENT-WISE SATISFACTORY SCHEMES.....	26
SUMMARY OF FIELD MONITORING BY REGIONAL OFFICES	29
TREND ANALYSIS OF FIELD MONITORING OVER THE YEARS.....	30
TREND ANALYSIS OF OBSERVATION TYPE	31
DEPARTMENT-WISE TREND OF UNSATISFACTORY SCHEMES	31
THIRD PARTY MONITORING (TPM).....	33
OVERVIEW OF FINDINGS FROM FIELD MONITORING	34
MAJOR DECISIONS TO EMPOWER MEC	38
MAJOR FINDINGS FROM TECHNICAL ANALYSIS.....	38
SELECTED SNAPSHOTS OF VARIOUS ACTIVITIES	40
TRAINING OF LINE DEPARTMENT OFFICERS ON USING ADP PROGRESS MONITORINGDASHBOARD AND DISTRIBUTION OF SMARTPHONES	45
ANNEXURE A	48
ANNEXURE B	114
ANNEXURE C	118
ANNEXURE D	124



“FACILITATING GROWTH & DEVELOPMENT”

EXECUTIVE SUMMARY

This annual report presents an overview and analysis of the operations and achievements of Monitoring & Evaluation Cell, Planning & Development Department, Government of Sindh during fiscal year 2016-17. It focuses on the observations and conclusions that have been compiled from field monitoring over the year and various other data sources including from our indigenously built decision support software FILMS (Files Management System) and SMES (Schemes Management & Evaluation System) juxtaposed with the financial data of the Finance Department.



Monitoring and evaluation are essentially quality management tools, to keep a watch on the progress of development schemes and to proactively alert where interventions are required by the decision taking authorities. Not only the government benefits from this activity, but so does the community for which these works are aimed at. Based on the input of MEC with in-depth knowledge, the Administrative Departments rectify or modify the designs and their activities for a more effective, efficient and better results in their respective works.

Monitoring & Evaluation Cell, Planning & Development Department, Government of Sindh, presently established an ADP Progress Monitoring Dashboard with the World Bank support to keep a close-eye on the progress of development schemes. FY 2016-17, the ADP comprised of 2,773 schemes, with an allocation of Rs. 200bn. Releases of Rs. 173.071bn were made with a utilization of 91% (157.930m Expenditure) as against 82% (99,595 m) in the previous financial year. Conversely, in other words holistically, the total expenditure on development works this year was 63% higher than the previous year.

There was a drop in the percentage of unsatisfactory schemes from 26.72% in 2015-16 to 15.01% in FY 2016-17, primarily due to more extensive field monitoring and enhanced coordination between MEC and FD for financial releases. This implies that approximately one in every 7 schemes monitored was found to be unsatisfactory. However, the response rate for compliance, from the line departments, was 26%, down from 34%.

MESSAGE FROM THE CHAIRMAN, P&D BOARD, GOVT. OF SINDH



MUHAMMAD WASEEM

It takes a great team to build a great organization. As I review the details of this report, it is clear that the accomplishments recounted within it are the result of extraordinary collaboration by the M&E Cell's most important asset—its people. At every layer of our organisational structure, each individual plays a valued part in moving the department forward.

MEC is an organization for vigilantly monitoring the development portfolio of public works and proactively reporting for corrective and preventive measures; a team of qualified

professionals who create, pursue, perform, and achieve in support of the parent P&D Department's goals.

In this report, you will see a snapshots of activities and the challenges that MEC embarked upon, which taken together, make for a highly visible example of commitment and success.

With significantly visible level of efficiency in MEC, through the use of innovative IT solutions, it is able to keep the concerned authorities updated with quick and paperless online reporting. It utilizes modern smartphone technology to collect field data and transmit it through a workflow automation system, that connects our offices at Karachi, Hyderabad, Sukkur and Larkana. Such reporting helps the stakeholders in taking timely and informed decisions.

I congratulate MEC for their commendable work and look forward to their continual improvement for better proactive and corrective measures.

MESSAGE FROM THE EX-DIRECTOR GENERAL MEC



SYED IMTIAZ ALI SHAH

Over the years, we have built a tradition of excellence at M&E Cell. During the financial year 2016-17, we have collectively embarked on a journey to advance our vision and ensure that the delivery of services and quality of construction in public works are as desired.

This report documents one year's accomplishments of M&E Cell, overcoming the challenges faced by our field officers in reporting from remote and far-flung areas of province. It is with these unprecedented challenges in mind that I am distinctly pleased to present this annual report

of achievements and accomplishments along with a commentary on issues and observations recorded.

This year, we embarked upon effectively implementing the World Bank supported reforms for implementation of smartphone based reporting from the field. We also successfully established two more regional offices at Karachi and Larkana besides, the earlier presence at Sukkur and Hyderabad to increase capacity and monitor a larger number of provincial ADP schemes.

I would also like to acknowledge all the regional field monitoring offices of MEC, MIS Directorate and other associated officers for their tireless efforts and hard work for the successful achievement of MEC targets.

This publication presents a truly significant compilation of insights, advancements, and observations across a large portfolio of the Sindh Annual Development Plan.

MESSAGE FROM THE DIRECTOR GENERAL MEC



FAISAL AHMED UQAILI

In September - 2018, I honoured to be chosen as Director General (MEC), and lead the M&E Cell. This is my first Annual Report which is pending since a year for publishing, I take it as a challenge to finalize it by putting extra focus in its preparation, data analysis and presentation.

The first thing first, I start enhancing the capacity building of the Field monitoring report to adopt new era technique (available ISO standard Tests), its strategy, SOP to justify observations, quick and responsive recommendation with more depth analysis through its revision.

Next, I targeted to increase field monitoring visits of ADP schemes to

monitored maximum numbers of schemes next year by facilitating our monitoring regions through different trainings / capacity building programs offered by Sindh Government as well as setting up a new deadline for moniotirng visit plans and report submission.

Lastly, the experience and knowledge of our Director General (RT&W), Secretary (Planning) and Chairman (Planning & Development Board) Government of Sindh have been instrumental in guiding us through the challenges we faced in this Annual Report finalization.

I anticipate the output and outcome of MEC activities to become a model of excellence in service delivery.

OVERVIEW

MONITORING & EVALUATION CELL,
PLANNING & DEVELOPMENT DEPARTMENT
GOVERNMENT OF SINDH

VISION

Enable Precise Deliverables in Public Works through Proactive Facilitation




MISSION

1. To ensure that the Standard of Quality is maintained in development projects
2. To keep a regular watch on the progress of schemes
3. To enable timely & informed decisions through efficient reporting
4. To promote and enhance institutional learning and knowledge through instant availability of chronological indicators
5. To coordinate with various authorities for smooth and unhindered implementation
6. To Review and Evaluate the output & outcome of schemes.



HISTORY OF MEC

GROWTH & ADVANCEMENT



- MEC Established
- ADP Outlay: Rs. 1.533bn
- Strength: 8 Officers



2010-15
STRENGTHENING

- Est. Sukkur & Hyderabad Offices
- Est. MIS Directorate
- Internal Workflow Automation
- Portfolio Management System
- Strength: 70 Officers



- Est. Karachi & Larkana Regional Offices
- Est. Data Center
- ADP Progress Monitoring Dashboard
- Monitored over 846 schemes


TODAY

- Releases of every scheme are based on MEC reports
- MEC has Regional offices at Karachi, Hyderabad, Sukkur and Larkana
- Developed ADP Progress Monitoring Dashboard with the facilitation of World Bank
- Empowered to recommend Finance Department on financial releases for development schemes
- Today, MEC's role is accepted as vital for *decisions, prioritization, releases* and in provincial *annual budget allocation*.




FUNCTIONS OF MONITORING & EVALUATION CELL


The M&E Cell performs the following functions:

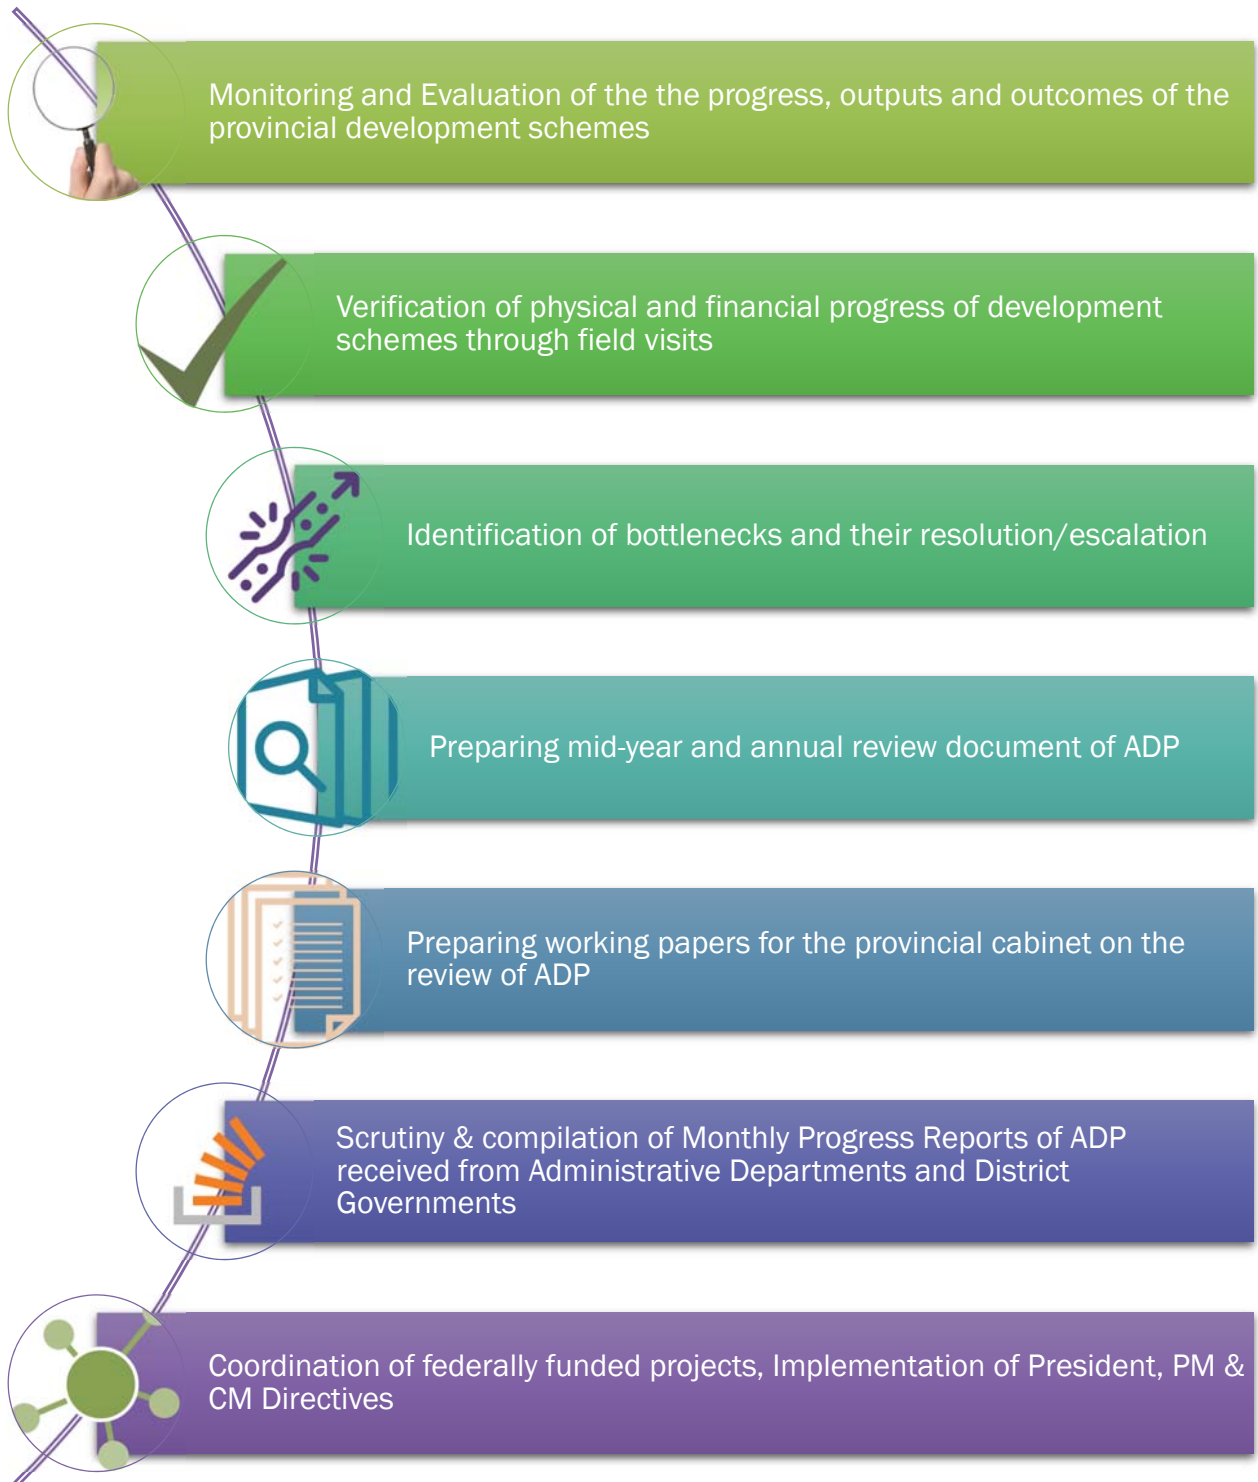

THE MONITORING PROCESS – FULLY AUTOMATED & PAPERLESS

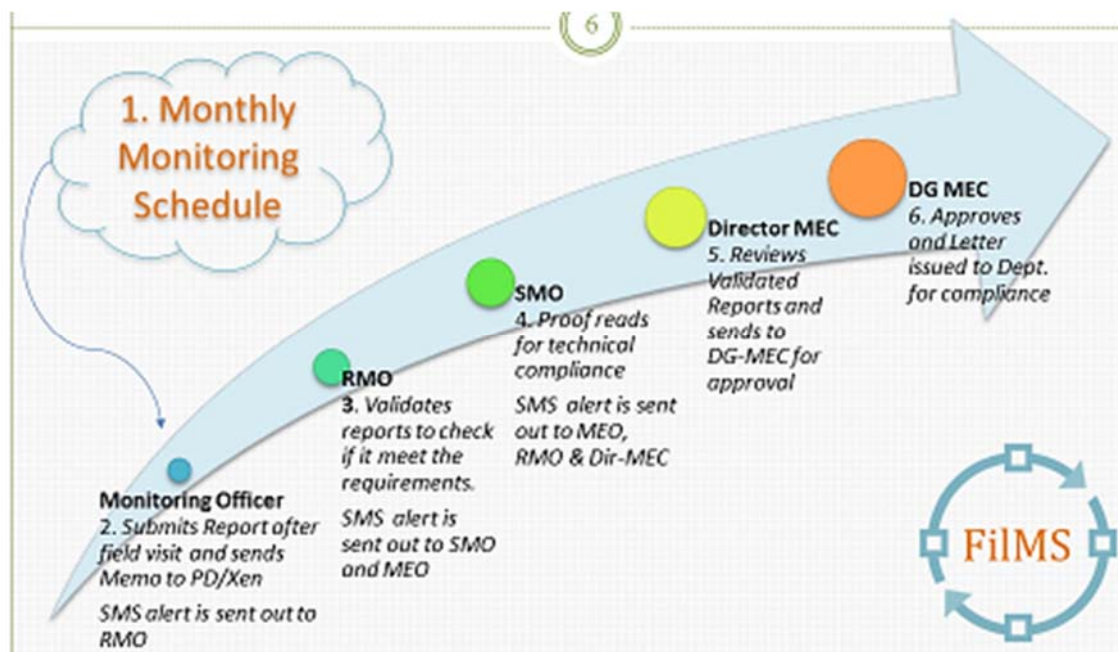


Following is the automated & paperless monitoring process used in MEC through an indigenously built online bespoke system called FiMS (File Management System):

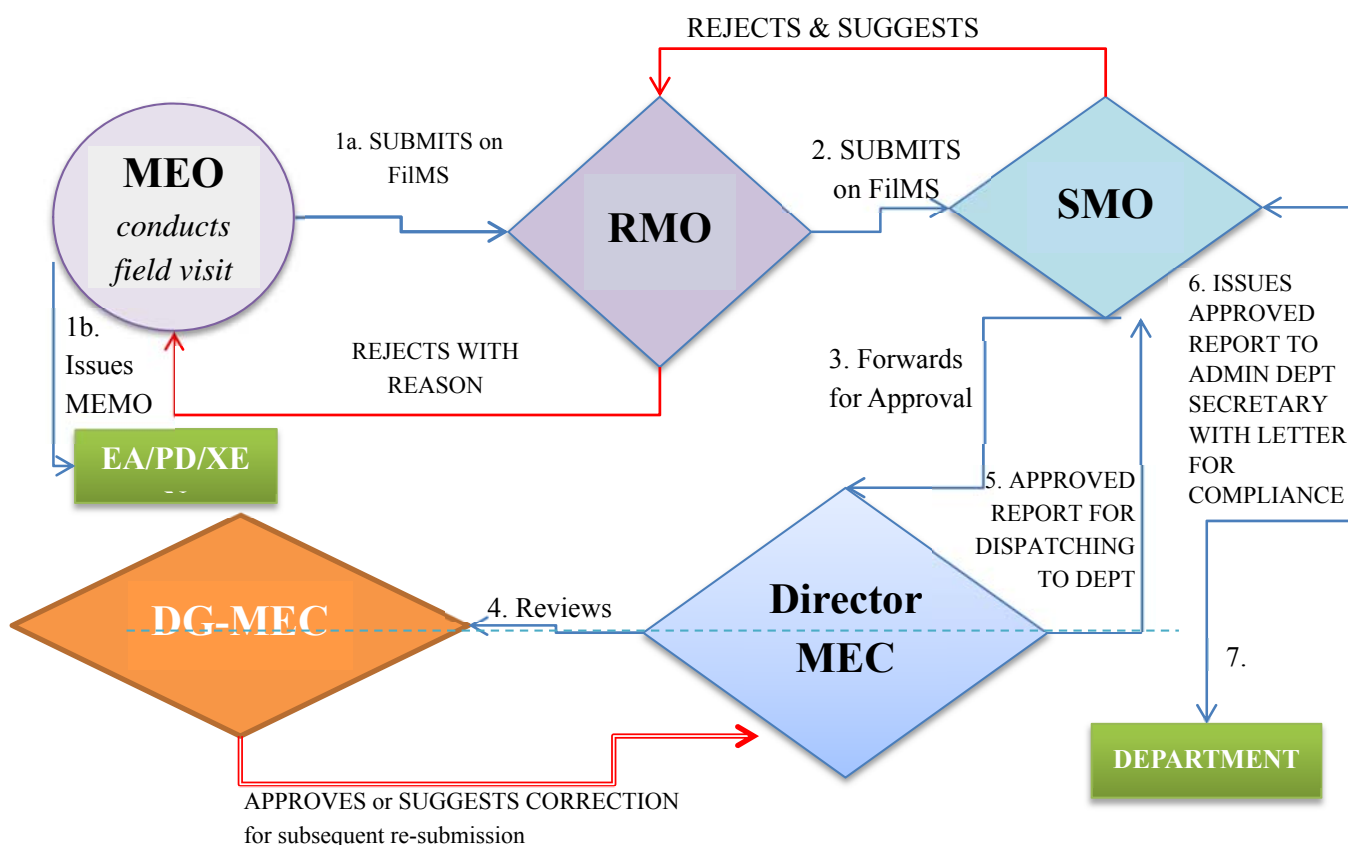

ADP PROGRESS MONITORING DASHBOARD

SYSTEM OVERVIEW

ADP Progress Monitoring Dashboard is a system for holistic monitoring of the Provincial ADP portfolio with a multi-dimensional aspects of data evaluation, at one place, to support informed and enhanced decisions.

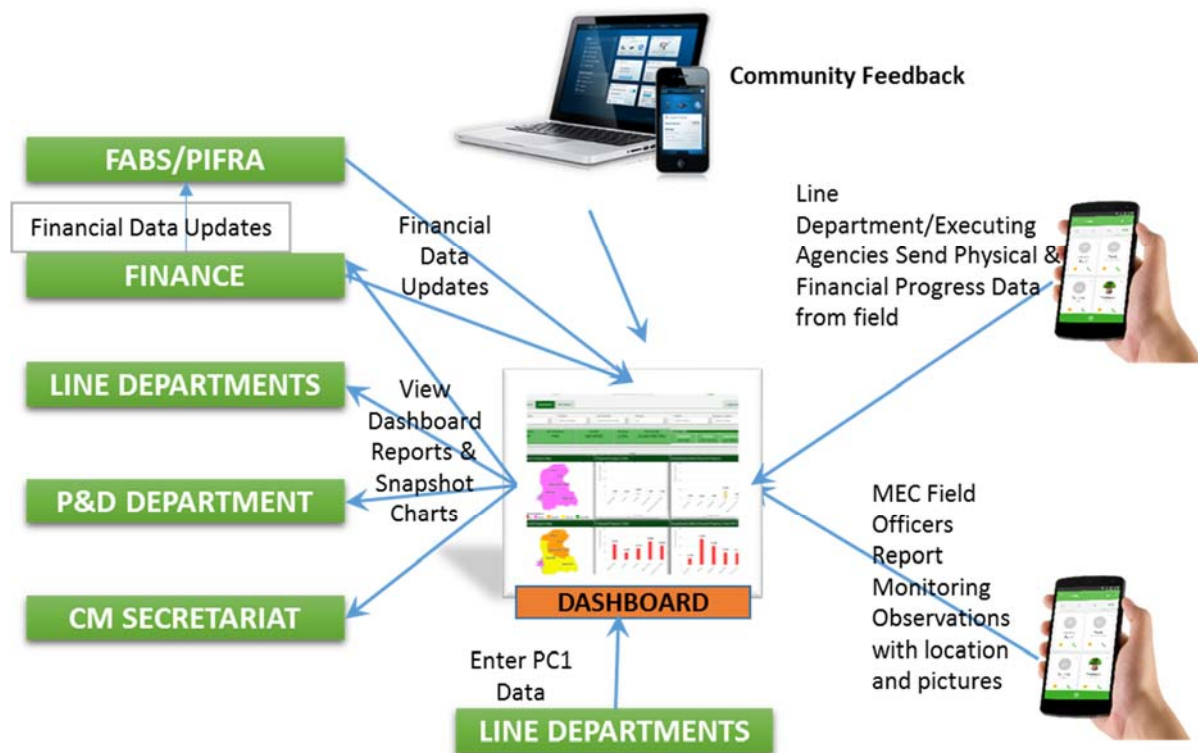

OBJECTIVE

To provide an online holistic view of the ADP portfolio by presenting information on:

1. GIS Maps with pin-pointed location of the development schemes
2. Financial progress as reported by FD/FABS
3. Physical progress reporting from the field by the line department and MEC
4. Beneficiary feedback
5. Analytical and Summarised Reports

UNIFIED REPORTING

The dashboard will integrate and consolidate data from various sources.

1. Integration with existing paperless workflow automation system of MEC called FILMS with construction quality detailed reports
2. Auto fetching of data from Finance Department
3. Constituency wise data Analysis & Reporting
4. Beneficiary feedback on a single platform
5. Every scheme will have a unique ID to enable tracking through the years

ANALYSIS AND VISUALIZATION

1. Data visualization in Grids/Charts with filters on multiple fields;
2. *One click + real time* access to information on the web through a simple log in;
3. Data input from Android smartphones from field is reflected in real-time in on-screen visual and tabular analytical reports
4. Department wise and District/Division wise reporting
5. Comparative Analysis of financial, physical and location based data.

SMARTPHONE APPLICATION

Previously, the key information required on frequent basis from MEC field monitors was submitted through an online web-based system called FILMS that included information on financial outlays, key issues faced and status of projects (satisfactory/unsatisfactory) acquired through field visits.

Now, the Smartphone App of the ADP Progress Monitoring Dashboard allows MEC and Line Department field monitoring officers to submit this key information on a real time basis through their Smartphone from the field with their geo-tagged location with pictures to report physical progress and inform of any issues/obstacles along with other details.

TARGET & PROGRESS

Initially Schemes costing above Rs500m of 5* Departments (PHED, Energy, Irrigation, W&S and Education) are to be uploaded. Of the selected 181 schemes, 124 PC1s have been uploaded.

(*6th Department "Sports and Culture also added in 2018-19).

SYSTEM ACCESS

Access to system is presently given to MEC and 5 Line Departments (PHE, W&S, Irrigation, Energy & Education) and will be extended to all departments and decision makers with relevant data access rights.

PROGRESS ACHIEVED

Target Departments	Total PC-I	PC-I Received from Dept.		PC-I Uploaded (Progress)		PC-I Not Received from Line Dept.	Android Reporting by Line Dept.		Android Reporting by MEC	
Education	56	35	63%	26	74%	21 (37%)	07	27%	11	42%
Energy	20	15	75%	14	93%	05 (25%)	01	7%	02	14%
Irrigation	53	46	87%	45	98%	07 (13%)	06	13%	15	33%
Public Health & Engineering	10	10	100%	10	100%	00 (00%)	08	80%	09	90%
Works & Services	42	29	69%	29	100%	13 (31%)	07	24%	10	34%
TOTAL	181	135	75%	124	92%	46 (25%)	29	23%	47	38%

Note: Schemes above Rs. 500m are targeted to be uploaded in first phase of the above departments

SNAPSHOT OF THE ADP PROGRESS MONITORING DASHBOARD



DATA ANALYSIS


PROVINCIAL ANNUAL DEVELOPMENT PROGRAM

FINANCIAL TREND ANALYSIS OF PROVINCIAL ADP

Below is the financial trend analysis of the Annual Development Programmes:



Rupees in million

ADP	On-going Schemes	New Schemes	Total Schemes	Allocation	Releases	Expenditure	Utilisation
2011-12	1,244	493	1,737	111,000.00	102,000.00 (92%)	84,520.00	83%
2012-13	1,288	1,323	2,611	161,000.00	85,640.00 (53%)	69,530.00	81%
2013-14	1,363	1,100	2,463	165,000.00	95,035.00 (58%)	86,287.00	91%
2014-15	1,658	1,279	2,937	143,000.00	110,360.00 (77%)	100,370.00	91%
2015-16	1,762	590	2,352	142,000.00	120,872.00 (85%)	99,595.00	82%
2016-17	1,776	995	2,773	200,000.00	173,070.30 (87%)	157,437.53	91%

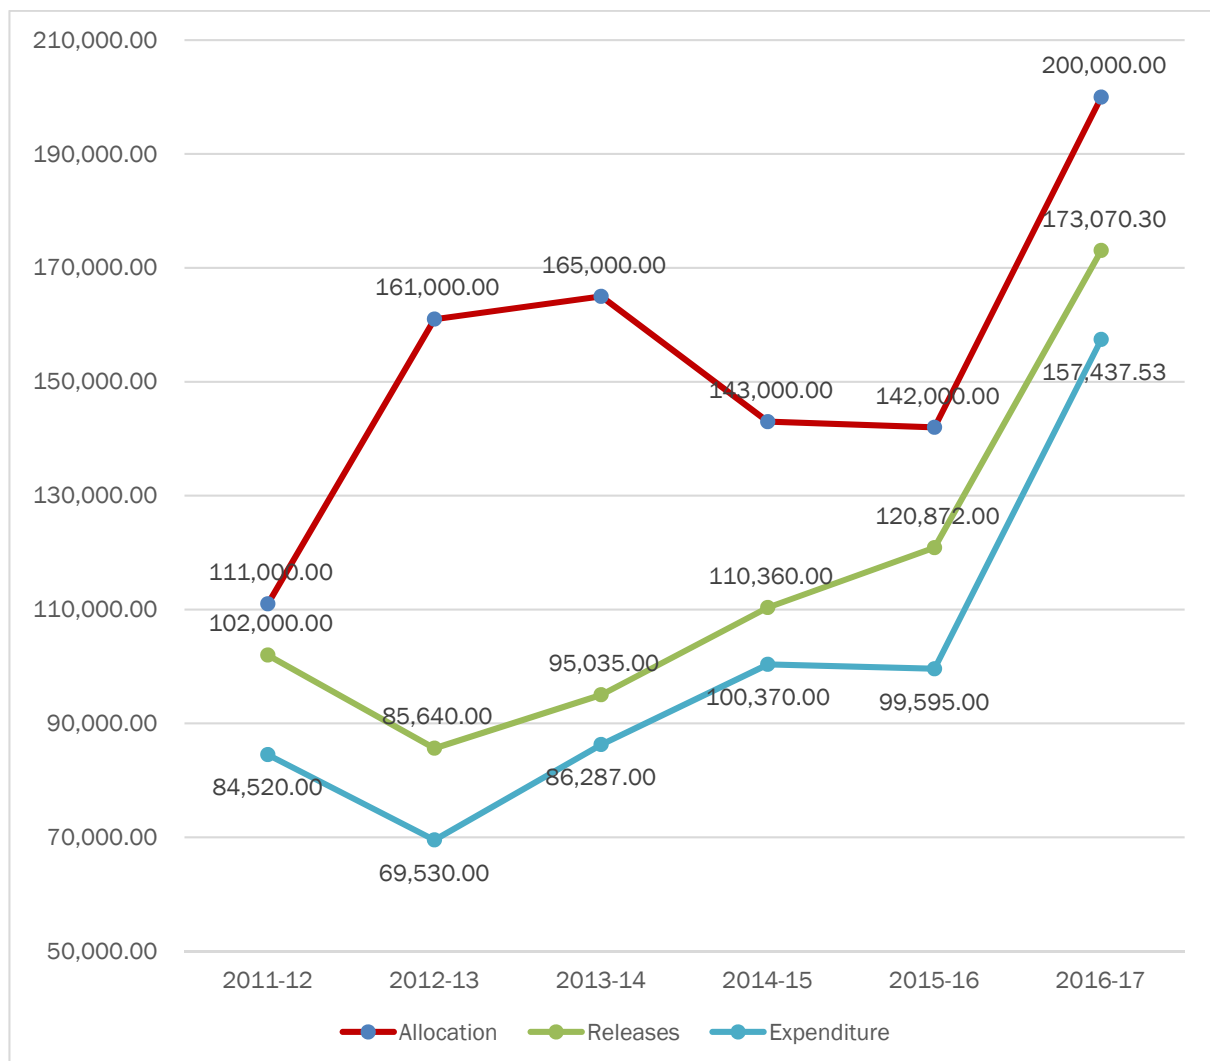

FINANCIAL COMPARATIVE ANALYSIS OF PROVINCIAL ADP


Below is the financial comparative analysis of the Annual Development Programmes:

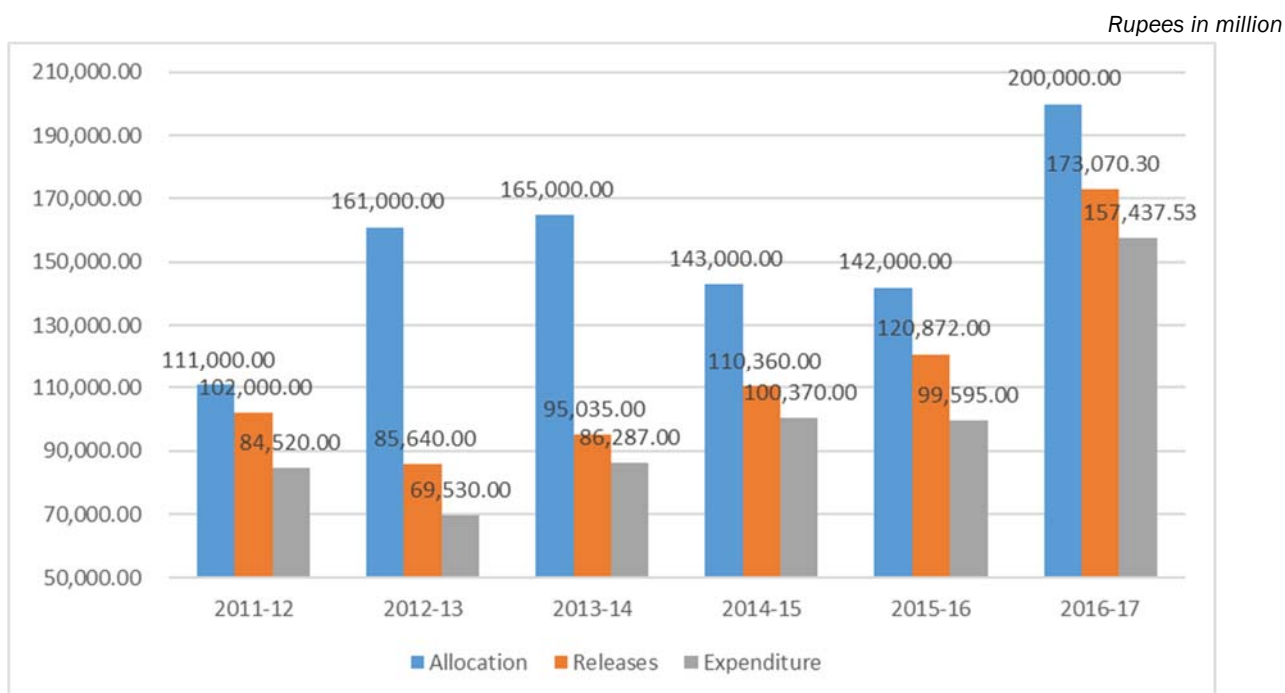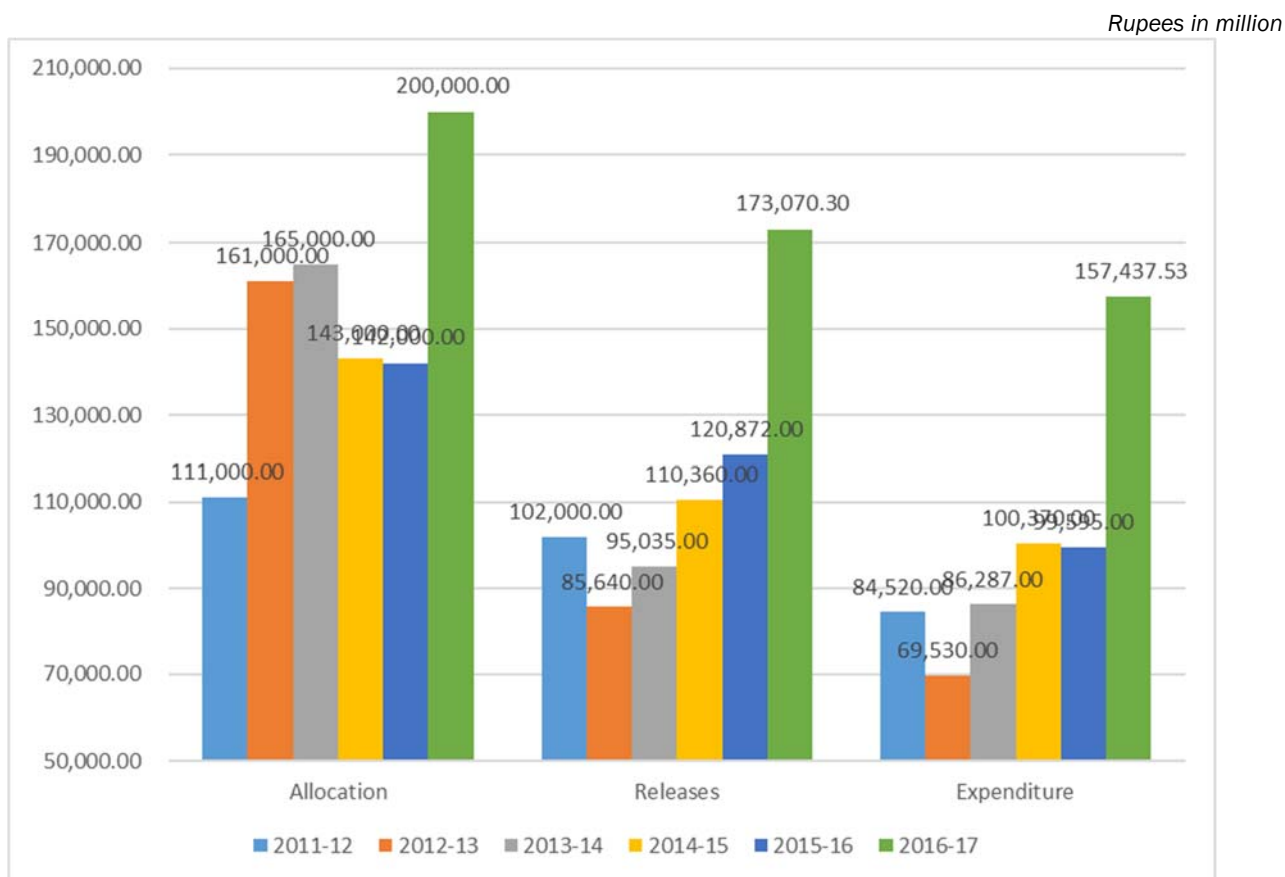


COST ANALYSIS OF ADP SCHEMES IN FY 2016-2017


SCHEME COST (Rs. in million)	COUNT (# of Schemes)	TOTAL SCHEMES COST (Rs. in million)
5,000 and above	27	222,945.48
Between 1,000 and 5,000	140	288,152.03
Between 500 and 1,000	192	134,862.72
Below 500	2,414	275,649.96
TOTAL	2,773	921,610.20

Count Analysis in terms of cost of ADP schemes

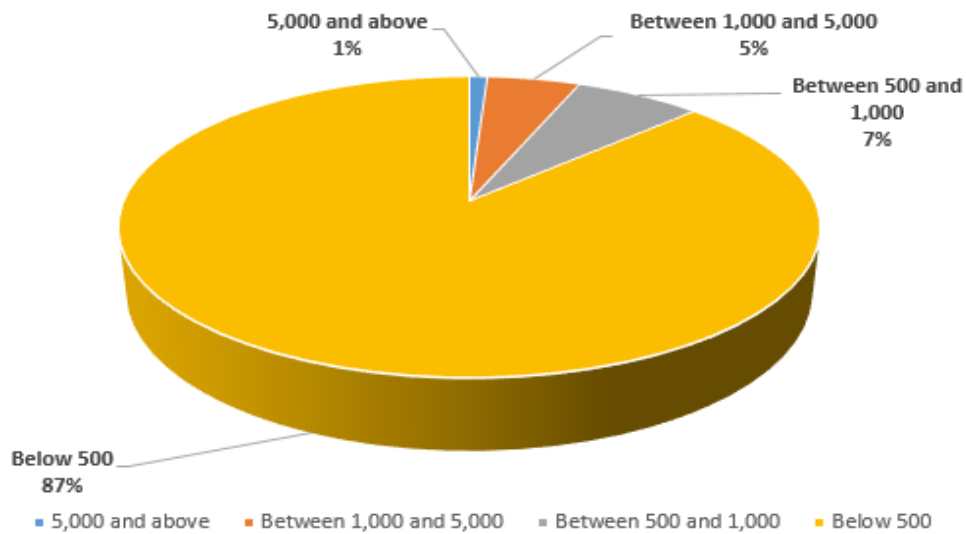

The Pie Chart below represent the distribution of total ADP funds (iRs. in million) among various sizes of ADP schemes (in terms of their cost)

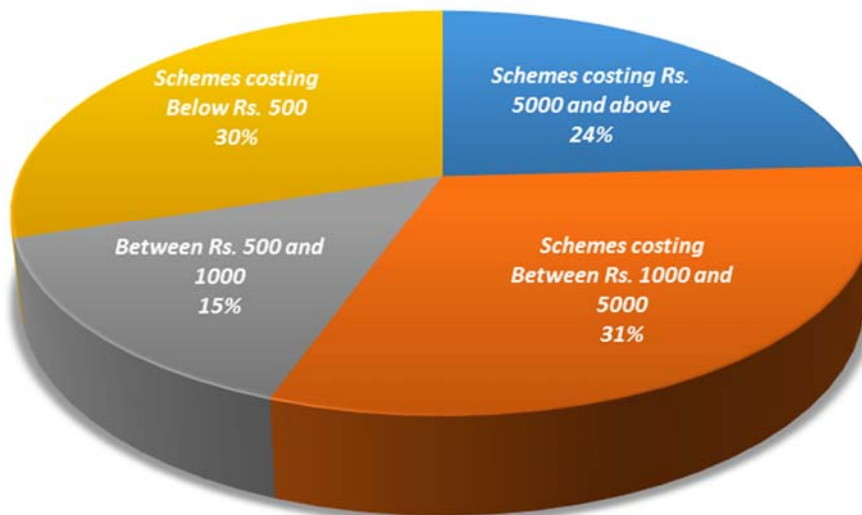

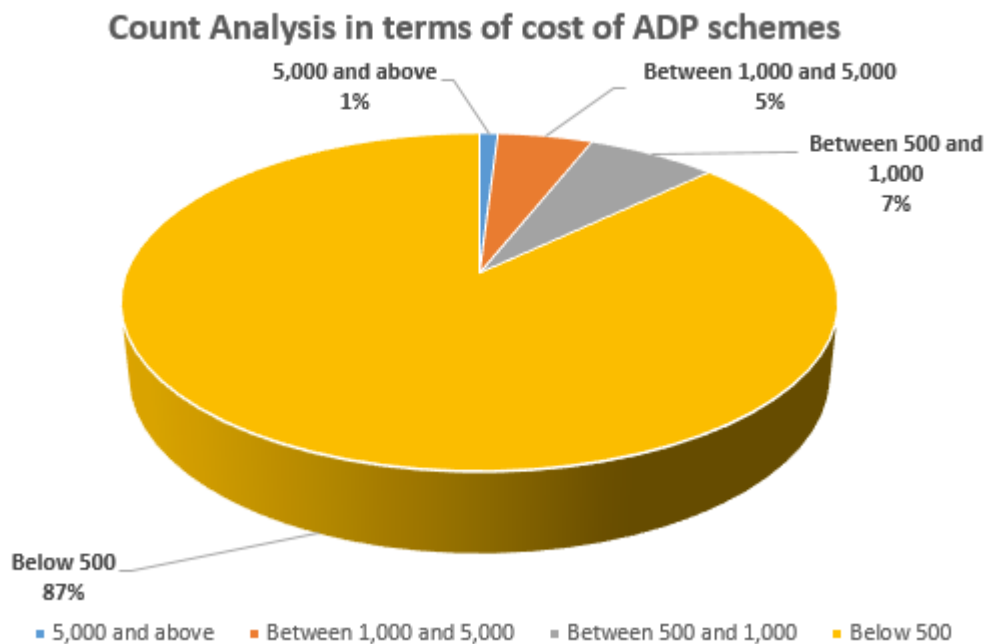


Deduction: From the charts and table above, it can be seen that in FY 2015-16:

more than half, that is, 55%, (of the total cost of all the ADP schemes was directed towards schemes costing Rs. 1 billion and above. That is:

- 55 % (31+24%) as compared to 51% in FY 2015-16
- 167 schemes as compared to 143 schemes in FY 2015-16
- While there were 167 (140+21) schemes (6%) costing 1billion and above in terms of the number/quantity of such schemes, out of the ADP outlay's 2,773 schemes

The % represents the aggregate cost of a particular slab of scheme's cost as a percentage of total total ADP schemes' cost) of the ADP FY 2016-17

DEPARTMENT-WISE ADP BUDGET ALLOCATION IN FY 2016-17

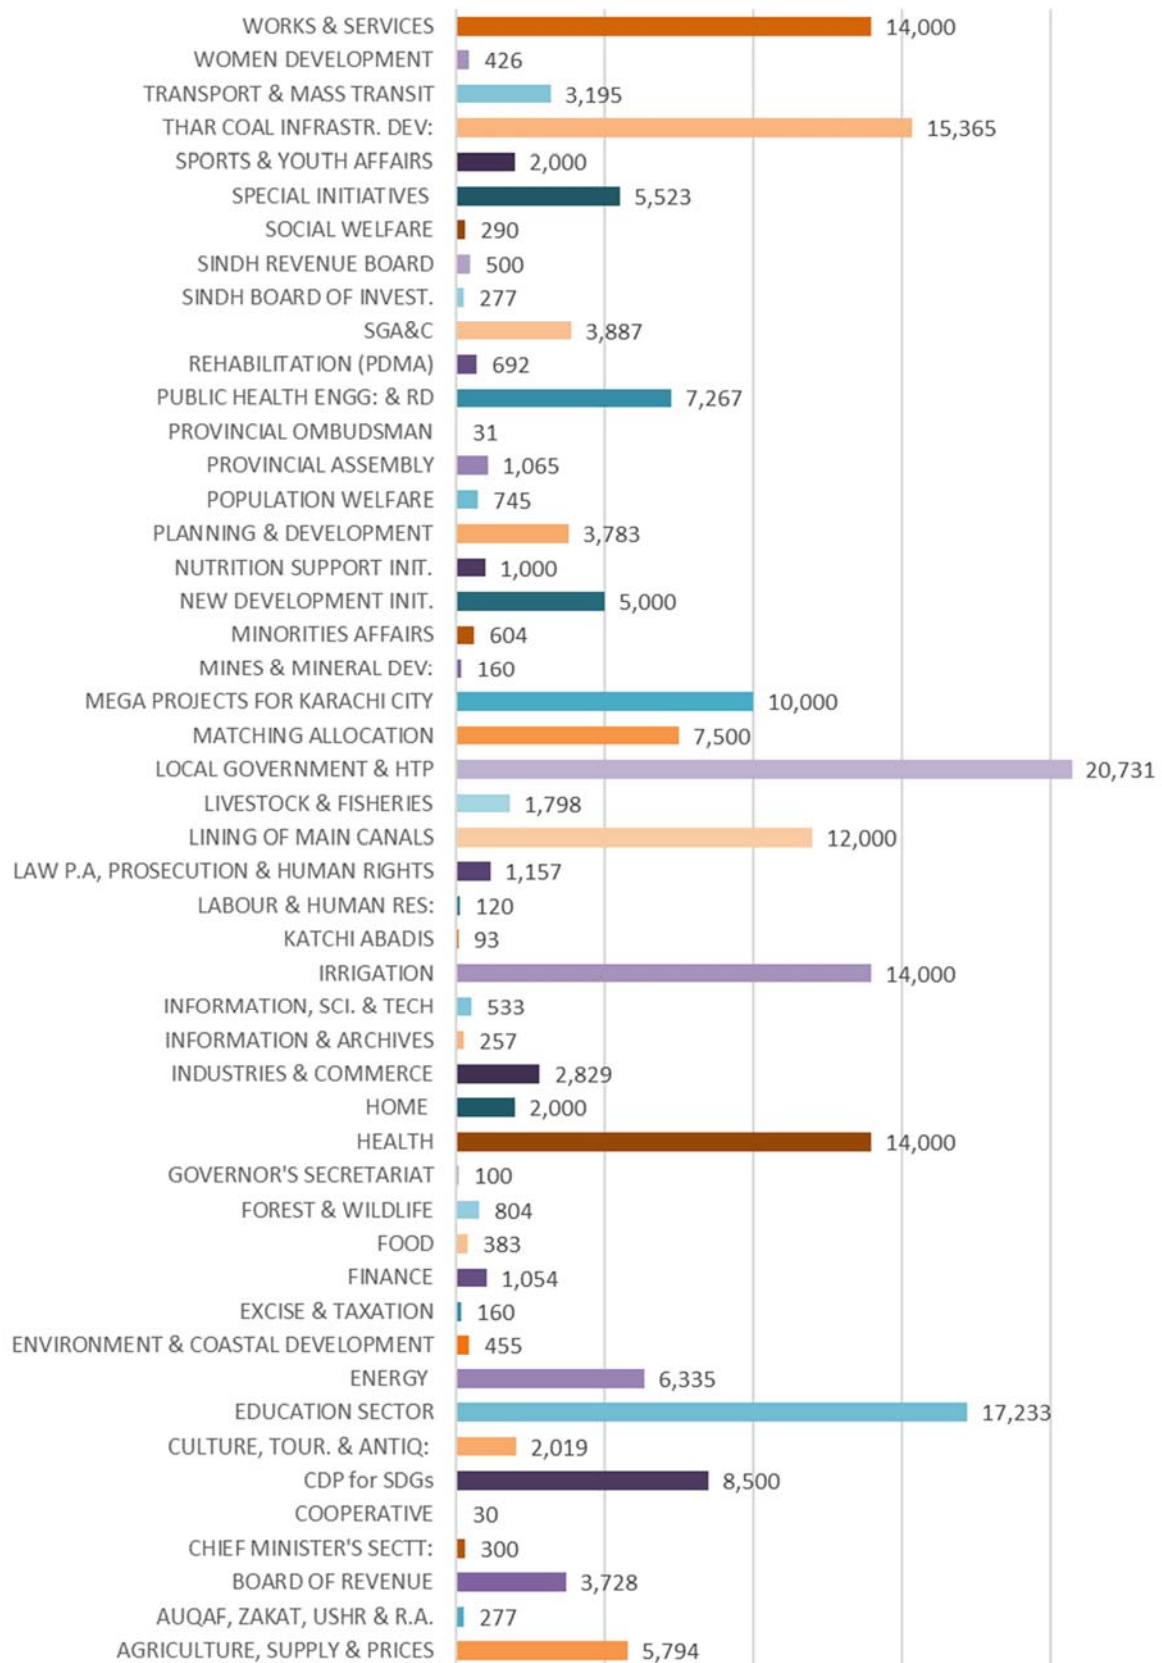

MONITORING REPORTS ANALYSIS & FINDINGS
GENERATED FROM ONLINE PAPERLESS FILE MANAGEMENT SYSTEM

DEPARTMENT-WISE MONITORING CONDUCTED IN FY 2016-17

Following is the summary of **department-wise** observations recorded from field monitoring conducted in the fiscal year 2016-17 (reports in-progress and published):

S.#.	Department/ Sector	# of Scheme							Compliance Reply Received	
		Visited	Satisfactory		Avg.		Un-Satisfactory			
1	Agriculture	23	18	78%	2	9%	3	13%	2	67%
2	Auqaf	4	4	100%	0	0%	0	0%	0	-
3	Board of Revenue	14	9	64%	1	7%	4	29%	0	0%
4	Chief Minister Secretariat	1	1	100%	0	0%	0	0%	0	-
5	Culture	35	17	49%	3	9%	15	43%	2	13%
6	Education and Literacy	85	57	67%	14	16%	14	16%	2	14%
7	Energy	3	2	67%	0	0%	1	33%	0	0%
8	Environment	3	2	67%	0	0%	1	33%	1	100%
9	Finance Dept	4	3	75%	1	25%	0	0%	0	-
10	Food	1	0	0%	0	0%	1	100%	0	0%
11	Forest, Wildlife & CDA	15	10	67%	1	7%	4	27%	0	0%
12	Health	76	36	47%	13	17%	27	36%	9	33%
13	Home	21	17	81%	1	5%	3	14%	0	0%
14	Human Rights	10	8	80%	0	0%	2	20%	1	50%
15	Industrial & Commerce	5	4	80%	1	20%	0	0%	0	-
16	Information & Archives	3	0	0%	2	67%	1	33%	0	0%
17	Information Technology	1	1	100%	0	0%	0	0%	0	-
18	Irrigation (Water & Drainage)	77	45	58%	13	17%	19	25%	0	0%
19	Labour Dept	6	3	50%	1	17%	2	33%	0	0%
20	Livestock and Fisheries	35	15	43%	4	11%	16	46%	5	31%
21	Local Government	112	75	67%	21	19%	16	14%	2	13%
22	Matching Allocation	1	1	100%	0	0%	0	0%	0	-
23	Minorities & Affairs	11	6	55%	0	0%	5	45%	0	0%
24	Planning & Development	1	1	100%	0	0%	0	0%	0	-
25	Population Welfare	1	1	100%	0	0%	0	0%	0	-
26	Public Health Engineering	64	42	66%	15	23%	7	11%	1	14%
27	Rehabilitation (PDMA)	1	1	100%	0	0%	0	0%	0	-
28	Rural Development	9	6	67%	2	22%	1	11%	0	0%

29	S.G.A.and Coordination	13	12	92%	1	8%	0	0%	0	-
30	Sindh Board of Investment (SBI)	1	1	100%	0	0%	0	0%	0	-
31	Social Welfare	3	2	67%	0	0%	1	33%	0	0%
32	Special Initiatives Unit	12	6	50%	6	50%	0	0%	0	-
33	Sports & Youth Affairs	25	15	60%	4	16%	6	24%	3	50%
34	STEFTA	1	0	0%	0	0%	1	100%	0	0%
35	Thar Coal Infrastructure Development	3	2	67%	0	0%	1	33%	0	0%
36	Transport & Comm. (Roads)	4	3	75%	1	25%	0	0%	0	-
37	Universities and Boards	5	3	60%	1	20%	1	20%	0	0%
38	Women Development	4	3	75%	0	0%	1	25%	0	0%
39	Work and Service	153	93	61%	19	12%	41	27%	23	56%
Total ADP Schemes Monitored		846	525	62%	127	15%	194	23%	51	26%

Highlighted: 0% compliance by the department


Highlighted: Over one-third of the schemes monitored were found to be unsatisfactory

Note: Compliance Percentage is calculated by total count of replies received from the department divided by sum of unsatisfactory schemes.

Deduction: On an average there was 26% compliance response from the departments against notices sent, down from 34% in the previous FY 2015-16.

DEPARTMENT-WISE SATISFACTORY SCHEMES


Below is a pictorial view of the **percentage** of provincial ADP schemes monitored that were found to be satisfactory in various departments:

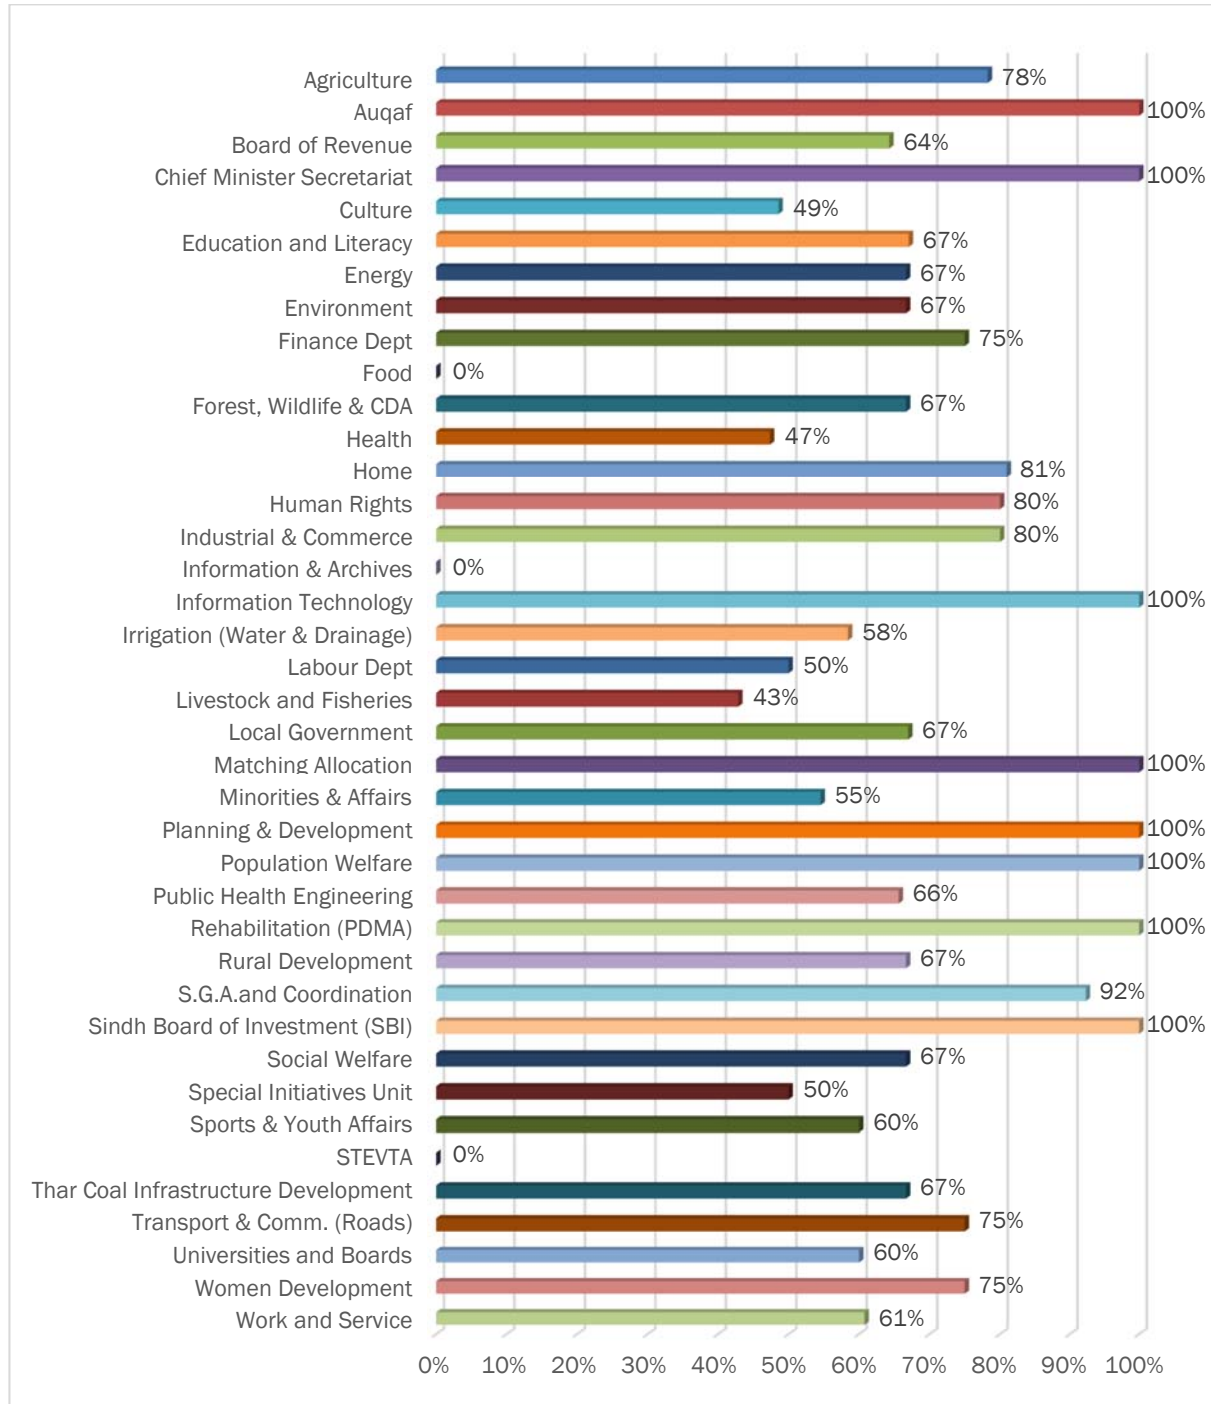

Note: 0% may denote that either no scheme of the department was monitored or all the schemes monitored were unsatisfactory. Likewise, 100% percent denotes that all schemes monitored were found to be satisfactory. See Annexure A for clarification details.

DEPARTMENT-WISE UNSATISFACTORY SCHEMES


Below is a pictorial view of the **percentage** of provincial ADP schemes monitored, which were found to be unsatisfactory in various line departments respectively:

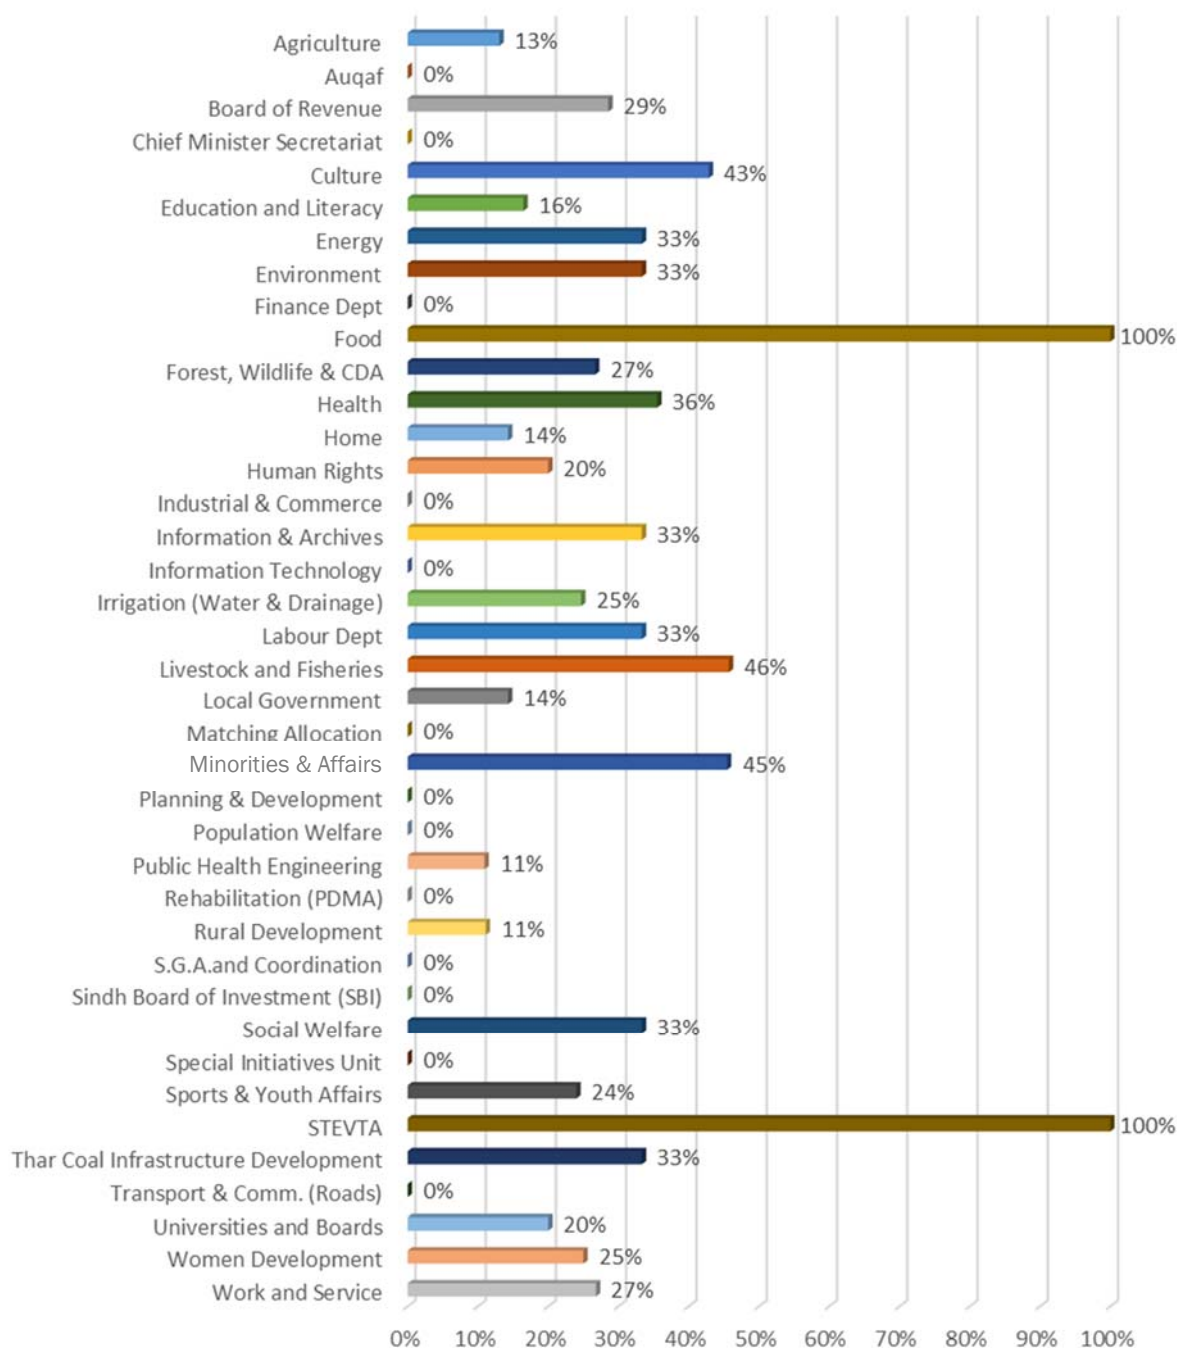

Note: 0% may denote that either no scheme of the department was monitored or all the schemes monitored were satisfactory. Likewise, 100% percent denotes that all schemes monitored were found to be unsatisfactory. See Annexure A for clarification and details.

RESPONSE RECEIVED FROM LINE DEPARTMENTS

Below is the pictorial representation of the percentage of response received from the line departments against notices sent to them for their unsatisfactory execution of ADP schemes.

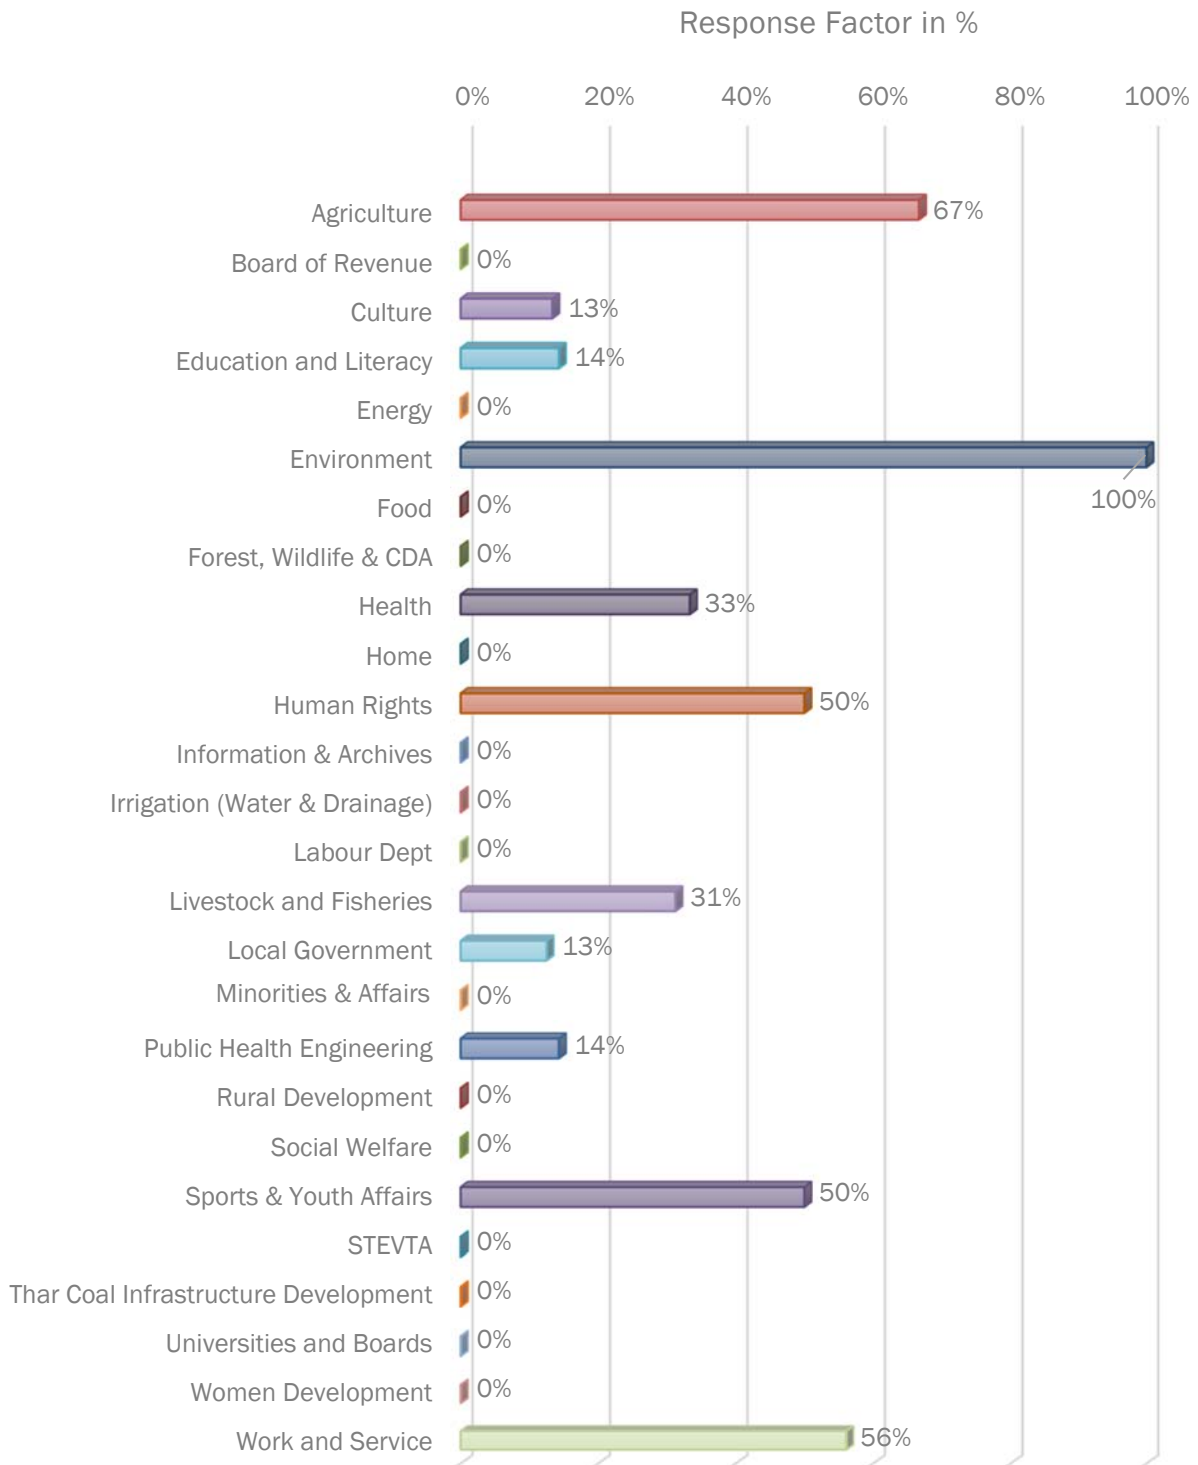


SUMMARY OF FIELD MONITORING BY REGIONAL OFFICES

SUMMARY OF PROVINCIAL ADP MONITORING

Below is the comparison of the schemes monitored by our two Regional Offices:

REGION	SATISFACTORY	AVERAGE	UNSATISFACTORY	TOTAL
Hyderabad	247	73	81	401
Sukkur	278	54	113	445
Total	525	127	194	846


PICTORIAL VIEW OF PROVINCIAL ADP MONITORING BY OBSERVATION TYPE

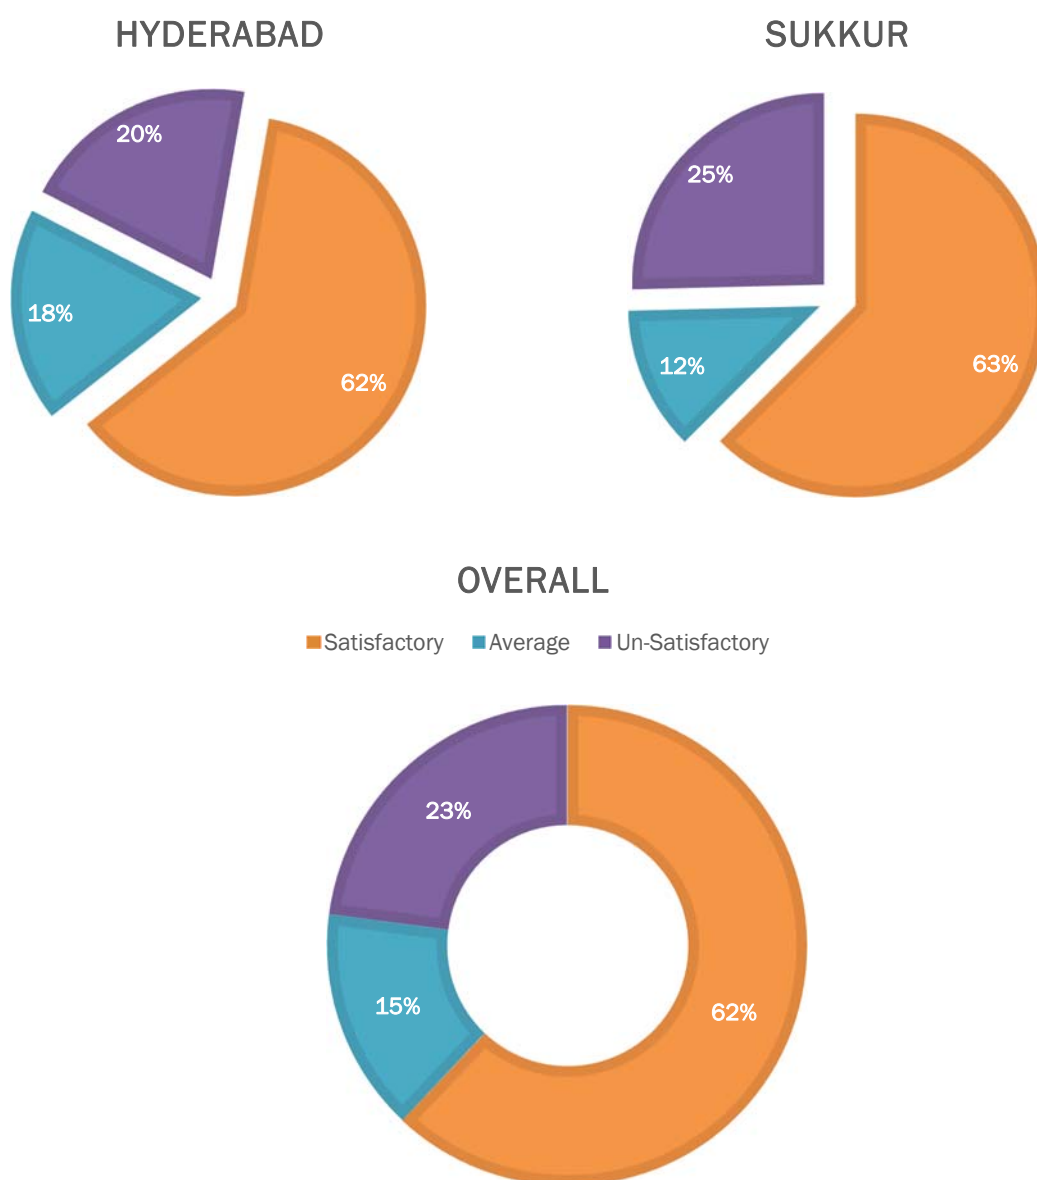

TREND ANALYSIS OF FIELD MONITORING OVER THE YEARS

Trend analysis of the number of field monitoring visits conducted over the last 6 years against the number of Annual Development Program schemes:


FISCAL YEAR	ADP SCHEMES	MONITORED	PERCENT
2010-11	1737	172	10%
2011-12	1373	493	36%
2012-13	2611	525	20%
2013-14	2463	1141	46%
2014-15	2937	821	28%
2015-16	2352	1017	43%
2016-17	2773	846	31%

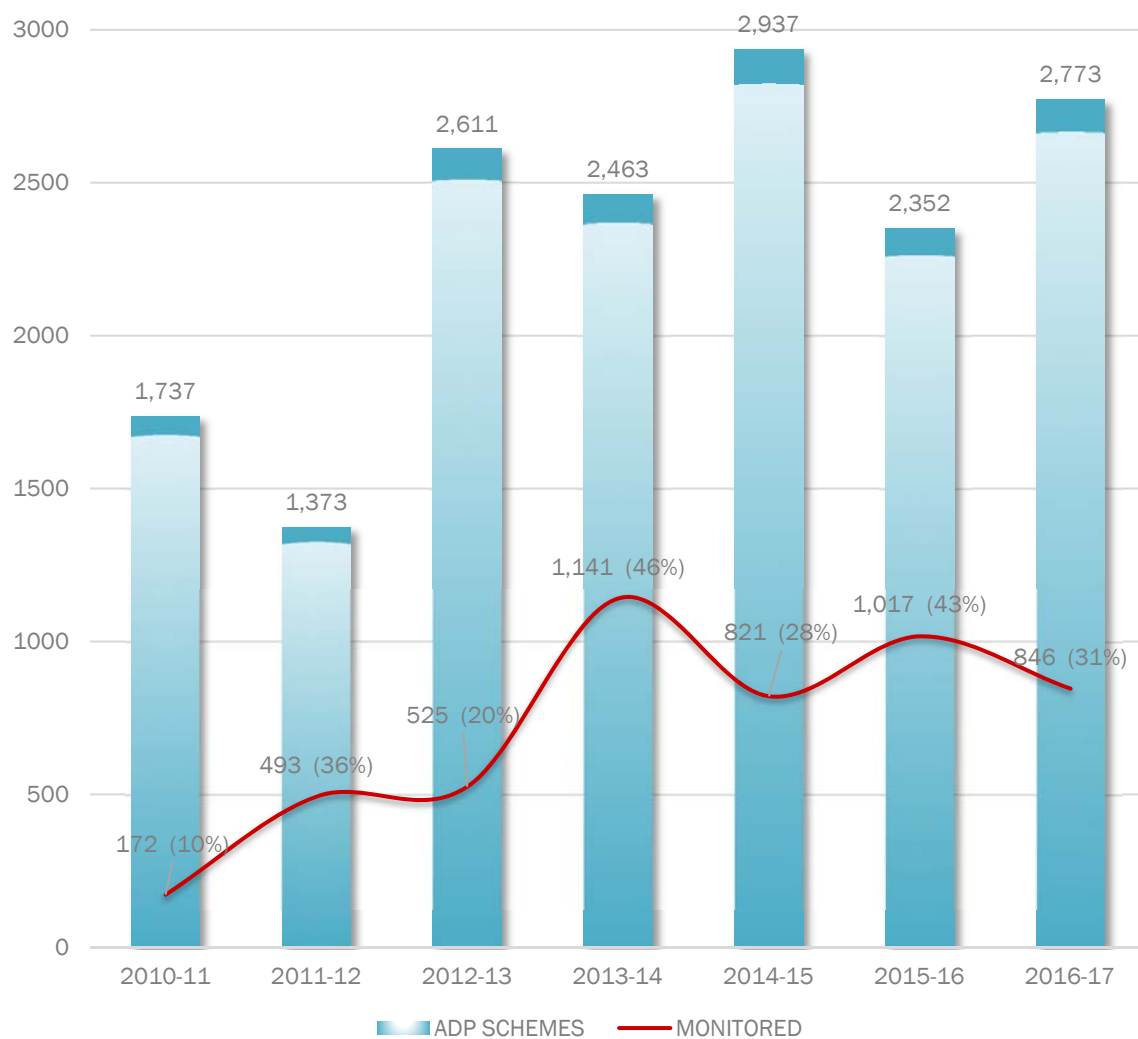

TREND ANALYSIS OF OBSERVATION TYPE

Below is the 5-year trend analysis of schemes found to be Satisfactory, Average and Unsatisfactory:

	2012-13	2013-14	2014-15	2015-16	2016-17
Satisfactory	20.57%	15.18%	20.15%	44.53%	62.06%
Average	52%	42.84%	42.56%	26.72%	15.01%
Unsatisfactory	27.43%	41.98%	37.29%	28.75%	22.93%

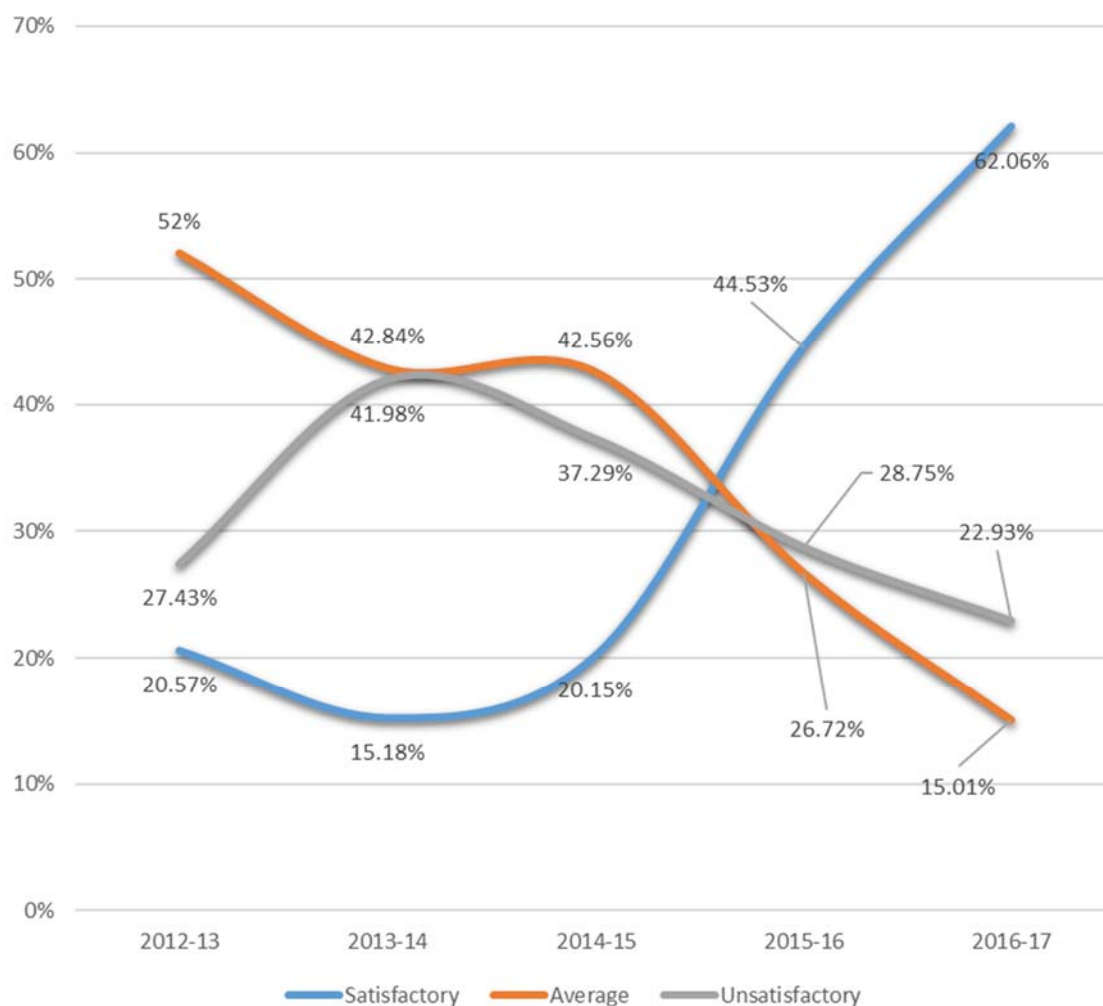

DEPARTMENT-WISE TREND OF UNSATISFACTORY SCHEMES

Below is a trend analysis of the number of schemes found to be unsatisfactory in FY 2016-17 as a percentage of total schemes monitored. Index arrow shows the increasing/decreasing trend in % of current FY's unsatisfactory schemes versus the mean of previous 3-year's % of unsatisfactory schemes.


DEPARTMENTS / SECTORS	% OF UNSATISFACTORY SCHEMES					INDEX
	2013-2014	2014-2015	2015-2016	3-YR AVG	2016-2017	
Agriculture	18%	35%	22%	25%	13%	↓
Auqaf	38%	50%	38%	42%	0%	↓
Board of Revenue	50%	38%	67%	52%	29%	↓
Culture	50%	31%	23%	35%	43%	↗
Education and Literacy	59%	43%	21%	41%	16%	↓
Energy	0%	0%	29%	10%	33%	↗
Environment	0%	100%	100%	67%	33%	↓
Food	28%	0%	0%	9%	100%	↗
Forest, Wildlife & CDA	23%	22%	13%	19%	27%	↗
Health	47%	64%	42%	51%	36%	↓
Home	25%	56%	9%	30%	14%	↓
Human Rights	100%	50%	43%	64%	20%	↓
Industrial & Commerce	75%	50%	50%	58%	0%	↓
Information Technology	0%	50%	40%	30%	0%	↓
Irrigation (Water & Drainage)	40%	28%	33%	34%	25%	↓
Labour Dept.	100%	25%	17%	47%	33%	↓
Livestock and Fisheries	32%	32%	28%	31%	46%	↗
Local Government	25%	25%	19%	23%	14%	↓
Minorities & Affairs	0%	50%	75%	42%	45%	↗
Planning & Development	0%	38%	11%	16%	0%	↓
Population Welfare	0%	0%	100%	33%	0%	↓
Public Health Engineering	48%	32%	21%	34%	11%	↓
Rural Development	50%	25%	14%	30%	11%	↓
S.G.A.and Coordination	20%	0%	17%	12%	0%	↓
Social Welfare	50%	50%	33%	44%	33%	↓
Special Initiatives Unit	0%	14%	60%	25%	0%	↓
Sports & Youth Affairs	43%	17%	22%	27%	24%	↓
STEVT	100%	100%	25%	75%	100%	↗
Transport & Comm. (Roads)	0%	0%	67%	22%	0%	↓
Women Development	67%	50%	100%	72%	25%	↓
Work and Service	45%	29%	29%	34%	27%	↓
AVERAGE	37%	36%	38%	37%	24%	↓
NO. OF DEPARTMENTS WHERE THE % OF UNSATISFACTORY SCHEMES DECREASED					↓	24
NO. OF DEPARTMENTS WHERE THE % OF UNSATISFACTORY SCHEMES INCREASED					↗	7

THIRD PARTY MONITORING (TPM)

Sindh Cabinet, taking initiative in its meeting held on 16-06-2008 to improve quality of construction through monitoring of projects by the Planning & Development Department, deduced that in order to seek un-biased report, Third Part Monitoring (TPM) of the projects was necessary.

Year wise 1% Amount for Third Party Monitoring, for every development scheme, is being deposited into National Bank of Pakistan Account since 2008-09 for the same. Efforts are being made by the monitoring officers to ensure better recovery of this amount. Below is the summary of amount received so far:

YEAR WISE 1% TPM DETAIL	
Year	Amount (Rs. in million)
2008-09	5.778
2009-10	22.184
2010-11	12.628
2011-12	29.787
2012-13	32.759
2013-14	33.416
2014-15	77.316
2015-16	60.465
2016-17	66.000
TOTAL	340.333

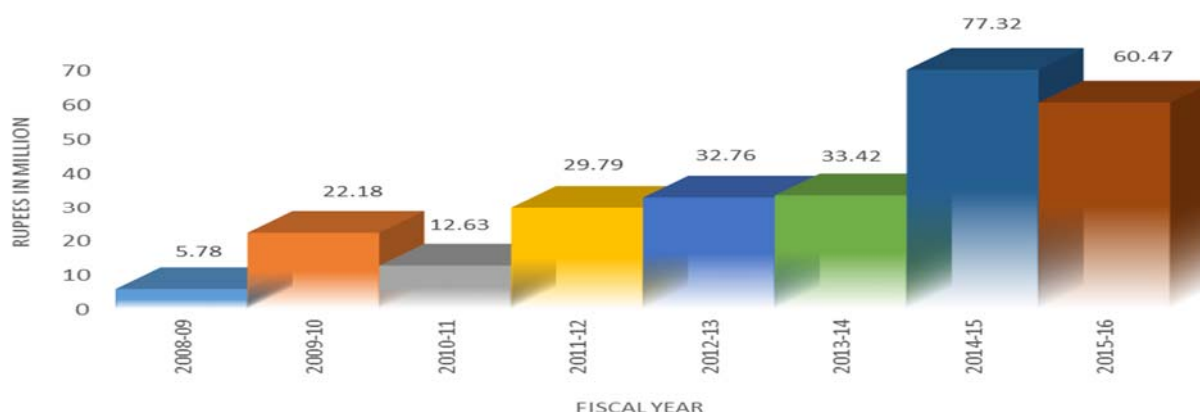

The use of third party monitoring as a risk management tool in near and far-flung volatile areas has helped highlight, neutral, unbiased, important quality, ethical, and highly technical issues reporting.

Such professional reporting methodology, taking various aspects of examination has helped MEC officers, in not just improving better and more comprehensive reporting but also highlighted rectification way forward steps for easier understanding of issues for the non-technical decision making officers – This has helped in taking some major decisions empower MEC, as listed later in this annual report.

OVERVIEW OF FINDINGS FROM FIELD MONITORING

The below findings from the crust of flaws and the common lessons learnt making the Monitoring Year of 2016-17, that have accumulated as a result of MEC's monitoring and evaluation regime vide project documentation analysis. These documents include project's PC-I, MEC Project Profile, Site Observations, Financial Instruments, Tender Documents, Drawings & Test Reports, Revenue as well as Capital Components of both, the Infrastructure as well as Social Sector Projects.



As in any M&E Plan, the documentation analysis is then compared to the Government Rules and Regulations made by regulatory bodies such as SPPRA, SEPA and PEC as well as the National and International Standards set for Engineering Works such as Pakistan Building Code, Composite Rates, ACI code for buildings and AASHTO standards for roads. These comparisons materialize into the shortcomings that have been reflected below according to the type of infrastructure mentioned.

ROADS

- Use of oversize & unsuitable stone in sub base & base
- Test regime is totally missing including Field Density tests and Soil classification tests etc.
- Compaction of earth work not being carried out as per specifications
- Meagre allocation on some schemes which take years to complete
- Camber Control is missing; no use of camber plates at execution level
- Berms/shoulders are not properly dressed and compacted
- Uneven road top with undulations at certain places (Road Grade not controlled properly)
- Improper control of super elevation at curves
- Use of poor quality bricks for road edging
- Concrete ratio less than specification in top slab of culverts
- Improper concrete cover to steel in concretion operations
- Lack of supervision was observed in execution work
- Engagement of more than one contractor on a single project.



IRRIGATION (WATER & DRAINAGE)

- Test regime is totally missing in the works. No tests reports were available at site at all places visited
- The back filling is not being properly carried out along retaining walls
- Suitability of material for embankment raising is not taken care of
- No soil classification of the material is carried out from any reputable laboratory
- It was found that sides of canals/minor/distributaries were not correctly dressed and sloped at both sides
- Gaps/spaces in stone pitching works were not filled with specified cement mortar.
- Damaged stone pitching work was found at most of the places
- In the stone work, the size of stones was not as per specification and at most of the places, oversize stone was used. Quality of stones was also found to be not up to mark
- CC coping work was not found at most of stone pitching works
- In most of the cases, quality of plaster work was poor
- Most culverts had no parapet walls
- Quality of shuttering, including props, should be improved
- Spacing of Reinforcement Steel and use of Spacer Blocks to needed to be ensured
- Deployment of engineering staff with contractors as per Pakistan Engineering Council By-laws has to be enforced
- Multiple contracts for small portion of work should be discouraged/avoided.



PUBLIC HEALTH AND ENGINEERING (PHED)

- The main reason for non-functionality of PHED schemes is non-provision of electric connection/energization of the schemes
- The engineers lack the knowledge of the new methodology of working on M.S. Pipe and P.E pipes
- The waste water is generally disposed in to the nearby river and canals without treatment at the oxidation ponds
- Sand blasting is not done for removal of rust from the pipes
- Wrapping and coating of pipes is not properly done
- Welding /Jointing is done by the unskilled workers



- Sand Cushion to pipes is mostly not done at the bottom and side for the protection of thrust created by the water pressure
- Pressure testing not done of M.S. pipe & P.E pipe for checking the leakages, in either the joints or the pipes which are buried in the soil
- Oxidation ponds are not constructed at some places for natural treatment of water
- Invert levels and gradient is not being properly maintained with the result that water remains stagnant in most of the drains
- Low quality CC in streets is being done with improper cement concrete ratio & improper thickness.

BUILDINGS

- Test regime is totally missing in Building works as well. Tests like slump test, gradation of fine & coarse aggregates, cube crushing test, steel tests (yield & tensile strength) & soil test (classification of soil) are not carried out in most of the cases
- Pakistan Engineering Council (PEC) bylaws require deployment of Project Engineers by the contractors. This requirement is being completely ignored
- Honey combing was found to be visible in many structures, which shows improper mixing and placement of concrete (No concrete mix design is prepared even in heavy concreting work)
- Purchase of steel was generally being made locally having no recognized good quality make. The use of under gauge steel was observed in some projects
- Appropriate attention is not being paid for quality of shuttering, use of spacer blocks for proper concrete cover and placement of reinforcement steel in structural members
- Quality of bricks and concrete blocks was not up to the mark.
- The compaction of the earth filling inside plinth is not taken care of.
- Lack of supervision was observed in execution work by the XEN concerned.



EDUCATION

- Poor survey for need for establishment of a school in terms of enrolment
- Duplication of schools in some areas as source of funding varies i.e. from federal, Provincial, district or other source
- Misuse of school buildings in villages especially used as autaq, store rooms, cattle farms, grain go-downs, used marriage venue. At one place in Shikarpur a school was being used as a police station building



- The purchasing of Revenue component is centralized and barely any data is given at district level since at local level there is very little knowledge concerning purchasing of revenue component

HEALTH

- Overall quality of construction works was found to be as is in building sector
- The health officials have very little knowledge on how to operate the latest & costly machines
- The machines are purchased but are not installed at most of the places & kept in packing for years which then become obsolete
- Temperature control maintenance is very poor due to which the vaccines & other drugs lose efficacy
- Duplication of Revenue component as no-one knows from which source the purchasing has been made i.e. Federal, Provincial, Donor Agency or NGO (no tagging of source is done for purpose of identification)
- Rarely the procurement procedure for revenue component is shared with field teams.



AGRICULTURE & FOREST, LIVESTOCK & FISHERIES

- The issues in the building component works are identical as specified above under the Buildings Sector
- Under utilization of the Revenue component is the biggest issue observed of the schemes falling under these departments
- A centralized purchasing system has been observed in most of the schemes.
- The regional offices are without financial powers to run their offices efficiently
- Limited coordination with MEC team by these departments
- Delay in providing PC-I and statical data related to scheme
- In Sindh-Based Schemes, District-wise financial bifurcation is not provided
- Mostly Sindh based schemes are operated and controlled by the head offices at Hyderabad & local offices have little knowledge about the schemes.



MAJOR FINDINGS FROM TECHNICAL ANALYSIS

1. Over the years, there has been an increase in the total financial allocation/budget for the ADP, from 111bn in 2011-12 to 200bn in 2016-17, a decrease in the releases is observed, from 92% to 87%, while the utilization factor jumped from 83% to 91%
2. The number of total ADP schemes *increased* from 1,737 to 2,773, and *new schemes* from 493 to 995, the weight of on-going schemes *increased* from 1244 in FY 2011-12 to 1776 in FY 2016-17
3. The highest total cost of schemes in FY 2016-17 was of the Irrigation Department at Rs. 119,923.625 million followed by the Works & Services Department at Rs. 111,941.050 million
4. Only 6% of the ADP 2016-17 comprised of schemes costing Rs. 1 billion and above as compared to 55% in the previous FY.
5. Highest allocation of funds for ADP schemes was given to Local Government and House Town Planning Department (Rs. 20,731), followed by Education Sector (Rs. 17,233bn.)
6. Highest percentage of unsatisfactory schemes monitored by MEC, reported through field monitoring, were found to be in Livestock & Fisheries, Minorities & Affairs and Culture Departments respectively.
7. 15 out of 39 departments completely failed to comply against the observations & recommendations of MEC
8. Of the 846 schemes that were visited by the MEC, during the FY 2016-17, 62% were found to be satisfactory, 15% to be average while 23% of the schemes were unsatisfactory.
9. The average compliance response received from the line departments was 26% against the set of observations and recommendations of MEC reported to the secretaries of the concerned line departments respectively.



MAJOR DECISIONS TO EMPOWER MEC

Some of the important decisions recently taken include:

- ✓ Funds to be released by Finance Dept. based on the recommendation of MEC.
- ✓ Publication of MEC Annual Report to be a regular activity.
- ✓ Schemes which are marked as Unsatisfactory by MEC and subsequently there is non-compliance by the line departments to rectify as recommended in the report, will be referred to anti-corruption agencies for necessary action
- ✓ Development of ADP Progress Monitoring Dashboard is being developed with the assistance of World Bank to help gain better insights on development works
- ✓ Establishment of new monitoring regional offices of MEC at Karachi and Larkana
- ✓ Construction of MEC buildings at Hyderabad and Sukkur
- ✓ Provincial ADP Scheme #1733 “Construction of Regional Office of MEC, P&D Department at Hyderabad & Sukkur” included in ADP 2016-17 to strengthen M&E.
- ✓ Regularization of contractual staff of MEC Scheme “Strengthening of MEC including Third Party Monitoring”
- ✓ Inclusion of New ADP 2017-18 Scheme #1963 “Strengthening & capacity building of Regional Offices of M&E Cell at Hyderabad & Sukkur”
- ✓ Expansion in the of number of Line Departments data in the ADP Progress Monitoring System being implemented with the technical assistance of the World Bank.



PICTORIAL OVERVIEW

GENERATED FROM ONLINE PAPERLESS FILE MANAGEMENT SYSTEM

SELECTED SNAPSHOTS OF VARIOUS ACTIVITIES

Some selective snapshots of MEC field visits during fiscal year 2016-17.



Front View of Police Facilitation Centre at Sukkur



Measuring thickness of Asphalt layer at SITE Sukkur



Monitoring visit of Solar Tube wells at Cantonment area of Pano Akil



Discussion with E/A regarding scheme of Solar tube wells at Cantonment area of Pano Akil



Soft Launch of ADP PROGRESS MONITORING DASHBOARD at MEC MIS DIRECTORATE



Measuring thickness of Coping of CC lining of Gajra Branch
Shaheed Benazirabad



View of a Cafeteria at
Cadet College Ghotki



View of a Class room at Cadet College
Ghotki



Stone pitching of IP side of Rice Canal Larkana



Monitoring visit of boring of Solar tube wells at Cantonment area of
Pano Akil



Checking of coping of CC lining Gajra Wah Shaheed Benazirabad



Monitoring visit of RO Plants
at Larkana



Missing taps for RO Plants
at Larkana



Some Selected Field Visit Spanshots



Presentation On ADP Progress Monitoring Dashboard At Foakh Tower Office Of MEC MIS Directorate



MEC Karachi Team At Foakh Tower Office

Training of Line Department Officers on using ADP Progress Monitoring Dashboard and distribution of Smartphones



INTENTIONALLY LEFT BLANK



*EXAMINING QUALITY,
FACILITATING PROGRESS*

ANNEXURE A

**DEPARTMENT WISE SCHEMES MONITORED
PAGE 49 TO PAGE 112**

DEPARTMENT-WISE LIST OF SCHEMES MONITORED

Visit & Publish Date from: 01/07/2016 To: 30/06/2017

Status: In Process & Published Reports

#	ADP #	Name of Scheme	Report Type	Visit Date	Department	Report Published	Location	Cost
1.	26	Modernization of training and research facility in agricultural engineering through establishment of agricultural engineering training institute at Nareja.	Un-Satisfactory	14-04-2017	Agriculture	14-05-2017	Hyderabad	383.885
2.	04	Development of technology for production of hybrid seed in Sindh	Satisfactory	14-03-2017	Agriculture	11-04-2017	Thatta, Hyderabad	100.000
3.	1	Reclamation of Saline Soils through Effective Measures.	Satisfactory	15-02-2017	Agriculture	28-04-2017	Thatta, Badin	256.545
4.	26	Modernization of Training & Research Facilities in Agriculture Engineering Workshop, Nareja (Revised) (Compliance visit)	Average	16-01-2017	Agriculture	17-02-2017	Hyderabad	383.885
5.	33	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted)	Satisfactory	16-12-2016	Agriculture	07-03-2017	Tando Allahyar	6,120.000
6.	35	Additional Lining of Already Improved Water Courses in Sindh, Total Cost Rs.990.222 M (GOS share-Rs.634.572 M & Farmer share-Rs.355.65 M 3	Satisfactory	14-12-2016	Agriculture	19-01-2017	Ghotki	634.572
7.	33	Sindh Irrigated Agriculture Productivity Enhancement Program Phase-I Project (World Bank Assisted) (Total Cost Rs.30139.75 M, IDA Share Rs.18686.64 M, GoS share: Rs.6120.0 M and Farmers share Rs.5333.11 M) (C:11651.08 M+R:18488.669 M)	Satisfactory	16-11-2016	Agriculture	24-01-2017	Mirpurkhas	6,120.000
8.	10	Establishment of Agro-Export Processing Zone for Fruits, Vegetables, Flowers & Allied Processing Products from Local Farms / Processing Units to Overseas Markets Karachi, Hyderabad, Badin Mirpurkhas, Shaheed Benazirabad, Naushero Feroz, Khairpur and	Satisfactory	14-11-2016	Agriculture	02-12-2016	Thatta, Karachi	490.513
9.	5	Additional Lining of Already Improved Water Courses in Sindh, Total Cost Rs.990.222 M (GOS share-Rs.634.572 M & Farmers share-Rs.355.65 M 2	Satisfactory	14-11-2016	Agriculture	15-12-2016	Khairpur	634.572
10.	8	Up-Gradation of Pesticide and Fertilizer Quality Control and Testing Laboratories (Re-revised) (C:10.075+R:49.133)	Satisfactory	08-11-2016	Agriculture	29-11-2016	Mirpurkhas	59.208

11.	1	Reclamation of Saline Soils through Effective Measures (Total Cost Rs.431.595 M GOS share Rs.256.545 M)	Satisfactory	18-10-2016	Agriculture	15-12-2016	Mirpurkhas, Badin	256.545
12.	2	Rehabilitation of Rice and Cotton Research Station Thatta (Compliance visit)	Average	10-10-2016	Agriculture	18-11-2016	Thatta	110.210
13.	10	Establishment of Agro-Export Processing Zone for Fruits, Vegetables, Flowers & Allied Processing Products from Local Farms / Processing Units to Overseas Markets Karachi, Hyderabad, Badin MPKS, SBA, Naushero Feroz, Khairpur & Ghotki (Compliance Visit)	Un-Satisfactory	03-10-2016	Agriculture	31-10-2016	Karachi	490.513
14.	11	Construction of Training Resource Centre and Repair of Existing facilities at Agriculture Training Institute, Sakrand (C:75.317+R:13.683)	Satisfactory	19-09-2016	Agriculture	18-10-2016	Shaheed Benazirabad	89.000
15.	35	Additional Lining of Already Improved Water Courses in Sindh, Total Cost Rs.990.222 M (GOS share-Rs.634.572 M & Farmer share-Rs.355.65 M)	Satisfactory	19-09-2016	Agriculture	15-12-2016	Jamshoro	634.572
16.	35	Additional Lining of Already Improved Water Courses in Sindh, Total Cost Rs.990.222 M (GOS share-Rs.634.572 M & Farmer share-Rs.355.65 M)	Satisfactory	24-08-2016	Agriculture	15-12-2016	Tando Mohd. Khan	634.572
17.	08	Up-Grading of Pesticide and Fertilizer Quality Control and Testing Laboratories (Revised) (C:10.075+R:49.133) Sukkur	Satisfactory	15-08-2016	Agriculture	19-09-2016	Sukkur, Mirpurkhas, Larkana	59.208
18.	1	Renovation construction and expansion of office building of Bureau of Supply & Prices (C:189.074+R:10.0)	Satisfactory	02-08-2016	Agriculture	03-10-2016	Karachi	199.074
19.	35	Additional lining of already improved water courses in Sindh. (Location: District Badin)	Satisfactory	28-07-2016	Agriculture	19-09-2016	Badin	634.572
20.	31	Additional lining of watercourses No-27-BR Baharwah,87-L Mirwah and 56-L, Pandhirowah District Khairpur	Satisfactory	27-05-2016	Agriculture	03-08-2016	Khairpur	50.300
21.	12	Construction of Training Resource Centre and Repair of Existing facilities at Agriculture Training Institute, Sakrand (C.75.317 + R.13.683) CAPITAL	Un-Satisfactory	02-05-2016	Agriculture	01-08-2016	Shaheed Benazirabad	89.000
22.	08	Horticulture Training Project for increasing earning capability of subsistence Farmers (Revised) N.Feroze	Satisfactory	28-03-2016	Agriculture	01-07-2016	Naushero Feroz	75.719

23.	10	Adoption of Farmers Field School Approach in Agriculture Extension for Dissemination Agriculture Technology Among the Farming Communities.(QSKot &Larkana)	Satisfactory	16-03-2016	Agriculture	01-07-2016	Larkana, Qambar Shahdadkot	50.960
24.	47	Construction of Mosque & Allied Facilities at Dargah Miskeen Shah at District Kamber Shahdadkot	Satisfactory	09-08-2016	Auqaf	07-09-2016	Qambar Shahdadkot	22.000
25.	43	Construction / Reconstruction / Rehabilitation & allied facilities of Dargahs in Sindh (6 Nos)T.M Khan (01), Thatta (02), Khairpur (01) Hyderabad (01) and Larkana (01).	Satisfactory	22-07-2016	Auqaf	22-09-2016	Hyderabad	10.811
26.	43	Construction / Reconstruction / Rehabilitation & allied facilities of Dargahs in Sindh (6 Nos)T.M Khan (01), Thatta (02), Khairpur (01) Hyderabad (01) and Larkana (01).	Satisfactory	18-07-2016	Auqaf	19-09-2016	Thatta	34.396
27.	43	Construction / Reconstruction / Rehabilitation & allied facilities of Dargahs in Sindh (6 Nos)T.M Khan (01), Thatta (02), Khairpur (01) Hyderabad (01) and Larkana (01).	Satisfactory	13-07-2016	Auqaf	22-09-2016	Tando Mohd. Khan	32.802
28.	63	Construction of Office of District Registrar , at Karachi andSub-Registrar Offices (22 Nos) at Head Quarters all Districts inSindh	Worst	13-03-2017	Board of Revenue	18-04-2017	Thatta	160.200
29.	63	Construction of Office of District Registrar , at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sind	Satisfactory	10-01-2017	Board of Revenue	15-02-2017	Jamshoro	160.200
30.	63	Construction of Office of District Registrar , at Karachi and Sub-Registrar Offices(22 Nos) at Head Quarters all Districts in Sindh	Average	05-01-2017	Board of Revenue	15-02-2017	Tando Mohd. Khan	160.200
31.	63	Construction of Office of District Registrar , at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sindh	Satisfactory	22-12-2016	Board of Revenue	11-01-2017	Tando Allahyar	160.200

32.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	21-10-2016	Board of Revenue	29-11-2016	Hyderabad	9,420.880
33.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	19-10-2016	Board of Revenue	08-12-2016	Tando Mohd. Khan	9,420.880
34.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	18-10-2016	Board of Revenue	08-12-2016	Jamshoro	9,420.880
35.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	14-10-2016	Board of Revenue	08-12-2016	Sujawal	9,420.880
36.	63	Construction of Office of District Registrar , at Karachi and Sub-Registrar Offices (22 Nos) at Head Quarters all Districts in Sindh 2-Kashmore Kandhkot	Satisfactory	14-10-2016	Board of Revenue	09-11-2016	Kashmore	160.200
37.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	10-10-2016	Board of Revenue	08-12-2016	Thatta	9,420.880
38.	62	Development of townships in major urban centres (50,000 Nos 120 square yard plots with all civic services) (Revised)	Satisfactory	04-10-2016	Board of Revenue	08-12-2016	Karachi	9,420.880
39.	47	Computerization and Establishment of Land Administration & Revenue Management Information System (LARMIS) , BOR, Sindh	Un-Satisfactory	30-05-2016	Board of Revenue	08-08-2016	Karachi	4,997.453
40.	47	Computerization and Establishment of Land Administration & Revenue Management Information System (LARMIS) , BOR, Sindh	Un-Satisfactory	30-05-2016	Board of Revenue	08-08-2016	Karachi	4,997.453
41.	47	Computerization and Establishment of Land Administration and Revenue Management Information System (LARMIS) ADP # 47 (2015-16)	Un-Satisfactory	13-05-2016	Board of Revenue	08-08-2016	Khairpur, Shikarpur, Sukkur	4,997.453
42.	71	Renovation & Rehabilitation of Chief Minister House, Karachi	Satisfactory	04-09-2016	Chief Minister Secretariat	29-11-2016	Karachi	123.890
43.	111	Restoration of Two Vehicles of Madere-e-Millat Fatima Jinnah (Compliance Visit)	Satisfactory	10-05-2017	Culture	15-05-2017	Karachi	30.000
44.	94	Research, Compilation, Consolidation & Printing of history of Sindh. (Compliance Visit)	Satisfactory	09-05-2017	Culture	15-05-2017	Karachi	47.497

45.	77	Establishment of Museum at Kot Diji, District Khairpur (C:32.490+R:6.337)	Un-Satisfactory	07-02-2017	Culture	03-04-2017	Khairpur	38.827
46.	96	Construction of Motel / Hotel at Garhi Khuda Bux Bhutto Larkano. (C:92.266+R:27.375)	Un-Satisfactory	25-01-2017	Culture	20-05-2017	Larkana	119.641
47.	99	Improvement / Renovation of Facilities at Mithi Rest House at Tharparkar (C:49.626+R:9.784)	Satisfactory	19-01-2017	Culture	17-02-2017	Tharparkar	59.410
48.	120	Missing allied facilities at Motel Nagarparkar (C:17.153+R:2.847)	Un-Satisfactory	20-12-2016	Culture	03-01-2017	Tharparkar	20.000
49.	119	Interior & Exterior Conservation & Surface Decoration of Khudabad Mosque, Dadu (C:37.884+R:2.116)	Un-Satisfactory	13-12-2016	Culture	03-01-2017	Dadu	40.000
50.	79	Estt. Of Public Libraries in Sindh including Pir-jo-Goth Khairpur, Sachal Goth Karachi and Cultural Complexes(C:128.269+R:15.379)	Un-Satisfactory	13-12-2016	Culture	11-01-2017	Karachi	143.648
51.	116	Conservation / Restoration / Construction of Masjid Muhammad Bin Qasim Arore, District Sukkur (C:27.500+R:2.500)	Un-Satisfactory	24-11-2016	Culture	03-04-2017	Sukkur, Sanghar	30.000
52.	113	Renovation / Extension of Sambara Inn Larkana	Satisfactory	23-11-2016	Culture	17-01-2017	Larkana	40.000
53.	111	Restoration of Two Vehicles of Mader-e-Millat Fatima Jinnah (R:30.00)	Un-Satisfactory	22-11-2016	Culture	07-03-2017	Karachi	30.000
54.	94	Research, Compilation, Consolidation and Printing of History of Sindh.(R:51.813)	Un-Satisfactory	21-11-2016	Culture	07-03-2017	Karachi	47.497
55.	101	Construction of Office of the Department of Antiquities at Karachi and Sub Offices at Jamshoro and Sukkur (C:216.611+R:18.255) Karachi	Average	21-11-2016	Culture	16-12-2016	Karachi	234.866
56.	102	Conservation & Rehabilitation of Shah Jahan Mosque Thatta (C:61.752+R:5.952)	Un-Satisfactory	14-11-2016	Culture	29-11-2016	Thatta	67.704
57.	117	Re-Construction of Shah Abdul Latif Library Ratodero (C:31.470+R:8.530)	Un-Satisfactory	24-10-2016	Culture	29-11-2016	Larkana, Jacobabad	40.000
58.	101	Construction of Office of the Department of Antiquities at Karachi and Sub Offices at Jamshoro and Sukkur(C:216.611+R:18.255)	Satisfactory	20-10-2016	Culture	29-11-2016	Jamshoro	234.866
59.	121	Establishment of Shaheed Mohtarma Benazir Bhutto Public Library at Taluka Garhi Khairo (C:26.070+R:7.930)	Un-Satisfactory	17-10-2016	Culture	09-11-2016	Jacobabad	34.000
60.	112	Re-construction of Tomb of Gen: Hosh Mohammad Sheedi at District Hyderabad (C:17.00+R:3.00)	Average	20-09-2016	Culture	30-09-2016	Hyderabad	20.000

61.	101	Construction of Office of the Department of Antiquities at Karachi and Sub Offices at Jamshoro and Sukkur (C:216.611+R:18.255)	Satisfactory	30-08-2016	Culture	19-09-2016	Sukkur	234.866
62.	78	Establishment of Sindh Kashi Institute at Bhitshah and Conservation & Restoration of Dabgeer Mosque Thatta (C:59.011+R:61.014)	Un-Satisfactory	22-08-2016	Culture	06-10-2016	Thatta	120.025
63.	105	Conservation / Rehabilitation & Rescue of Jamia Mosque Zangipur Distt. Jacobabad (C:25.785+R:6.271)	Satisfactory	18-08-2016	Culture	07-09-2016	Jacobabad	32.056
64.	83	Establishment of Public Libraries in Sindh (T.M Khan, S.B.A, Dadu, N.Feroze, Karachi, Kashmore, Sukkur & Jamshoro) (C:346.510+R:101.830)	Un-Satisfactory	15-08-2016	Culture	22-09-2016	Dadu	448.340
65.	87	Establishment of Abdul Aziz Public Library at Pano Akil (C:25.955+R:7.514)	Un-Satisfactory	12-08-2016	Culture	19-09-2016	Sukkur	33.469
66.	81	Construction of Larkana Art Complex at Larkana. (C:53.327+R:23.611)	Satisfactory	08-08-2016	Culture	07-09-2016	Larkana	53.327
67.	100	Establishment of Archaeological Museum at Sukkur (C:26.177+R:3.352)	Satisfactory	05-08-2016	Culture	19-09-2016	Sukkur	29.529
68.	82	Establishment of Sindh Cultural Up-gradation of National Museum Karachi	Satisfactory	20-07-2016	Culture	22-09-2016	Karachi	340.963
69.	57	Establishment of Museum at Kot Diji	Satisfactory	23-05-2016	Culture	01-08-2016	Khairpur	38.827
70.	82	Rehabilitation of Wooden Roof of Shahi Bazar Shikarpur (C:54.786)	Satisfactory	16-05-2016	Culture	10-08-2016	Shikarpur	54.786
71.	98	Conservation/Rehabilitation of Jamia Mosque Hyder Wagho, District Jacobabad (C:21.158+R:7.180)	Satisfactory	26-04-2016	Culture	29-07-2016	Jacobabad	28.338
72.	105	Establishment of Khairpur Estate Museum (C:46.684+R:9.004)	Satisfactory	14-04-2016	Culture	29-07-2016	Khairpur	55.688
73.	97	Conservation & Restoration of Old Mukhtiarkari Building Shikarpur	Average	24-12-2015	Culture	01-07-2016	Shikarpur	54.786
74.	74	Protection, Preservation, Promotion and Development of World Heritage site of Mohenjo Daro ADP # 74	Satisfactory	28-09-2015	Culture	19-07-2016	Larkana	285.429
75.	90	Establishment of Archaeological Museum at Sukkur ADP.NO:90(2015-16)	Un-Satisfactory	11-08-2015	Culture	13-07-2016	Sukkur	29.529
76.	82	Rehabilitation Of Wooden Roof of Shahi Bazar Shikarpur	Satisfactory	10-08-2015	Culture	13-07-2016	Shikarpur	59.000
77.	258	Strengthening of Sukkur Institute of Business Administration (Sukkur IBA)	Satisfactory	06-08-2015	Culture	23-08-2016	Sukkur	492.070
78.	392	Establishment of Junior Section and Solar Energy Project at	Satisfactory	28-04-2017	Education and Literacy	31-05-2017	Larkana	629.258

		Cadet College Larkana (C: 413.339 + R: 215.919)2						
79.	256	Addition of Class rooms, Construction of Labs and Library in existing Secondary and Higher Secondary Schools in Sindh(2007-08 Programme.) (230 Units) (C: 885.951 + R: 339.620)	Average	27-04-2017	Education and Literacy	08-06-2017	Sukkur	1,225.571
80.	147	Construction of Two Rooms Shelterless Primary Schools in Sindh (2007-08 Programme) (450 Units) (C:468.152 + R: 53.550)	Satisfactory	21-04-2017	Education and Literacy	16-06-2017	Ghotki	521.702
81.	377	Establishment of Boys / Girls Degree Colleges in Sindh (2010-11 Programme) (23 Units)(C: 2243.732 + R: 181.171)	Un-Satisfactory	20-04-2017	Education and Literacy	19-05-2017	Tando Allahyar	2,424.903
82.	256	Addition of Class rooms, Construction of Labs and Library in Existing Secondary & Higher Secondary Schools in Sindh (2007-08 Programme.) (230 Units) (C: 885.951 + R: 339.620)	Un-Satisfactory	20-04-2017	Education and Literacy	13-06-2017	Shikarpur	1,225.571
83.	147	Construction of Two Rooms Shelterless Primary Schools in Sindh (2007-08 Programme) (450 Units) (C:468.152 + R: 53.550)	Un-Satisfactory	17-04-2017	Education and Literacy	07-06-2017	Kashmore	521.702
84.	372	Establishment of Benazir Bhutto Shaheed Institute of Management Science Dadu (C: 402.524 + R: 275.790)	Satisfactory	17-04-2017	Education and Literacy	14-05-2017	Dadu	678.314
85.	369	Establishment of Boys / Girls Degree Colleges in Sindh (23 Units) (C: 1217.733 + R: 181.171)	Satisfactory	17-04-2017	Education and Literacy	19-05-2017	Sukkur	1,398.904
86.	388	Establishment of Five (5) IBA Community Colleges (C: 498.901 + R: 251.944)	Average	17-04-2017	Education and Literacy	14-05-2017	Dadu	750.844
87.	251	Establishment of Public Schools in Sindh (05 Units) (Revised) (C: 1243.851 + R: 88.760)	Satisfactory	14-04-2017	Education and Literacy	14-05-2017	Tando Allahyar	1,332.611
88.	146	Up-gradation of Primary Schools to Middle Schools in Sindh (2007-08 Programme) (460 Units) (C: 1192.705 + R:109.020)	Average	13-04-2017	Education and Literacy	19-05-2017	Larkana	1,301.725
89.	373	Construction / Improvement of Hostel, Dinning Hall & OtherFacilities at Cadet Colleges at Larkana, Sanghar and Petaro(Revised) (C: 886.894 + R: 44.050)	Satisfactory	12-04-2017	Education and Literacy	14-05-2017	Jamshoro	930.944
90.	148	Introduction of Computer Education in Middle Schools in Sindh (2007-08 Programme) (230	Satisfactory	11-04-2017	Education and Literacy	19-06-2017	Shikarpur	525.382

		Units)(C: 236.042 + R: 289.340)						
91.	146	Up-gradation of Primary Schools to Middle Schools in Sindh (2007-08 Programme) (460 Units) (C: 1192.705 + R:109.020)	Un-Satisfactory	10-04-2017	Education and Literacy	31-05-2017	Shikarpur	1,301.725
92.	143	Provision of Missing Facilities Under Education Sector Reforms (ESR) (C:600.922 + R:6.752)	Un-Satisfactory	10-04-2017	Education and Literacy	19-06-2017	Jacobabad	607.674
93.	400	Installation of Solar System and LED Lights at Sukkur IBA (C: 11.435 + R: 245.798)	Satisfactory	21-03-2017	Education and Literacy	13-05-2017	Sukkur	257.234
94.	387	Remaining Works of Cadet College Ghotki (C: 461.990 + R: 35.981)	Un-Satisfactory	20-03-2017	Education and Literacy	19-05-2017	Ghotki	745.027
95.	456	Additional Work and Renovation of Scouts Auditorium Hall of Sindh Boys Scouts Association Karachi	Satisfactory	08-03-2017	Education and Literacy	13-04-2017	Karachi	15.483
96.	454	Construction of Scouting Facilities and Administration Block at Training Centre, Gulshan-e-Iqbal & Provision of Missing Facilities at Provincial Scouts Saddar Head Quarter Karachi (C: 46.734 + R: 2.000)	Satisfactory	06-03-2017	Education and Literacy	13-04-2017	Karachi	48.734
97.	526	Establishment of Model School at Shah Abdul Latif University Khairpur (Revised) (C:87.238 + R:1.960)	Satisfactory	06-03-2017	Education and Literacy	13-05-2017	Khairpur	89.198
98.	297	Repair & Renovation of Existing Primary & Secondary Schools (Boys/ Girls) Gulshan-e-Iqbal & New Karachi Towns Karachi	Average	03-03-2017	Education and Literacy	13-04-2017	Karachi	30.846
99.	281	Re-construction of Dangerous Elementary / High Schools in District Karachi Central . (C: 44.729 + R: 4.000)	Satisfactory	21-02-2017	Education and Literacy	03-04-2017	Karachi	48.729
100.	280	Re-construction of Dangerous Elementary / High Schools in District Karachi East . (C: 51.375 + R: 2.043)	Un-Satisfactory	13-02-2017	Education and Literacy	05-05-2017	Karachi	53.418
101.	277	Rehabilitation of Existing High Schools & Higher Secondary Schools, District Karachi East. (C:51.481 + R:6.000)	Satisfactory	08-02-2017	Education and Literacy	20-03-2017	Karachi	57.481
102.	415	Construction of Mohtarma Benazir Bhutto Auditorium Hall, Hostel & Other Facilities at Cadet College Larkana	Satisfactory	06-02-2017	Education and Literacy	03-04-2017	Larkana	412.436
103.	497	Sindh Skills Development Project (Component BBSYDP-I and STEVTA-II & III) (Cost	Un-Satisfactory	18-01-2017	Education and Literacy	28-02-2017	Khairpur	431.046

		Rs.2155.230 million) IDA Share: Rs.1724.184 million G.O.S Share: Rs:431.046 million						
104.	265	Re-construction / Improvement / Addition of Classrooms & Addition of XI-XII Classes in Existing Secondary Schools at Landhi & Korangi Towns, Karachi (02 Units) (C: 128.802 + R: 6.008)	Satisfactory	12-01-2017	Education and Literacy	11-04-2017	Karachi	134.810
105.	238	Re-construction of Elementary College for Women Korangi (Phase-II) (C: 64.326 + R:2.043)	Average	11-01-2017	Education and Literacy	15-02-2017	Karachi	66.369
106.	149	Up-gradation of Primary Schools to Middle Schools in Malir (C: 52.554+ R: 5.100)	Satisfactory	09-01-2017	Education and Literacy	03-04-2017	Karachi	57.654
107.	398	Strengthening of Sukkur Institute of Business Administration (Sukkur IBA) (C: 348.208 + R:143.862)	Satisfactory	06-01-2017	Education and Literacy	13-03-2017	Sukkur	492.070
108.	402	Rehabilitation of Existing College at Government Boys Degree College Sakrand, Government Degree College Malir Cantt. & Government Girls Degree College Sheikh Zaid Gulshan-e-Iqbal Karachi (C: 43.515 + R: 2.882)	Average	22-12-2016	Education and Literacy	27-02-2017	Shaheed Benazirabad	46.397
109.	239	Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh.	Satisfactory	21-12-2016	Education and Literacy	03-01-2017	Sanghar	428.763
110.	239	Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh (Compliance Visit)	Average	07-12-2016	Education and Literacy	02-01-2017	Badin	428.763
111.	383	Construction of Women Hostels for Teaching Staff in the Existing Girls Colleges in Sindh (Compliance Visit)	Satisfactory	06-12-2016	Education and Literacy	02-01-2017	Thatta	428.763
112.	177	Establishment of Single Section High School at Mir Ali Bazar Khairpur(C: 41.314 + R: 3.812), (To be funded out of 10% share of Royalty) 2	Satisfactory	24-11-2016	Education and Literacy	15-12-2016	Khairpur	45.126
113.	185	Up-gradation of Secondary Schools to Higher Secondary Schools in Sindh (2005-06 Programme) (C: 713.819 + R: 136.080)	Satisfactory	08-11-2016	Education and Literacy	15-12-2016	Sukkur	849.899
114.	254	Establishment of Single Section High Schools in Sindh (2008-09 Programme) (53 Units) (C: 1092.792 + R: 200.340)	Satisfactory	06-11-2016	Education and Literacy	15-12-2016	Sukkur	1,293.132
115.	276	Rehabilitation of Existing High Schools & Higher Secondary Schools, District Larkana	Satisfactory	25-10-2016	Education and Literacy	10-11-2016	Larkana	56.393

116.	403	Construction / Re-construction of Building in Existing Degree Colleges I. Government Boys Degree College (GBDC) Rato Dero & II. GBDC Larkano (B.Sc Block)	Average	24-10-2016	Education and Literacy	10-11-2016	Larkana	58.301
117.	279	Re-construction of Dangerous Elementary / High Schools in District Sanghar (C: 26.816 + R: 4.000)	Average	18-10-2016	Education and Literacy	30-12-2016	Sanghar	30.816
118.	372	Establishment of Benazir Bhutto Shaheed Institute of Management Sciences, Dadu	Satisfactory	17-10-2016	Education and Literacy	08-11-2016	Dadu	678.314
119.	255	Up-gradation of Middle Schools to High Schools (230 Units) & High Schools to Higher Secondary Schools (115 Units) in Sindh (2007-08 Programme) (C: 3081.519 + R: 1298.825)	Average	13-10-2016	Education and Literacy	09-11-2016	Shikarpur	4,380.344
120.	396	Immediate Needs for Sukkur IBA (Revised) (C: 287.561 + R: 39.979)	Satisfactory	23-09-2016	Education and Literacy	26-10-2016	Sukkur	327.540
121.	273	Rehabilitation of Existing High Schools & Higher Secondary Schools, District Hyderabad (AASP) (C: 53.119 + R: 5.600)	Satisfactory	22-09-2016	Education and Literacy	18-10-2016	Hyderabad	58.179
122.	288	Re-construction of Government Boys High School (GBHS) Makhdoom Ghulam Hyder, GBHS Saeed Khan Leghari Taluka Hala & Government Boys Primary School Panjmore, Taluka Saeedabad, Distt Matiari	Average	21-09-2016	Education and Literacy	18-10-2016	Matiari	37.741
123.	377	Establishment of Boys / Girls Degree Colleges in Sindh (2010-11 Programme) (23 Units) (C: 2243.732 + R: 181.171)	Satisfactory	19-09-2016	Education and Literacy	26-10-2016	Sukkur	105.430
124.	286	Improvement of Existing Public Schools in S.B.A Division	Satisfactory	09-09-2016	Education and Literacy	19-10-2016	Shaheed Benazirabad	38.927
125.	286	Improvement of Existing Public Schools in S.B.A Division	Satisfactory	06-09-2016	Education and Literacy	02-11-2016	Naushero Feroz	59.035
126.	392	Establishment of Junior Section and Solar Energy Project at Cadet College Larkana (C: 413.339 + R: 215.919)	Satisfactory	02-09-2016	Education and Literacy	21-10-2016	Larkana	629.258
127.	290	Repair / Renovation / Restoration / Up-liftment of GGHSS N.J.V Karachi	Satisfactory	26-08-2016	Education and Literacy	19-10-2016	Karachi	59.968
128.	289	Re-construction of Dangerous Government Boys Secondary School Camp-4 & Repair of Government Girls Secondary School Camp-5 of PAF Base Sindh Government Schools located at P.A.F Base Faisal, Karachi (C:55.428 + R:3.014)	Average	25-08-2016	Education and Literacy	21-10-2016	Karachi	58.442

129.	455	Construction / Re-construction of Existing Offices of Field Officers of Education & Literacy Department Larkana Division (C: 46.269 + R: 4.026)	Satisfactory	24-08-2016	Education and Literacy	19-09-2016	Shikarpur	50.295
130.	282	Construction / Re-construction of Building in Existing Secondary Schools PAF Base Shahbaz Jacobabad. (C: 54.000 + R: 2.397)	Un-Satisfactory	18-08-2016	Education and Literacy	19-09-2016	Jacobabad	56.397
131.	385	Establishment of Jam Mumtaz Hussain Dahar Government Boys Degree College Ubaro, District Ghotki (C: 98.119 + R: 7.877)	Satisfactory	09-08-2016	Education and Literacy	22-09-2016	Ghotki	105.996
132.	458	Construction / Re-construction of Divisional Sub-Head Quarter of Sindh Boy Scouts Association at Shikarpur (C: 46.036 + R: 1.434)	Satisfactory	05-08-2016	Education and Literacy	19-09-2016	Shikarpur	47.470
133.	179	Rehabilitation / Addition of Class Rooms & Gymnasium Hall at GBPS St. Marie & GGSS Safia Memorial Jamshed Town, Karachi	Average	02-06-2016	Education and Literacy	13-07-2016	Karachi	84.918
134.	287	Schools Improvement through Adopt a School Intervention Sukkur Division (AASP)	Satisfactory	31-05-2016	Education and Literacy	18-08-2016	Shaheed Benazirabad	60.000
135.	185	Up-gradation of Secondary Schools to Higher Secondary Schools in Sindh (2005-06 Programme)	Satisfactory	27-05-2016	Education and Literacy	01-08-2016	Sukkur	42.495
136.	220	Provision of Furniture to Schools Constructed under SBEP in District Khairpur (Taluka Faiz Gang, Gambat, Kingri, Kot Diji & Sobo Dero)	Satisfactory	16-05-2016	Education and Literacy	01-09-2016	Khairpur	45.000
137.	Non-ADP	Rehabilitation of existing primary schools in Districts Sanghar under Pak MDG's community Development Programme.	Satisfactory	09-05-2016	Education and Literacy	13-07-2016	Sanghar	2.566
138.	1238	Integrated rehabilitation of existing Elementary Schools in District Larkana	Satisfactory	05-05-2016	Education and Literacy	17-08-2016	Larkana	50.965
139.	1233	Integrated rehabilitation and provision of missing facilities to existing elementary schools Taluka Ratodero, District Larkana (50 units).	Satisfactory	05-05-2016	Education and Literacy	12-08-2016	Larkana	195.668
140.	1234	Integrated rehabilitation and provision of missing facilities to existing elementary schools, District Larkana (69 units).	Satisfactory	05-05-2016	Education and Literacy	19-09-2016	Larkana	295.913
141.	1237	Construction of additional lecture halls (10 Nos.) @ Govt. Girls Degree College Larkana.	Satisfactory	04-05-2016	Education and Literacy	01-08-2016	Larkana	40.590

142.	136	Construction of One Additional Class Room in Existing Primary Schools (03 Nos.) & Rehabilitation of Primary School (01 No.) in District Kashmore	Un-Satisfactory	28-04-2016	Education and Literacy	03-08-2016	Kashmore	8.500
143.	227	Establishment of Benazir Bhutto Shaheed Institute of Management Sciences, Dadu	Satisfactory	28-04-2016	Education and Literacy	22-07-2016	Dadu	678.314
144.	233	Establishment of Shaheed Mohtarma Benazir Bhutto Govt.College of Education at Larkana	Satisfactory	27-04-2016	Education and Literacy	10-08-2016	Larkana	178.761
145.	161	Establishment of Single Section High Schools in Sindh (2008-09 Programme) (53 Units)	Un-Satisfactory	15-04-2016	Education and Literacy	16-08-2016	Shaheed Benazirabad	73.083
146.	1230	Rehabilitation of Government Naz High School Khairpur, Taluka Khairpur	Satisfactory	15-04-2016	Education and Literacy	01-08-2016	Khairpur	10.000
147.	161	Establishment of Single Section High Schools in Sindh (2008-09 Programme) (53 Units)	Un-Satisfactory	12-04-2016	Education and Literacy	16-08-2016	Sukkur	73.197
148.	224	Establishment of Boys / Girls Degree Colleges in Sindh (23 Units)	Un-Satisfactory	11-04-2016	Education and Literacy	24-08-2016	Sukkur	105.430
149.	1229	Construction & Establishment of Science Laboratories for High School Khairpur	Satisfactory	25-03-2016	Education and Literacy	29-07-2016	Khairpur	13.056
150.	1227	Rehabilitation of Superior Science College Khairpur, Taluka Khairpur	Satisfactory	24-03-2016	Education and Literacy	01-08-2016	Khairpur	10.000
151.	220	Provision of Furniture to Schools Constructed under SBEP in District Sukkur	Satisfactory	18-03-2016	Education and Literacy	25-08-2016	Sukkur, Khairpur	40.000
152.	2014-15 164	Introduction of Computer Education in Existing Middle Schools in Sindh 2007-08 Programme	Satisfactory	04-03-2016	Education and Literacy	07-09-2016	Shaheed Benazirabad	525.382
153.	2014-15 409	Estt. of Boys / Girls Degree Colleges in Sindh	Satisfactory	03-03-2016	Education and Literacy	21-10-2016	Shaheed Benazirabad	1,398.904
154.	1228	Rehabilitation of Women College Khairpur, Taluka Khairpur	Satisfactory	07-01-2016	Education and Literacy	12-08-2016	Khairpur	15.000
155.	159	Up gradation of Middle Schools to High Schools in Sindh (115-Units) in Sindh (ADP No. 159/2008-09 Programme).	Satisfactory	14-12-2015	Education and Literacy	17-08-2016	Shaheed Benazirabad	86.840
156.	1226	Rehabilitation of Mumtaz College Khairpur, Taluka Khairpur	Satisfactory	29-09-2015	Education and Literacy	19-09-2016	Khairpur	20.000
157.	174	Establishment of English Medium Schools in Sindh (25 Units) in Cambridge System Nursery to O level (One in Each District) (Sukkur, Larkana Ghotki)	Average	14-09-2015	Education and Literacy	24-01-2017	Ghotki, Larkana, Sukkur	3,500.000

158.	236	Establishment of Cadet College at Karampur	Satisfactory	07-09-2015	Education and Literacy	07-09-2016	Kashmore	983.580
159.	499	Establishment of Mono Technic Institute at Garhi Khuda Bux(Revised) (C: 48.515 + R: 66.442)	Un-Satisfactory	15-08-2015	Education and Literacy	05-05-2017	Larkana	114.957
160.	1721	Establishment of Model School at SALU Khairpur ADP # 1721	Satisfactory	13-08-2015	Education and Literacy	13-07-2016	Khairpur	89.198
161.	1231	Rehabilitation of Middle School Waris Ghambhir U.C. Mehar Ali, Taluka Khairpur	Satisfactory	16-05-2015	Education and Literacy	18-08-2016	Khairpur	4.000
162.	Non-ADP	Construction of 5 Roomed River Side School of Excellence at Village Muhammad Laik Bhutto Near punj Nalka @ Achyoon Qubyoon	Satisfactory	25-03-2015	Education and Literacy	26-08-2016	Sukkur	10.000
163.	540	Village Electrification Programme in Sindh (Phase-VII).	Satisfactory	19-04-2017	Energy	07-06-2017	Tando Mohd. Khan, Hyderabad	3,000.000
164.	541	Electrification of Goths (Villages) in Karachi.(Phase-VI).	Satisfactory	18-04-2017	Energy	19-05-2017	Karachi	600.000
165.	541	Electrification of Goths (Villages) in Karachi. (Phase-VI).	Un-Satisfactory	15-09-2016	Energy	21-10-2016	Karachi	600.000
166.	546	Study Of Environmental & Health Impacts of Pesticides and Chemical Fertilizer in Sindh Province (Larkana)	Satisfactory	11-05-2017	Environment	15-05-2017	Larkana	33.000
167.	546	Study of Environmental & Health Impacts of Pesticides and Chemical Fertilizer in Sindh Province (Larkana, Mirpurkhas, Jacobabad, Kashmore, Ghotki, Sukkur, SBA, T.A.Yar, Thatta & Badin)	Un-Satisfactory	19-10-2016	Environment	10-11-2016	Larkana	33.000
168.	341	Rehabilitation/Renovation of Existing Go downs in Sindh (Hyderabad and Sukkur Regions) (C.980.01+R.9.899) Sukkur	Satisfactory	08-03-2016	Environment	16-08-2016	Sukkur	989.918
169.	560	Construction of 8 new Treasury Offices in Sindh (Revised)	Average	03-03-2017	Finance Dept	03-04-2017	Jamshoro	252.687
170.	560	Construction of 8 new Treasury Offices in Sindh (Revised).	Satisfactory	16-12-2016	Finance Dept	11-01-2017	Matari	252.687
171.	560	Construction of 8 new Treasury Offices in Sindh (Revised). Kashmore	Satisfactory	26-08-2016	Finance Dept	19-09-2016	Kashmore	252.687
172.	560	Construction of 8 new Treasury Offices in Sindh (Revised).	Satisfactory	10-08-2016	Finance Dept	19-09-2016	Qambar Shahdadkot	252.687
173.	341	Rehabilitation/Renovation of Existing Go downs in Sindh (Hyderabad and Sukkur Regions) (C.980.01+R.9.899)Ghotki	Un-Satisfactory	30-03-2016	Food	14-07-2016	Ghotki	989.918

174.	571	Enhancing Forest Cover on State Forest Lands in Sindh.	Un-Satisfactory	22-03-2017	Forest Wildlife & CDA	13-04-2017	Hyderabad	708.000
175.	571	Enhancing Forest Cover on State Forest Lands in Sindh (C:21.00+R:687.00)-	Satisfactory	22-03-2017	Forest Wildlife & CDA	13-04-2017	Ghotki	708.000
176.	571	Enhancing Forest Cover on State Forest Lands in Sindh (C:21.00+R:687.00)-	Satisfactory	10-03-2017	Forest Wildlife & CDA	11-04-2017	Khairpur	708.000
177.	570	Mass Scale Tree Plantation Outside Forest Area to Mitigate Climate Change Effects in Sindh.	Satisfactory	06-03-2017	Forest Wildlife & CDA	03-04-2017	Tando Mohd. Khan, Jamshoro	705.000
178.	570	Mass Scale Tree Plantation Outside Forest Area to Mitigate Climate Change Effects in Sindh	Satisfactory	09-02-2017	Forest Wildlife & CDA	20-03-2017	Tando Allahyar, Matiari	705.000
179.	570	Mass Scale Tree Plantation Outside Forest Area to Mitigate Climate Change Effects in Sindh	Satisfactory	19-01-2017	Forest Wildlife & CDA	21-03-2017	Dadu	705.000
180.	579	Rehabilitation & Improvement of Haleji and Langh Lakes Wildlife sanctuary (C:107.184+R:43.787)	Average	20-12-2016	Forest Wildlife & CDA	11-01-2017	Thatta	150.971
181.	573	Geo-referred demarcation and construction of Earthen bunds for protection of forest land and upgradation of GIS Laboratory at Hyderabad (Larkana, Kandhkot, Shikarpur, Dadu, Sukkur, Ghotki, Khairpur, SBA, Sanghar, Thatta, T.M. Khan, Karachi, N. Feroz, Tha	Un-Satisfactory	06-12-2016	Forest Wildlife & CDA	02-01-2017	Thatta	246.483
182.	571	Enhancing Forest Cover on State Forest Lands in Sindh (C:21.00+R:687.00)	Satisfactory	02-12-2016	Forest Wildlife & CDA	02-01-2017	Karachi	708.000
183.	571	Enhancing Forest Cover on State Forest Lands in Sindh	Un-Satisfactory	21-11-2016	Forest Wildlife & CDA	16-12-2016	Tando Mohd. Khan	708.000
184.	570	Mass Scale Tree Plantation Outside Forest Area to Mitigate Climate Change Effects in Sindh (C:64.644+R:640.357)	Satisfactory	22-09-2016	Forest Wildlife & CDA	08-12-2016	Thatta	705.000
185.	571	Enhancing Forest Cover on State Forest Lands in Sindh (C:21.00+R:687.00)	Satisfactory	15-08-2016	Forest Wildlife & CDA	15-12-2016	Dadu	708.000
186.	571	Enhancing tree cover on state forest lands in Sindh.(Visit Location: Mirpurkhas range at Tharparkar)	Satisfactory	27-07-2016	Forest Wildlife & CDA	03-10-2016	Mirpurkhas	708.000
187.	355	REHABILITATION & IMPROVEMENT OF HALEJI & LUNGH LAKES WILDLIFE SANCTUARY & ESTABLISHMENT OF WETLAND INFORMATON CENTRE AT LUNGH LAKE	Satisfactory	25-02-2016	Forest Wildlife & CDA	26-07-2016	Qambar Shahdadkot	57.224

188.	345	Mass Scale Tree Plantation Outside Forest Area to Mitigate Climate Change Affects in Sindh (C:64.644+R:640.357) Kashmore, Kandhkot	Un-Satisfactory	23-02-2016	Forest Wildlife & CDA	12-07-2016	Kashmore	705.000
189.	584	Establishment of 25 Bedded Trauma Centre at Sindh Government Lyari General Hospital, Karachi.(C: 275.969+R: 521.168)	Satisfactory	25-05-2017	Health	08-06-2017	Karachi	797.137
190.	587	Establishment of Gastroenterology & Neuropsychiatry Unit at NICH, Karachi (Compliance Visit)	Satisfactory	08-05-2017	Health	19-05-2017	Karachi	192.788
191.	716	Prevention & Control of Blindness (PCB) in Sindh	Average	03-05-2017	Health	16-06-2017	Karachi	329.304
192.	638	Expansion & Rehabilitation of Sir C.J Institute of Psychiatry Hyderabad including construction of New Female Ward, Rehabilitation Centre & OPD Block, Psychiatric Emergency 50 Bedded Ward. (C: 119.163+R: 31.048)	Un-Satisfactory	14-04-2017	Health	20-05-2017	Hyderabad	150.211
193.	709	Establishment of Constituent Medical College of Liaquat University of Medical & Health Sciences at Khairpur Mirs	Satisfactory	30-03-2017	Health	10-04-2017	Khairpur	1,575.992
194.	649	Providing additional facilities in Rural Health Centre at Naudero, Taluka Ratodero, District Larkana (Revised) (C: 104.937+R: 28.465)	Satisfactory	27-03-2017	Health	04-05-2017	Larkana	133.402
195.	644	Upgradation of existing Rural Health Centre to Taluka Headquarter Hospital at Garhi Khairo, District Jacobabad. (C:170.178+R:25.000)	Satisfactory	23-03-2017	Health	20-05-2017	Jacobabad	195.178
196.	634	Up gradation of (3) Maternity Homes in Karachi (i) PIB Colony (ii) Soldier Bazar & (iii) Patel Para, Jahangir Road. (C: 146.528+R: 53.243)	Satisfactory	15-03-2017	Health	03-04-2017	Karachi	199.771
197.	634	Up gradation of (3) Maternity Homes in Karachi (i) PIB Colony (ii) Soldier Bazar & (iii) Patel Para, Jahangir Road. (C: 146.528+R: 53.243)	Satisfactory	08-03-2017	Health	03-04-2017	Karachi	199.771
198.	634	Up gradation of (3) Maternity Homes in Karachi (i) PIB Colony (ii) Soldier Bazar & (iii) Patel Para, Jahangir Road. (C: 146.528+R: 53.243)	Satisfactory	07-03-2017	Health	03-04-2017	Karachi	199.771
199.	2014-15 617	Modernization of electrification distribution network work at civil	Satisfactory	02-03-2017	Health	27-04-2017	Karachi	321.294

		hospital Karachi (Re-revised) - (Compliance Visit)						
200.	722	Hepatitis Prevention & Control Program in Sindh (Chief Minister Initiative) Re-Visit	Satisfactory	23-02-2017	Health	01-03-2017	Jamshoro	3,629.008
201.	722	Hepatitis Prevention & Control Program in Sindh (Chief Minister Initiative) Re-Visit	Satisfactory	23-02-2017	Health	01-03-2017	Thatta	3,629.008
202.	722	Hepatitis Prevention & Control Program in Sindh (Chief Minister Initiative) Re-Visit	Satisfactory	22-02-2017	Health	01-03-2017	Mirpurkhas	3,629.008
203.	722	Hepatitis Prevention & Control Program in Sindh (Chief Minister Initiative) Re-Visit	Satisfactory	22-02-2017	Health	01-03-2017	Tando Mohd. Khan	3,629.008
204.	585	Strengthening and Improvement of Jinnah Postgraduate Medical Centre (JPMC), Karachi. (C: 151.512+R: 271.277)	Average	22-02-2017	Health	03-04-2017	Karachi	422.789
205.	720	Maternal Neonatal Child Health Programme in Sindh. (GoS: 198.656+GoP: 292.942=Total: 491.598	Un-Satisfactory	21-02-2017	Health	13-05-2017	Tando Mohd. Khan, Tando Allahyar	198.656
206.	720	Maternal Neonatal Child Health Programme in Sindh. (GoS: 198.656+GoP: 292.942=Total: 491.598	Un-Satisfactory	20-02-2017	Health	13-05-2017	Badin, Matiari	198.656
207.	722	Prevention & control of Hepatitis in Sindh (Chief Minister Initiative)	Satisfactory	20-02-2017	Health	01-03-2017	Shaheed Benazirabad	3,956.450
208.	586	Strengthening and Improvement of National Institute of Child Health (NICH), Karachi. (C: 65.401+R: 133.749	Satisfactory	13-02-2017	Health	31-03-2017	Karachi	199.150
209.	711	Renovation & rehabilitation of Chandka Medical College and Construction of New Noori Girls Hostel of Shaheed Mohtarma Benazir Bhutto Medical University, Larkana. (C: 1066.581+R: 44.630)	Satisfactory	09-02-2017	Health	14-05-2017	Larkana	1,111.211
210.	2146	Construction of Sports Stadium in Sindh (8 Nos.) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar)	Un-Satisfactory	07-02-2017	Health	03-04-2017	Jacobabad	225.704
211.	587	Establishment of Gastroenterology and Neuropsychiatry Unit at NICH, Karachi. (C: 89.660+R: 103.128)	Un-Satisfactory	23-01-2017	Health	21-03-2017	Karachi	192.788
212.	656	Expansion & Improvement of DHQ Hospitals in Sindh. (03 Nos). (1) Khairpur (2) Badin & (3) Shikarpur (Revised) (C: 2516.747+R: 923.828) 2	Average	20-01-2017	Health	27-04-2017	Shikarpur	3,440.575
213.	652	Up gradation of Taluka Hospital Sehwan to Syed Abdullah Shah	Satisfactory	19-01-2017	Health	21-03-2017	Jamshoro	321.766

		Institute of Medical and Health Sciences(Revised).						
214.	704	Establishment of Medical College at Karachi. (C: 741.164+R: 392.200+PIU: 7.836).	Average	12-01-2017	Health	10-04-2017	Karachi	1,141.200
215.	618	Up gradation of Chemico Bacteriological Laboratory, Karachi (Revised). (C: 4.063+R: 206.648)	Average	12-01-2017	Health	03-03-2017	Karachi	210.711
216.	706	Purchase of Land 200 Acres and Construction of Boundary Wall at People s University of Health and Medical Sciences at Shaheed Benazirabad (Revised) (C: 61.600+R: 120.521).	Satisfactory	09-01-2017	Health	27-04-2017	Shaheed Benazirabad	155.521
217.	640	Purchase & Installation of MRI at RHC Punhal Khan Chandio, Taluka Sakrand, District Shaheed Benazirabad (C:7.515+R: 83.286)	Satisfactory	19-12-2016	Health	19-01-2017	Shaheed Benazirabad	90.801
218.	717	Enhanced HIV/AIDS Control Programme in Sindh. (R: 637.161).	Un-Satisfactory	16-12-2016	Health	27-01-2017	Karachi	637.161
219.	584	Establishment of 25 Bedded Trauma Centre at Sindh Government Lyari General Hospital, Karachi. (C: 275.969+R: 521.168)	Un-Satisfactory	15-12-2016	Health	13-01-2017	Karachi	797.137
220.	583	Renovation works at Sindh Government Lyari General Hospital, Karachi. (C: 126.502+R: 6.500)	Average	15-12-2016	Health	03-02-2017	Karachi	133.002
221.	615	Strengthening of Services Hospital, Karachi (C: 43.130+R: 119.347)	Un-Satisfactory	07-12-2016	Health	11-01-2017	Karachi	162.477
222.	716	Prevention & Control of Blindness (PCB) in Sindh.	Un-Satisfactory	07-12-2016	Health	11-01-2017	Karachi	329.304
223.	705	Establishment of Shaheed Benazir Bhutto Medical College Lyari, Karachi. (C: 802.916+R: 392.2+PIU: 9.877).	Satisfactory	18-11-2016	Health	02-01-2017	Karachi	1,204.993
224.	625	Establishment of Shaheed Benazir Bhutto Medical Complex at National High Way, near Razaqabad, Bin Qasim Town, Karachi (C: 1120.582+R: 308.857) 15-NOV-2016	Satisfactory	17-11-2016	Health	15-12-2016	Hyderabad, Karachi	1,429.439
225.	612	Establishment of cardiac emergency centre at Baldia Town, Karachi (C: 149.857+R: 149.077) (GoS: 149.467+KMC: 149.467)	Satisfactory	16-11-2016	Health	02-01-2017	Hyderabad, Karachi	149.467
226.	591	Upgradation of Neonatal & Paediatric Services at Liaquat University Hospital,	Satisfactory	31-10-2016	Health	29-11-2016	Hyderabad	127.825

		Hyderabad (C: 79.205+R: 48.620)						
227.	656	Expansion & Improvement of DHQ Hospitals in Sindh. (03 Nos). (1) Khairpur (2) Badin & (3) Shikarpur (Revised) (C: 2516.747+R: 923.828)	Satisfactory	27-10-2016	Health	15-12-2016	Khairpur	3,440.575
228.	707	Ghulam Muhammad Mahar Medical Collage, Sukkur ADP# 707 (2016-17)	Satisfactory	26-10-2016	Health	04-11-2016	Sukkur	3,322.714
229.	620	Expansion & Improvement of 03 Urban Health Centres in Karachi. (1) Orangi No-15 (2) Malir City (3) Kamari and additional Indoor Block at Sindh Government Hospital, KorangiNo. 5, Karachi. (C: 203.134+R: 164.861) (Malir city unit)	Un-Satisfactory	24-10-2016	Health	31-10-2016	Karachi	367.995
230.	2014-15 708	Up gradation of BHU to RHC Haji Fateh Mohammad Rajar(C.48.521+R.15.902)	Average	19-10-2016	Health	08-12-2016	Umerkot	64.423
231.	659	Up gradation of THQ Hospitals to the level of DHQ Hospitals in newly created Districts in Sindh (03 Nos) (i) Matiari (ii)Kamber at Shahdadkot & (iii) Umerkot (Revised). (C: 1875.856+R: 608.005)	Average	18-10-2016	Health	10-11-2016	Umerkot	2,483.861
232.	658	Expansion & Improvement of DHQ Hospitals (06 Nos) at (1) Thatta (2) Dadu (3) Naushero Feroz (4) Mirpurkhas (5) Sanghar & (6) Mirpur Mathelo at Ghotki (C: 2154.695 + R: 1094.171)	Un-Satisfactory	17-10-2016	Health	29-11-2016	Dadu	3,248.866
233.	652	Up gradation of Taluka Hospital Sehwan to Syed Abdullah Shah Institute of Medical and Health Sciences (Revised). (C: 230.704 + R:91.062)	Average	17-10-2016	Health	29-11-2016	Jamshoro	321.766
234.	651	Up gradation of MCH Centre to the level of BHU at Village Lutufullah Panhwar, Taluka Bhiria, District N.Feroze. (C: 17.317+R: 0.812)	Un-Satisfactory	07-10-2016	Health	10-11-2016	Naushero Feroz	18.129
235.	659	Up gradation of THQ Hospitals to the level of DHQ Hospitals in newly created Districts in Sindh (03 Nos) (i) Matiari (ii)Kamber at Shahdadkot & (iii) Umerkot (Revised). (C: 1875.856+R: 608.005)	Average	07-10-2016	Health	16-12-2016	Matiari	2,483.861
236.	650	Up gradation of THQ Hospital at Shahdakot Qubo Saeed Khan, Nasirabad Sujawal and Miro Khan. (C: 340.163+R: 70.373)	Satisfactory	26-09-2016	Health	31-10-2016	Qambar Shahdadkot	410.536
237.	642	Strengthening of Gambat Institute of Medical Sciences at Gambat (Revised). (C: 1129.670+R: 299.551)	Satisfactory	20-09-2016	Health	10-11-2016	Khairpur	1,429.221

238.	700	Upgradation of Basic Health Unit to the level of Rural Health Centre at Village Muhammad Hassan Dal, District Tando ALLAH Yar	Satisfactory	09-09-2016	Health	15-12-2016	Tando Allahyar	60.000
239.	641	Construction of Accident & Emergency Centre at Daulatpur, Taluka Kazi Ahmed, District Shaheed Benazirabad. (C: 51.768+R: 36.182)	Average	08-09-2016	Health	31-10-2016	Shaheed Benazirabad	87.950
240.	659	Up gradation of THQ Hospitals to the level of DHQ Hospitals in newly created Districts in Sindh (03 Nos) (i) Matiari (ii)Kamber at Shahdadkot & (iii) Umerkot (Revised). (C: 1875.856+R: 608.005)	Satisfactory	05-09-2016	Health	08-12-2016	Qambar Shahdadkot	2,483.861
241.	585	Strengthening and Improvement of Jinnah Postgraduate Medical Centre (JPMC), Karachi.	Un-Satisfactory	26-08-2016	Health	26-10-2016	Karachi	422.789
242.	716	Prevention & Control of Blindness (PCB) in Sindh. (R: 329.304)	Un-Satisfactory	25-08-2016	Health	26-10-2016	Mirpurkhas, Karachi	329.304
243.	720	Maternal Neonatal Child Health Programme in Sindh. (GoS: 198.656+GoP: 292.942=Total: 491.598)	Satisfactory	24-08-2016	Health	07-03-2017	Shaheed Benazirabad	198.656
244.	597	Establishment / Construction of 50 bedded Medical & Surgical ICU and expansion of Casualty & OPD Department at Ghulam Mohammad Mahar Medical College Hospital, Sukkur (Revised) (C: 134.688+R:147.520)	Un-Satisfactory	19-08-2016	Health	19-09-2016	Sukkur	282.208
245.	715	Strengthening of Provincial Tuberculosis Control Programme in Sindh. (R: 1190.741).	Average	19-08-2016	Health	20-05-2017	Hyderabad	1,190.741
246.	593	Establishment of Madam Faryal Talpur Cardiac Surgery Complex having facilities of: i. Coronary Angiography Cardiac Catheterized Lab. ii. Cardiac Bypass Surgery iii. Chest Surgery at Chandka Medical College Hospital Larkana (C: 51.123+R: 239.394)	Un-Satisfactory	16-08-2016	Health	19-09-2016	Larkana	290.517
247.	722	Hepatitis Prevention & Control Program in Sindh. (Chief Minister's Initiative) (GoS: 3629.008+GoP: 327.442= Total:3956.450) (Sehwan Unit)	Un-Satisfactory	16-08-2016	Health	22-09-2016	Jamshoro	3,629.008
248.	720	Maternal Neonatal Child Health Programme in Sindh. (GoS: 198.656+GoP: 292.942=Total: 491.598)	Satisfactory	15-08-2016	Health	07-03-2017	Larkana	198.656

249.	722	Hepatitis Prevention & Control Program in Sindh. (Chief Minister's Initiative) (GoS: 3629.008+GoP: 327.442= Total: 3956.450)	Un-Satisfactory	09-08-2016	Health	03-10-2016	Jamshoro	3,629.008
250.	638	Expansion & Rehabilitation of Sir C.J Institute of Psychiatry Hyderabad including construction of New Female Ward, Rehabilitation Centre & OPD Block, Psychiatric Emergency 50 Bedded Ward. (C: 119.163+R: 31.048)	Satisfactory	25-07-2016	Health	23-09-2016	Hyderabad	150.211
251.	708	Establishment of Medical College at Hyderabad. (C: 984.973+R: 398.871+PIU: 10.623).	Satisfactory	21-07-2016	Health	04-11-2016	Hyderabad	1,394.467
252.	625	Establishment of Shaheed Benazir Bhutto Medical Complex at National High Way, near Razaqabad, Bin Qasim Town, Karachi (C: 1120.582+R: 308.857)	Un-Satisfactory	19-07-2016	Health	19-09-2016	Karachi	1,429.439
253.	465	Safe Blood Transfusion Reforms in Sindh. (All Districts). (IIIrd Revision). (75.227 incurred +46.715 to be incurred). (C: 30.568+R: 91.374).	Un-Satisfactory	19-05-2016	Health	02-09-2016	Sukkur	121.942
254.	474	Extension of Malaria Control Programme for roll back Malaria initiative in Sindh.	Average	17-05-2016	Health	19-10-2016	Kashmore, Khairpur, Larkana, Naushero Feroz, Shikarpur, Sukkur	897.080
255.	422	Up gradation of MCH Centre to the level of BHU at Village Lutufullah Panhwar, Taluka Bhiria District N'Feroze. (C: 17.317+R: 0.812)	Un-Satisfactory	25-04-2016	Health	27-07-2016	Naushero Feroz	18.129
256.	361	Shaheed Mohtarma Benazir Bhutto Accident, Emergency & Trauma Centre and Ancillary Services Complex at Civil Hospital, Karachi. (IIIrd Revision). (C: 3463.345+R: 2619.586)	Satisfactory	13-04-2016	Health	22-11-2016	Karachi	6,082.931
257.	473	Prevention & control of Hepatitis in Sindh (Chief Minister's Initiative)	Un-Satisfactory	22-03-2016	Health	30-09-2016	Sukkur, Jacobabad, Kashmore, Khairpur, Larkana, Naushero Feroz, Qambar Shahdadkot, Shaheed Benazirabad, Shikarpur	3,412.115
258.	373	Up gradation of Surgery Department, Surgery Equipment for OT, Modernization of Laboratory, Blood Bank & Establishment of Oncology Treatment Ward	Un-Satisfactory	16-03-2016	Health	27-07-2016	Larkana	143.235

		(30 Bedded) at CMC Hospital, Larkana.						
259.	372	Construction of Neuro Science Complex at CMCH Larkana, containing: 1. Neuro Surgery Department 2. Neuro Medicine (Neurology Department) 3. Psychiatry Department	Un-Satisfactory	14-03-2016	Health	14-07-2016	Larkana	214.635
260.	1252	Construction of New Khairpur Building for District TB Hospital at Khairpur.	Satisfactory	16-02-2016	Health	25-08-2016	Khairpur	159.129
261.	460	Establishment of Constituent Medical College of Liaquat University of Medical & Health Sciences at Khairpur Mirs	Un-Satisfactory	25-01-2016	Health	25-08-2016	Khairpur	795.208
262.	458	Ghulam Muhammad Mahar Medical Collage, Sukkur	Un-Satisfactory	19-01-2016	Health	13-07-2016	Sukkur	1,911.980
263.	1253	CONSTRUCTION OF HEART CENTRE IN CIVIL HOSPITAL KHAIRPUR.	Un-Satisfactory	15-01-2016	Health	18-10-2016	Khairpur	457.180
264.	1257	Construction of Shaheed Mohtarma Benazir Bhutto Charity Hospital at Mirpurkhas City. (Revised). (C: 75.817+R:24.183) (Rs. 68.479 incurred+Rs. 31.521 to be incurred)	Satisfactory	06-01-2016	Health	25-07-2016	Mirpurkhas	100.000
265.	732	Construction of (07 Nos:) Police Posts on Highway (KPT, PQA) Karachi	Satisfactory	16-03-2017	Home	03-04-2017	Karachi	15.000
266.	730	Construction of Buildings for Sindh Police at various location under Police Package , Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, SBA, Kamber & Sukkur)	Satisfactory	14-03-2017	Home	03-04-2017	Karachi	474.736
267.	735	Construction of Police Station (Category-C) & Bachelor Barracks (Ground+1) at Nindo District Badin.	Satisfactory	09-03-2017	Home	03-04-2017	Badin	37.198
268.	737	Construction of Police Station (Category-C) with Bachelor Barrack (Ground + 1) at Jahanwah Village Sheranpur Taluka Shikarpur	Satisfactory	21-02-2017	Home	27-03-2017	Shikarpur	50.357
269.	790	Construction of Special Court 10 Nos to 20 Nos Courts (G+1) 10 Nos on each floor) at Central Prison Karachi (Re-revised)(C:359.990+R:68.001)	Satisfactory	02-02-2017	Home	03-04-2017	Karachi	427.991

270.	801	Block Allocation for six (6) phased out schemes of ADPs:- ADP 2011-12 # 1624 Rs. 10 M ADP 2014-15 # 832 Rs. 4 M ADP 2014-15 # 833 Rs. 4 M ADP 2014-15 # 834 Rs. 3 M ADP 2014-15 # 835 Rs. 3 M ADP 2014-15 # 836 Rs. 3 M	Un-Satisfactory	13-01-2017	Home	04-05-2017	Shikarpur	620.726
271.	801	Block Allocation for six (6) phased out schemes of ADPs:- ADP 2011-12 # 1624 Rs. 10 M ADP 2014-15 # 832 Rs. 4 M ADP 2014-15 # 833 Rs. 4 M ADP 2014-15 # 834 Rs. 3 M ADP 2014-15 # 835 Rs. 3 M ADP 2014-15 # 836 Rs. 3 M	Satisfactory	13-01-2017	Home	16-02-2017	Kashmore	620.726
272.	801	Block Allocation for six (6) phased out schemes of ADPs:- ADP 2011-12 # 1624 Rs. 10 M ADP 2014-15 # 832 Rs. 4 M ADP 2014-15 # 833 Rs. 4 M ADP 2014-15 # 834 Rs. 3 M ADP 2014-15 # 835 Rs. 3 M ADP 2014-15 # 836 Rs. 3 M	Satisfactory	13-01-2017	Home	03-04-2017	Shikarpur	620.726
273.	801	Block Allocation for six (6) phased out schemes of ADPs:- ADP 2011-12 # 1624 Rs. 10 M ADP 2014-15 # 832 Rs. 4 M ADP 2014-15 # 833 Rs. 4 M ADP 2014-15 # 834 Rs. 3 M ADP 2014-15 # 835 Rs. 3 M ADP 2014-15 # 836 Rs. 3 M	Satisfactory	12-01-2017	Home	16-02-2017	Jacobabad	620.726
274.	485	Constt. of Police Station Tamachani at Shikarpur - Sukkur Road 2	Satisfactory	22-11-2016	Home	16-12-2016	Sukkur	29.110
275.	738	Renovation / Construction of DIG House Sukkur	Satisfactory	16-11-2016	Home	08-12-2016	Sukkur	13.500
276.	730	Construction of Buildings for Sindh Police at various location under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, SBA, Kamber & Sukkur) Kamber	Satisfactory	26-09-2016	Home	18-10-2016	Qambar Shahdadkot	474.736
277.	730	Construction of Buildings for Sindh Police at various location under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, SBA, Kamber & Sukkur) SBA	Un-Satisfactory	20-09-2016	Home	02-11-2016	Shaheed Benazirabad	474.736
278.	730	Construction of Buildings for Sindh Police at various location under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, SBA, Kamber & Sukkur) Sukkur	Satisfactory	07-09-2016	Home	18-10-2016	Sukkur, Sujawal	474.736
279.	791	Construction of Boundary Wall around District Prison Badin	Satisfactory	11-08-2016	Home	22-09-2016	Badin	60.000

280.	730	Construction of Buildings for Sindh Police at various location under Police Package (Karachi, Hyderabad, Sujawal, Dadu, Thatta, Matiari, SBA, Kamber & Sukkur)	Satisfactory	14-07-2016	Home	22-09-2016	Matiari	32.975
281.	489	Construction of Police Station(Category-'C') at Kambhra. DistrictGhotki	Satisfactory	27-04-2016	Home	18-08-2016	Ghotki	25.626
282.	485	Constt. of Police Station Tamachani at Shikarpur - Sukkur Road	Average	20-04-2016	Home	01-08-2016	Sukkur	29.110
283.	490	Construction of Police Station (Category-C) with Bachelor Barrack (Ground + 1) at Jahanwah Village Sheranpur Taluka & District Shikarpur	Satisfactory	08-04-2016	Home	27-07-2016	Shikarpur	50.357
284.	2011-12 481	Construction of Highway Patrolling Posts in Sindh 105 Nos.	Satisfactory	24-12-2015	Home	06-10-2016	Sukkur	436.000
285.	481	High Way Patrolling Post (105 Nos) in Sindh (Karachi, Hyderabad, Mirpurkhas, SBA, Sukkur, Ghotki, N. Feroz, Larkana, Jacobabad	Un-Satisfactory	22-12-2015	Home	07-09-2016	Naushero Feroz	436.044
286.	1184	Rehabilitation of Old High Court Building & Annexe Building at Circuit Bench Hyderabad	Satisfactory	06-02-2017	Human Rights	17-04-2017	Hyderabad	46.884
287.	1168	Construction of 2 Nos Bungalows at Hala	Satisfactory	09-09-2016	Human Rights	18-10-2016	Matiari	23.274
288.	904	Construction of District Court Building Matiari (Revised)	Satisfactory	09-09-2016	Human Rights	16-12-2016	Matiari	144.608
289.	1165	Construction of 2 Nos. Bungalows @ Matiari.	Satisfactory	08-09-2016	Human Rights	30-09-2016	Matiari	20.381
290.	1204	Construction of officers/officials residential accommodation for the prosecutors in Sindh.	Un-Satisfactory	24-08-2016	Human Rights	03-10-2016	Tando Mohd. Khan	359.161
291.	1177	Construction of one Court for Civil Judge at Pano Aqil	Satisfactory	12-08-2016	Human Rights	19-09-2016	Sukkur	21.796
292.	906	Construction of Bar room library, Litigant shade with canteen and Vehicle shade at High Court Circuit Bench at Larkana.	Satisfactory	13-05-2016	Human Rights	01-08-2016	Larkana	45.556
293.	902	Construction of District Court Building at Qambar	Un-Satisfactory	05-05-2016	Human Rights	17-08-2016	Qambar Shahdadkot	177.265
294.	892	Construction of 2 Nos Bungalows @ Sakrand (Revised)	Satisfactory	03-05-2016	Human Rights	29-07-2016	Shaheed Benazirabad	24.550
295.	918	Installation of Lifts (5 Nos) at City Court Premises Karachi	Satisfactory	22-04-2016	Human Rights	22-07-2016	Karachi	48.758
296.	824	Construction of officers residential accommodation office of the Deputy Director Industries.	Satisfactory	09-01-2017	Industrial & Commerce	15-02-2017	Hyderabad	57.695
297.	812	Development of Infrastructure at SITE Nooriabad, Karachi, Hyderabad & Sukkur.	Satisfactory	21-12-2016	Industrial & Commerce	11-01-2017	Hyderabad	1,019.470
298.	812	Development of Infrastructure at SITE Nooriabad, Karachi,Hyderabad & Sukkur.	Average	08-12-2016	Industrial & Commerce	11-01-2017	Jamshoro	1,019.470

299.	808	Establishment of un-developed area of SIE Thatta	Satisfactory	14-11-2016	Industrial & Commerce	02-12-2016	Thatta	45.320
300.	812	Development of Infrastructure at SITE Nooriabad, Karachi, Hyderabad & Sukkur.	Satisfactory	03-10-2016	Industrial & Commerce	16-12-2016	Karachi, Jamshoro, Hyderabad	1,019.470
301.	830	Establishment of District Archives Mirpurkhas	Average	17-03-2017	Information & Archives	11-04-2017	Mirpurkhas	40.410
302.	829	Establishment of District Archives Hyderabad	Average	01-03-2017	Information & Archives	31-05-2017	Hyderabad	32.256
303.	542	Establishment of Reprography Lab at Sindh Archives	Worst	02-06-2016	Information & Archives	02-09-2016	Karachi	58.400
304.	849	Pre-clinical & Clinical Studies for Drug Development against infectious diseases	Satisfactory	23-12-2016	Information Technology	11-01-2017	Karachi	20.000
305.	1070	CC Lining of Noor Wah Ex: Thar Canal of Umerkot Sub Division	Satisfactory	21-04-2017	Irrigation (Water & Drainage)	19-05-2017	Mirpurkhas	795.756
306.	1027	Rehabilitation of Thar Canal System & Lining of Sohrab Distry about 24 RDs	Satisfactory	20-04-2017	Irrigation (Water & Drainage)	19-05-2017	Umerkot	883.842
307.	1022	Constructing Stone Pitching along Nasir Branch from RD-0 to 220 Both Sides (eroded portions)	Un-Satisfactory	13-04-2017	Irrigation (Water & Drainage)	07-06-2017	Tando Allahyar	755.280
308.	1021	CC Lining of Chaker Distry i/c Constructing of new & temporary outlets from RD - 0 to 44.5 & 44.5 to 114.10 and Removing of spoils along Zour Minor from RD - 0 to 49 both sides	Un-Satisfactory	12-04-2017	Irrigation (Water & Drainage)	07-06-2017	Tando Allahyar	575.850
309.	977	Construction of Stone Studs & Pitching along Upper Nara Canal b/w RD-225 to 575 and Rehabilitation of Khipro Canal from 14th Mile to 49th Mile & Constructing Pre-stressed Bridge at RD 415 Nara Canal (Revised)	Satisfactory	11-04-2017	Irrigation (Water & Drainage)	19-05-2017	Sanghar	817.616
310.	1048	Restoration / Rehabilitation of Sultani Branch, Mir Wah System, Morjhar Branch System and Imam Wah Jagir System	Satisfactory	10-04-2017	Irrigation (Water & Drainage)	31-05-2017	Badin	540.497
311.	1146	Construction of 2 Nos. Small Storage & Delay Action Dams Miskeen Jahan Khan Khoso and Bartlao Dam in Taluka Nagarparkar	Satisfactory	22-03-2017	Irrigation (Water & Drainage)	13-05-2017	Tharparkar	198.926
312.	872	Construction / Extension of Sub-Drain S-2R from RD-24+674 to 72+194 in Taluka & District Sanghar	Satisfactory	21-03-2017	Irrigation (Water & Drainage)	13-05-2017	Sanghar	154.103
313.	1152	Construction of Meer Chakar Weir along (Abdar & Mol Nai) Gadap Town, Karachi	Satisfactory	20-03-2017	Irrigation (Water & Drainage)	13-05-2017	Karachi	366.229

314.	904	Re-boring of 25 Nos Bore failure Tube wells including Restoration of old direct disposal arrangement and Refurbishment of SCARP Tube wells and Installation of 15 Nos New Tube wells in different Dehs in Tube well Division No.II Hala & Surface Drainage scheme	Satisfactory	10-03-2017	Irrigation (Water & Drainage)	13-05-2017	Matiari	374.786
315.	1031	Providing stone pitching along PFL RD 120 to 130 IP side RD 135 to 140 NIP side, RD 152 to 160 and 161 to 163 NIP side Village Abral and Re-Sectioning of Gunj Bahar Branch and Repair of Head Regulator, Road Bridge, dumping of stone pitching and Rehabilitate	Average	06-03-2017	Irrigation (Water & Drainage)	13-05-2017	Tando Mohd. Khan	350.160
316.	1031	Providing stone pitching along PFL RD 120 to 130 IP side RD 135 to 140 NIP side, RD 152 to 160 and 161 to 163 NIP side Village Abral and Re-Sectioning of Gunj Bahar Branch and Repair of Head Regulator, Road Bridge, dumping of stone pitching and Rehabilitate	Average	03-03-2017	Irrigation (Water & Drainage)	13-05-2017	Sujawal	350.160
317.	882	Construction of Link Drain at RD 0.0 to 25 out-falling in Seerani Branch Drain at RD 40 IP side for Village Pir Buksho and ARO Pusio, U.C Seerani; (ii) Construction of Link Drain RD 0.0 to 14 out-falling in 6-R Tando Bago Sub-Drain at RD 22 IP side for Vi	Satisfactory	01-03-2017	Irrigation (Water & Drainage)	20-03-2017	Badin	119.278
318.	1015	Rehabilitation of Old X-Regulator along Rohri Main Canal(Stage-II) (Rohri, Dad, Hala Divisions)	Satisfactory	01-03-2017	Irrigation (Water & Drainage)	03-04-2017	Sanghar	457.504
319.	1067	Pilot Project for Lining of Rohri Canal from RD-616 to RD-647	Average	17-02-2017	Irrigation (Water & Drainage)	11-04-2017	Shaheed Benazirabad	3,120.000
320.	976	Rehabilitation of Rice Canal RD-372 to 407 and its off-takes viz, Mehar Branch, Dhamrao Branch and Sehar Branch	Un-Satisfactory	16-02-2017	Irrigation (Water & Drainage)	13-05-2017	Dadu	299.082
321.	1066	New Manufacturing / Replacement of Gates of Head Regulator and X-ing Regulators of Kotri Barrage Region	Satisfactory	15-02-2017	Irrigation (Water & Drainage)	05-05-2017	Thatta	350.366
322.	876	Installation of 40 Nos Tube wells in various Dehs under Directives including Two Nos T/Wells of Misri Khan Jamali	Average	15-02-2017	Irrigation (Water & Drainage)	27-04-2017	Shaheed Benazirabad	270.000

323.	993	Rehabilitation / Resectioning of Johi Branch from Head to Tail (RD-0.0 to 238.560) in Southern Dadu Division & Lining of Pahore and Kharoo Minor	Average	10-02-2017	Irrigation (Water & Drainage)	10-04-2017	Dadu	299.837
324.	978	Rehabilitation of Irrigation Channels & Infrastructure at Taluka Ghorabari District Thatta.	Satisfactory	03-02-2017	Irrigation (Water & Drainage)	03-04-2017	Thatta	360.000
325.	1028	Rehabilitation of Sakro Branch & Infrastructure at Taluka Mirpur Sakro District Thatta.	Satisfactory	02-02-2017	Irrigation (Water & Drainage)	10-04-2017	Thatta	389.966
326.	1127	Construction of CC Lining along Doso Disty (RD-0+00 to 77+450) & Doso Feeder	Satisfactory	23-01-2017	Irrigation (Water & Drainage)	21-03-2017	Mirpurkhas	443.139
327.	910	Construction of Surface Drain (Kanday Chukhi Branch Drain) Sub-Drain 1L Kanday Chukhi i/c Structures for Disposal of Water Kanday Chukhi Poned Area in KN Shah	Satisfactory	19-01-2017	Irrigation (Water & Drainage)	21-03-2017	Dadu	70.713
328.	1050	Construction of Bridge over Dadu Canal at RD-0 To 28+500 and Restressed Bridge across RD-508- 508 at Village Phat	Satisfactory	19-01-2017	Irrigation (Water & Drainage)	21-03-2017	Dadu	99.918
329.	1106	Lining of Gharib Disty	Average	13-01-2017	Irrigation (Water & Drainage)	20-05-2017	Tando Allahyar	172.547
330.	1081	Rehabilitation & Renovation of 3-Bedded Bungalow NoA-I/21, in SCARP Colony, Khairpur	Average	12-01-2017	Irrigation (Water & Drainage)	16-02-2017	Khairpur	10.036
331.	964	Remaining Work along J-Spur at Mile 0/7 Abad Manguli Extension bund in Norther Dadu Division Larkana (Revised)	Un-Satisfactory	11-01-2017	Irrigation (Water & Drainage)	07-03-2017	Larkana	608.070
332.	1004	Rehabilitation / Stone pitching of Nazar Shakh off taking from Abro Minor Ghar Division, Larkana (7 RDs)	Satisfactory	11-01-2017	Irrigation (Water & Drainage)	28-02-2017	Larkana	43.829
333.	1007	Up-gradation / Rehabilitation of pumping scheme I/C Lining of Channels in Taluka Manjhand	Satisfactory	04-01-2017	Irrigation (Water & Drainage)	21-03-2017	Jamshoro	391.235
334.	939	Rehabilitation & Renovation of Office Buildings (i) Akram Wah Division Badin (ii) office of Rohri Canal Circle including inspection Bungalow Shahdadpur	Average	21-12-2016	Irrigation (Water & Drainage)	27-01-2017	Sanghar	198.950
335.	1055	CC Lining of Sui Qandar Branch, Pae Minor, Dhardo Minor and Bhabhar Minor & Matiari Minor	Un-Satisfactory	16-12-2016	Irrigation (Water & Drainage)	27-01-2017	Matiari	934.100
336.	1068	Rehabilitation / Replacement X-Regulators & Head Regulators in SIDA	Un-Satisfactory	08-12-2016	Irrigation (Water & Drainage)	03-04-2017	Ghotki	199.000

337.	885	Construction of Ladiun Branch Drain System (Remaining Works)	Un-Satisfactory	06-12-2016	Irrigation (Water & Drainage)	27-01-2017	Thatta, Sujawal	249.859
338.	984	Providing Stone Pitching along Daro Branch RD 0 to 50 and Pinyari Branch RD 130 to 145 both side (Pinyari Circle).	Satisfactory	17-11-2016	Irrigation (Water & Drainage)	16-12-2016	Sujawal	164.901
339.	1073	De-silting of DIM Branch from RD-0 to 166.6 (Tail)	Satisfactory	15-11-2016	Irrigation (Water & Drainage)	16-12-2016	Mirpurkhas, Sanghar	33.201
340.	1026	CC Lining of Sultanpur Minor from RD 0+00 to 23+600 Ex: Rohri Main Canal.	Un-Satisfactory	14-11-2016	Irrigation (Water & Drainage)	16-12-2016	Matari	55.399
341.	851	Establishment of Planning, Monitoring & Evaluation Cell in Irrigation & Power Department (Revised)	Satisfactory	11-11-2016	Irrigation (Water & Drainage)	29-11-2016	Thatta, Karachi	50.603
342.	1063	Construction of retaining wall at RD-51, Road Bridge along Mithiani Disty, Dalepota Minor RD-0 to 38 and Construction of road Bridge along Late Minor at Rd-4, Rd-34, 38, 40, RD-14 Dalepota Minor and Strengthening of weak portion of Dalepota and Ubji Mino	Satisfactory	26-10-2016	Irrigation (Water & Drainage)	04-11-2016	Naushero Feroz	75.316
343.	869	Remodelling and CC Lining of Carrier Drain of Talpur Wada Pump Station, Construction of Sim Drainage Channel near Jumani, and Bridge over Sim Nala Village Haji Shah & near at Pir Musafir and MG-1L Sub-Drain near Village Jalbani and KN-1L Sub-Drain Shah Hus	Average	20-10-2016	Irrigation (Water & Drainage)	18-01-2017	Khairpur	199.591
344.	957	Rehabilitation of Ratodero Branch from RD- 0 to Tail	Un-Satisfactory	18-10-2016	Irrigation (Water & Drainage)	10-11-2016	Larkana	171.215
345.	1057	Remodelling of Regulators of Gungri Large RD 20, Sujawal X-Regulator RD 90 and Chahto Large RD 108 of Darro Branch and Providing gates in Regulators of (i) Chahto X-Regulator RD 108 of Darro Branch, (ii) Head Regulator Sattah Branch RD 170 to Darro Branch,	Satisfactory	14-10-2016	Irrigation (Water & Drainage)	08-12-2016	Sujawal	349.787
346.	1107	Lining of Saieen Hyderi Minor & Indo Disty in Distt Thatta	Satisfactory	22-09-2016	Irrigation (Water & Drainage)	14-10-2016	Thatta	119.480
347.	1150	Construction of Gravity Weir / recharge Dam across Gamrach Dhoro in Central Kohistan & Construction of Guwari recharge Dam in Central Kohistan near Jhangara Taluka Sehwan	Satisfactory	21-09-2016	Irrigation (Water & Drainage)	18-10-2016	Jamshoro	484.608

348.	1048	Restoration / Rehabilitation of Sultani Branch, Mir Wah System, Morjhar Branch System and Imam Wah Jagir System.(compliance report).	Satisfactory	19-09-2016	Irrigation (Water & Drainage)	29-09-2016	Badin	540.497
349.	866	Construction of Surface Drainage Scheme of DehDobi and Akanwari in Taluka& District Sanghar. (Compliance report).	Satisfactory	01-09-2016	Irrigation (Water & Drainage)	29-09-2016	Sanghar	258.482
350.	1023	De-silting of Landhi-I Minor RD-0 to 25.4, Shaikh Moosa Minor RD-0 to 11.0, Tando Allahyar-II Distry RD-0 to 53.30, Tando Soomro-I Distry RD-0 to 31.6 Tando Soomro-II Distry RD-0 to 43.60, Naghar Distry RD-0 to 82.50 and Gharib Distry RD-0 to 48.0	Satisfactory	29-08-2016	Irrigation (Water & Drainage)	19-10-2016	Tando Allahyar	89.792
351.	927	Remodelling / De-Silting of Sim Nali 5-L Sujawal Upto 30 RDSand Extension of 8 RDS	Average	23-08-2016	Irrigation (Water & Drainage)	19-10-2016	Sujawal	41.781
352.	907	Construction of Thatta Escape Drain Out falling Indus River	Satisfactory	22-08-2016	Irrigation (Water & Drainage)	19-10-2016	Thatta	552.721
353.	1033	Rehabilitation of Saida Wah Regulator of Jalalani Sub Division of Guni Division & Remodelling / Rehabilitation of Main Guni Canal RD 0 to 210 & Hassan Ali Branch RD 0 to 60.5.(compliance report).	Satisfactory	17-08-2016	Irrigation (Water & Drainage)	29-09-2016	Badin	270.000
354.	1078	Construction of Bridges, Structures and other works in Left Bank AWB Badin	Satisfactory	12-08-2016	Irrigation (Water & Drainage)	18-10-2016	Badin	199.762
355.	928	Pocket Drainage System for Part Command of Dehs Kalhorki, Jhurkandi, Keranddi and Chorhal including Badin Cantonment Area Tapo, Taluka & District Badin	Satisfactory	11-08-2016	Irrigation (Water & Drainage)	18-10-2016	Badin	270.832
356.	1151	Rehabilitation / Restoration of Malir weirs – I, II, III & Thado Dam.	Satisfactory	09-08-2016	Irrigation (Water & Drainage)	19-10-2016	Karachi	399.669
357.	1021	CC Lining of Chaker Distry i/c Constructing of new & temporary outlets from RD - 0 to 44.5 & 44.5 to 114.10 and Removing of spoils along Zour Minor from RD - 0 to 49 both sides.	Satisfactory	29-07-2016	Irrigation (Water & Drainage)	18-10-2016	Tando Allahyar	575.850
358.	1062	CC Lining of Muhammad Khan Distry.	Satisfactory	28-07-2016	Irrigation (Water & Drainage)	21-10-2016	Tando Allahyar, Tando Mohd. Khan	185.276
359.	913	Construction of Sub Drain & Installation of 06 Nos Tube wells in Deh Langhano and Ghado, Taluka Jhundho Marri, District Tando Allahyar	Un-Satisfactory	27-07-2016	Irrigation (Water & Drainage)	30-09-2016	Mirpurkhas	169.692

360.	662	Rehabilitation of Dingro Wah RD-0 to 104.5 and Construction Retaining Wall at RD 23.5 to 26.0 and Repair to Modules.	Un-Satisfactory	12-05-2016	Irrigation (Water & Drainage)	26-07-2016	Ghotki	64.520
361.	585	Construction of Small Surface Drainage Scheme Chanjni. Surface Drainage System ADP # 585	Un-Satisfactory	11-05-2016	Irrigation (Water & Drainage)	26-07-2016	Ghotki	57.610
362.	663	Rehabilitation of Bundh Minor at RD 31 to 84 Providing StonePitching and Repair to Modules.	Un-Satisfactory	10-05-2016	Irrigation (Water & Drainage)	26-07-2016	Ghotki	34.087
363.	655	Constructing New Office Block of Executive Engineer & Assistant Ex. Engineer of Mirpur Division (Irrigation) @ Mirpur Mathelo ADP # 655 of 2015-16.	Un-Satisfactory	09-05-2016	Irrigation (Water & Drainage)	26-07-2016	Ghotki	66.803
364.	573	Surface Drainage Schemes UC Sabu Rahu (Nakur) & Jam Sahib District Shaheed Benazirabad ADP No. 573/2015-16	Average	05-05-2016	Irrigation (Water & Drainage)	25-07-2016	Shaheed Benazirabad	198.462
365.	594	Installation of 40 Nos Tube Wells in Various Dehs under Directive including Two Nos Tube Wells of Misiri Khan Jamali ADP No. 594/2015-16	Satisfactory	04-05-2016	Irrigation (Water & Drainage)	14-07-2016	Shaheed Benazirabad	270.262
366.	572	Surface Drainage Schemes (02 Nos.) UC Kumb leema, Deh Asgharabad District Shaheed Benazirabad ADP No. 572/2015-16	Satisfactory	04-05-2016	Irrigation (Water & Drainage)	19-07-2016	Shaheed Benazirabad	198.058
367.	741	Pre-Stressed Concrete Bridge over Faiz Wah RD-12 near village Doongar Khan Burdi.	Un-Satisfactory	22-04-2016	Irrigation (Water & Drainage)	12-07-2016	Khairpur	19.958
368.	750	Constructing Protection Wall along Kupri Minor RD-0.00 to 8.00 Both Sides	Satisfactory	22-04-2016	Irrigation (Water & Drainage)	12-07-2016	Khairpur	18.679
369.	742	Construction of Lift System on W/C No.77-BL Ex: Mirwah Canal in Deh Noor Bozdar, Taluka Kot Diji	Un-Satisfactory	19-04-2016	Irrigation (Water & Drainage)	01-07-2016	Khairpur	19.490
370.	590	Construction of Seepage Drain from RD-0+000 to 14+000, Link Drain from RD-0+000 to 3+000 & Pumping Station Ghulam Hussain Bhambro along Right side of Rohri Main Canal at RD-245+000. ADP # 590	Satisfactory	11-04-2016	Irrigation (Water & Drainage)	13-07-2016	Khairpur	59.808
371.	678	Rehabilitation of Kundho Minor 0 to 8. ADP # 678	Satisfactory	30-03-2016	Irrigation (Water & Drainage)	15-07-2016	Qambar Shahdadkot	59.503
372.	704	Construction of office Building and Residence of AXEN, Kambar, Dhamrao & Mehar sub Division. ADP # 704	Satisfactory	30-03-2016	Irrigation (Water & Drainage)	14-07-2016	Qambar Shahdadkot	33.097

373.	784	Lining of Thul Distry District Jacobabad	Average	24-03-2016	Irrigation (Water & Drainage)	14-07-2016	Jacobabad	397.065
374.	593	Providing RCC slab over Retaining wall along 2R Sub drain of Larkana Souther system from RD 8+700 to 13+00	Satisfactory	17-03-2016	Irrigation (Water & Drainage)	01-07-2016	Larkana	55.964
375.	687	Construction of protection wall (Retaining wall) along warah Branch at RD 89,90,94,109,114,117,121, IP Side (common Bank) & RD 100,117 NIP Side in madeji sub Division ADP # 687	Satisfactory	17-03-2016	Irrigation (Water & Drainage)	27-07-2016	Larkana	176.989
376.	589	Construction of Surface Drainage Scheme in Deh Dethki in Union Council Shahmir Rahu Taluka New Saeedabad District Matiari	Satisfactory	09-03-2016	Irrigation (Water & Drainage)	14-07-2016	Matiari	170.733
377.	670	Revitalization of Mechanical Wing of Irrigation Department.	Average	26-02-2016	Irrigation (Water & Drainage)	26-07-2016	Hyderabad, Jamshoro, Thatta	150.000
378.	2014-15 950	Procurement of Consultancy Services for the Feasibility Study & Detailed Design for Preparing Master Drainage Plan for In Drainage Division L.B.O.D Shaheed Benazirabad ADP # 950(2014-15)	Satisfactory	28-01-2016	Irrigation (Water & Drainage)	15-07-2016	Shaheed Benazirabad	16.047
379.	584	Boring & Installation of 250 Nos Tube wells on Solar Energy for Assured Supply of 100 cusecs for Thar Coal from LBOD Spinal Drain RD-362.	Un-Satisfactory	12-01-2016	Irrigation (Water & Drainage)	25-07-2016	Badin, Hyderabad	1,971.000
380.	2014-15 1100	ADP # 1100 of 2014-15 Construction of Stone Pitching Along Rohri Main Canal in (Vulnerable Reaches) of Rohri Hala & Dad Division)	Un-Satisfactory	24-07-2015	Irrigation (Water & Drainage)	18-08-2016	Naushero Feroz, Shaheed Benazirabad	600.000
381.	2014-15 968	ADP # 968 of 2013-14 Excavation & Earth work of Sim Nala from Ripri to Khuhra and Construction of Pumping Station along Right side of Rohri Main Canal (Between Setharja & Dejarja).	Un-Satisfactory	24-07-2015	Irrigation (Water & Drainage)	19-09-2016	Khairpur	57.790
382.	1160	Construction of Buildings for Nine (9) Employment Exchanges and repair / renovation of two existing building employment in Sindh (Karachi, Badin, Sanghar, SBA, Khairpur, Thatta,N.Feroze, Shikarpur & Jacobabad) (C:99.701+R:28.024)2	Satisfactory	20-02-2017	Labour Dept	27-03-2017	Naushero Feroz	127.725

383.	1160	Construction of Buildings for Nine (9) Employment Exchanges and repair / renovation of two existing building employment in Sindh (Karachi, Badin, Sanghar, SBA, Khairpur, Thatta, N.Feroze, Shikarpur & Jacobabad) (C:99.701+R:28.024)	Average	21-09-2016	Labour Dept	18-10-2016	Badin	127.725
384.	1160	Construction of Buildings for Nine (9) Employment Exchanges and repair / renovation of two existing building employment in Sindh (Karachi, Badin, Sanghar, SBA, Khairpur, Thatta, N.Feroze, Shikarpur & Jacobabad) (C:99.701+R:28.024)	Un-Satisfactory	02-08-2016	Labour Dept	05-05-2017	Shikarpur	127.725
385.	1160	Construction of Buildings for Nine (9) Employment Exchanges and repair / renovation of two existing building employment in Sindh (Karachi, Badin, Sanghar, SBA, Khairpur, Thatta, N.Feroze, Shikarpur & Jacobabad) (C:99.701+R:28.024)	Un-Satisfactory	01-08-2016	Labour Dept	22-09-2016	Khairpur	127.725
386.	887	Constriction of office of Assistant Director Labour	Satisfactory	27-04-2016	Labour Dept	12-08-2016	Larkana	56.749
387.	887	Construction of office of Assistant Director Labour (Sukkur)	Satisfactory	22-04-2016	Labour Dept	18-10-2016	Sukkur	56.749
388.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparkar, Umerkot and Karachi) (C: 125.591 + R: 121.785).	Un-Satisfactory	28-03-2017	Livestock and Fisheries	27-04-2017	Naushero Feroz	247.376
389.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparkar, Umerkot and Karachi) (C: 125.591 + R: 121.785).	Satisfactory	27-03-2017	Livestock and Fisheries	24-04-2017	Kashmore	247.376
390.	1213	The project on sustainable Livestock Development for Rural Sindh (Compliance Visit)	Un-Satisfactory	17-03-2017	Livestock and Fisheries	05-05-2017	Hyderabad	175.500
391.	1210	Provision of Sheds, Improved laboratory for semen collection, preparation and preservation for genetically improved animals. (C: 106.755 + R: 92.772)	Satisfactory	15-03-2017	Livestock and Fisheries	03-04-2017	Hyderabad	199.527

392.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparkar, Umerkot and Karachi) (C: 125.591 + R: 121.785).	Average	10-03-2017	Livestock and Fisheries	24-04-2017	Ghotki	247.376
393.	1216	Establishment of Cattle Colonies with District and Private participation Phase-I - Revised(C: 1377.272 + R: 64.178)	Average	19-01-2017	Livestock and Fisheries	17-02-2017	Tharparkar	1,441.450
394.	1242	Model Village for Fishermen at Hawksbay, Zero Point Badin, Manchhar lake & Keenjhar lake Thatta (C: 430.295 + R: 51.530)	Satisfactory	17-01-2017	Livestock and Fisheries	17-04-2017	Badin	481.825
395.	1220	Provision of Model Veterinary Centres in the Arid Zone of Sindh (Tharparkar, Khairpur, Jamshoro, Dadu, Ghotki, Hyd, Umerkot & T.Allahyar)(C:43.318 + R: 5.984)	Un-Satisfactory	12-01-2017	Livestock and Fisheries	15-02-2017	Dadu	49.302
396.	1242	Model Village for Fishermen at Hawksbay, Zero Point Badin, Manchhar lake & Keenjhar lake Thatta (C: 430.295 + R: 51.530)	Satisfactory	11-01-2017	Livestock and Fisheries	03-04-2017	Thatta	481.825
397.	1213	Project on Sustainable Livestock Development for Rural Sindh -	Un-Satisfactory	17-11-2016	Livestock and Fisheries	11-01-2017	Tando Mohd. Khan, Hyderabad	175.500
398.	1221	Introduction of High Yielding Boer Goat Breed in Sindh	Un-Satisfactory	15-11-2016	Livestock and Fisheries	16-12-2016	Hyderabad	59.500
399.	1217	Surveillance & Characterization of Circulating Pathogens of Poultry in Sindh including Avian Influenza Containment Programme. (Karachi, Sukkur,Larkana, Hyd. M.Khas, Tharparkar & Thatta) (C: 78.97	Un-Satisfactory	10-11-2016	Livestock and Fisheries	05-05-2017	Thatta, Mirpurkhas	198.422
400.	1216	Establishment of Cattle Colonies with District and Private participation Phase-I - Revised (C: 1377.272 + R: 64.178)	Average	19-10-2016	Livestock and Fisheries	16-12-2016	Umerkot	1,441.450
401.	1220	Provision of Model Veterinary Centres in the Arid Zone of Sindh (Tharparkar, Khairpur, Jamshoro, Dadu, Ghotki, Hyd, Umerkot & T.Allahyar)(C:43.318 + R: 5.984)	Un-Satisfactory	18-10-2016	Livestock and Fisheries	01-12-2016	Tando Allahyar	49.302
402.	1239	Strengthening and Improvement of Fish and Shrimp Hatcheries in Sindh (Karachi, Thatta, Badin, Dadu, N.Feroze, Shikarpur &	Un-Satisfactory	18-10-2016	Livestock and Fisheries	05-05-2017	Naushero Feroz	784.013

		Sukkur) (C: 579.963 + R: 204.068) 2						
403.	1220	Provision of Model Veterinary Centres in the Arid Zone of Sindh (Tharparkar, Khairpur, Jamshoro, Dadu, Ghotki, Hyd, Umerkot & T.Allahyar)(C:43.318 + R: 5.984)	Un-Satisfactory	04-10-2016	Livestock and Fisheries	02-12-2016	Hyderabad	49.302
404.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparkar, Umerkot and Karachi) (C: 125.591 + R: 121.785)	Un-Satisfactory	23-09-2016	Livestock and Fisheries	18-10-2016	Karachi	247.376
405.	1239	Strengthening and Improvement of Fish and Shrimp Hatcheries in Sindh (Karachi, Thatta, Badin, Dadu, N.Feroze, Shikarpur & Sukkur) (C: 579.963 + R: 204.068)	Un-Satisfactory	22-09-2016	Livestock and Fisheries	26-10-2016	Shikarpur	784.013
406.	1209	Strengthening of Viral and Protozoan Disease Diagnostic Facilities at Central Veterinary Diagnostic laboratory (CVDL), Tando Jam - Revised (C:21.399 + R:209.448)	Satisfactory	22-09-2016	Livestock and Fisheries	02-12-2016	Hyderabad	230.847
407.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparkar, Umerkot and Karachi) (C: 125.591 + R: 121.785) Kashmore	Un-Satisfactory	21-09-2016	Livestock and Fisheries	18-10-2016	Kashmore	247.376
408.	1217	Surveillance & Characterization of Circulating Pathogens of Poultry in Sindh including Avian Influenza Containment Programme. (C: 78.978 + R: 119.444)	Un-Satisfactory	31-08-2016	Livestock and Fisheries	05-05-2017	Tharparkar	198.422
409.	1215	Generation & Dev. of effective Vaccines to prevent Recurring infections of Newcastle Disease in Peacock & Rural Poultry (C: 13.162 + R: 46.788)	Satisfactory	30-08-2016	Livestock and Fisheries	02-12-2016	Tharparkar	59.950
410.	1219	Programme for Women Empowerment through Rehabilitation of Rural Poultry in Sindh (Karachi, Tharparkar, Jamshoro, Dadu, Larkana & Jacobabad)(C: 2.053 + R:57.507)	Satisfactory	25-08-2016	Livestock and Fisheries	02-12-2016	Karachi	59.560

411.	1219	Programme for Women Empowerment through Rehabilitation of Rural Poultry in Sindh (Karachi, Tharparker, Jamshoro, Dadu, Larkana & Jacobabad)(C: 2.053 + R:57.507)	Average	18-08-2016	Livestock and Fisheries	02-12-2016	Jamshoro	59.560
412.	1217	Surveillance & Characterization of Circulating Pathogens of Poultry in Sindh including Avian Influenza Containment Programme. (Karachi, Sukkur, Larkana, Hyd. M.Khas, Tharparker & Thatta) (C: 78.97	Satisfactory	10-08-2016	Livestock and Fisheries	02-12-2016	Hyderabad	198.422
413.	1216	Establishment of Cattle Colonies with District and Private participation Phase-I - Revised (C: 1377.272 + R: 64.178) Khairpur	Satisfactory	04-08-2016	Livestock and Fisheries	19-09-2016	Khairpur	1,441.450
414.	1217	Surveillance & Characterization of Circulating Pathogens of Poultry in Sindh including Avian Influenza Containment Programme. (Karachi, Sukkur, Larkana, Hyd. M.Khas, Tharparker & Thatta) (C: 78.97	Satisfactory	03-08-2016	Livestock and Fisheries	19-10-2016	Karachi	198.422
415.	1215	Generation & Dev. of effective Vaccines to prevent Recurring infections of Newcastle Disease in Peacock & Rural Poultry (C: 13.162 + R: 46.788)	Satisfactory	02-08-2016	Livestock and Fisheries	22-09-2016	Karachi	59.950
416.	1242	Model Village for Fishermen at Hawksbay, Zero Point Badin, Manchhar lake & Keenjhar lake Thatta	Un-Satisfactory	29-07-2016	Livestock and Fisheries	30-09-2016	Badin, Thatta	481.825
417.	1214	Establishment of Stationery and Mobile Veterinary Diagnostic lab. Units for disease confirmation and control in Milk and Meat zone of Sindh Province.	Satisfactory	26-07-2016	Livestock and Fisheries	03-10-2016	Badin, Mirpurkhas, Thatta	59.868
418.	1218	Expansion of Poultry Hatcheries & Backyard Farming in Sindh including Poultry Controlled Atmosphere Shed - Revised (N.Feroze, Ghotki, Kashmore, Tharparker, Umerkot and Karachi) (C: 125.591 + R: 121.785) Ghotki	Un-Satisfactory	22-06-2016	Livestock and Fisheries	31-10-2016	Ghotki	247.376
419.	931	Strengthening of Sindh Poultry Vaccine Centre Korangi, Karachi	Satisfactory	30-05-2016	Livestock and Fisheries	15-07-2016	Karachi	202.523
420.	934	Establishment of disease control zone of livestock in sindh	Un-Satisfactory	28-03-2016	Livestock and Fisheries	25-07-2016	Shaheed Benazirabad	196.627

421.	939	Surveillance and characterization of circulating pathogens of poultry in Sindh including avian influenza containment program.Larkana	Satisfactory	15-12-2015	Livestock and Fisheries	30-09-2016	Larkana	99.069
422.	939	Surveillance and characterization of circulating pathogens of poultry in Sindh including avian influenza containment program.Sukkur	Satisfactory	05-12-2015	Livestock and Fisheries	07-09-2016	Sukkur	99.069
423.	1527	Construction of road from Tharu Shah Pathak to connect Bharti, Manjhat & Tharu Shah road Mile 0/0-3/2 (5.00 km)	Average	03-05-2017	Local Government	19-05-2017	Naushero Feroz	50.000
424.	1332	Rehabilitation of Adam Khan Road, (KMC)	Satisfactory	18-04-2017	Local Government	14-05-2017	Karachi	209.920
425.	1369	Construction of Link Road from Khadim Hussain Zardari to Village Munawar Zadari and Sultan Meleno to Lala Israr Mile 0/0-5/5 (9.00 KMS), (Revised)	Satisfactory	21-03-2017	Local Government	13-04-2017	Sanghar	59.894
426.	1625	Up-gradation of BHU to RHC at Khawaja Goth Sultanabad District Tando Allahyar. (C: 49.826+R: 5.876),	Satisfactory	20-03-2017	Local Government	11-04-2017	Tando Allahyar	55.702
427.	1403	Reconditioning of Road from Manghanwari to village Hassan Phulpoto and Sain Dino Maitlo Taluka Kingri (4.00 KM).-	Satisfactory	20-03-2017	Local Government	13-05-2017	Khairpur	40.000
428.	1438	Construction of Road from Tando Jan Mohammad Jhudo Road via link Road Allah Bachayo Laghari via Khushi Mohammad Arain Deh 202 (4.00 km)	Satisfactory	17-03-2017	Local Government	11-04-2017	Mirpurkhas	35.603
429.	1605	Establishment of Begum Nusrat Bhutto Girls Degree College, Larkana (Cap:Rs.133.299 m + Rev.Rs.9.810 m)	Average	17-03-2017	Local Government	13-05-2017	Larkana	143.109
430.	1424	Construction of road from Nawabshah-Sarhari road (Bakhshio Jamali) to village Afzil / Mahar Ali Bhangwar, UC Gupchani, Taluka Daur.	Satisfactory	16-03-2017	Local Government	24-04-2017	Shaheed Benazirabad	28.208
431.	1425	Construction of road from Nawabshah-Sarhari road to connect Nawabshah-Varr road via Haji Muhammad Bux Brohi, Allah Dito Magsi, Jan Muhammad Brohi and Ghulam Hyder Zardari, UC Khadhar & Gupchani, Taluka Sakrand & Daur, Mile 0/0-3/1	Satisfactory	16-03-2017	Local Government	07-06-2017	Shaheed Benazirabad	54.065
432.	1434	Construction of road at village Muhammad Khan Sethar to Old village Lal Bux Shahani new village Muhammad Alam Shahani	Satisfactory	16-03-2017	Local Government	04-05-2017	Shaheed Benazirabad	39.929

		Taluka Daur District (S.B.A)(4.00 km)						
433.	1422	Construction of Road in Mohallah Al Reheem Raza Block F-II, Abdullah Shah Gazi Goth Malir Karachi (3.5 km)	Satisfactory	13-03-2017	Local Government	11-04-2017	Karachi	30.000
434.	1430	Construction of road Abad Hussain Zardari to village Shah Nawaz Zardari, Taluka Moro, District Naushehro Feroz -	Satisfactory	13-03-2017	Local Government	08-06-2017	Naushehro Feroz	40.000
435.	1262	Construction / Rehabilitation of water supply and drainage of Talty, Karampur, Murad Ali Shah, Wahur & adjoining areas	Satisfactory	10-03-2017	Local Government	03-04-2017	Jamshoro	199.056
436.	1611	Rehabilitation of RHC s in various Talukas at Sobhadero, Kingri, Faiz Ganj & Thari Mirwah (04 Nos). (C: 261.993+R: 50.208)	Average	09-03-2017	Local Government	04-05-2017	Khairpur	312.201
437.	1276	Rural Drainage Scheme Manhayoon Jamshoro	Satisfactory	08-03-2017	Local Government	03-04-2017	Jamshoro	56.188
438.	1279	Rehabilitation of drainage works & construction of new CC flooring in village Ber Sharif, Taluka Kamber	Satisfactory	07-03-2017	Local Government	24-04-2017	Qambar Shahdadkot	48.000
439.	1540	Reconstruction of road in Nazimabad # 4 around Nazimabad Club (4 Km)	Satisfactory	01-03-2017	Local Government	03-04-2017	Karachi	50.000
440.	1431	Improvement of road from National High Way to Rahib Khan Mooro (3.5 Kms)-	Satisfactory	21-02-2017	Local Government	11-04-2017	Naushehro Feroz	25.000
441.	1277	Imp. & Ext. of Water Supply (Pir Murad Nako) Dadu City	Average	16-02-2017	Local Government	19-05-2017	Dadu	32.913
442.	1405	Construction/Reconditioning of road from Rahimabad to Lodra via Chol Canal right bank mile 0/0-7/5 (12.26 KM)	Un-Satisfactory	14-02-2017	Local Government	11-04-2017	Shikarpur	87.462
443.	1435	Reconditioning of Road from Lodra Stop to Habibullah Kehar Village 4.00 km	Un-Satisfactory	14-02-2017	Local Government	27-03-2017	Shikarpur	28.471
444.	1404	Construction / Reconditioning of road from Kamal Shah to K.B. Allah Bux road mile 0/0-3/0 (4.81 Km)	Un-Satisfactory	13-02-2017	Local Government	02-06-2017	Shikarpur	37.011
445.	1283	Drainage System of Aliabad, Khursheed Town & village Laloo Lashari at Hyderabad	Satisfactory	10-02-2017	Local Government	03-04-2017	Hyderabad	481.767
446.	1416	Improvement of road from Piaro Road to village Arz Muhammad mile 0/0-2/1 (Phase-I) (3.325 Km)	Average	10-02-2017	Local Government	04-04-2017	Dadu	29.130

447.	1402	Construction of link road from Dau Muhammadpur Road to village Rizwanabad Mile 0/0-2/5 (4.24 KM)	Un-Satisfactory	09-02-2017	Local Government	13-05-2017	Jacobabad	33.486
448.	1460	Revival Surrounding of Empress Market and its adjoining AreasSaddar (Phase-I)	Satisfactory	08-02-2017	Local Government	21-03-2017	Karachi	98.702
449.	1270	Providing / laying sewerage lines in village Shaheed Makhdoom Bilawal	Satisfactory	07-02-2017	Local Government	20-03-2017	Karachi	11.271
450.	1461	Re-Carpeting and Laying of CC Flooring at PAF Base Faisal, Karachi	Satisfactory	07-02-2017	Local Government	21-03-2017	Karachi	44.780
451.	44	Construction of Dargah Sadaruddin Badshah (Rizvi) situated at Deh Bakhar Taluka Rohri District Sukkur Ph-I.	Un-Satisfactory	06-02-2017	Local Government	14-05-2017	Sukkur	42.304
452.	1412	Construction of road from Tando Jan Muhammad Dehi road at point 57 Mori to village Muhammad Salim Dada Deh 197 and Link to Muhammad Asif Deh 201 District Mirpur Khas (4.5 Km)	Satisfactory	06-02-2017	Local Government	20-03-2017	Mirpurkhas	49.809
453.	1448	Balance work for improvement and rehabilitation of 150 ft wide road in sector 23 from Road 3000 to Raod 5000 at Korangi	Satisfactory	01-02-2017	Local Government	20-03-2017	Karachi	127.320
454.	1344	Construction of Link Road from Lakha road Hot Khan Jalbani to village Ghulam Abbas Vighio Taluka Mehrabpur, Distt: Naushehro Feroz (3.2 Kms)	Satisfactory	26-01-2017	Local Government	01-03-2017	Naushero Feroz	40.000
455.	1353	Construction of Road from Goth Saindad Banbhan to village Moli Dino Nangore (Pir Ghulam Ali Musfir) Road Mile 0/0-3/1 (5.0 KM)	Average	26-01-2017	Local Government	17-02-2017	Naushero Feroz	55.000
456.	1383	Construction of road from Asian Bank road @ 3/6 to village Sultan Sethar (to connect Rahimdad Mari) road Mile 0/0-2/4 (4.00 KM).	Un-Satisfactory	24-01-2017	Local Government	16-02-2017	Shaheed Benazirabad	34.687
457.	1281	Construction of Zoological park in Khairpur.	Satisfactory	24-01-2017	Local Government	27-01-2017	Khairpur	45.000
458.	1317	Construction of Revenue Complex at Khairpur	Satisfactory	19-01-2017	Local Government	16-02-2017	Khairpur	21.882
459.	2014-15 1605	Providing solar energy lights for09 rural union couyncils of taluka Khairpur(Compliance visit)	Average	18-01-2017	Local Government	22-02-2017	Khairpur	90.000
460.	1360	Rehabilitation of road from Dargah Mashore road to village Dadhra Kalhoro.	Un-Satisfactory	17-01-2017	Local Government	28-02-2017	Larkana	34.715

461.	1354	Rehabilitation of road Larkana Khairpur road to Naonabad to Dargah Syed Bukhari.	Satisfactory	16-01-2017	Local Government	07-03-2017	Larkana	26.921
462.	1322	Office accommodation for district government secretariat and renovation of existing office Ghotki at Mirpur Mathelo.	Satisfactory	16-01-2017	Local Government	28-02-2017	Ghotki	69.753
463.	1259	Construction of paver block and cc drains in various streets of Larkana City	Satisfactory	16-01-2017	Local Government	04-05-2017	Larkana	70.000
464.	1359	Construction of road from Bridge Dadu Canal to village Mohallah Sangi & Sial Mohallah and via Masood Chandio street and Muzaffar Chandio st.village Madbhu to Bakrani road	Un-Satisfactory	12-01-2017	Local Government	03-04-2017	Larkana	16.987
465.	1447	Construction of Flyover at Korangi Crossing	Satisfactory	11-01-2017	Local Government	21-03-2017	Karachi	404.926
466.	1621	Construction of 2 BHUs in Kot Lashari and Naon Wahan, UC Talti, Taluka Sehwan, District Jamshoro. (C: 41.705+R: 3.112)	Average	09-01-2017	Local Government	04-05-2017	Jamshoro	44.817
467.	1318	Construction of District Election Commissioner's Office, Khairpur and residence at first floor, Khairpur	Satisfactory	05-01-2017	Local Government	07-03-2017	Khairpur	30.457
468.	1407	Rehabilitation of road from Khuhra Ripri Regulator road to Pir Jeelani (5 Km)	Average	22-12-2016	Local Government	11-01-2017	Khairpur	28.817
469.	1352	Construction of Road in Sanghar (6.00 Kms)	Satisfactory	21-12-2016	Local Government	24-01-2017	Sanghar	50.000
470.	1423	Construction of road from County Garden road to Sachal Goth	Satisfactory	19-12-2016	Local Government	27-01-2017	Karachi	31.587
471.	1426	Construction of road along with side drains and foot paths from Shah Petrol Pump to Bab-e-Khayber, Metroville Site, Karachi.	Satisfactory	19-12-2016	Local Government	24-01-2017	Karachi	91.738
472.	1659	Integrated Solid Waste Management Project Nawabshah Municipal Committee, Shaheed Benazirabad District. (Phase I) (Front end Collection System and two Garbage Transfer Stations). Total Cost = Rs. 438.326 M N.M.C Share = Rs. 154.000 M ADP Share	Average	16-12-2016	Local Government	07-03-2017	Shaheed Benazirabad, Karachi	284.326
473.	1417	Reconditioning of road from Tharu Shah Mithiani road to village Suleman Dehraj via Azmat Dero road (4.5 Km)	Satisfactory	13-12-2016	Local Government	11-01-2017	Naushero Feroz	40.500
474.	1370	Widening /Reconditioning of link road from Tail Mori to Tando Allahyar Sugar Mill via Sobhraj mile 2/0-5/6 (6.03 Kms)	Satisfactory	02-12-2016	Local Government	27-01-2017	Tando Allahyar	77.409

475.	1437	Construction of Roads in Tando Allah Yar (10 Kms)	Average	02-12-2016	Local Government	27-01-2017	Tando Allahyar	85.131
476.	1321	Construction of Boundary wall at ISI Head Quarters, Sukkur	Un-Satisfactory	21-11-2016	Local Government	13-12-2016	Sukkur	10.000
477.	1411	Construction of Link Road from Boharo Ketu Bunder Road from Jat Stop to village Molvi Mohd Alim Jat UC Mehar taluka Ghora Bari (4.0 km)	Satisfactory	10-11-2016	Local Government	16-12-2016	Thatta	40.049
478.	1342	Widening and Reconditioning of Road from Tando Muhammad Khan Bulri Shah Karim from Ditta Wah at mile 19/2 to Qadir Dino Shah Mori via Jinhan Soomro road mile 0/0-4/0 +376 ft (Revised).	Satisfactory	02-11-2016	Local Government	29-11-2016	Tando Mohd. Khan	92.748
479.	1176	Reconditioning / Rehabilitation Hazrat Bilal Umer Farooq Road (25 ft), Korangi Industrial area.	Un-Satisfactory	01-11-2016	Local Government	29-11-2016	Karachi	55.000
480.	1622	Construction of Government Dispensaries in Taluka Sakrand and Kazi Ahmed District Shaheed Benazirabad (04 Nos.). (C: 20.297+R: 2.888)	Satisfactory	31-10-2016	Local Government	10-11-2016	Shaheed Benazirabad	23.185
481.	1636	Constt. of Compound wall for Graveyards (05 Nos) in Distt: SBA	Satisfactory	28-10-2016	Local Government	09-11-2016	Shaheed Benazirabad	27.716
482.	1609	Construction of Veterinary Centres-cum-Residence in District Shaheed Benazirabad (9 units). (C:Rs.34.359+R:7.200)	Average	27-10-2016	Local Government	10-11-2016	Shaheed Benazirabad	41.559
483.	1349	Construction of road HI bed Shaheed Station village Saddam Hussain UC-Tangwani-3 Taluka Tangwani. (3.5 Kms).	Un-Satisfactory	25-10-2016	Local Government	09-11-2016	Kashmore	46.000
484.	1348	Construction of Road from Kandhkot Malguzar (Lohi Pull) road to village Mureed Khan Khoso road mile 0/0-2/6 (4.42 Km)	Average	24-10-2016	Local Government	09-11-2016	Kashmore	35.260
485.	1319	Constt. Of Taluka Office and other required Building in QaziAhmed 2	Satisfactory	21-10-2016	Local Government	04-11-2016	ShaheedBenazirabad	79.620
486.	1280	Constuction of Drainage and Sewerage at village Baquar Khan Maree, Taluka Mehrabpur, N. Feroz	Satisfactory	19-10-2016	Local Government	10-11-2016	Naushero Feroz	14.116
487.	1264	Constt. of open drainage system including CC Topping of different streets of Khairpur city at the original level	Satisfactory	14-10-2016	Local Government	10-11-2016	Khairpur	50.000
488.	1345	Construction of link road from village Ghulam Abid to Zanwar Saindad Darban, Union Council Sami, Taluka Sobhodero road mile 0/0-2/4(4.0 Km).	Satisfactory	06-10-2016	Local Government	04-11-2016	Khairpur	38.484

489.	1260	Sewerage System (Phase-II) Works at Taluka Qasimabad Hyderabad	Average	06-10-2016	Local Government	07-03-2017	Hyderabad	1,283.930
490.	1272	Construction / Rehabilitation of Kalri Nallah in Lyari Machar Colony.	Satisfactory	04-10-2016	Local Government	25-10-2016	Karachi	219.868
491.	1340	Rehabilitation of Road from Tatri Mori to Rawat Khero road Taluka Dokri	Satisfactory	27-09-2016	Local Government	21-10-2016	Larkana	37.578
492.	1391	Construction of Bus Terminal and Taxi Stand Retodero and Naudero Cities of Taluka Retodero (2 Nos.)	Satisfactory	27-09-2016	Local Government	18-10-2016	Larkana	153.896
493.	1257	Improvement and Extension of Water Supply in Badin City	Satisfactory	23-09-2016	Local Government	18-10-2016	Badin	478.861
494.	1258	Improvement & Extension of Urban Drainage Scheme Badin	Satisfactory	23-09-2016	Local Government	18-10-2016	Badin	263.294
495.	1394	Construction of Underpass at Golimar Intersection Nazimabad No. 1	Satisfactory	15-09-2016	Local Government	18-10-2016	Karachi	450.734
496.	1372	Construction of road from Wori Dhora Road to Saringhiar Taluka Chachro (5 Kms)	Average	09-09-2016	Local Government	21-10-2016	Tharparkar	57.915
497.	1637	Construction of Open Air Theatre at District Shaheed Benazirabad	Satisfactory	08-09-2016	Local Government	30-09-2016	Shaheed Benazirabad	36.843
498.	1341	Improvement /Construction of Road from village Allahyar Chachar to village mazar Chachar via Hamid Chachar (2.5 km) Taluka Ubaro.	Satisfactory	05-09-2016	Local Government	21-10-2016	Ghotki	23.727
499.	1610	Rehabilitation of District Council Medical Dispensaries (13 Nos), Maternity Homes (09 Nos) and Constuction/ Rehabilitation of Dispensaries (02 N0s) in District Khairpur (24 Units). (C:89.681+R: 11.265)	Un-Satisfactory	23-08-2016	Local Government	03-10-2016	Khairpur	100.946
500.	1613	Construction of BHU at village Khawaja Ghulam Rasool UC Noorpur, Taluka Kingri, District Khairpur. (C: 20.073+R: 3.145)	Satisfactory	04-08-2016	Local Government	26-08-2016	Khairpur	23.218
501.	1612	Up-gradation of Basic Health Unit (BHU) to the level of Rural Health Centre (RHC) at Kolab Jail, Taluka Kingri, District Khairpur. (C:44.695+R:14.448)	Satisfactory	03-08-2016	Local Government	19-09-2016	Khairpur	59.143
502.	1340	Imp: & Ext: of Water Supply Scheme Bothoro. (To be funded out of 10% share of Royalty)	Satisfactory	25-07-2016	Local Government	19-09-2016	Dadu	21.834
503.	994	Construction of surface drains, Pavers mettling of Road & Supply of Electricity & Transformers at various Streets of iron Market, Golimar Sukkur.	Satisfactory	16-05-2016	Local Government	25-08-2016	Sukkur	40.000

504.	1426	Drainage Scheme Rato Dero.	Satisfactory	12-05-2016	Local Government	26-08-2016	Larkana	275.700
505.	1278	Rehabilitation/Renovation of Jaral Shah Dargah at Larkana	Satisfactory	11-05-2016	Local Government	29-07-2016	Larkana	6.544
506.	1275	Construction of Shaheed Muhammad Anwar Bhutto Library at City Banguldero.	Satisfactory	10-05-2016	Local Government	26-07-2016	Larkana	7.882
507.	1436	C.C Block of Streets and Drainage System at Village Zakria Maheasar U.C Kothi Kalhori Taluka Larkana.	Satisfactory	09-05-2016	Local Government	01-08-2016	Larkana	13.174
508.	1235	Construction of Begum Nusrat Bhutto woman library and multipurpose hall at Larkana	Satisfactory	04-05-2016	Local Government	17-08-2016	Larkana	140.034
509.	1120	Constt of Madar-e-Jamhoriyat Nusrat Bhutto Under pass at Mehran Hotel.	Satisfactory	03-05-2016	Local Government	13-07-2016	Karachi	458.761
510.	1262	Construction of Government Dispensaries in Taluka Sakrand and Kazi Ahmed District Shaheed Benazirabad (04 Nos.). (C: 20.297+R: 2.888)	Un-Satisfactory	02-05-2016	Local Government	27-07-2016	Shaheed Benazirabad	23.185
511.	1353	Providing the Facility of Drinking Ground Water to Khairpur City (Remaining Areas 09 villages) (Revised)	Satisfactory	29-04-2016	Local Government	23-08-2016	Khairpur	214.828
512.	1271	Construction of Medical Dispensaries in various villages of District Larkana (11 Nos.) (Cap:Rs.55.973 m - Rev.Rs.7.942 m)	Satisfactory	24-04-2016	Local Government	27-07-2016	Larkana	63.915
513.	1313	Rural W/S Scheme Tharo Mengal UC-5 Songal Gadap Town.	Satisfactory	22-04-2016	Local Government	13-07-2016	Karachi	38.945
514.	972	Providing Lying Jointing and Testing 110 mm polyethelene Pipelne for solving the water problem in Gulshan-e-Sikandarabad Keamari, Karachi	Un-Satisfactory	21-04-2016	Local Government	14-07-2016	Karachi	30.531
515.	966	Establishment of water testing laboratory at Chilya, Karachi.	Satisfactory	13-04-2016	Local Government	14-07-2016	Thatta	30.740
516.	1274	Constt: of Ladies & Children Park at Mir Ali Bazar Khairpur (Branch Higher Secondary School Khairpur)	Satisfactory	11-04-2016	Local Government	14-07-2016	Khairpur	13.134
517.	1350	Construction of W/S Scheme of various villages (15 Nos.) of District Kamber @ Shahdad Kot.	Satisfactory	31-03-2016	Local Government	31-08-2016	Qambar Shahdadkot	83.492
518.	182	ADP : 182 Establishment of single section school at shaheed benazir bhutto model village at Tajjal Nara dist: Khairpur	Satisfactory	29-03-2016	Local Government	27-07-2016	Khairpur	45.497

519.	1251	Construction of Government Dispensary at village (i) Qadir Bux Jalbani UC Machyoon taluka and district Khairpur (ii) Hafeez Chandio taluka Kingri district Khairpur (iii) Kumbai Metlo UC Pir Mangio taluka and district Khairpur (iv) Pir Bux Metlo UC Mo	Un-Satisfactory	28-03-2016	Local Government	12-07-2016	Khairpur	24.000
520.	979	Construction of C.C Block & C.C Drain in Various Villages of Taluka Rato dero PS-37	Average	17-03-2016	Local Government	14-07-2016	Larkana	99.110
521.	Non-ADP	Imp/Rehabilitation Of Water/Sewerage System & Repairing Of Road In Uc No-01 (Paposh) North Nazimabad Zone.	Satisfactory	04-03-2016	Local Government	03-10-2016	Karachi	5.000
522.	1270	Rehabilitation/Renovation of existing various Health Facilities i/c(06 Nos) Ambulances in District Larkana.	Average	23-02-2016	Local Government	26-08-2016	Larkana	145.300
523.	1281	Construction of Zoological park in Khairpur	Un-Satisfactory	15-02-2016	Local Government	29-07-2016	Khairpur	45.000
524.	1246	Construction of Veterinary Centres at various village of District Shaheed Benazirabad.(09 Nos.)	Satisfactory	25-01-2016	Local Government	26-08-2016	Shaheed Benazirabad	41.559
525.	1371	Road from Shahpur Chakkar to Maqsoodo Rind Taluka Shahdadpur	Satisfactory	23-01-2016	Local Government	17-02-2017	Sanghar, Qambar Shahdadkot	19.903
526.	1436	Construction and Rehabilitation of Ghlam Nabi Shah Road from Irrigation Rest House Khahi road upto village sarhandi via Muhammad Siddiq Abu Bhai road (04 km)	Average	23-01-2016	Local Government	15-02-2017	Sanghar	39.200
527.	1279	Construction of remaining works at District Scout Head quarter at old National Highway Taluka/ District Khairpur.	Satisfactory	21-01-2016	Local Government	31-08-2016	Khairpur	14.695
528.	1410	Improvement of road from Razzakabad via Pir Sarhandi Goth to Sheedi Goth, Bin Qasim Town,Karachi.(4.00 Km)	Satisfactory	19-01-2016	Local Government	15-02-2017	Karachi	54.987
529.	1457	Drainage Scheme for Village Ghouspur Town Taluka Kandhkot.(To be funded out of 10% share of Royalty)	Satisfactory	31-12-2015	Local Government	17-08-2016	Kashmore	54.639
530.	1456	Drainage Scheme for village Dari Taluka Kandhkot.	Average	30-12-2015	Local Government	29-07-2016	Kashmore	48.612
531.	Non-ADP	Renovation of Paver road/Drain at different streets/villages of (Pak MDG)	Satisfactory	05-11-2015	Local Government	13-07-2016	Ghotki	20.000
532.	1358	Water Supply Scheme Daharki (To be funded out of 10% share of Royalty)	Average	28-09-2015	Local Government	12-07-2016	Ghotki	199.400

533.	991	Providing Water Supply & Drainage schemes at various places of District SBA	Satisfactory	18-09-2015	Local Government	29-07-2016	Shaheed Benazirabad	425.000
534.	2014-15 1902	Construction of C.C drains i/c Brick CC Block in UC-8,9,10&11 Larkana City	Average	10-06-2015	Local Government	12-07-2016	Larkana	24.920
535.	1672	Greater Karachi Water Supply Scheme (K-IV Phase-I, 260 MGD) Cost Rs. 25.551 Billion with 50% by GoS.	Satisfactory	24-10-2016	Matching Allocation	11-01-2017	Karachi	25,551.770
536.	1706	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkana, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar)-	Satisfactory	17-03-2017	Minorities & Affairs	13-05-2017	Larkana	59.170
537.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh(Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs,)	Satisfactory	18-01-2017	Minorities & Affairs	17-02-2017	Thatta	99.063
538.	1707	Reconstruction / Uplift / Expansion of Minorities Places in Sindh (Karachi, Shikarpur, Jamshoro, Umerkot, Thatta & Hyderabad)	Satisfactory	04-01-2017	Minorities & Affairs	15-02-2017	Umerkot	57.690
539.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs,)	Worst	23-12-2016	Minorities & Affairs	13-01-2017	Larkana	99.063
540.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs,)	Satisfactory	15-12-2016	Minorities & Affairs	11-01-2017	Karachi	99.063
541.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs,)	Satisfactory	09-12-2016	Minorities & Affairs	31-05-2017	Ghotki	99.063
542.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot	Un-Satisfactory	07-12-2016	Minorities & Affairs	31-05-2017	Khairpur	99.063

		& Khairpur Mirs,)						
543.	1705	Construction/ Repair and Renovation/ Restoration of Religious Places of Minorities in Sindh (Karachi, Ghotki, Thatta, Sukkur, Matiari, Shikarpur, Sanghar, Tharparkar, Larkana, Umerkot & Khairpur Mirs,)	Un-Satisfactory	06-12-2016	Minorities & Affairs	16-06-2017	Sukkur	99.063
544.	1706	Repair / Renovation of various Mandirs in Sindh (Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkana, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar)	Satisfactory	05-12-2016	Minorities & Affairs	02-01-2017	Thatta	59.170
545.	1707	Reconstruction / Uplift / Expansion of Minorities Places in Sindh (Karachi, Shikarpur, Jamshoro, Umerkot, Thatta & Hyderabad)	Un-Satisfactory	01-12-2016	Minorities & Affairs	02-01-2017	Hyderabad	57.690
546.	1706	Repair / Renovation of various Mandirs in Sindh(Karachi, Dadu, Thatta, Tharparkar, Jamshoro, Hyderabad, Larkana, N.Feroze, Khairpur Mirs, Matiari & T.Allahyar)	Un-Satisfactory	16-01-2016	Minorities & Affairs	17-02-2017	Hyderabad	59.170
547.	1721	Community Development Program through Civil Society Organizations and others, including Corporate Sector (Revised)	Satisfactory	08-12-2016	Planning & Development	11-01-2017	Karachi	26.998
548.	1736	Construction of office/ hostel/ residential building for Population Welfare Training Institute (PWTI), Karachi (C: 119.000)	Satisfactory	03-05-2017	Population Welfare	19-05-2017	Karachi	119.000
549.	1875	Improvement & Extension of Urban Drainage Scheme T.M.Khan (Compliance Visit)	Average	02-05-2017	Public Health Engineering	20-05-2017	Tando Mohd. Khan	202.780
550.	1876	Rural Drainage Scheme Saeedpur Takkar (Compliance Visit)	Average	02-05-2017	Public Health Engineering	20-05-2017	Tando Mohd. Khan	37.080
551.	1780	Upgradation of Pipe Line Water Supply Scheme Naukot-Mithi upto Chelhar	Satisfactory	21-04-2017	Public Health Engineering	20-05-2017	Tharparkar	950.000
552.	1779	Pipe Line W/S Scheme Lunio Dano Dandhal Nagarparkar	Average	20-04-2017	Public Health Engineering	20-05-2017	Tharparkar	506.876
553.	1790	Water Supply Scheme (Filtration) Dadu	Un-Satisfactory	17-04-2017	Public Health Engineering	20-05-2017	Dadu	754.737
554.	1900	Imp: & Ext: Drainage Scheme Dadu City	Average	17-04-2017	Public Health Engineering	20-05-2017	Dadu	589.700
555.	1751	Ultra Filtration Water supply Scheme Tando Jam District Hyderabad.	Satisfactory	10-04-2017	Public Health Engineering	14-05-2017	Hyderabad	617.441

556.	1885	Drainage Scheme at Kingri Muhalla Pir-jo-Goth	Average	22-03-2017	Public Health Engineering	07-06-2017	Khairpur	33.274
557.	1804	Water Supply Scheme (Filtration) Sakrand Town.	Satisfactory	09-03-2017	Public Health Engineering	19-06-2017	Shaheed Benazirabad	400.473
558.	1791	Water Supply Scheme Village Sim, Uris Leghari & Mureed Babar Taluka Johi	Average	17-02-2017	Public Health Engineering	03-04-2017	Dadu	13.071
559.	1789	Water Supply Schemes for various villages of Taluka K.N.Shah & Mehar	Satisfactory	10-02-2017	Public Health Engineering	21-03-2017	Dadu	67.307
560.	1971	Block Allocation for 15 schemes of ADP 2014-15 phased-out from ADP 2015-16 (CC Blocks at Asif Colony Bachal Shah Miani. (ADP 2014-15 S# 1891))	Satisfactory	07-02-2017	Public Health Engineering	13-05-2017	Sukkur	994.750
561.	1748	Rural W/S Scheme Abdullah Gabol Goth UC-5 Songal Gadap Town	Satisfactory	17-01-2017	Public Health Engineering	17-02-2017	Karachi	78.180
562.	1792	Water Supply Scheme Loung Mehasar Taluka Mehar	Satisfactory	13-01-2017	Public Health Engineering	11-04-2017	Dadu	12.457
563.	1754	Water Supply Scheme Village Mohammad Khan Shoro (Dabhoo) Taluka Kotri	Satisfactory	11-01-2017	Public Health Engineering	21-03-2017	Jamshoro	37.950
564.	1971	Block Allocation for 15 schemes of ADP 2014-15 phased-out from ADP 2015-16 (No.1698 - Rs.5.367), (No.1703 - Rs.3.754), (No.1729 - Rs.10.503), (No.1752 - Rs.10.511), (No.1708 - Rs.3.750), (No.1857 - Rs.10.869), (No.1922 - Rs.10.00), (No.1914 -Rs.3.648),	Satisfactory	09-01-2017	Public Health Engineering	07-03-2017	Shaheed Benazirabad, Other	994.750
565.	1750	Extension of Water Supply Scheme of Village Mori Manger, Shaikh Hafiz and Alam Abro Taluka & District Hyderabad	Satisfactory	09-01-2017	Public Health Engineering	20-05-2017	Hyderabad	25.410
566.	1908	Drainage Scheme Amorte Sharif Ghari Yaseen	Satisfactory	28-12-2016	Public Health Engineering	17-02-2017	Shikarpur	13.200
567.	1914	Drainage Scheme for Village Dari Taluka Kandhkot	Satisfactory	21-12-2016	Public Health Engineering	17-02-2017	Kashmore	48.612
568.	1807	Construction of Water Supply scheme Village Rais Muhammad Khan Chandio U.C Ratokot Taluka Larkana	Average	20-12-2016	Public Health Engineering	14-05-2017	Larkana	12.500
569.	1803	Water Supply Scheme Deh-89 Nawabshah 2	Average	15-12-2016	Public Health Engineering	17-02-2017	Shaheed Benazirabad	10.870
570.	1847	Drainage System facilities for 300 Beds D.H.Q Hospital	Un-Satisfactory	05-12-2016	Public Health Engineering	02-01-2017	Badin	17.496
571.	1910	Rehabilitation of Drainage Scheme village Hassan Jamali	Satisfactory	17-11-2016	Public Health Engineering	30-12-2016	Shaheed Benazirabad	18.165
572.	1866	Sewerage Facilites at PMA Nur Goth village, at Gujo Thatta	Satisfactory	16-11-2016	Public Health Engineering	29-11-2016	Thatta	10.082

573.	1867	Construction of Drainage Schemes in Chhato Chand City, Gujjo City, Ghulamullah City, Ghara City, Mirpur Sakro City, Buhara City, Jungshahni City, Jhimpir City, Sonehri City, Gulmanda City, Ghulam Muhammad Brohi	Average	16-11-2016	Public Health Engineering	02-12-2016	Thatta	15.770
574.	1891	Development Schemes of NA-204 Larkana Construction of C.C.Drains including C.C Blocks for various U.Cs Larkana	Average	16-11-2016	Public Health Engineering	02-12-2016	Larkana, Karachi	31.462
575.	1798	Construction of Water Supply Scheme at (15 Nos.) villages of District Kamber at Shahdad Kot	Satisfactory	14-11-2016	Public Health Engineering	02-12-2016	Qambar Shahdadkot	83.492
576.	1768	Improvement of Water Supply System, Ward No.2, Sakro City, Tehsil Mirpur Sakro	Satisfactory	10-11-2016	Public Health Engineering	02-12-2016	Thatta	43.817
577.	1770	Rural Water Supply Scheme for village Allahdina Mirbahar	Satisfactory	10-11-2016	Public Health Engineering	02-12-2016	Thatta	20.288
578.	1806	Construction of Water Supply Scheme Kashmore Town	Average	10-11-2016	Public Health Engineering	29-11-2016	Kashmore	30.194
579.	1787	Water supply Scheme village Muhammad Rahim Chang & Adjoining Villages	Satisfactory	08-11-2016	Public Health Engineering	02-12-2016	Badin	13.178
580.	1871	Rural Drainage Scheme Satyoon Sharif	Un-Satisfactory	03-11-2016	Public Health Engineering	29-11-2016	Sujawal	19.822
581.	1875	Improvement & Extension of Urban Drainage Scheme T.M.Khan	Un-Satisfactory	02-11-2016	Public Health Engineering	01-12-2016	Tando Mohd. Khan	202.780
582.	1876	Rural Drainage Scheme Saeedpur Takkar	Un-Satisfactory	02-11-2016	Public Health Engineering	29-11-2016	Tando Mohd.Khan	37.080
583.	1796	Improvement & Extension of Urban Water Supply Scheme Lakhi (Filtration)	Satisfactory	17-10-2016	Public Health Engineering	09-11-2016	Shikarpur	167.400
584.	1887	Drainage Scheme Fateh Ali Chandio UC-Noorpur Taluka Kingri	Satisfactory	13-10-2016	Public Health Engineering	04-11-2016	Khairpur	21.135
585.	1799	Water Supply Scheme Village Kot Mir Mohammad	Satisfactory	07-10-2016	Public Health Engineering	31-10-2016	Khairpur	28.636
586.	1886	Drainage Scheme Rind Hajano Villagers	Satisfactory	22-09-2016	Public Health Engineering	26-10-2016	Khairpur	12.600
587.	1883	Providing new scheme for Mohalla Dabar	Average	21-09-2016	Public Health Engineering	26-10-2016	Khairpur	10.500
588.	1802	Providing and installing Reverse Osmosis (R.O) Plants at various location of NA-199	Average	09-09-2016	Public Health Engineering	21-10-2016	Sukkur	30.500
589.	1904	Drainage Scheme Village Moledino Rajper 2	Satisfactory	07-09-2016	Public Health Engineering	18-10-2016	Naushero Feroz	24.000
590.	1794	Water Supply Scheme for Village Sobho Khan Chang and Kamal Chang UC Jeando Rajpar	Satisfactory	06-09-2016	Public Health Engineering	18-10-2016	Naushero Feroz	28.580
591.	1884	Drainage Scheme Village Danwro U.C Khanpur Taluka Khairpur	Average	12-08-2016	Public Health Engineering	31-08-2016	Khairpur	16.800

592.	1800	Water Supply Scheme from Sathio Wah to Village Hidayatullah Katohar & other Villages	Satisfactory	11-08-2016	Public Health Engineering	07-09-2016	Khairpur	12.700
593.	1801	Rehabilitation of Water Supply Scheme Manghanwari Taluka Kingri	Satisfactory	10-08-2016	Public Health Engineering	19-09-2016	Khairpur	13.800
594.	1748	Rural W/S Scheme Abdullah Gabol Goth UC-5 Songal Gadap Town.	Un-Satisfactory	08-08-2016	Public Health Engineering	19-10-2016	Karachi	78.180
595.	1922	Drainage Scheme for Village Sardar Raza Muhammad Dahri	Satisfactory	02-08-2016	Public Health Engineering	31-08-2016	Shaheed Benazirabad	15.484
596.	1921	Drinage Schme for Village Loung Khan Soomro.	Satisfactory	01-08-2016	Public Health Engineering	26-08-2016	Shaheed Benazirabad	16.862
597.	1347	Imp: & Ext for Rural W/S Scheme Bahu Khoso Taluka Thull	Satisfactory	18-05-2016	Public Health Engineering	23-08-2016	Jacobabad	14.968
598.	1453	Drainage Scheme for various village Shaheed Banazirabad	Satisfactory	25-04-2016	Public Health Engineering	31-08-2016	Shaheed Benazirabad	5.513
599.	1355	Imp: & Ext: of W/S Scheme New Gud UC Purano Abad Taluka Bakrani.	Average	21-04-2016	Public Health Engineering	23-08-2016	Larkana	22.165
600.	1449	Rehabilitation Drainage Scheme Village New Batho.	Satisfactory	13-04-2016	Public Health Engineering	23-08-2016	Shaheed Benazirabad	12.537
601.	1356	Water Supply Scheme Deh-89 Nawabshah	Satisfactory	13-04-2016	Public Health Engineering	07-09-2016	Shaheed Benazirabad	10.870
602.	1428	Development Schemes relating to Drainage Sector C.C.Drains and C.C Bloks in various Muhalla of U.C -07 Larkana City.	Satisfactory	30-03-2016	Public Health Engineering	18-08-2016	Larkana	21.387
603.	1344	Urban Water Supply Scheme Dray Khan Mari (Revised).	Satisfactory	28-03-2016	Public Health Engineering	18-08-2016	Naushero Feroz	4.794
604.	1424	Drainage Scheme in Village Abul Khair Ujjan Tehsil Kingri District Khairpur.	Satisfactory	24-03-2016	Public Health Engineering	18-08-2016	Khairpur	10.302
605.	1351	Water Supply Scheme for Village Dhupwaro.	Satisfactory	10-03-2016	Public Health Engineering	12-08-2016	Khairpur	19.470
606.	1451	Rehabilitation of Drainage Scheme village Hassan Jamali.	Satisfactory	25-01-2016	Public Health Engineering	10-08-2016	Shaheed Benazirabad	18.165
607.	1971	Block Allocation for 15 schemes of ADP 2014-15 phased-out from ADP 2015-16 (No.1698 - Rs.5.367), (No.1703 - Rs.3.754), (No.1729 - Rs.10.503), (No.1752 - Rs.10.511), (No.1708 - Rs.3.750), (No.1857 - Rs.10.869), (No.1922 - Rs.10.00), (No.1914 -Rs.3.648),	Worst	19-01-2016	Public Health Engineering	17-02-2017	Sukkur	994.750
608.	1450	Urban Drainage Scheme Kaiynat Nagar	Satisfactory	21-12-2015	Public Health Engineering	01-08-2016	Shaheed Benazirabad	45.680
609.	Non-ADP	Construction of surface drain village Hajo dur Muhammad Baagat UC pir Hayat Taluka	Satisfactory	27-10-2015	Public Health Engineering	07-09-2016	Khairpur	0.826
610.	Non-ADP	Construction of surface drain village Wazir Ali Bhatti UC sami Tluka Sobhodero	Satisfactory	26-10-2015	Public Health Engineering	29-07-2016	Khairpur	1.100

611.	Non-ADP	Construction of CCBlock Village Tando Mir Karam UC Pir Hayat Ali Shah	Satisfactory	26-10-2015	Public Health Engineering	26-07-2016	Khairpur	1.400
612.	1349	Extension & Rehabilitation of existing W/S Scheme Shahdad Kot Town.	Satisfactory	30-09-2015	Public Health Engineering	14-07-2016	Qambar Shahdadkot	456.918
613.	2061	Consultancy for establishment of Sindh Emergency Rescue Service (1122) (Phase-I)	Satisfactory	14-03-2017	Rehabilitation (PDMA)	14-05-2017	Karachi	20.000
614.	1978	Rehabilitation / Reconditioning of Link Road from Kakar Pipri Road to Bordi Road, Taluka K.N. Shah District Dadu	Satisfactory	09-03-2017	Rural Development	03-04-2017	Dadu	20.000
615.	1982	Construction of road from Meher- Radhan road to village Ali Hyder Jhatial Taluka Mehar	Satisfactory	17-02-2017	Rural Development	03-04-2017	Dadu	20.000
616.	2039	Installation of 4 Solar Tube Wells in the UC Manahro, Taluka Kazi Ahmed District Shaheed Benazirabad.	Satisfactory	15-12-2016	Rural Development	16-02-2017	Shaheed Benazirabad	30.000
617.	1981	Construction of Road around Dargah Sufi Shah Inayat Shaheed and from Sim Nala to Dargah Makhdoom Sadaruddin, Khoso Goth	Average	17-11-2016	Rural Development	16-12-2016	Sujawal	30.000
618.	1975	Constt. of Road Ibrahim Jakhro to village Bharam Burfat UC Jangshahi Taluka & District Thatta (5 Kms)	Un-Satisfactory	14-11-2016	Rural Development	29-11-2016	Thatta	20.000
619.	1983	Development of existing Graveyard at village Sheranpur Taluka Garhi Khoro	Satisfactory	18-10-2016	Rural Development	09-11-2016	Jacobabad	15.000
620.	1496	Construction of C.C Topping, Brick Pavement & Open Surface Drain (Drainage System) Water Tank In (i) Ghareeb Abad U/C Daur, (ii) Village Aitabar Khan Rind U/C Jamal Shah, (iii) Village Wali Mohammad U/C Abul Hassan, (iv) Village Foji Mohammad Siddiqu	Satisfactory	04-05-2016	Rural Development	23-08-2016	Shaheed Benazirabad	51.000
621.	1495	Constt. of C.C Topping in Village Ghulam Nabi Brohi and Ismail Brohi UC Jam Sahib Taluka Daur.(ii) C.C. Topping in village Pheroze Shah Pharsi UC Ismail Khan Brohi & Ali Murad Brohi UC Jam Sahib Taluka Daur (iii) C.C Topping in Ward No: 3,7,8, UC Dau	Satisfactory	03-05-2016	Rural Development	25-08-2016	Shaheed Benazirabad	90.000
622.	1514	Installation of Solar Light in Municipal and Town Committees of Sindh.	Average	18-02-2016	Rural Development	25-08-2016	Khairpur	4,000.000
623.	2067	Sindh Government Officers Club at GOR Bath Island	Satisfactory	08-02-2017	S.G.A.and Coordination	03-04-2017	Karachi	813.569

		Karachi (Re-revised).						
624.	2090	Renovation of Circuit House Sukkur	Satisfactory	03-02-2017	S.G.A.and Coordination	07-03-2017	Sukkur	10.000
625.	2074	Construction of New Circuit House, Khairpur (Revised)	Satisfactory	05-01-2017	S.G.A.and Coordination	07-03-2017	Khairpur	124.527
626.	2083	Renovation & rehabilitation of Secretaries flats at GOR-I, Bath Island, Karachi	Satisfactory	03-01-2017	S.G.A.and Coordination	03-04-2017	Karachi	41.438
627.	2076	Renovation of Commissioner House Sukkur (Revised)	Satisfactory	21-12-2016	S.G.A.and Coordination	19-01-2017	Sukkur	25.162
628.	2073	Construction of office and residences of Enquiries and Anti-Corruption Establishment at Matiari, Tando Allahyar, Tando Muhammad Khan, Ghotki, Kashmore, Kambar and Jamshoro 2	Satisfactory	21-11-2016	S.G.A.and Coordination	30-12-2016	Qambar Shahdadkot	221.575
629.	2073	Construction of office and residences of Enquiries and Anti-Corruption Establishment at Matiari, Tando Allahyar, Tando Muhammad Khan, Ghotki, Kashmore, Kambar and Jamshoro 2	Satisfactory	16-11-2016	S.G.A.and Coordination	16-12-2016	Kashmore	221.575
630.	2073	Construction of office and residences of Enquiries and Anti-Corruption Establishment at Matiari, Tando Allahyar, Tando Muhammad Khan, Ghotki, Kashmore, Kambar and Jamshoro	Satisfactory	19-09-2016	S.G.A.and Coordination	18-10-2016	Tando Mohd. Khan	221.575
631.	2075	Construction of Circuit House, Nawabshah	Satisfactory	09-09-2016	S.G.A.and Coordination	18-10-2016	Shaheed Benazirabad	59.736
632.	2065	Construction of New Secretariat Complex No. 7	Average	21-07-2016	S.G.A.and Coordination	19-09-2016	Karachi	4,726.000
633.	1577	Rehabilitation and reconstruction of residential area of Commissioner Office (4, Club Road), Karachi	Satisfactory	31-05-2016	S.G.A.and Coordination	22-07-2016	Karachi	67.553
634.	Non-ADP	MDG Scheme Widening & Reconditioning of Tando Adam BhitShah Road 1.0 KM	Satisfactory	09-05-2016	S.G.A.and Coordination	15-07-2016	Sanghar	19.996
635.	Non-ADP	Electrification of Village Bajeer paro near dargha main jam muhammad UC Umerkot -II.	Satisfactory	28-03-2016	S.G.A.and Coordination	14-07-2016	Umerkot	0.800
636.	1616	Entrepreneurship Development Programme.	Satisfactory	06-05-2016	Sindh Board of Investment (SBI)	31-10-2016	Sukkur	50.000
637.	2115	Establishment & Strengthening of Darul Aman at Mirpurkhas & Jacobabad	Un-Satisfactory	09-02-2017	Social Welfare	05-05-2017	Mirpurkhas, Jacobabad	89.044
638.	2115	Establishment & Strengthening of Darul Aman at Mirpurkhas & Jacobabad	Satisfactory	03-02-2017	Social Welfare	31-05-2017	Mirpurkhas	89.044

639.	1619	Establishment of Darul Aman at Mirpurkhas & Jacobabad (C:69.940 + R:19.104)	Satisfactory	26-04-2016	Social Welfare	26-08-2016	Jacobabad	89.044
640.	1795	Urban Water Supply Scheme Thull Town	Average	15-02-2017	Special Initiatives Unit	08-06-2017	Jacobabad	585.700
641.	2128	Solar Power Generation for Water Filtration Plants- Drinking Water Hubs Projects (Phase-I & II) (Revised)	Average	23-01-2017	Special Initiatives Unit	13-05-2017	Khairpur	2,135.000
642.	2126	Establishment of Drinking Water Hubs (Phase-II) for 750 Units	Average	18-01-2017	Special Initiatives Unit	03-04-2017	Naushero Feroz	4,000.000
643.	2126	Establishment of Drinking Water Hubs (Phase-II) for 750 Units	Average	10-01-2017	Special Initiatives Unit	07-03-2017	Shaheed Benazirabad	4,000.000
644.	2132	Establishment of IBA Campus Thatta (Capital Rs.773.37+Rev:Rs.224.51)	Satisfactory	20-12-2016	Special Initiatives Unit	27-01-2017	Thatta	997.880
645.	2133	Allocation for Various Development Schemes for District Thatta and Sujawal	Satisfactory	17-11-2016	Special Initiatives Unit	16-12-2016	Thatta, Sujawal	1,500.000
646.	2134	New Drainage System for Thatta City	Average	14-11-2016	Special Initiatives Unit	29-11-2016	Thatta	192.000
647.	1629	Solar Power Generation for Water Filtration Plants- Drinking Water Hubs Projects (Phase-I & II) (Revised) (C.2080+R.55)	Average	30-05-2016	Special Initiatives Unit	24-10-2016	Sukkur	21,350.000
648.	1627	Establishment of Drinking Water Hubs (Phase-II) for 750 Units (C.3823.768+R.176.232)	Satisfactory	25-05-2016	Special Initiatives Unit	27-09-2016	Khairpur	4,000.000
649.	1627	Establishment of Drinking Water Hubs (Phase-II) for 750 Units (C.3823.768+R.176.232)	Satisfactory	19-05-2016	Special Initiatives Unit	27-09-2016	Shikarpur	4,000.000
650.	55	Allocation of community Development Program (CDP) for sustainable development Goals (SDGs)	Satisfactory	28-04-2016	Special Initiatives Unit	31-08-2016	Shikarpur	7,000.000
651.	Non-ADP	Street paverment at Mohalla Raza Shah U.C Baberloi Taluka District Khairpur	Satisfactory	20-11-2015	Special Initiatives Unit	12-07-2016	Khairpur	5.017
652.	2148	Consolidation / Improvement and Additional Facilities at Sindh Sports Board Complex, Hyderabad. (Revised)	Un-Satisfactory	22-04-2017	Sports & Youth Affairs	16-06-2017	Hyderabad	157.949
653.	2156	Development of Shadab Sports Ground Orangi Town (C:57.886+R:2.016)	Satisfactory	02-03-2017	Sports & Youth Affairs	10-04-2017	Karachi	59.902
654.	2146	Construction of Sports Stadium in Sindh (8 Nos.) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar)	Un-Satisfactory	21-02-2017	Sports & Youth Affairs	03-04-2017	Shikarpur	225.704
655.	2161	Construction of Academy Players Hostel & Allied Facilities at NNG Ground at Block-H, North Nazimabad	Satisfactory	21-02-2017	Sports & Youth Affairs	03-04-2017	Karachi	60.000

656.	2163	Multi-purpose Ground Pavilion and Allied Facilities at Garhi Khairo District Jacobabad	Satisfactory	17-02-2017	Sports & Youth Affairs	03-04-2017	Jacobabad	59.742
657.	2169	Construction of Sports Ground Multi-purpose Hall at Mehar Town	Un-Satisfactory	16-02-2017	Sports & Youth Affairs	10-04-2017	Dadu	59.749
658.	2146	Construction of Sports Stadium in Sindh (8 Nos.) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar)	Satisfactory	14-02-2017	Sports & Youth Affairs	10-04-2017	Tando Allahyar	225.704
659.	2146	Construction of Sports Stadium in Sindh (8 Nos.) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar)	Satisfactory	10-02-2017	Sports & Youth Affairs	20-03-2017	Jamshoro	225.704
660.	2146	Construction of Sports Stadium in Sindh (8 Nos.) (Part-I). (Matiari, Jamshoro, Hyderabad, Tharparkar, Sanghar, Shikarpur, Jacobabad & Tando Allahyar)	Average	09-02-2017	Sports & Youth Affairs	20-03-2017	Matiari	225.704
661.	648	Renovation and Rehabilitation of Paramedical Institute, Larkana. (C: 47.948+R: 19.785)	Satisfactory	08-02-2017	Sports & Youth Affairs	29-03-2017	Larkana	67.733
662.	2158	Construction of Sports Club, Umer Muhallah Faqeer Colony Orangi Town	Satisfactory	07-02-2017	Sports & Youth Affairs	03-04-2017	Karachi	42.211
663.	2157	Construction of Grassy Cricket Ground at village Tharo KhanMengal U/C 5 Gadap Town (C:39.404+R:2.117)	Average	01-02-2017	Sports & Youth Affairs	31-05-2017	Karachi	41.522
664.	2164	Construction of boundry Wall and Installation of Flood Lights for Synthetic Hockey Ground at Shaheed Z.A Bhutto Sports Complex Mirpurkhas	Satisfactory	23-01-2017	Sports & Youth Affairs	21-03-2017	Mirpurkhas	59.997
665.	2166	Laying of Old Synthetic Hockey Turf at KHA Ground NIPA, Karachi	Satisfactory	17-01-2017	Sports & Youth Affairs	17-02-2017	Karachi	43.996
666.	2162	Laying of Synthetic Hockey Turf at Nawabshah	Satisfactory	23-12-2016	Sports & Youth Affairs	03-04-2017	Shaheed Benazirabad	87.999
667.	2152	Construction of Cricket Stadium at Mehrabpur (C:36.037+R:1.205)	Satisfactory	19-12-2016	Sports & Youth Affairs	27-04-2017	Naushero Feroz	37.242
668.	2153	Construction of Sports Stadium at Karachi (5 Units) Gulberg, New Karachi, Landhi, Orangi and Baldia Towns(C:528.307+R:30.263)	Satisfactory	14-12-2016	Sports & Youth Affairs	11-01-2017	Karachi	558.570
669.	2160	Rehabilitation and Installation of Flood Lights at Malir Football Stadium, Saudabad	Satisfactory	14-12-2016	Sports & Youth Affairs	11-01-2017	Karachi	50.564
670.	2202	Construction of Youth Hostel at Jacobabad	Average	07-12-2016	Sports & Youth Affairs	10-04-2017	Jacobabad	57.469
671.	2205	Women Skill Development Centre at Kashmore	Un-Satisfactory	10-11-2016	Sports & Youth Affairs	02-12-2016	Kashmore	44.000
672.	2167	Laying of Synthetic Hockey Turf at Luqman Hockey	Average	28-09-2016	Sports & Youth Affairs	18-10-2016	Khairpur	102.189

		Ground, Khairpur						
673.	2155	Construction of Malakhara Stadium at Sehwan Sharif	Un-Satisfactory	18-08-2016	Sports & Youth Affairs	03-10-2016	Jamshoro	59.638
674.	2153	Construction of Sports Stadium at Karachi (5 Units) Gulberg, New Karachi, Landhi, Orangi and Baldia Towns(C:528.307+R:30.263)	Un-Satisfactory	09-08-2016	Sports & Youth Affairs	31-08-2016	Karachi	558.570
675.	2153	Construction of Sports Stadium at Karachi (5 Units) Gulberg, New Karachi, Landhi, Orangi and Baldia Towns(C:528.307+R:30.263)	Satisfactory	08-08-2016	Sports & Youth Affairs	31-08-2016	Karachi	558.570
676.	1674	Youth Empowerment Space (Compliance Visit)	Satisfactory	21-07-2016	Sports & Youth Affairs	25-10-2016	Karachi	59.991
677.	1692	Sindh Skills Development Project (Component BBSYDP-I and STEVTA-II & III)	Un-Satisfactory	30-08-2016	STEVTA	16-02-2017	Hyderabad,Karachi	431.046
678.	2222	Widening/Improvement of Road from Wango More to Thar Coalfield Area (Phase-II) (Mile 0/0-83/2 (134.86 km). (Revised)(Cap. Rs. 8159.600 + Rev. Rs. 29.030 = T. Rs. 8188.630)	Satisfactory	21-04-2017	Thar Coal Infrastructure Development	19-05-2017	Tharparkar	8,188.630
679.	2221	Improvement & Widening Road Network from Seaport Karachi to Thar Coalfield Area via Thatta, Badin, Wango, Mithi, Islamkot (Phase-I Upto Wango More 124.5 Mile= 200 KM) (Re-revised) (Cap. Rs. 8318.543 + Rev. Rs. 31.738 = T. Rs. 8350.281)	Un-Satisfactory	19-09-2016	Thar Coal Infrastructure Development	25-10-2016	Badin	8,350.281
680.	2221	Improvement of Road Network from Thatta to WangoMor Via Sujawal, Badin with construction of by passes for Shadi Large , Khoski, Nindo,Badin and Sujawal, Construction of Overhead Bridge over Railway Level Crossing on Badin Bypass, Construction of a	Satisfactory	20-01-2016	Thar Coal Infrastructure Development	06-02-2017	Badin	8,350.281
681.	2241	Construction of Bus Terminals in Thatta, Badin, and Kamber Shahdadkot at Miro Khan. (C.214.355 +R.66.097)	Average	24-03-2017	Transport & Comm. (Roads)	19-05-2017	Thatta, Qambar Shahdadkot, Badin, Larkana	280.452
682.	2240	Rehabilitation of Drivers Training School under public private partnership at Karachi/ Hyderabad/ Sukkur/Larkana (C: 29.639 + R.72.569)	Satisfactory	06-03-2017	Transport & Comm. (Roads)	03-04-2017	Hyderabad	102.208
683.	2242	Construction of BRTS Orange Line (C.2335.925+R.28.265)	Satisfactory	24-10-2016	Transport & Comm. (Roads)	29-11-2016	Karachi	2,364.190
684.	1702	Construction of Bus Terminals in Thatta & Badin, and Kamber Shahdadkot at Miro Khan. (C.214.355 +R.66.097)	Satisfactory	12-05-2016	Transport & Comm. (Roads)	16-08-2016	Qambar Shahdadkot	280.452

685.	523	Establishment of Innovation & Entrepreneurship Centre (IEC)-An Extension of MUET, Jamshoro. (C:47.807 + R:147.514)	Average	20-10-2016	Universities and Boards	29-11-2016	Jamshoro	195.321
686.	512	Establishment of Department of Serobiology and providing power generation by gas along with heat recovery system at Ojha Campus of Dow University of Health Sciences, Karachi(C: 310.811+R:	Satisfactory	25-08-2016	Universities and Boards	26-10-2016	Karachi	410.265
687.	535	Establishment of Shaheed Benazir Bhutto Chair at SALU Khairpur (C:28.766 + R:12.132)	Un-Satisfactory	08-08-2016	Universities and Boards	19-09-2016	Khairpur	40.898
688.	525	Establishment of Faculty of Pharmacy at Benazir Bhutto Shaheed University Lyari in Joint Venture with Benazir Bhutto Medical University Larkana	Satisfactory	19-07-2016	Universities and Boards	19-09-2016	Karachi	46.297
689.	1717	Establishment of Khairpur College of Agriculture Engineering and Technology at Khairpur Mirs Constituent College of Sindh Agriculture University Tandojam	Satisfactory	11-08-2014	Universities and Boards	24-08-2016	Khairpur	601.750
690.	1634	Rehabilitation / Renovation of Jaral Shah Dargah at Larkana (Revised)	Satisfactory	08-02-2017	Women Development	29-03-2017	Larkana	20.440
691.	2253	Advocacy for Women Empowerment in Sindh.	Satisfactory	01-12-2016	Women Development	28-12-2016	Karachi	49.386
692.	2252	Establishment of Women Development Complex at SBA.	Un-Satisfactory	17-11-2016	Women Development	01-06-2017	Shaheed Benazirabad	44.767
693.	2254	Women Development complex at Sukkur	Satisfactory	17-11-2016	Women Development	27-02-2017	Sukkur	210.307
694.	2277	Construction / Improvement of road from Ruk to Garhiyasin via Amrote, Nausharo Abro road Mile 0/0-12/2	Un-Satisfactory	10-05-2017	Work and Service	19-05-2017	Shikarpur	342.152
695.	2149	Construction of Sports Stadium Covering remaining Districts in Sindh (08 Units) ghotki	Un-Satisfactory	09-05-2017	Work and Service	19-05-2017	Ghotki	519.400
696.	2632	Construction of Road from Kotpull Shadi Dhooan to village Manghelo Khan Jalbani via Sabul Khan Jalbani mile 0/0-1/2 (2.51 kms)	Satisfactory	03-05-2017	Work and Service	19-05-2017	Khairpur	26.195
697.	2701	Construction of link road from Kot Lalu Darya Khan Mari to Mehrabpur via Sangi Minor road (42.00 Kms)	Un-Satisfactory	21-04-2017	Work and Service	19-05-2017	Naushero Feroz	574.000
698.	2686	Construction of road from RQC Highway to Chohi Shakh via Mitha pur	Satisfactory	18-04-2017	Work and Service	27-04-2017	Shikarpur	31.111
699.	2395	W/R of road National Highway to Tando Adam via Bhit Shah mile 0/0-17/0 (27.20 Kms)	Average	18-04-2017	Work and Service	31-05-2017	Sanghar, Matiari	747.346

700.	2373	Provision for Improvement of roads in Sindh (N.Feroze, Khairpur, Suk, Gotki, Shikarpur, Larkano, Shahdadko, J abad, Kashmore, Thatta, Hyderabad, TA Yar, T.M. Khan, Matiari, M.Khas, Sujawal, Thar, Sanghar, U.Kot, Badin, Jamshoro, S.B.A. Dadu & Karachi)	Satisfactory	13-04-2017	Work and Service	20-05-2017	Tando Allahyar, Hyderabad, Matiari, Tando Mohd. Khan	2,324.114
701.	2471	W/R of Sanghar to Khipro via Dillon Shakh with Asphalt - Phase-I	Average	13-04-2017	Work and Service	07-06-2017	Sanghar	700.000
702.	2739	Construction of Abdul Salam Thahim Flyover Bridge at Shahdadpur over Jatia Railway Phatak	Satisfactory	12-04-2017	Work and Service	20-05-2017	Sanghar	688.231
703.	2411	Widening / Reconditioning Tando Allahyar - Tando Adam road (28.96 Kms)	Average	10-04-2017	Work and Service	20-06-2017	Tando Allahyar	728.185
704.	Non-ADP	District ADP Reconditioning of Road Nauabad to Jhole-Bobi Via Sahib Khan Liskani Road 0/0-4/7-5/0 +436 ft & 9/4 - 12/4 Total 13.69 KM	Satisfactory	27-03-2017	Work and Service	13-04-2017	Sanghar	99.984
705.	2501	Construction of road NHA Via Mehar Shah Main Drain up to Wada Mehesar Road road mile 0/0-7/0 (11.26 Kms)	Un-Satisfactory	07-03-2017	Work and Service	20-05-2017	Khairpur	84.527
706.	2014-15 1430	Extension/Improvement of Urban Drainage scheme Jacobabad	Un-Satisfactory	22-02-2017	Work and Service	14-03-2017	Jacobabad	1,187.000
707.	2639	Construction of road from Torri to Gaji Shah road mile 0/0-1/6 (2.80 Km).	Un-Satisfactory	16-02-2017	Work and Service	03-04-2017	Dadu	23.492
708.	2497	Construction of road from Kaser Dasti to Village Wahid Bux Mazari Mangwani mile 0/0-4/0 (6.44 Kms)-	Un-Satisfactory	16-02-2017	Work and Service	02-06-2017	Ghotki	83.810
709.	2541	Construction of Road from main Thull / Jacobabad Road (Lakhi Pir) to village Amir Khan Khoso via Lal bux Khoso to link Road Zanglipur / Bahadurpur Road (Chatrri Masjid) (4.5 Kms)	Un-Satisfactory	10-02-2017	Work and Service	13-05-2017	Jacobabad	52.593
710.	2669	Reconstruction of black top road from Tando Jan Muhammad - Jhuddo road Nasirabad to Ghuram Bhatti (4.0 Kms.)	Satisfactory	03-02-2017	Work and Service	20-03-2017	Mirpurkhas	28.818
711.	2332	Improvement / Construction of road from Rajputana Hospital to National Highway Bypass via Gulistan-e-Sajjad village BudhoPalariMakhdoomRafiq-uz-Zaman road dual carriagewayroad mile 0/0-2/4 (4.0Kms) Replacement scheme.	Satisfactory	18-01-2017	Work and Service	16-02-2017	Hyderabad	300.548

712.	2594	Construction of Road from FFC Factory to connect Mirpur Mathelo road on LP Path Massu Wah mile 0/0-2/0 (3.32 Kms)	Satisfactory	16-01-2017	Work and Service	17-02-2017	Ghotki	42.525
713.	2648	Construction of road from Mirpurkhas - Khan road to village Khan Bahadur Ghulam Muhammad Wasan mile 0/0-3/2 (5.20 Kms)	Satisfactory	16-01-2017	Work and Service	21-03-2017	Mirpurkhas	44.948
714.	2562	Construction of road from J.J.V.L Gas Company to village Zain Farm road mile 0/0-1/7 (3.0 Kms).	Satisfactory	09-01-2017	Work and Service	17-02-2017	Hyderabad, Matiari	45.535
715.	2530	Const: of road from Umerkot to Soofi Dhoro Naro road on Krowah Path via Hurabad 7 mile mori 18.00 Kms	Un-Satisfactory	04-01-2017	Work and Service	17-02-2017	Umerkot	90.000
716.	2446	Reconditioning of road from Parillal line to Mohalla Saleemabad via Faizabad colony upto Red Palace Hotel near old National Highway i/c Masonry Structure 1/2 Premix Carpet (4.00 Kms).	Average	04-01-2017	Work and Service	17-02-2017	Khairpur	38.270
717.	2618	Construction of road from Wada Bhatti to Ali gohar and from Bhillo Jo Bhit to village Muhammad Hashim Bhatti from Main road Bolooji Bhits (2.0 kms)	Average	28-12-2016	Work and Service	11-01-2017	Khairpur	21.325
718.	2392	Reconditioning of road from Sagyoon to Waryam Sial Abdul Karim Kharal road mile 0/0-4/0(6.43Kms)	Satisfactory	26-12-2016	Work and Service	11-01-2017	Khairpur	46.737
719.	2570	Const. of road from village Tariq Khokhar to Jamot Farm mile 0/0-1/6 (2.82 Kms)	Satisfactory	22-12-2016	Work and Service	24-01-2017	Tando Allahyar	43.786
720.	2359	Improvement of Road from Fakir Mohammad Path Road to Darawahan Shakh mile 0/0-2/6 (4.40 kms)	Un-Satisfactory	21-12-2016	Work and Service	11-01-2017	Sukkur	28.470
721.	2394	W/R National Highway to Mori Yousuf Khan Hajano via DargahHazrat Syed Ahmed Shah Lakyari road (7.00 Kms)	Satisfactory	16-12-2016	Work and Service	24-01-2017	Matiari	124.105
722.	2425	Improvement of road from Hatim Jatoi Phattak to Phulji Station road mile 0/0-6/7 (11.06 Kms).	Satisfactory	13-12-2016	Work and Service	27-01-2017	Dadu	102.441
723.	2449	Reconditioning of Road From Begu Kaka to village Agro Rahu Taluka Saeedabad (3.2 Kms).	Satisfactory	09-12-2016	Work and Service	27-01-2017	Matiari	20.815
724.	2643	Construction of road from Kalro link road to village Kot Makhdom Piniladho village Ali Akbar Jakhro mile 0/0-2/4	Satisfactory	09-12-2016	Work and Service	24-01-2017	Matiari	54.143

725.	2448	Reconditioning of Road From Telegraph Colony to Muslim Town (3.2 Kms)	Satisfactory	08-12-2016	Work and Service	24-01-2017	Jamshoro	25.335
726.	2374	Improvement of Mataro Kario Ganhwar to Kharwah road 0/0-24/0 (38.64 Kms)	Average	07-12-2016	Work and Service	11-01-2017	Badin	622.044
727.	Non-ADP	District ADP Dadu Improvement/ Extension of road from police post Larkana to Shaheed Makhdoom Bilawal Gate Dadu (Paving Block, Divider foot path & drain) District Dadu Phase 1	Satisfactory	05-12-2016	Work and Service	13-01-2017	Dadu	20.000
728.	Non-ADP	District ADP Dadu Improvement from Gym khana to Shah Jahan Park Dadu i.e Paving block, Divider foot path & drain) District Dadu (Phase 1)	Satisfactory	05-12-2016	Work and Service	13-01-2017	Dadu	20.000
729.	Non-ADP	District ADP Dadu Improvement/ Extension of road Al-Makkah Hotel to Shaheed Zulfiqar Bhutto Gate Dadu i.e Paving block, Divider foot path & drain) District Dadu (Phase 1)	Satisfactory	05-12-2016	Work and Service	13-01-2017	Dadu	20.000
730.	Non-ADP	District ADP Dadu Improvement of Gymkhana to Sikanadar Khuharo Petroleum/c paving block, divider foot path drain District Dadu Phase 1	Average	05-12-2016	Work and Service	13-01-2017	Dadu	20.000
731.	2690	Reconditioning of Road From X-National Highway @ Mile 171/4 to village Bhai Khan Sohejo VIA Golo Unar and Karo Ketu Mile 0/0-3/1 (5.0 Km)	Satisfactory	01-12-2016	Work and Service	11-01-2017	Hyderabad, Matiari	34.758
732.	2300	Improvement of Hyderabad Tando Fazal Seri road mile 0/0-24/0(38.64 Kms).	Satisfactory	01-12-2016	Work and Service	24-01-2017	Hyderabad	146.744
733.	2557	Construction of road from Bhai Khan Chandio via Kanti Wah to village Rasool Bux Baloch mile 0/0-1/7 (3.0 Kms)	Average	22-11-2016	Work and Service	16-12-2016	Thatta	29.222
734.	2556	Construction of road from Udassi link road to Haji Ibrahim Baloch road mile 0/0-1/2 (2.00 Kms)	Un-Satisfactory	18-11-2016	Work and Service	20-12-2016	Thatta	19.990
735.	2308	W/R N Feroz Paddidan Phull meet Kot Kumb Kot Lalu Road mile 0/0-24/0 (38.61 Kms).	Un-Satisfactory	18-11-2016	Work and Service	02-01-2017	Naushero Feroz	139.903
736.	2592	Construction of Road from Sada Wah Pacci Mori to Baba Ashique Hussain Dargah, Taluka Bhiria City, Bhiria Road (3.0 kms)	Satisfactory	18-11-2016	Work and Service	22-12-2016	Naushero Feroz	33.859
737.	2661	Construction of Haleji-Nooriabad road to Jungshahi Eidgah road	Average	14-11-2016	Work and Service	16-12-2016	Thatta	23.999

738.	2500	Bhango Pholare road (Ameer Poto) to Village Ghulam Rasool Janwari Via Kamalo Bhango Haji Murad Burdi pir Bux Jarper & Kalhora Village mile 0/0- 7/4 (12.0 Kms).	Un-Satisfactory	08-11-2016	Work and Service	15-12-2016	Khairpur	84.080
739.	2666	Construction of Road from Haji Baig Mohammad Panhwar to Mitho than Marri District N Feroz (4.00 Km)	Satisfactory	08-11-2016	Work and Service	16-12-2016	Sukkur, Naushero Feroz	35.815
740.	2299	W/R of road from Digri to Rajo Khanani via Bhudho Qambrani Deh-170 Mile 0/0 - 20/4 (33.0 Kms)	Un-Satisfactory	07-11-2016	Work and Service	16-12-2016	Badin	237.985
741.	2391	Rehabilitation of road from Gambat to Ranipur (6.40 Kms)	Satisfactory	07-11-2016	Work and Service	08-12-2016	Khairpur	82.560
742.	2644	Construction of road from Basic Health Unit (B.H.U) Mattaro Mandharo road @ Mile 5/4 to village Uris Bhatti mile 0/0-4/2 (6.80 km)	Average	07-11-2016	Work and Service	08-12-2016	Badin	66.869
743.	2304	Widening / Reconditioning of Bulri Shah Karim to Khorwah Chowk mile 0/0-21/0 (33.81 Kms).	Average	02-11-2016	Work and Service	16-12-2016	Tando Mohd. Khan	85.238
744.	Non-ADP	Reconditioning of Road Naubad to Jhole Road Via Village Sahib Khan Liskani Road	Un-Satisfactory	17-10-2016	Work and Service	29-11-2016	Sanghar	97.404
745.	2383	W/R of road from Mirpur Buriro to village Garhi Syed (5.03Kms)	Satisfactory	17-10-2016	Work and Service	09-11-2016	Jacobabad	85.760
746.	2683	Construction of Link Road Through Sim Nala Raj Malik Road at point village Muhammad Ayoob Thaheem to village mamuBhadaee (8.00 Kms)	Average	14-10-2016	Work and Service	08-12-2016	Sujawal, Thatta	126.991
747.	2699	Re-Construction of road from Seri to Tando Muhammad Khan Mula Katiar road along Pinyari canal (10.60 kms) (Phase-I link).	Satisfactory	10-10-2016	Work and Service	08-12-2016	Tando Mohd. Khan	398.355
748.	Non-ADP	Construction of Bridge Across River Indus Linking Jheeruk with Mulla Katiar	Satisfactory	10-10-2016	Work and Service	08-12-2016	Thatta, Tando Mohd. Khan	5,402.000
749.	2353	Reconditioning of Road from Phull Masur Ji Wah Road to village Din Mohammad Leghari via Budho Leghari mile 0/0-3/0 (5.0 Kms)	Un-Satisfactory	07-10-2016	Work and Service	09-11-2016	Naushero Feroz	40.522
750.	2352	Reconditioning of Road from Ratodero Naudero Road to village Daro Illahi Bux mile 0/0-1/7 (3.0 kms)	Satisfactory	26-09-2016	Work and Service	21-10-2016	Larkana	31.850

751.	2547	Construction of road from Hyderabad road to meet Mirwah road near Abdin Pump (Mirpurkhas Southern Bypass) mile 0/0-7/4(12.07 km)	Satisfactory	23-09-2016	Work and Service	19-10-2016	Mirpurkhas	383.726
752.	2635	Construction of road from RD 97 Takani Regulator to village Mirza Khan Gabol Mile 0/0-1/7 (3.00 Kms)	Average	22-09-2016	Work and Service	14-10-2016	Thatta	31.005
753.	2435	Improvement of road from Allah wala Chowk to Shah Habib Petrol pump via Dargah Shah Abdul Latif Bhittai Bhit Shah road (3.2 Kms)	Satisfactory	21-09-2016	Work and Service	18-10-2016	Matari	54.303
754.	2452	Reconditioning of road Mirpur Mathelo to Kheenjar Fateh Ali khan via Dad Laghari (4.00 Kms)	Satisfactory	06-09-2016	Work and Service	21-10-2016	Ghotki	31.645
755.	2686	Construction of road from RQC Highway to Chohi Shakh via Mithapur (3.20 Kms)	Un-Satisfactory	02-09-2016	Work and Service	01-11-2016	Shikarpur	31.111
756.	2348	Improvement of road from Manzoor Ali Pitafi to Dad Jarwar Mile 0/0-3/2 (5.02 Kms)	Satisfactory	29-08-2016	Work and Service	18-10-2016	Tando Allahyar	35.080
757.	2513	Construction of Main Jhullori-Dengan road to Main Umerkot road, connect 78 mile Mori road / Sugar Mill road via Tawakal Lashari, Wagho Kolhi, Dhani Buksh Malkani & Hemraj Kolhivillage mile 0/0-7/4	Un-Satisfactory	26-08-2016	Work and Service	18-10-2016	Mirpurkhas	114.061
758.	2354	Reconditioning of Road from National Highway to Jamali Pump to Phul Bughio mile 0/0-2/4 (4.0 kms)	Satisfactory	23-08-2016	Work and Service	19-09-2016	Naushero Feroz	27.176
759.	2419	W/R of road from Kumb Nawabshah to Daood ji Mori to Village Mahram Khan Nagore via Ibrahim Larik road mile 0/0-2/4 (4.00 Kms)	Satisfactory	22-08-2016	Work and Service	19-09-2016	Naushero Feroz	65.180
760.	2548	Construction of road from Sukhio Mori to Amir Peer Mori via Budhar Babariyoon including links to Qadir Bux Chahwan, Roshan Chahwani Wadero Qaim Panhwar Wali Muhammad Bughio Haji Ali Akbar Chahwan Ghulam Nabi Bughio and Nasurllah Bughio mile 0/0-5/0 (8 Km)	Average	18-08-2016	Work and Service	19-10-2016	Jamshoro, Dadu	124.370
761.	2749	Construction of road from Dubar to Bhilini Mile 0/0-12/0 (19.30 KM)	Un-Satisfactory	17-08-2016	Work and Service	19-09-2016	Sukkur	161.628

762.	2647	Construction of metalled road Indus Highway to Murad Khushik via Birmani Bagh Ali Qureshi Palio Lohar mile 0/0-2/1+330 (3.50 Kms)	Un-Satisfactory	16-08-2016	Work and Service	18-10-2016	Dadu	24.741
763.	2496	Construction of Road from Indus Highway at Mile 157/0 to Suprio Bund along Rajwah inspection Park Mile 0/0-10/0 16 Kms)	Un-Satisfactory	16-08-2016	Work and Service	18-10-2016	Dadu	117.082
764.	2379	Improvement of road from Kandi Chukhi to Kumb village mile 0/0-3/1 (5.0 kms)	Un-Satisfactory	16-08-2016	Work and Service	18-10-2016	Dadu	37.244
765.	2610	Construction of remaining portion of road from Serai Piyaro Khan to Gambat (3.41 Kms)	Satisfactory	16-08-2016	Work and Service	19-09-2016	Khairpur	36.352
766.	Non-ADP	District ADP Reconditioning of Sanghar Khipro off taking road	Satisfactory	15-08-2016	Work and Service	14-10-2016	Sanghar	99.984
767.	1829	W/R of road from Khorwah to Khorwah Chowk mile 0/0-8/0(12.88)	Satisfactory	12-08-2016	Work and Service	18-10-2016	Badin	178.992
768.	2534	Construction of Road from Malak Chowdagi to Nandi Thari (12.0 Km) Khairpur	Un-Satisfactory	11-08-2016	Work and Service	19-09-2016	Khairpur	64.397
769.	2533	Construction of Road from Nara Tajjal Gate Road to Khumbhrah Channel (Nauabad) (10.25 Kms)	Un-Satisfactory	10-08-2016	Work and Service	07-09-2016	Khairpur	50.713
770.	2700	Construction / Impvment of Awan Road Sukkur City mile 0/0-1/4 (2.40 Kms) (Phase-II)	Un-Satisfactory	04-08-2016	Work and Service	19-09-2016	Sukkur	80.090
771.	Non-ADP	MDG Schemes Reconstruction of Tando Adam Tando allahyar road (Town portion Usman Shah Ji Huri Mile 0/0-0/6 +330 ft (1.31 KM)	Satisfactory	28-07-2016	Work and Service	25-08-2016	Tando Allahyar	20.000
772.	2311	Widening & Reconditioning of ThattaPirPatho to Ghora Bari Road 0/0-25/0=40.22 Kms	Un-Satisfactory	20-07-2016	Work and Service	30-09-2016	Thatta	302.260
773.	1149	Rehabilitation of Roads internal streets Block-4 Bath island PS-112 Saddar Town Karachi.	Satisfactory	19-07-2016	Work and Service	30-09-2016	Karachi	19.233
774.	1219	EARTH WORK / REMODLING OF UMAR KASS MINOR /WAH DSP OFFIC TO NEW YARD ADP # 1219	Un-Satisfactory	31-05-2016	Work and Service	15-07-2016	Sukkur	20.000
775.	517	Construction of Covered Passage for Prisoners from Central Prison-II, to District & Session court Sukkur.	Satisfactory	30-05-2016	Work and Service	13-07-2016	Sukkur	7.249
776.	507	Repair & Renovation of Barrack,@ Central Prison-1,Sukkur.	Average	30-05-2016	Work and Service	13-07-2016	Sukkur	49.153

777.	2081	Construction of road from Bus stand Goth Ahmed Khan Almani to Otaq Ahmed Khan Almani road Mile 0/0 -1/0	Satisfactory	27-05-2016	Work and Service	13-07-2016	Hyderabad	22.925
778.	2085	Construction of road from Village Bhutto Hajano darya baig mughal to Vakri band road mile 0/0-1/0	Satisfactory	27-05-2016	Work and Service	13-07-2016	Hyderabad	26.475
779.	2150	Construction of road from Waryam Wandiar to village Mir Khan Mangnejo Road Mile 0/0-1/2. (2.00 Km).	Satisfactory	26-05-2016	Work and Service	02-08-2016	Khairpur	19.378
780.	2148	Construction of road from Balouch Khan Zardar to Government High School Muhammad Shah road mile 0/0-1/6 (2.80 Kms).	Satisfactory	25-05-2016	Work and Service	02-08-2016	Khairpur	30.594
781.	2051	Construction of Road Imam Bux Katohar to village Mohammad Arab Katohar Road mile 0/0-2/0 (3.20 kms)	Satisfactory	24-05-2016	Work and Service	04-08-2016	Khairpur	16.804
782.	2147	Construction of road from Thari Seneso to Resident of Ahmed Ali Janvri & Fouj Ali Janvri road mile 0/0-1/7 (3.0 kms)	Satisfactory	24-05-2016	Work and Service	02-08-2016	Khairpur	33.594
783.	2050	Construction of Road from over the top of Kupri minor Tunia Pull to Shahal Dhani road mile 0/0-1/2 (2.0 kms)	Un-Satisfactory	23-05-2016	Work and Service	01-08-2016	Khairpur	21.344
784.	508	Renovation of Central Jail Khairpur.	Satisfactory	23-05-2016	Work and Service	13-07-2016	Khairpur	73.310
785.	1861	Reconditioning of Road from National Highway Qalandari pump to village Marri Road mile 0/0-1/7 (3.0 Kms)	Satisfactory	17-05-2016	Work and Service	04-08-2016	Khairpur, Naushero Feroz	20.576
786.	1887	Renovation / reconditioning of road from village Rasheed Arain, Taluka Tando Bagho, District Badin to Jhuda Sangi Pharaho road mile 0/0-2/1 (3.5 Kms)	Satisfactory	12-05-2016	Work and Service	14-07-2016	Badin	21.916
787.	2143	CONSTRUCTION OF ROAD FROM AMIR BUX UMAR TO VILLAGE ISLAM KHAN LASHARI MILE 0/0 - 1/0 (1.60 KMS) (ADP NO: 2143).	Satisfactory	12-05-2016	Work and Service	10-08-2016	Ghotki	16.826
788.	2144	Construction of road from Khanpur Mahar-Sardar Garh Road to village Ganhwar Khan Malik 0/0-1/2 (2.0 kms)	Un-Satisfactory	11-05-2016	Work and Service	01-08-2016	Ghotki	19.015
789.	2043	Construction of Road from machhka Road to Miani Road via Ghulam Hyder Dashti (0/0-2/0 (3.21 Kms)	Satisfactory	09-05-2016	Work and Service	19-09-2016	Ghotki	32.670

790.	2141	Construction of link road from village Sahib Khan Lund to village Khooh Meenhon (2 Kms)	Satisfactory	09-05-2016	Work and Service	19-09-2016	Ghotki	19.618
791.	2142	Construction of road from Mathelo Jarwar to Beero Malano mile 0/0-1/4 (2.40 kms)	Satisfactory	09-05-2016	Work and Service	04-08-2016	Ghotki	22.101
792.	2048	Construction of Road from Larkana Ratodero Road at village Fatehpur to village Haji Motayo Jagirani via Khair Mohammad Jagirani (Parellel to Mirwah) mile 0/0-1/4 (2.40 Kms)	Satisfactory	05-05-2016	Work and Service	10-08-2016	Larkana	35.898
793.	2114	Construction of mettalled Road from the Bridge of Dadu Canal at Pir Sher to Noor Khan Jatoi 0/0-0/7.	Satisfactory	05-05-2016	Work and Service	08-08-2016	Larkana	19.467
794.	1854	Reconditioning of Road village Khair Mohammad Joyo to Sajan Joyo mile 0/0-0/5 (i/c 3000 Rft Retaining Wall)	Un-Satisfactory	04-05-2016	Work and Service	04-08-2016	Larkana	17.021
795.	1851	Improvement of Road off taking from Ratoder Shahdadkot Motorway @ mile 17/7 to Dhing Allah Bux Leghari mile 0/0-6/4 (10.4 Kms).	Satisfactory	04-05-2016	Work and Service	19-09-2016	Larkana, Qambar Shahdadkot	27.805
796.	2117	Construction of Road from village Khuda Bux Mohel to Dargah Pir Chozal ali Shah mile 0/0-1/0 (1.60 Km)	Satisfactory	04-05-2016	Work and Service	03-08-2016	Larkana	18.692
797.	1024	Constt. Of Taluka Office and other required Building in Qazi Ahmed.	Satisfactory	03-05-2016	Work and Service	14-07-2016	Shaheed Benazirabad	79.620
798.	2217	Construction of road from Latif Dino Palh to Trimunh Road mile 0/0-1/2 (2.0 kms)	Satisfactory	27-04-2016	Work and Service	19-09-2016	Sukkur	20.845
799.	2216	CONSTRUCTION OF ROAD FROM DINHO MALIK GOHAR TO BHAMBHO MALANO VIA THATT MINOR MILE 0/0-1/2	Satisfactory	27-04-2016	Work and Service	08-08-2016	Sukkur	23.365
800.	37	CONSTRUCTION OF DARGAH HAZRAT SADARUDDIN SHAH BADSHSH (RIZVI) SITUATED DEH BAKHAR AT TALUKA ROHRI DISTRICT SUKKUR (PHASE-I)	Satisfactory	25-04-2016	Work and Service	25-08-2016	Sukkur	42.300
801.	2215	Construction of Road from Lakho Phulpoto Sim Nala (2.40 km)	Satisfactory	21-04-2016	Work and Service	10-08-2016	Sukkur	24.112
802.	2211	Construction of Road from Arrore Bachal Shah road to village Kadan Khan Chakrani (2.0 kms)	Satisfactory	20-04-2016	Work and Service	03-08-2016	Sukkur	20.083

803.	2100	Construction of road from Tando Adam Jhol road to Daim Thahim mile 0/0-1/2 (2.0 Kms)	Satisfactory	19-04-2016	Work and Service	19-09-2016	Sanghar	20.669
804.	2101	Construction of road from Dargah Manthar Faqir to village GulMuhammad Rajar via village Jamd Rajar road mile 0/0-1/2 (2.00Kms).	Average	19-04-2016	Work and Service	22-09-2016	Sanghar	21.686
805.	492	Construction of Women Police Station.	Satisfactory	15-04-2016	Work and Service	13-07-2016	Khairpur	17.656
806.	2078	Construction of road from Village Boohar to Village Hassan Samejo Paka Karamalak Mile 0/0- 1 / 2 -2.00 Kms	Average	15-04-2016	Work and Service	13-07-2016	Sujawal	19.392
807.	2063	Construction of Village Ghani Kehar Pucca road to Village Jaffar Jat Manwani Mile 0/0- 1 / 2 -2.00 Kms	Average	15-04-2016	Work and Service	13-07-2016	Sujawal	21.140
808.	1826	Improvement / Construction of road from Rajputana Hospital to National Highway Bypass via Gulistan-e-Sajjad village Budho Palari Makhdoom Rafiq-uz-Zaman road dual carriageway road mile 0/0-2/4 (4.0Kms) Replacement scheme.	Satisfactory	13-04-2016	Work and Service	25-07-2016	Hyderabad	300.548
809.	2226	Construction of road from Village Khasso to Village Saleh Arain	Satisfactory	31-03-2016	Work and Service	19-09-2016	Sukkur	13.795
810.	2227	ADP NO: 2227 / CONSTRUCTION OF ROAD FROM HALEJI DHANDHI LINK ROAD TO TO JUNAS MILE 0/0 - 0/5.	Satisfactory	31-03-2016	Work and Service	10-08-2016	Sukkur	11.011
811.	Non-ADP	Construction of paving Block road & Drain@Achyoon qubyoon near christian Mission School of Taluka Rohri	Satisfactory	25-03-2016	Work and Service	18-08-2016	Sukkur	10.000
812.	2139	Construction of Road from Dali Mori link Road to Lakha Mori (2.0 Kms)	Satisfactory	22-03-2016	Work and Service	19-09-2016	Naushero Feroz	23.257
813.	2133	Construction of Road in village Wazir ali Zardari & Pahalwan Yaqoob Siyal (2.0 Kms)	Un-Satisfactory	21-03-2016	Work and Service	01-08-2016	Naushero Feroz	23.585
814.	2138	Construction of Road from village Sakhi Abad via village Mohammad Yousif Brohi Taluka Mehrabpur (2.0 kms)	Satisfactory	21-03-2016	Work and Service	19-09-2016	Naushero Feroz	22.998
815.	993	Construction of Paver Block & Drains in various Streets of Larkana City.	Satisfactory	17-03-2016	Work and Service	31-08-2016	Larkana	70.000
816.	Non-ADP	Construction of Brick pavements ,Surface Drains,CC topping ofvarious UCs of District Nauoshero Feroz (MDGs)	Satisfactory	14-03-2016	Work and Service	01-09-2016	Naushero Feroz	12.550
817.	1239	Construction of (2 Nos) of New rooms of Reference Section of Sir Shah Nawaz Bhutto Memorial Library, Larkana	Satisfactory	14-03-2016	Work and Service	08-08-2016	Larkana	24.806

818.	2196	Construction of Road from Ahmedpur Road to Sodhal Khan Shar via Malhar Shar Road mile 0/0-1/2 (2.0 Km)	Satisfactory	11-03-2016	Work and Service	17-08-2016	Khairpur	17.435
819.	2197	Construction of Road from Bindho Faiz Mohammad Road village Almani Narejo to Chuttal Narejo Road mile 0/0-1/2 (2.0 kms)	Satisfactory	11-03-2016	Work and Service	02-08-2016	Khairpur	22.620
820.	2055	Construction of Road Backside of Atteri to village Razi Goth (2.40 kms)	Un-Satisfactory	10-03-2016	Work and Service	01-08-2016	Khairpur	25.257
821.	2161	Construction of Road from village Mohabbatpur to Imdad Sahito UC Pir Hayat Shah Taluka Sobhodero Road mile 0/0-1/2 (2.0 kms).	Un-Satisfactory	10-03-2016	Work and Service	01-08-2016	Khairpur	26.258
822.	2180	Construction of internal road village Jiskani road mile 0/0-1/0 (1.60 Km)	Satisfactory	10-03-2016	Work and Service	02-08-2016	Khairpur	15.523
823.	2193	Construction of road from Pir Wassan Mehrabpur to village Faiz Mohammad Jojai Road mile 0/0-1/2 (2.0 kms)	Satisfactory	10-03-2016	Work and Service	04-08-2016	Khairpur	22.269
824.	2041	Construction of Road from Setharija Pir Budhro Road Haji Rajper via Khaskheli viillage 14.0 Km	Un-Satisfactory	09-03-2016	Work and Service	03-08-2016	Khairpur	58.511
825.	1871	Rehabilitation of (Dual Carriageway) road from National Highway near Staff Quarters to Jillani Mohalla i/c Asphalt concrete (1.0 Km)	Satisfactory	09-03-2016	Work and Service	04-08-2016	Khairpur	24.798
826.	2053	Construction of Road and retaining wall at village Wari Goth (1.40 km)	Satisfactory	09-03-2016	Work and Service	04-08-2016	Khairpur	29.596
827.	2175	Construction of road A.G Balouch to Ali Hyder Jalbani (1.40 km)	Satisfactory	09-03-2016	Work and Service	17-08-2016	Khairpur	18.014
828.	2179	Construction of Road village Tajo Khan Sakhani to village Saleem Shah (1.60 km)	Satisfactory	09-03-2016	Work and Service	02-08-2016	Khairpur	16.933
829.	2007	Construction of road from Talpur Wada to village Khawaja (3.00 Kms).	Un-Satisfactory	08-03-2016	Work and Service	01-08-2016	Khairpur	19.143
830.	2189	Construction of Road from new N.H.Way to Abdul Wahid Wassan road mile 0/0- 1/0 (1.60 km)	Satisfactory	08-03-2016	Work and Service	02-08-2016	Khairpur	18.245
831.	2191	Construction of Road from Sim Nala to village Faiz Mohammad Chakrani UC Deh Sohu Road mile 0/0-1/2 (2.0 km)	Satisfactory	08-03-2016	Work and Service	01-08-2016	Khairpur	21.040
832.	1873	Reconditioning / Construction of road N.H way to village Abdul	Satisfactory	07-03-2016	Work and Service	29-07-2016	Khairpur	20.954

		Sattar Phulpoto Road Mile 0/0-1/7. (3.00 Km).						
833.	1872	Recondition of Road from Rahuja Minor to Kot Pul (3.0 kms)	Average	07-03-2016	Work and Service	29-07-2016	Khairpur	18.162
834.	1280	Construction of play ground at Dabbar, Taluka Khairpur.	Un-Satisfactory	22-01-2016	Work and Service	16-08-2016	Khairpur	19.000
835.	889	Establishment of Dispensory Building at Khairpur & Sukkur.	Un-Satisfactory	23-12-2015	Work and Service	18-08-2016	Khairpur	8.058
836.	1096	Reconditioning of road from Hira Hospital to Ghanta Ghar patch work and asphalt concrete i/c link Teer Chowk to Bunder Road, Al-Habib Hotel to Karam Ali Shah and link to Shamsabad (3.5 Kms), (To be funded out of 10% share of Royalty)	Un-Satisfactory	19-12-2015	Work and Service	04-08-2016	Sukkur	116.715
837.	1023	Construction of District Election Commissioner's Office, Khairpur and residence at first floor Khairpur, (To be funded out of 10% share of Royalty)	Satisfactory	16-12-2015	Work and Service	03-08-2016	Khairpur	30.457
838.	481	High Way Patrolling Post (105 Nos) in Sindh (Karachi, Hyderabad, Mirpurkhas, SBA, Sukkur, Ghotki, N. Feroz, Larkana, Jacobabad)	Un-Satisfactory	15-12-2015	Work and Service	07-09-2016	Shaheed Benazirabad	436.044
839.	1852	W/R Nasirabad to Badeh Road mile 0/0-2/0 (Remaining Work) 2	Satisfactory	30-09-2015	Work and Service	10-08-2016	Larkana	54.090
840.	1820	Reconditioning of Road from Mirpur to Mohammadpur mile 4/0-8/0 (6.40 Kms), (To be funded out of 10% share of Royalty)	Satisfactory	28-09-2015	Work and Service	08-08-2016	Ghotki	50.376
841.	1804	W/R of road from Desert Area road to Hazrat Hout Fakir via Serai Mohabat Sethar road mile 0/0-5/4 (8.85 Kms)	Un-Satisfactory	18-09-2015	Work and Service	05-08-2016	Shaheed Benazirabad	189.202
842.	1797	W/R of road from 60 mile road to 3 chak suhello road mile 0/0-13/0 (asphalt)	Un-Satisfactory	17-09-2015	Work and Service	10-08-2016	Shaheed Benazirabad	250.854
843.	1799	Reconditioning of road from Mianshoro via Kallay Bux Rind Sakrand City road mile 0/0-3/5 (5.83 Kms).	Satisfactory	17-09-2015	Work and Service	10-08-2016	Shaheed Benazirabad	70.305
844.	1864	Reconditioning of Road from Shikarpur Zarkhail Road to Fakir Din Mohammad Kehar mile 0/0-2/0 (3.2 Kms)	Satisfactory	19-08-2015	Work and Service	08-08-2016	Shikarpur	21.246
845.	1761	W/R of road from Kandiaro - Taharu Shah via Derbelo.	Satisfactory	12-08-2015	Work and Service	17-08-2016	Naushero Feroz	199.902
846.	2890	Construction of Bridges in various District of Province (Badin, Thatta, Malir, Tharparkar, Sanghar, Khairpur & Sukkur)	Satisfactory	14-07-2015	Work and Service	05-08-2016	Khairpur, Sukkur	331.950
						Total:		443,186.300



*ENHANCING EFFICIENCY,
IMPROVING DELIVERABLES*

ANNEXURE B

SUMMARY OF SCHEMES COMPLETED IN 2016-17

FINANCIAL REVIEW OF ALLOCATION, RELEASES & UTILISATION

PAGE 115 TO PAGE 116

SUMMARY OF SCHEMES COMPLETED IN 2016-17

Total Ongoing New Completed

S.#.	Department	# of Schemes	Estimated Cost	Allocation
1	Agriculture	7	2,060.029	556.098
2	Board Of Revenue	1	4,997.453	1,322.782
3	Culture, Tursim & Antiquities Department	20	1,105.235	421.927
4	Education Literacy Department	16	1,340.796	540.523
5	Energy Department	1	934.820	1.000
6	Governors Secretariat	2	380.319	105.000
7	Health Department	8	7,758.153	1,885.170
8	Home Department	5	180.279	21.214
9	Information & Archives Department	3	172.000	142.878
10	Irrigation Department	37	3,813.597	771.331
11	Katchi Abadis & Spatial Development Department	1	57.120	57.120
12	Labour & Human Resources Department	2	106.830	24.675
13	LAW, P.A, Prosecution & Human Rights Department	4	270.304	59.341
14	Livestock & Fisheries Department	2	1,038.228	180.903
15	Local Government Department	161	20,870.980	5,696.225
16	Mines & Mineral Development Department	1	31.667	5.565
17	Planning & Development Department	1	639.332	71.415
18	Services. General Administration & Coordination Department	3	106.010	56.010
19	Sindh Board Investment	1	50.000	13.745
20	Social Welfare Department	2	81.248	47.349
21	Sport & Youth Affairs Department	12	543.519	258.854
22	Women Development Department	1	59.302	15.390
23	Works & Services Department	172	8,868.330	2,792.283
	TOTAL	463	55,465.551	15,046.798

FINANCIAL REVIEW – ALLOCATION, RELEASES & UTILISATION

Department	Schemes	Allocation	Release	Expenditure	Utilised	
AGRICULTURE, SUPPLY & PRICES	39	5,794	3,697.69	63.82%	3,231.02	87%
AUQAF, ZAKAT, USHR & R.A.	22	277	226.92	81.92%	219.17	97%
BOARD OF REVENUE	9	3,728	2,938.19	78.81%	1,889.02	64%
CHIEF MINISTER'S SECTT:	3	300	210.71	70.24%	210.71	100%
COOPERATIVE	2	30	19.27	64.24%	19.27	100%
CDP for SDGs	1	8,500	6,538.21	76.92%	6,231.29	95%
CULTURE, TOUR. & ANTIQ:	66	2,019	1,720.53	85.22%	1,524.99	89%
EDUCATION SECTOR	397	17,233	11,860.32	68.82%	10,126.68	85%
ENERGY	6	6,335	1,538.65	24.29%	1,504.05	98%
ENVIRONMENT & COASTAL DEVELOPMENT	10	455	228.75	50.27%	170.43	75%
EXCISE & TAXATION	4	160	66.15	41.35%	63.92	97%
FINANCE	4	1,054	155.78	14.78%	136.55	88%
FOOD	4	383	-	0.00%	-	0%
FOREST & WILDLIFE	14	804	546.89	68.02%	426.64	78%
GOVERNOR'S SECRETARIAT	1	100	100.00	100.00%	100.00	100%
HEALTH	146	14,000	9,867.81	70.48%	6,952.94	70%
HOME	75	2,000	1,761.83	88.09%	1,647.72	94%
INDUSTRIES & COMMERCE	22	2,829	1,730.79	61.18%	1,518.64	88%
INFORMATION & ARCHIVES	14	257	184.61	71.83%	176.36	96%
INFORMATION, SCI. & TECH	11	533	63.93	11.99%	52.87	83%
IRRIGATION	306	14,000	36,362.46	259.73%	35,515.22	98%
KATCHI ABADIS	3	93	44.00	47.31%	34.79	79%
LABOUR & HUMAN RES:	4	120	54.05	45.04%	30.06	56%
LAW P.A, PROSECUTION & HUMAN RIGHTS	44	1,157	1,214.05	104.93%	1,150.37	95%
LINING OF MAIN CANALS	1	12,000	-	0.00%	-	0%
LIVESTOCK & FISHERIES	40	1,798	1,085.55	60.38%	653.45	60%
LOCAL GOVERNMENT & HTP	422	20,731	17,565.93	84.73%	16,095.70	92%
MATCHING ALLOCATION	3	7,500	4,211.50	56.15%	3,365.19	80%
MEGA PROJECTS FOR KARACHI CITY	21	10,000	7,596.77	75.97%	7,538.75	99%
MINES & MINERAL DEV:	10	160	26.53	16.58%	6.84	26%
MINORITIES AFFAIRS	13	604	546.94	90.55%	509.93	93%
NEW DEVELOPMENT INIT.	1	5,000	-	0.00%	-	0%
NUTRITION SUPPORT INIT.	1	1,000	-	0.00%	-	0%
PLANNING & DEVELOPMENT	16	3,783	2,018.35	53.35%	1,455.00	72%
POPULATION WELFARE	6	745	273.91	36.77%	177.83	65%
PROVINCIAL ASSEMBLY	3	1,065	1,565.00	146.95%	1,565.00	100%
PROVINCIAL OMBUDSMAN	2	31	-	0.00%	-	0%
PUBLIC HEALTH ENGG: & RD	313	7,267	9,259.93	127.42%	8,888.71	96%
REHABILITATION (PDMA)	5	692	227.15	32.83%	67.03	30%
SGA&CD	43	3,887	2,273.48	58.49%	1,493.73	66%
SINDH BOARD OF INVEST.	5	277	122.04	44.06%	77.04	63%
SINDH REVENUE BOARD	1	500	-	0.00%	-	0%
SOCIAL WELFARE	12	290	117.25	40.43%	56.52	48%
SPECIAL INITIATIVES	20	5,523	3,336.80	60.42%	2,793.11	84%
SPORTS & YOUTH AFFAIRS	67	2,000	1,890.92	94.55%	1,820.80	96%
THAR COAL INFRASTR. DEV:	27	15,365	15,100.43	98.28%	14,621.64	97%
TRANSPORT & MASS TRANSIT	10	3,195	256.76	8.04%	183.37	71%
WOMEN DEVELOPMENT	11	426	84.67	19.88%	19.29	23%
WORKS & SERVICES	513	14,000	24,378.81	174.13%	23,609.25	97%
TOTAL	2,773	200,000	173,070.30	0.87	157,930.87	91%

INTENTIONALLY LEFT BLANK

ANNEXURE C

FINANCIAL REVIEW OF REALLOCATION & VARIANCE PROGRESS SUMMARY OF PSDP EXECUTED BY GOVT. OF SINDH PAGE 119 TO PAGE 121

FINANCIAL REVIEW OF REALLOCATION & VARIANCE

#	SECTOR / DEPARTMENT	ORIGINAL				REVISED		VARIANCE	
		Capital		Revenue		Total	Total	Total	
	PROVINCIAL PROGRAMME	Rs.	%	Rs.	%	Rs.	Rs.	Rs.	%
1	AGRICULTURE, SUPPLY & PRICES	607.691	10%	5,186.309	90%	5,794.105	2,390.972	-3,403.133	-59%
2	AUQAF, ZAKAT, USHR & R.A.	264.719	96%	12.281	4%	277.956	180.471	-97.485	-35%
3	BOARD OF REVENUE	1,919.011	51%	1,808.989	49%	3,728.515	2,020.480	-1,708.035	-46%
4	CHIEF MINISTER'S SECTT:	300.000	100 %	0.000	0%	301.000	0.000	-301.000	-100%
5	COOPERATIVE	25.272	84%	4.728	15%	30.842	19.279	-11.563	-37%
6	CDP for SDGs	8,500.000	100 %	0.000	0%	8,501.000	0.000	-8,501.000	-100%
7	CULTURE, TOUR. & ANTIQUITIES	1,495.558	74%	523.442	26%	2,019.741	1,282.519	-737.222	-37%
8	EDUCATION SECTOR	13,564.994	79%	3,668.006	21%	17,236.032	9,682.738	-7,553.294	-44%
	(i) Education & Literacy	10,165.971	78%	2,834.029	22%	13,000.782	7,250.202	-5,750.580	-44%
	(ii) Special Education	127.986	60%	85.014	40%	213.601	73.269	-140.332	-66%
	(iii) STEVTA	902.356	85%	162.644	15%	1,065.847	386.397	-679.450	-64%
	(iv) Universities & Boards	2,368.681	80%	586.319	20%	2,955.802	1,972.870	-982.932	-33%
9	ENERGY	6,210.000	98%	125.000	2%	6,335.980	1,538.645	-4,797.335	-76%
10	ENVIRONMENT & COASTAL DEVELOPMENT	159.328	35%	295.672	65%	455.351	228.748	-226.603	-50%
11	EXCISE & TAXATION	27.692	17%	132.308	83%	160.173	0.000	-160.173	-100%
12	FINANCE	305.780	29%	748.220	71%	1,054.290	525.710	-528.580	-50%
13	FOOD	383.000	100 %	0.000	0%	384.000	0.000	-384.000	-100%
14	FOREST & WILDLIFE	253.006	31%	550.994	69%	804.315	448.992	-355.323	-44%
15	GOVERNOR'S SECRETARIAT	100.000	100 %	0.000	0%	101.000	100.000	-1.000	-1%
16	HEALTH	7,646.656	55%	6,353.344	45%	14,000.546	8,066.887	-5,933.659	-42%
17	HOME	1,865.999	93%	134.001	7%	2,000.933	1,620.959	-379.974	-19%
18	INDUSTRIES & COMMERCE	2,745.500	97%	83.500	3%	2,829.970	1,065.260	-1,764.710	-62%
19	INFORMATION & ARCHIVES	128.385	50%	128.615	50%	257.500	20.322	-237.178	-92%
20	INFORMATION, SCI. & TECH	0.000	0%	533.000	100%	533.000	53.776	-479.224	-90%
21	IRRIGATION	13,928.363	99%	71.637	1%	14,000.995	32,177.993	18,176.998	130%
22	KATCHI ABADIS	93.000	100 %	0.000	0%	94.000	0.000	-94.000	-100%
23	LABOUR & HUMAN RESOURCE	91.976	77%	28.024	23%	120.766	54.045	-66.721	-55%
24	LAW P.A, PROSECUTION & HUMAN RIGHTS	1,109.400	96%	47.600	4%	1,157.959	1,160.595	2.636	0%
25	LINING OF MAIN CANALS	12,000.000	100 %	0.000	0%	12,001.000	0.000	-12,001.000	-100%
26	LIVESTOCK & FISHERIES	808.246	45%	989.754	55%	1,798.450	742.561	-1,055.889	-59%
27	LOCAL GOVERNMENT & HTP	19,559.435	94%	1,171.565	6%	20,731.943	13,447.734	-7,284.209	-35%
	(i) Local Government	16,027.795	99%	243.488	1%	16,272.268	13,220.733	-3,051.535	-19%
	(ii) Sindh Solid Waste Management	1,531.640	62%	928.077	38%	2,460.340	227.001	-2,233.339	-91%

	(iii) Improvement of Major Cities/ Towns	2,000.000	100 %	0.000	0%	2,001.000	0.000	-2,001.000	-100%
28	MATCHING ALLOCATION	7,500.000	100 %	0.000	0%	7,501.000	7,246.495	-254.505	-3%
29	MEGA PROJECTS FOR KARACHI CITY	9,501.000	95%	499.000	5%	10,000.950	6,207.528	-3,793.422	-38%
30	MINES & MINERAL DEVELOPMENT	0.000	0%	160.000	100%	160.000	26.528	-133.472	-83%
31	MINORITIES AFFAIRS	604.000	100 %	0.000	0%	605.000	546.820	-58.180	-10%
32	NEW DEVELOPMENT INITIATIVE	5,000.000	100 %	0.000	0%	5,001.000	0.000	-5,001.000	-100%
33	NUTRITION SUPPORT INITIATIVE	200.000	20%	800.000	80%	1,000.200	0.000	-1,000.200	-100%
34	PLANNING & DEVELOPMENT	1,057.000	28%	2,726.000	72%	3,783.279	3,349.655	-433.624	-11%
35	POPULATION WELFARE	306.500	41%	438.500	59%	745.411	273.912	-471.499	-63%
36	PROVINCIAL ASSEMBLY	1,065.000	100 %	0.000	0%	1,066.000	1,451.726	385.726	36%
37	PROVINCIAL OMBUDSMAN	10.681	34%	20.319	65%	31.345	0.000	-31.345	-100%
38	<u>PUBLIC HEALTH ENGG. & RD</u>	<u>5,967.000</u>	<u>82%</u>	<u>1,300.000</u>	18%	<u>7,267.821</u>	<u>7,362.287</u>	94.466	1%
	(i) Public Health Engineering	4,267.000	100 %	0.000	0%	4,268.000	3,787.672	-480.328	-11%
	(ii) Rural Development	1,700.000	57%	1,300.000	43%	3,000.567	3,574.615	574.048	19%
39	REHABILITATION (PDMA)	557.000	80%	135.000	19%	692.805	152.287	-540.518	-78%
40	SGA&C	3,758.543	97%	128.457	3%	3,887.967	1,827.106	-2,060.861	-53%
41	SINDH BOARD OF INVEST.	200.000	72%	77.000	28%	277.722	122.035	-155.687	-56%
42	SINDH REVENUE BOARD	450.000	90%	50.000	10%	500.900	0.000	-500.900	-100%
43	SOCIAL WELFARE	220.000	76%	70.000	24%	290.759	117.250	-173.509	-60%
44	SPECIAL INITIATIVES	4,342.935	79%	1,180.065	21%	5,523.786	2,910.140	-2,613.646	-47%
45	SPORTS & YOUTH AFFAIRS	1,774.344	89%	225.656	11%	2,000.887	1,137.138	-863.749	-43%
46	THAR COAL INFRASTR. DEV.	14,976.685	97%	388.315	3%	15,365.975	14,791.549	-574.426	-4%
47	TRANSPORT & MASS TRANSIT	2,711.375	85%	483.625	15%	3,195.849	592.343	-2,603.506	-81%
48	WOMEN DEVELOPMENT	87.500	21%	338.500	79%	426.205	64.128	-362.077	-85%
49	WORKS & SERVICES	13,972.392	100 %	27.608	0%	14,000.998	21,376.261	7,375.263	53%
TOTAL PROVINCIAL		168,354.966	84%	31,645.034	16%	200,037.220	146,383.874	-53,653.346	-27%

* Data regarding "Revised Allocation" is not available in the Budget Book Volume-V for the year 2017-2018.

PROGRESS SUMMARY OF PSDP 2016-17 SCHEMES EXECUTED BY GOVT. OF SINDH

Rs. in million

#	Name of the Division	# of Schemes	Estimated Cost		Expenditure up to June 2016	Throw-forward as on 01-07-16	Allocation 2016-17			Releases position as per Planning Commission website on 30-06-2017	Releases as per Finance Department, GOS as on 30-06-2017	Expenditure during 2016-17
			Total	Foreign Aid			Foreign Aid	Rupee	Total			
1	FINANCE DIVISION	9	30,008.320	0.000	12,511.633	17,616.774	0.000	28,51.425	28,51.425	2,057.804	1,457.804	1,457.804
2	NATIONAL HEALTH SERVICES, REGULATIONS & COORDINATION	9	37,206.523	0.000	19,558.963	17,647.560	0.000	4,986.590	4,986.590*	2,557.925	2,914.925	0.000
3	<u>WATER & POWER DIVISION (WATER)</u>	7	118,786.972	0.000	54,372.580	64,414.392	0.000	5,400.000	5,400.000	2,054.535	2,054.535	2,054.535
	GRAND TOTAL	25	186,001.815	0.000	86,443.176	99,678.726	0.000	13,238.015	13,238.015	6,670.264	6,427.264	3,512.339

INTENTIONALLY LEFT BLANK



ELEMENT BEHIND SUCCESS

ANNEXURE D

MEC OFFICES & TEAM MEMBERS

ACRONYMS

MEC OFFICES & TEAM MEMBERS

SECRETARIAT HEAD OFFICE	
FAISAL AHMED UQAILI	Director General
Syed Imtiaz Ali Shah	Ex-Director General
Riaz Ali Abbasi	Director (MEC)
Syed R. Hashmi	Deputy Director (MEC)
Ghullan Khan Khaskheli	Deputy Director (CM Directives)
Javed Ali Khawaja	Sector Monitoring Officer (SMO) - Social Sector
Saeed Ahmed Nizamani	Procurement Specialist
Naweed Saleh Memon	System Analyst
M. Javed Khan	Assistant Director (Accounts)
Iqbal Lakhmair	Assistant Director (Admin)

MIS DIRECTORATE	
NAVEED MANSOOR	Director (MIS)
Sarfaraz Ahmed	Assistant Director (Programming)
Amjad Ali	Assistant Director (Network)
Mohsin Ali	Assistant Director (Coord)
Tufail Ahmed Shaikh	Assistant Director (Content Management)
Ashraf Baloch	Sr. Programmer
Shadab Hussain	Programmer(.Net)
Bilal Bin Ismail	Programmer (OS)
Parkash Kumar	Programmer (GIS)
Teerath Kumar	Network Admin

REGIONAL MONITORING OFFICE HYDERABAD	
TUFAIL AHMED ABRO	Regional Monitoring Officer
Muhammad Azeem Jarwar	MEO(Roads)
Muhammad Salman Shaikh	MEO(Education)
Aurangzeb Vistro	MEO(Irrigation)
Muhammad Amir Arain	MEO(Health)
Muhammad Naeem Korejo	MEO(Agriculture)
Dr. Shamsuddin Mahesar	MEO(Live/Stock)
Ghulamullah Mahar	MEO(Building)
Dr. Saima	MEO(Health)
Mr. Imran	MEO(Road)
Mr. Muhammad Amjad Hussain	MEO (Roads)
Bilal Ahmed	MEO (Education)
Sallah Saleh Thebo	Admin & Accounts Officer
Shabbir Ahmed Pandhiani	Evaluation Officer
Thakur Das	Evaluation Officer

REGIONAL MONITORING OFFICE KARACHI

DR. AZIZ CHANNA	Regional Monitoring Officer (RMO)
Mr. Fateh Uddin Junejo	Sector Monitoring Officer - SMO - Infrastructure
Mr. Hafeez-ur-Rehman Janwari	Assistant Director (HR)
Dr. Mohsin Siddiqui	MEO (Health)
Mr. Shah Faisal	MEO (Livestock & Fish)
Mr. Nadeem Ahmed Daudpota	System Support Engineer
Mr. Muhammad Hanif Hingoro	MEO (Social Sector)
Mr. Abdul Qayoom	MEO (Water Supply & Drainage)
Ms. Rabia Muhammad Ali	MEO (Building)
Mr. Tanveer Ahmed Shaikh	MEO (Building)
Mr. Umair Aslam	MEO (Roads)
Mr. Muhammad Amjad Hussain	MEO (Roads)
Bilal Ahmed	MEO (Education)
Sallah Saleh Thebo	Admin & Accounts Officer
Shabbir Ahmed Pandhiani	Evaluation Officer
Thakur Das	Evaluation Officer

REGIONAL MONITORING OFFICE SUKKUR

Shahzeb Ahmed Shaikh	Regional Monitoring Officer (RMO)
Rasheed Ahmed Jumani	Monitoring & Evaluation Officer (Agriculture)
Shafquat Shah	Monitoring & Evaluation Officer (Health)
Kashif Anwar	Monitoring & Evaluation Officer (WS&D)
Dr. Shazia Mahar	Monitoring & Evaluation Officer (Livestock & Fisheries)
Rameez Bajkani	Monitoring & Evaluation Officer (Roads)
Moin Umer	Monitoring & Evaluation Officer (Buildings)
Shuja Ahmed Lanjar	Programmer

REGIONAL MONITORING OFFICE LARKANA

SARFRAZ ALI MEMON	Regional Monitoring Officer (RMO)
Ahmed Hussain Mahar	Monitoring & Evaluation Officer (Agriculture)
Nisar Ahmed Khatti	Monitoring & Evaluation Officer (Irrigation)
Ali Raza Mangi	Monitoring & Evaluation Officer (Roads)
Ashiq Hussain Jatoi	Monitoring & Evaluation Officer (Health)
Jahanzeb Mallah	Monitoring & Evaluation Officer (Education)
Dr. Jahangir Khan Chandio	Monitoring & Evaluation Officer (Live Stock & Fishries)
Mohsan Ali Memon	Monitoring & Evaluation Officer (Social Sector)
Muhammad Halar Zaman	Monitoring & Evaluation Officer (Water Supply & Drainage)
Mr. Muhammad Hanif Abro	Monitoring & Evaluation Officer (Buildings)
Ghulam Murtaza Khan	System Support Engineer

ACRONYMS

#	ACRONYM	DETAIL
1	ACS	Additional Chief Secretary
2	AD	Administrative Department
3	ADB	Asian Development Bank
4	ADP	Annual Development Plan
5	CD/CDA	Coastal Development Authority
6	CDWP	Central Development Working Party
7	CM	Chief Minister
8	CMS	Content Management System
9	DC	Deputy Commissioner
10	DDWP	District Development Working Party
11	DEV	Development
12	DG	Director General
13	DS	Deputy Secretary
14	EA	Executing Agency
15	FD	Finance Department
16	FiMS	File Management System
17	FY	Fiscal Year
18	GIS	Geographic Information System
19	GOS	Government Of Sindh
20	GPS	Global Positioning System
21	HR	Human Resource
22	IMP	Implementation
23	KMC	Karachi Metropolitan Corporation
24	M&E	Monitoring and Evaluation
25	MEC/M.E.C.	Monitoring and Evaluation Cell
26	MEO/MO	Monitoring and Evaluation Officer
27	MIS	Management Information System
28	P&D	Planning and Development
29	PD	Project Director
30	PDWP	Provincial Development Working Party
31	PHED	Public Health Engineering Department
32	PM	Prime Minister
33	PMESI	Project Monitoring and Evaluation System Improved
34	PS	Personal Secretary
35	RMEO/RMO	Regional Monitoring and Evaluation Officer
36	SBI	Sindh Board of Investment
37	SGACD	Services General Administration and Coordination
38	SGRRP	Sindh Growth and Rural Rehabilitation Program
39	SMEO/SMO	Sector Monitoring and Evaluation Officer
40	SMES	Schemes Management & Evaluation System
41	SMS	Short Messaging Service
42	TPM	Third Party Monitoring
43	XEN	Executive Engineer

